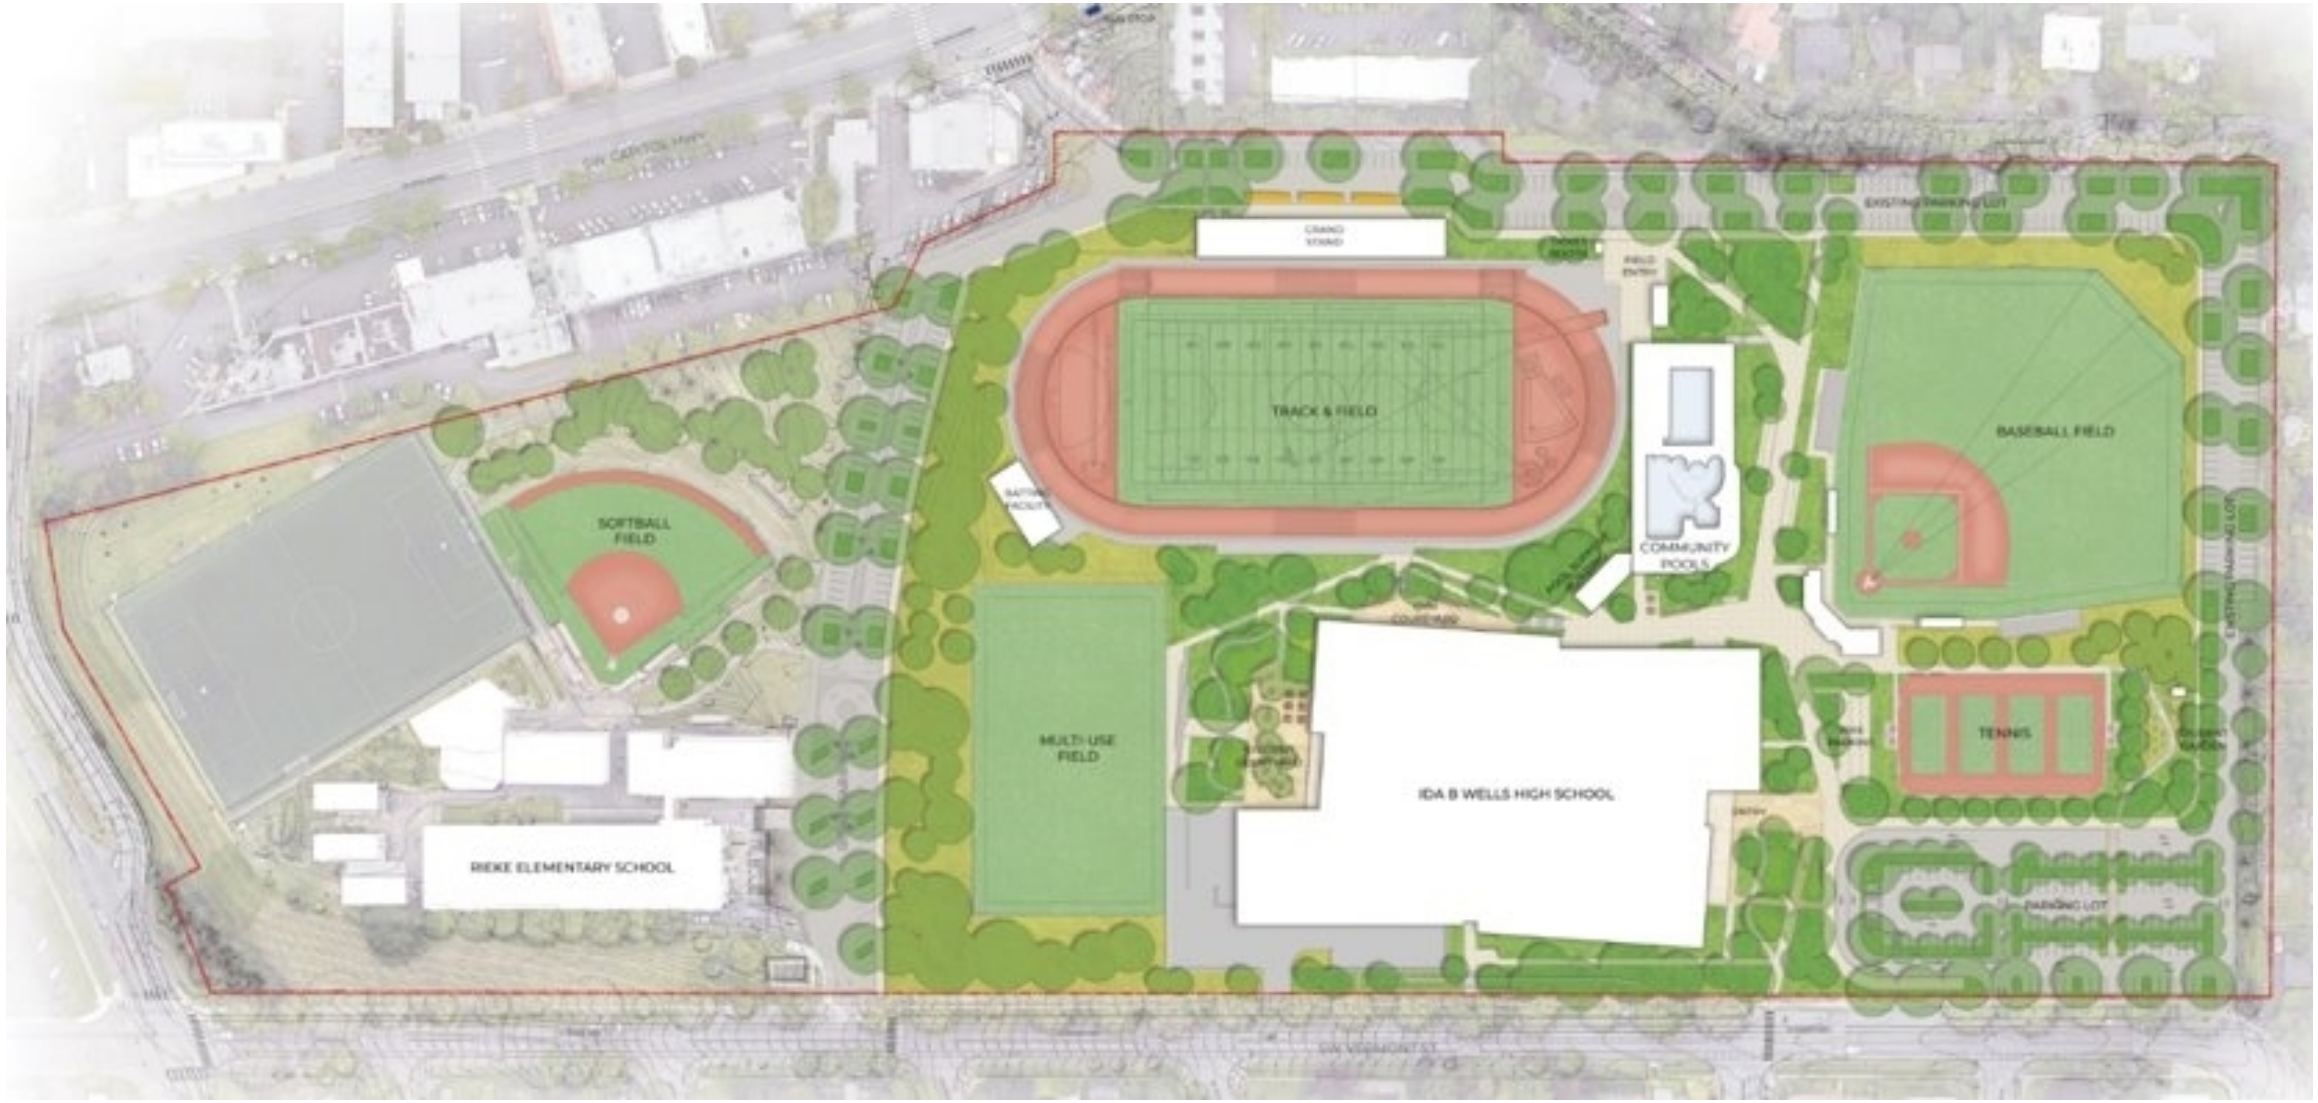


Ida B. Wells High School Modernization Comprehensive Plan Update


October 14th, 2025

PORTLAND PUBLIC SCHOOLS


Site Design



TRACK & FIELD
SOFTBALL FIELD
COMMUNITY POOLS
BASEBALL FIELD
MULTI-USE FIELD
IDA B WELLS HIGH SCHOOL
TENNIS
RIEKE ELEMENTARY SCHOOL

Building Organization

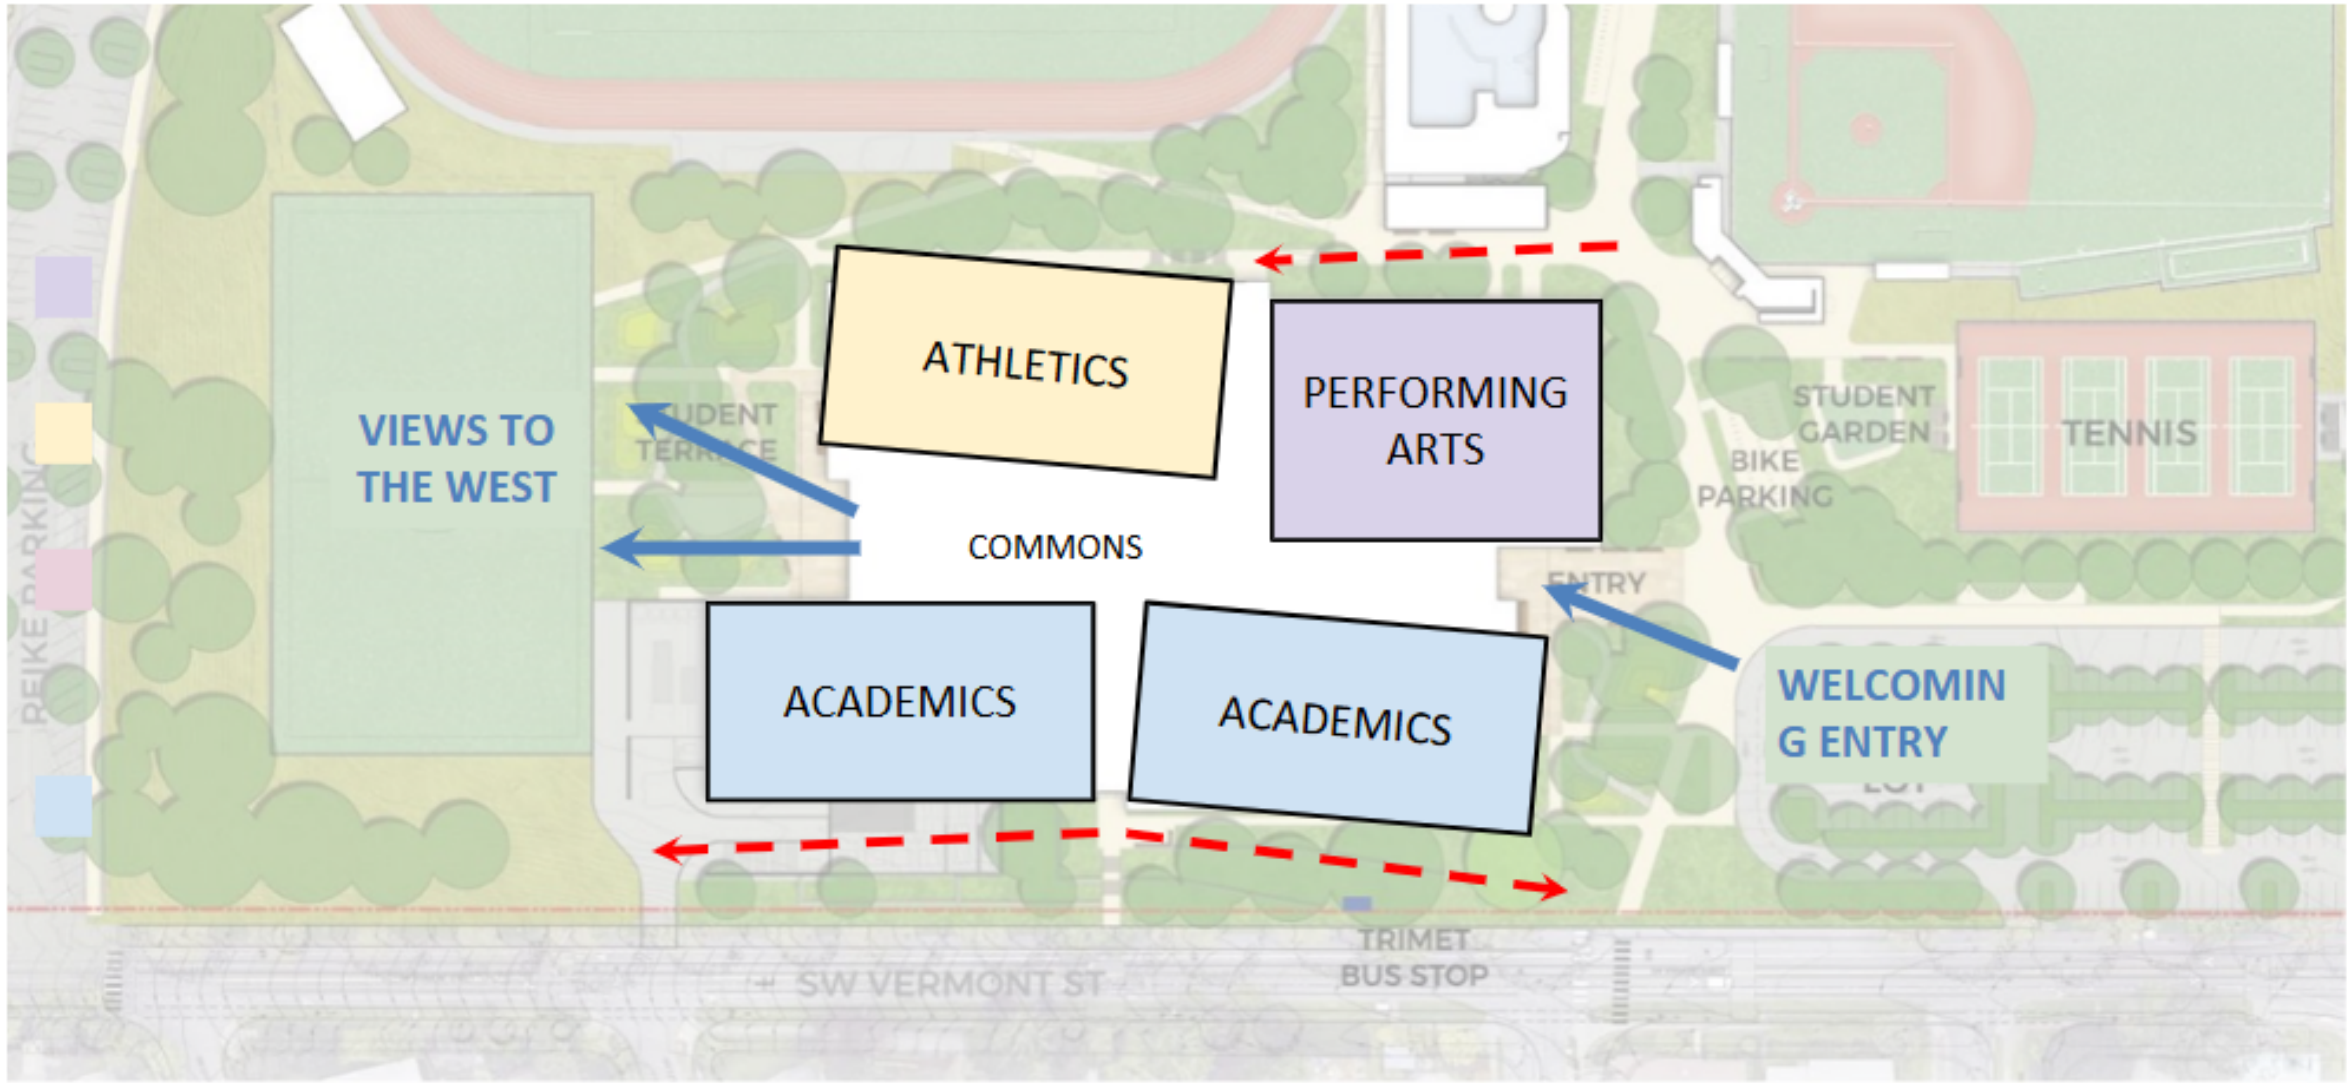

Level 1 (Main Entrance Level) & Level 0 (Terrace Level) Floor Plan

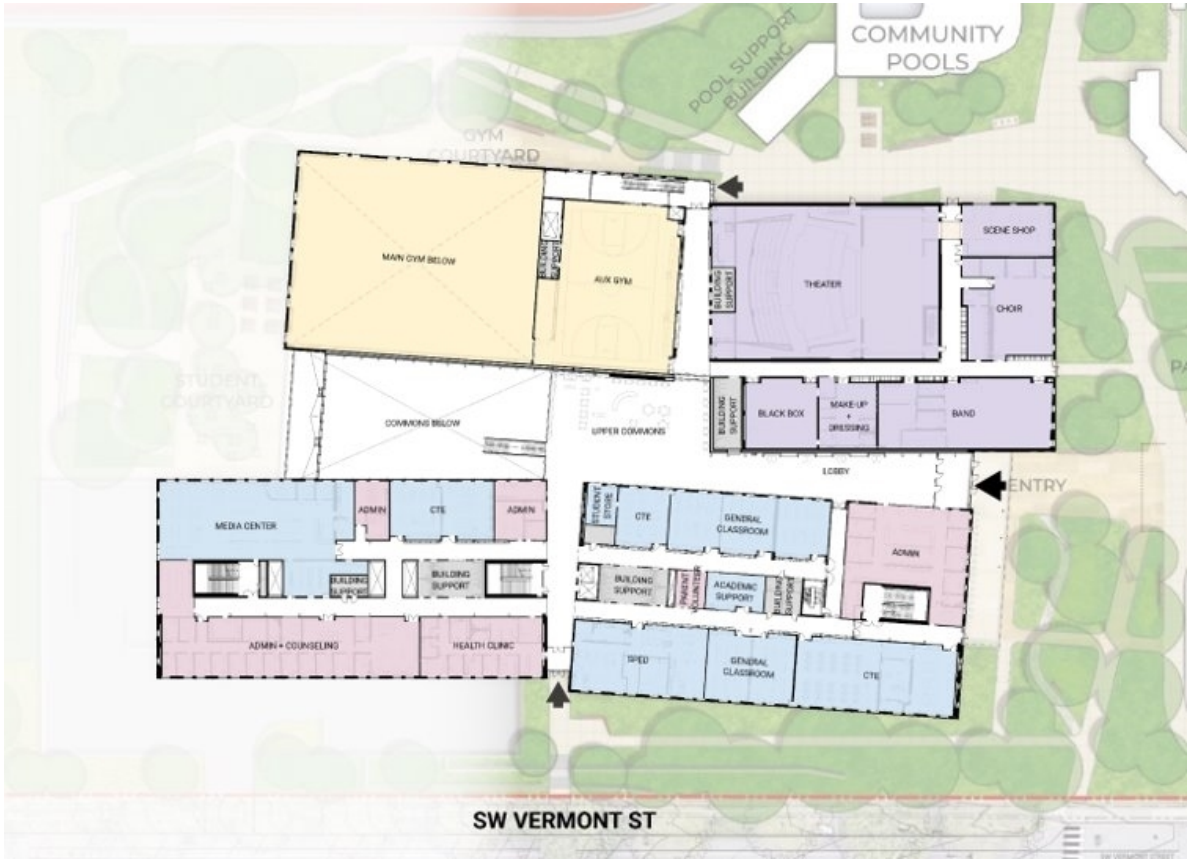

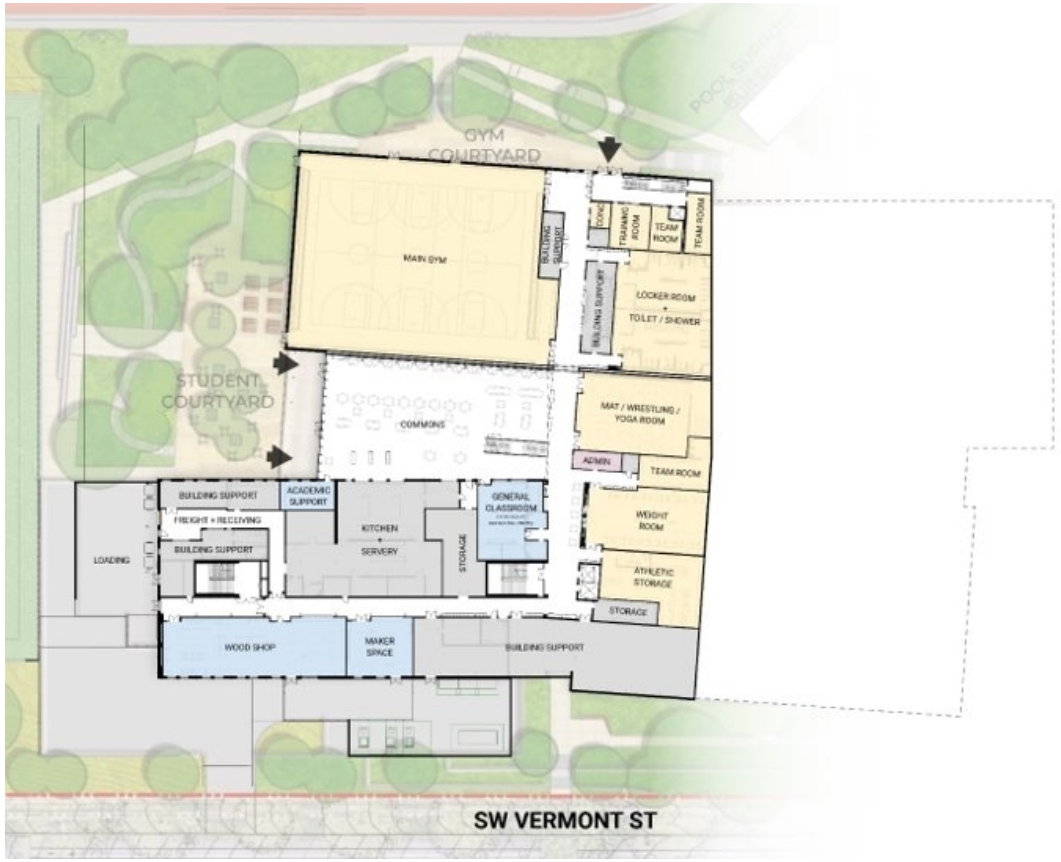


Level 2 & 3 Floor Plan






SCHOOL BOARD FRAMEWORK

"REDUCE BUILDING AREA TO APPROXIMATELY 295,000 sf"

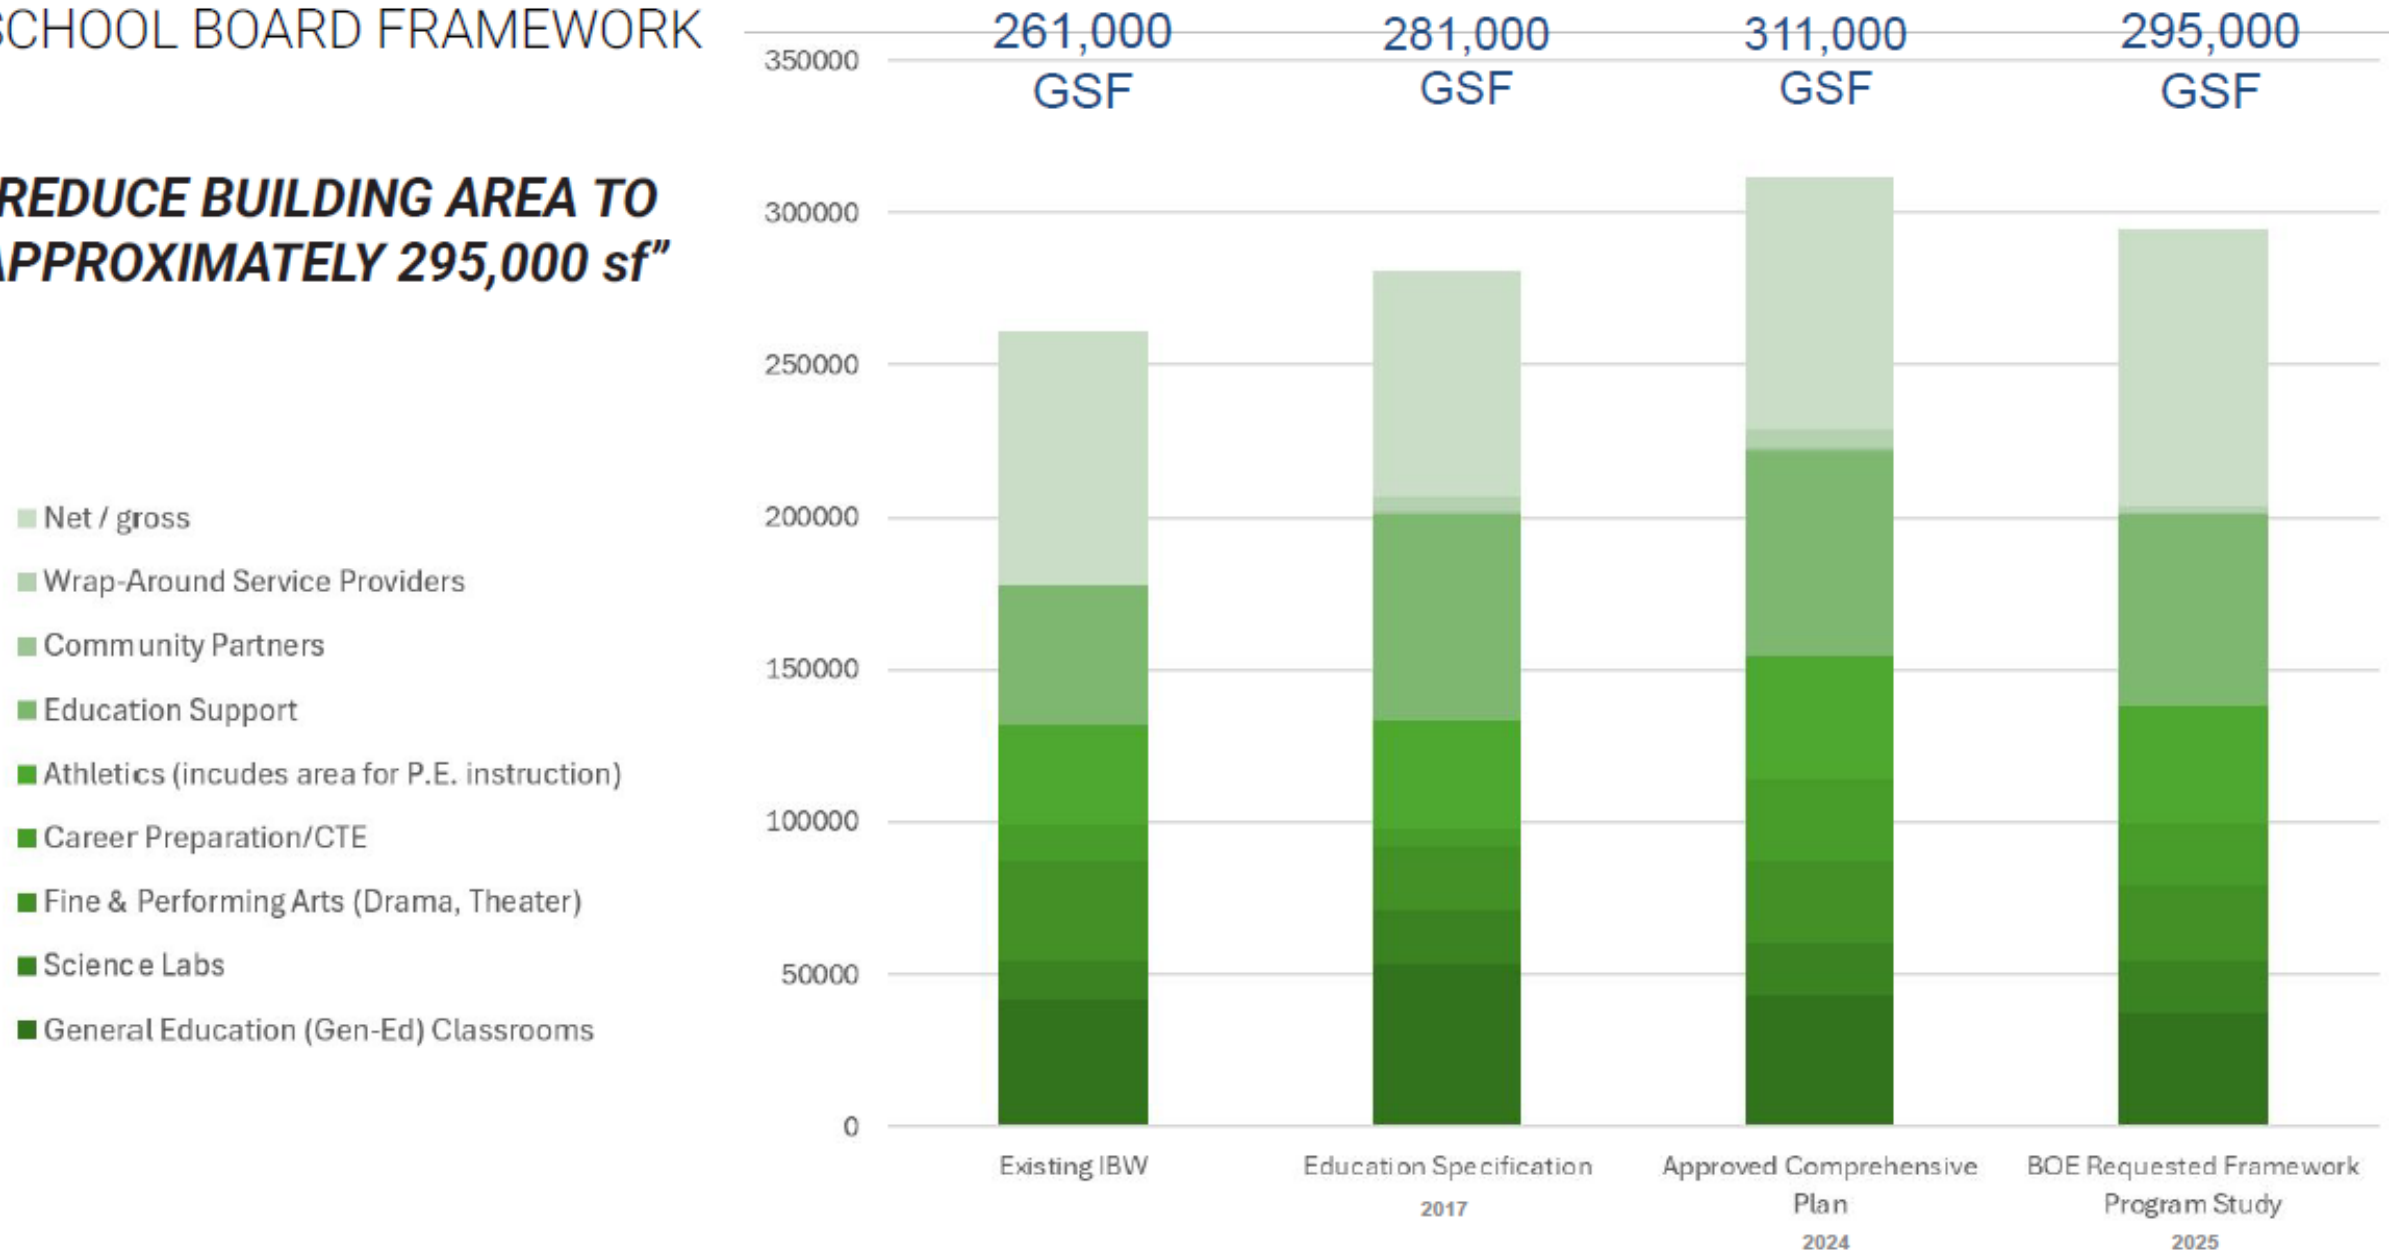


Board's Framework

Area Program Comparison

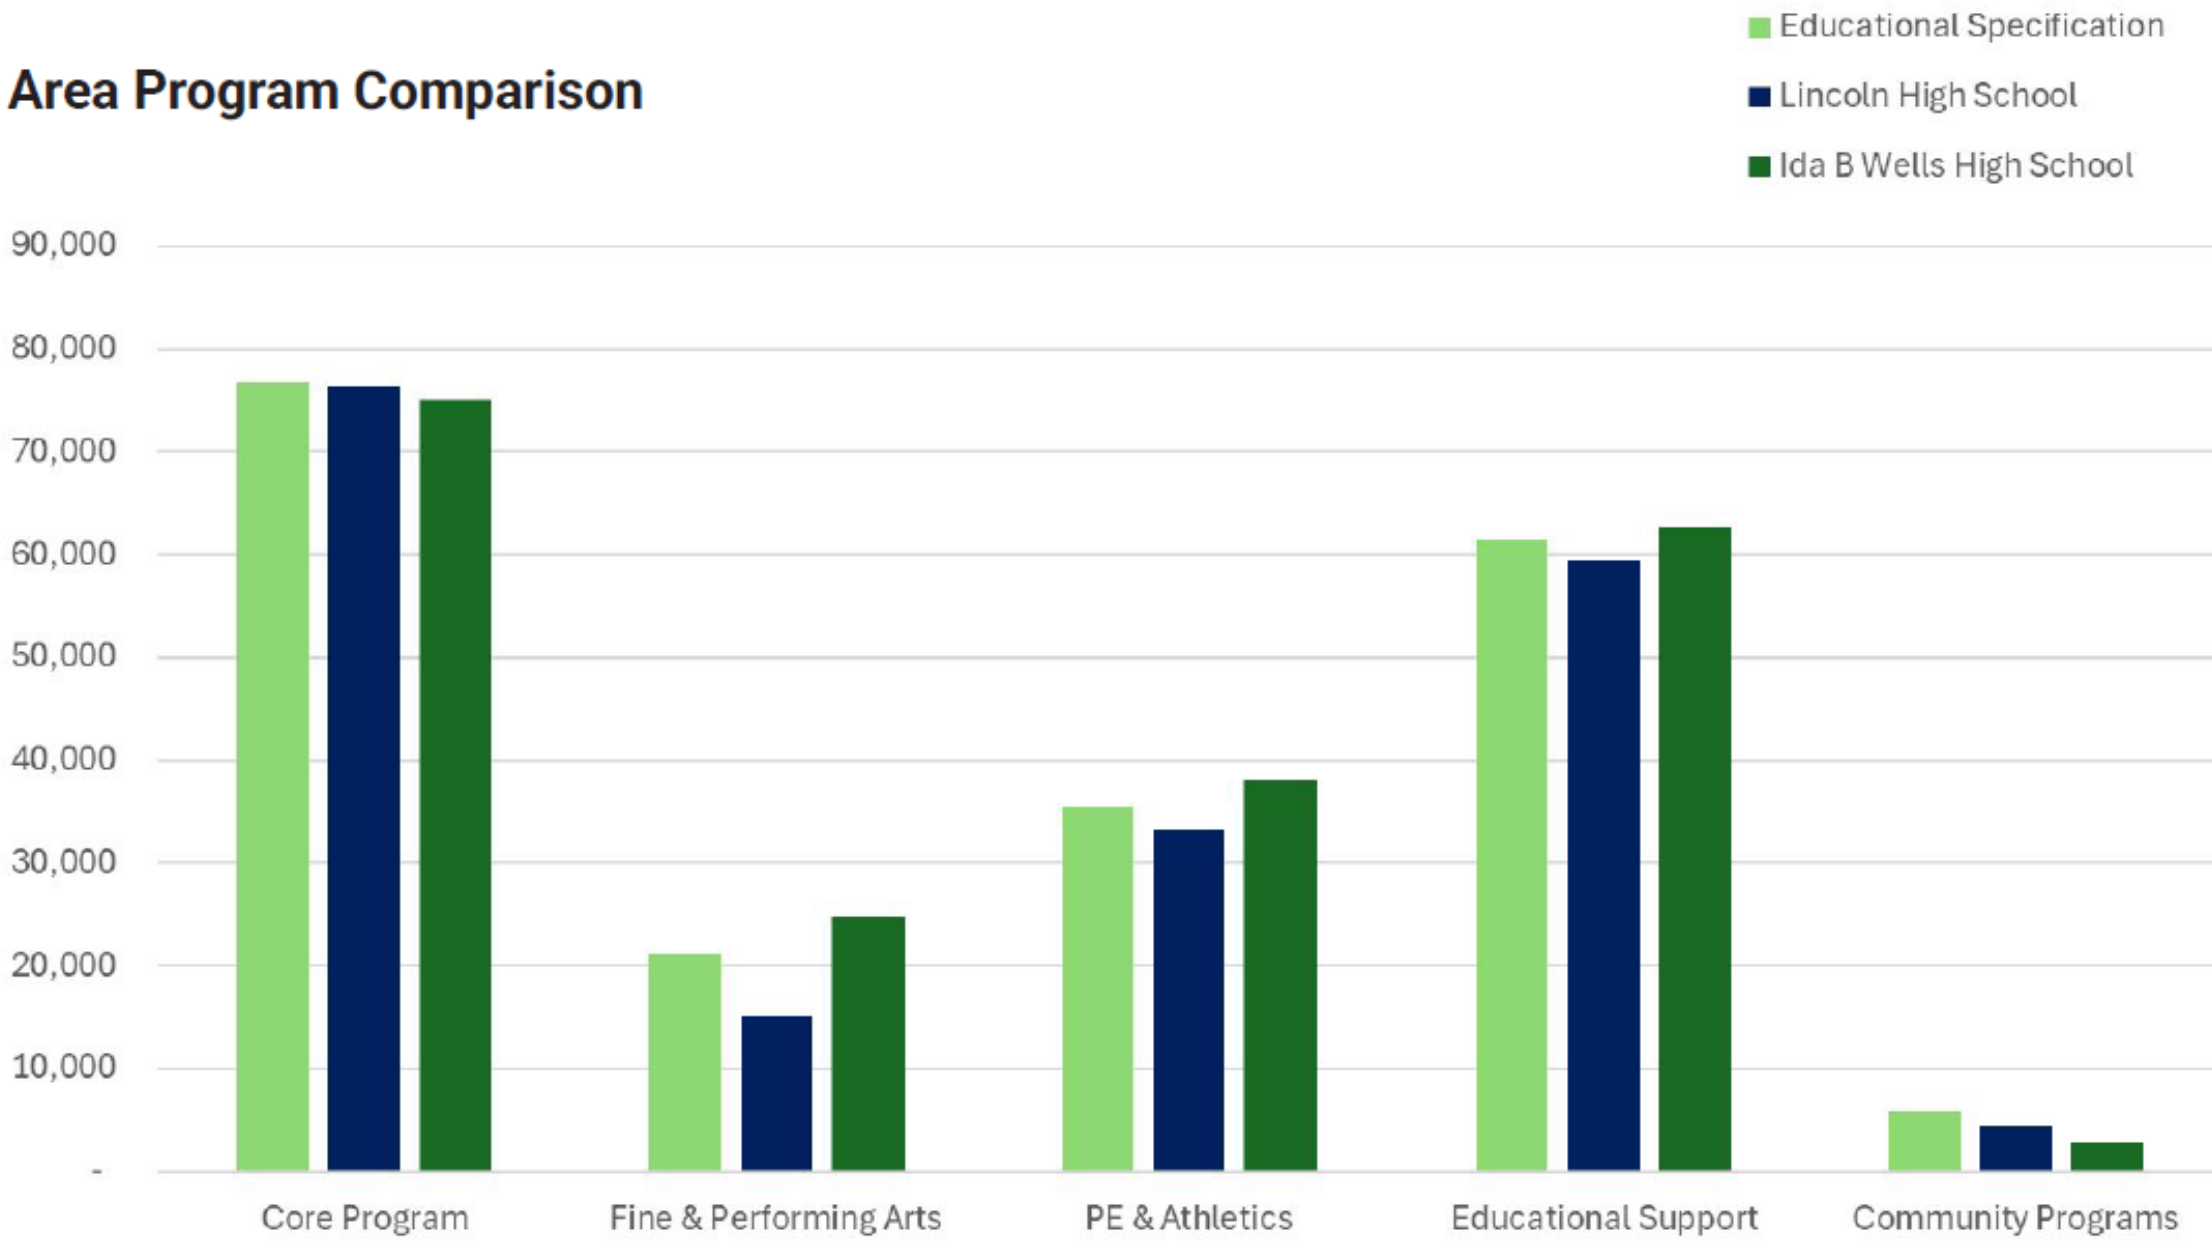

IBW Overall Project Schedule

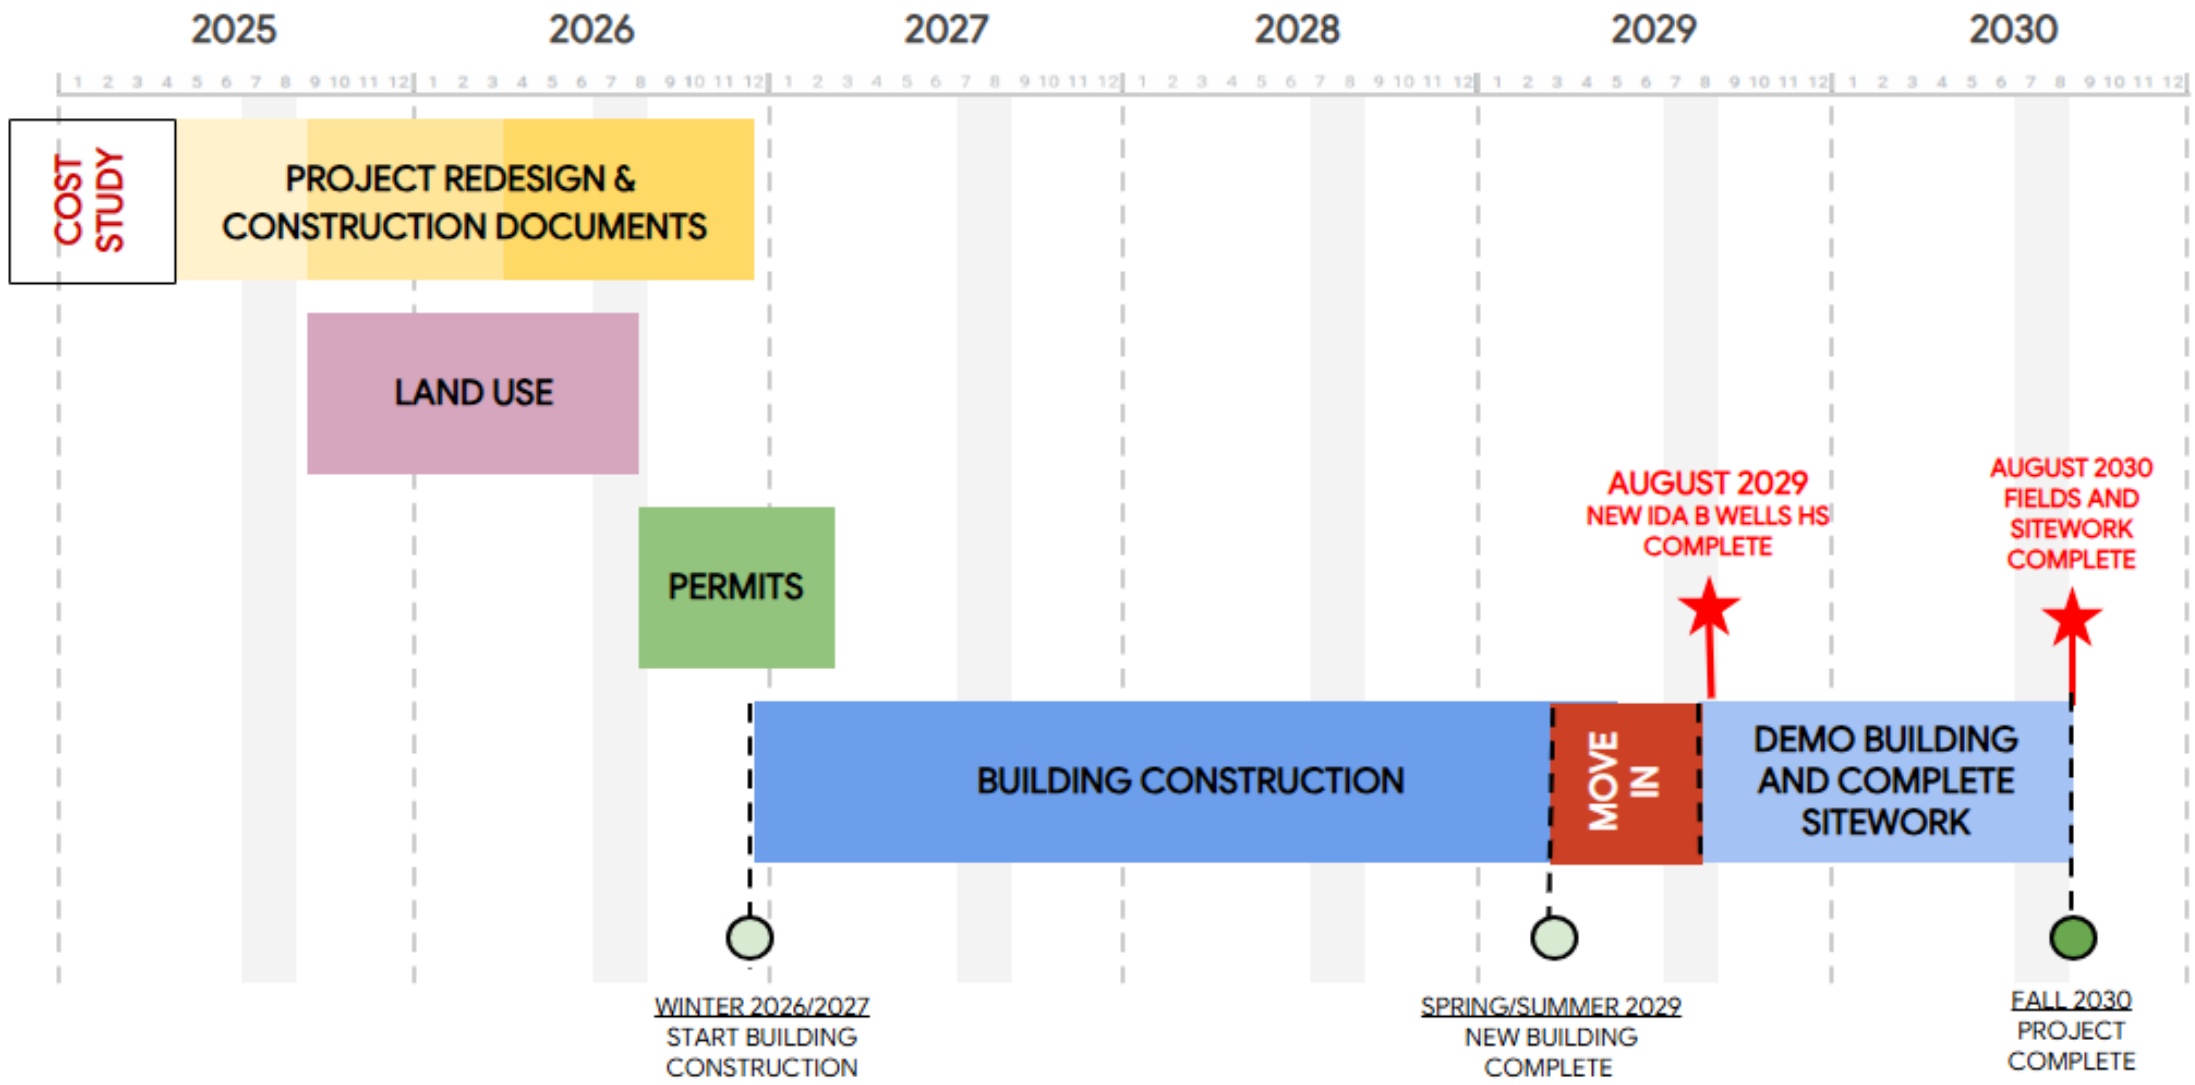

Budget Summary

IBW MODERNIZATION BUDGET SUMMARY

			2024	2025
COMPONENT	**COMMENTS**		**BOE APPROVED COMPREHENSIVE PLAN**	**CURRENT REVISED COMPREHENSIVE PLAN**
Hard Cost	Building & Site Work 2025: Includes actuals paid-to-date to CM/GC		$359,310,855	$345,000,000
1.5% Green Energy Tech			$ 5,989,663	Included above
Subtotal			$365,300,518	$345,000,000
Owner Direct Hard Costs	2025: Utilities, additional right-of-way/ public improvements		$2,200,000	$4,750,000
TOTAL HARD COSTS			**$367,500,518**	**$349,750,000**
Soft Costs	(Includes design, engineering, consultant services, permitting, insurance, etc) 2025: Includes Added Redesign Costs		$36,300,000	$45,500,000
Fixtures, Furniture & Equipment, including technology	Approx. $36 per SF		$10,000,000	$10,750,000
Moves / Swing Space / Temp Facilities			Included in soft costs	$2,500,000
Contingency	10% of Total Costs (add'l 5% CM/GC contingency included in Hard Cost Estimate)		$41,200,000	$40,850,000
Escalation	Included in Hard & Soft Costs			
TOTAL PROJECT BUDGET*			**$**455,000,518	**$**449,350,000
SAVINGS FROM 2024 DESIGN	***Expecting 2025 100% SD Estimates and subsequent Value Engineering Workshop Results by end of September 2025.**			$ (5,650,518)

Next Steps

- Schematic Design (SD) Phase Approval
  - Receiving Two Cost Estimates based on SD drawings – September 12, 2025
  - Value Engineering Workshop – September 15-17 and 24, 2025

- Community Engagement
  - Design Advisory Group (DAG) - September 25, 2025
  - Community Design Workshop - October 22, 2025
  - Information Table Events - Ongoing
