PORTLAND PUBLIC SCHOOLS
JEFFERSON HIGH SCHOOL

JEFFERSON HIGH SCHOOL MODERNIZATION PROJECT: COMPREHENSIVE ANALYSIS, OPTIONS, AND PROPOSED MANAGEMENT APPROACH

OCTOBER 22, 2025

PORTLAND PUBLIC SCHOOLS

PROCEDEO

PORTLAND PUBLIC SCHOOLS
JEFFERSON HIGH SCHOOL

JEFFERSON HIGH SCHOOL MODERNIZATION PROJECT
COMPREHENSIVE ANALYSIS, OPTIONS, AND PROPOSED MANAGEMENT APPROACH

01 | CONTRACT DELIVERABLES

02 | OBSERVATIONS & RECOMMENDATIONS

03 | JEFFERSON HIGH SCHOOL OPTIONS

04 | SCHEDULE ANALYSIS

05 | JEFFERSON HIGH SCHOOL BUDGET ANALYSIS TO DATE

06 | APPENDIX - CURRENT PLAN, CONDITIONS, & SCHEDULE

PROCEDEO

SECTION 01

CONTRACT DELIVERABLES

PROCEDEO

CONTRACT DELIVERABLES

1. As it relates to the Jefferson High School Project, a comprehensive written summary of the existing conditions of Portland Public School's decision-making protocols, project and construction management team structure, and oversight structures.

2. An analysis of Jefferson High School (JHS) Project challenges and recommendations (per above).

3. A dedicated project staffing plan adaptable to other high school modernization efforts.

SCOPE OF CONSULTANT'S SERVICES

This contract is intended to (1) provide actionable recommendations to reduce the costs of the Jefferson High School Modernization Project and expedite the project schedule; and (2) help define/inform the scope of the RFPs. The contractor's central point of contact and contract manager at Portland Public Schools (PPS) will be the Senior Director of the Office of School Modernization.

Consultant will:

- Review existing Jefferson Project documentation and data
- Engage with PPS staff, existing consultants, designers, and contractors
- Conduct a comprehensive assessment of the project's risks and opportunities
- Assess existing stakeholder engagement, decision making, and oversight protocol
- Deliver actionable recommendations aimed at accelerating the project timeline for the Jefferson High School Project by up to 12 months and reducing overall costs

All recommendations must be data-driven and include:

- Estimated time and cost impacts (savings or increases)
- Feasibility assessments for implementation of recommendations

Example recommendations may include:

- Additional consulting support scopes of work tailored to project acceleration and cost control such as: independent peer reviews, third-party cost estimating, third party value engineering analysis, and program administration enhancements related to:

    1. Process improvement strategies.
    2. Decision-making protocol evaluations.
    3. District project management and construction management team structure and roles and responsibilities.
    4. Communications plans, media strategies (website, social media, newsletters, etc), constructive transparency strategies.
    5. Contract modifications.

- Design, Permitting, Construction Sequencing and Phasing strategies
- Major equipment procurement strategies

INTRODUCTION AND PURPOSE OF STUDY

Portland Public Schools (PPS) is moving forward with the modernization of Jefferson High School (JHS), alongside projects at Cleveland and Ida B. Wells, to deliver safe, modern, cost-efficient learning environments. In response to rising construction costs and evolving programmatic needs, the PPS Board of Education unanimously approved a refined approach that right-sizes each school while preserving academic excellence.

Jefferson High School, founded in 1908, holds deep historic and cultural significance as a central institution in North Portland, long serving as an anchor for the city's African-American community. Its academic, athletic, and artistic achievements—including a nationally recognized dance program and championship basketball teams—make it both a community symbol and a citywide asset. Modernization is an investment in honoring and sustaining JHS's enduring legacy.

PPS leadership has directed our team to provide actionable recommendations that minimize the impact to project costs and expedite delivery of the Jefferson High School Modernization Project. PPS has established a maximum building size of approximately 295,000 square feet, aligning with other recent high school modernizations, to ensure cost efficiency without sacrificing programming. The framework directs PPS and consultants to identify savings through reductions in building size, alternative materials and systems, and efficiencies in contractor costs.

Following the directive of Portland Public Schools, our team of experts has been engaged to review the history and current plan for the Jefferson High School Modernization Project, and to assess the feasibility of expediting the schedule and delivery of the new building. The team will provide multiple options, along with pros and cons for each proposed plan. The report includes a summary of existing conditions, an analysis of the project's challenges, observations and recommendations for next steps. Recommendations will be data-driven, addressing cost, time savings, and feasibility. Examples may include peer reviews, third-party cost estimating, value engineering, and enhanced program administration.

Our goal is to provide strategic support to Portland Public Schools' Office of School Modernization by ensuring that consulting and construction services are scalable, responsive, and capable of meeting the evolving needs of the District over the next five to ten years. The Modernization Project is more than a construction endeavor; it reflects the district's values of equity, transparency, and accountability. In summary, this study serves as both a roadmap and a commitment: to deliver a right-sized, cost-effective, future-ready Jefferson High School that upholds its historic legacy while equipping students for generations to come.

CONTRACT DELIVERABLES

OVERVIEW OF ANALYSIS AND RECOMMENDED SOLUTIONS

Following the directive of PPS, we were tasked to review previously conducted analysis' and project documentation to provide actionable recommendations to expedite the project schedule, and help define the next steps to be taken to ensure the project is managed effectively, efficiently and within community expectations.

SITE ANALYSIS: Our team visited the site on multiple occasions and conducted a preliminary analysis of the existing conditions and challenges. Key issues identified include:

- Existing utilities that will require coordination.
- Easement agreements that need to be initiated and carefully tracked.
- Parking availability, which will pose challenges for construction workers, staff, students, and teachers.
- Construction laydown and staging areas, which must be identified to maintain clear separation between construction activities and daily school operations, ensuring safety for staff and students.

BUILDING ANALYSIS: This report will address the current conditions of the existing campus and some of the challenges and pain points faced while working with a 117-year-old school. Jefferson High School's campus is a patchwork of structures ranging from the original 1908 Renaissance Revival building to later additions. Over the years, multiple additions were constructed (in 1928, 1952, 1964, and 1968), expanding the total facility. Structurally, the school is a mix of wood framing, unreinforced masonry, steel, and concrete systems, reflecting the eras of construction. Although fully sprinklered and generally code-compliant for fire-life safety, the buildings require significant seismic upgrades to meet current standards.

ALTERNATIVE OPTIONS: As directed by the Superintendent of Portland Public Schools, we will compare the Current Plan to alternative options through pros and cons critical to project completion. Each option includes a phasing plan outline of the option as well as schedule implications.

GUIDING PRINCIPLES & PROJECT GOALS

1) STEWARDSHIP OF FUNDS

Be responsible with budget resources, maximizing value so that funds can also support improvements in PPS's aging schools.

2) RIGHTSIZING

Limit total building area to about 295,000 square feet (or similarly scaled) to control costs, while still meeting essential program requirements and community expectations. However, we found that the current plan, capacity, and utilization exceed both current and projected student enrollment. If cost challenges arise in the future, establishing a reasonably sized building and defining alternates would offer a practical solution. This approach would help manage potential cost escalation while avoiding the need to return to the community for additional funding.

3) MAINTAIN STRONG EDUCATIONAL PROGRAMMING

Ensure core programs (academics, arts, athletics, CTE, etc.) are preserved or enhanced, even while making cost reductions.

4) COMMUNITY ENGAGEMENT & ALIGNMENT

Center stakeholder input (students, staff, parents, community) so that design reflects community values, historic legacy, and neighborhood priorities.

5) ON-SITE OPERATIONS DURING CONSTRUCTION

Aim to keep students and staff safe through construction.

6) SITE & ENTRY PRIORITIES

Keep the main building on Kerby, maintain relationship of field/athletics adjacent to Gym on Commercial, activate Killingsworth frontage, ensure cross-block connections.

7) EQUITY, SUSTAINABILITY & CLIMATE POLICY COMPLIANCE

Adhere to PPS's climate and equity policies: all electric infrastructure, reduce carbon emissions, evaluate embodied carbon (mass timber vs steel), consider alternatives to LEED Gold if those are more cost-effective.

8) CONSTRUCTION COST REDUCTIONS & TRADE-OFFS

Identify opportunities to reduce costs via building systems, materials, structural options, specialized spaces, eliminating or reducing basement construction, etc.

9) HEALTH & SUPPORT FACILITIES

Include health center and teen-parent/child center only where there is demonstrated need and/or a provider commitment; integrate into main building to reduce cost.

10) TIME EFFICIENCY & PROJECT ACCELERATION

Speed up the design and approval process where possible, balancing the need for community input with the urgency of delivering facilities and controlling escalating costs.

SECTION 02

OBSERVATIONS & RECOMMENDATIONS

PROCEDEO

PROCEDEO'S OBSERVATIONS, CONCERNS, & RECOMMENDATIONS

1. IMPLEMENTING DESIGN OR SCOPE CHANGES WITHOUT A CLEAR UNDERSTANDING OF THE PPS BUDGETARY AND SCHEDULING IMPLICATIONS.

When significant design or scope changes are introduced without fully evaluating their consequences, the project can quickly experience cost overruns and schedule delays. Even changes that seem minor at first, such as material substitutions, layout adjustments, or additional program elements, can have a cascading effect on design and procurement timelines, coordination requirements, and construction sequencing. Without a clear understanding of these downstream impacts, decisions may be made that unintentionally compromise the overall project delivery, increase risk, and strain resources.

RECOMMENDATIONS

1) CLEAR DELEGATION OF AUTHORITY
Defining who is authorized to make changes (and at what level of impact) prevents unauthorized or informal decisions from slipping through.

2) STRUCTURED CHANGE MANAGEMENT PROCESS
Any proposed change should go through a formal review process where impacts to budget, schedule, and scope are documented and approved before moving forward.

3) DEFINED DECISION-MAKING & ESCALATION
Establishing the right decision-makers (and escalation protocols) ensures that changes are reviewed at the right level — small tweaks can be approved quickly, while major changes require higher-level authorization.

4) COMMUNICATION & TRANSPARENCY
Making sure all stakeholders understand the potential consequences of changes helps avoid "surprise" impacts. Regular updates and cost/schedule tracking help reinforce this.

5) EARLY IMPACT ANALYSIS
A system where every change triggers a quick impact assessment (budget, schedule, risk) and makes it clear what trade-offs are involved before approval.

**Currently, eBuilder workflows are used for change management, but workflows within the system have not been reviewed for efficiencies and transparency in several years.. An in depth review of all current workflows is recommended to ensure that the systems are still applicable to the current state of Office of School Modernization (OSM).*

PROCEDEO'S OBSERVATIONS, CONCERNS, & RECOMMENDATIONS

2. STAFFING AND DECISION-MAKING EFFICIENCY

Current Project Manager (PM) roles have limited decision-making authority, which reduces overall efficiency and increases coordination workload. Because Project Managers have limited decision making independence, every issue must be elevated for input, review, and decision by committee. This slows progress, adds extra layers of communication, and forces PMs into a primarily coordinating role rather than a guiding one. Instead of streamlining decisions, the process multiplies hand-offs and approvals, which strains both staff time and project schedules. As a result, meetings often include four to five Project Managers to ensure alignment, but this size makes meetings less efficient.

To avoid gaps in communication or missed approvals, multiple PMs attend the same meetings. While this ensures everyone stays informed, it dilutes effectiveness: conversations become repetitive, agendas expand, and the decision-making process stalls. Time that could be spent advancing the project is instead spent on reconciling multiple perspectives and re-communicating information. This redundancy creates a perception of over staffing, when in reality it reflects the inefficiency of the decision-making structure. We witnessed multiple meetings of 20-25 people that were extremely inefficient and often led to more confusion than clarity.

RECOMMENDATIONS

To improve efficiency, OSM's staffing plan should be restructured to give Project Managers clearer authority over day-to-day decisions within defined parameters (budget thresholds, schedule constraints, and scope alignment). By empowering PMs to make certain decisions independently, the workload of constant approvals can be reduced, and meetings can focus on higher-level strategy rather than operational details.

A streamlined staffing model would assign one lead PM per project, supported by specialists or coordinators as needed, instead of having four to five PMs in every meeting. This "single point of accountability" approach ensures alignment while minimizing redundancy. Additional PMs could then be reassigned to support across projects, provide technical expertise, or manage discrete work streams, rather than overlapping on the same tasks.

Clear delegation of authority, combined with an escalation framework for higher-impact decisions, would balance oversight with efficiency. This structure reduces unnecessary coordination, accelerates decision-making, and allows OSM staff to spend more time proactively guiding projects rather than managing process bottlenecks.

PROCEDEO'S OBSERVATIONS, CONCERNS, & RECOMMENDATIONS

3. LACK OF STANDARDIZED PROCESSES, CONSISTENCY, AND LEADERSHIP. STREAMLINE THE PROCESSES AND PROCEDURES, MAKE THEM CONSISTENT, AND IDENTIFY CLEAR ROLES AND RESPONSIBILITIES.

OSM has been managing on a per-project basis instead of on a program basis. When there is no clear process in place, every project team is forced to "reinvent the wheel." This leads to inconsistent approaches across projects, inefficiencies, and confusion among stakeholders. Without standardized tools, such as meeting templates, reporting formats, or decision logs, each team documents and communicates differently, making it difficult to track progress, compare projects, or ensure accountability.

The absence of consistency creates unnecessary duplication of work — for example, teams spend time re-creating slide decks, decision trackers, or reports, instead of focusing on advancing the project itself. Critical information may be missed, misinterpreted, or buried in long documents, which undermines confidence in the process and slows decision-making.

Lack of leadership clarity within teams compounds the problem. When roles and responsibilities are not clearly defined, decisions are delayed or second-guessed, and multiple people may duplicate efforts or work at cross-purposes. This creates frustration for OSM staff, design partners, and stakeholders alike. Without a clear decision-making hierarchy, authority is diluted — leading to prolonged discussions, stakeholder disagreements, and frequent re-work.

The result is a system that consumes excessive staff time in coordination and communication rather than problem-solving. It would also produce inconsistent deliverables that frustrate stakeholders and diminish credibility. Delayed critical decisions will lead to schedule impacts, budget uncertainty, and create a perception of disorganization and lack of accountability at the District level.

RECOMMENDATIONS

To improve efficiency and reduce confusion, processes and procedures should be outlined, simplified, standardized, and consistently applied across all projects. Establishing clear, repeatable workflows helps eliminate duplication, accelerates decision-making, and creates predictability for both OSM and design teams. **Consistency is key** — having a uniform set of tools and practices allows everyone to work from the same playbook. For example:

STANDARDIZED MEETING MINUTE TEMPLATES. A single, easy-to-use format ensures that decisions, action items, and follow-ups are documented consistently, making it easier for teams to track accountability across multiple projects.

UNIFIED PRESENTATION TEMPLATE. A District-approved slide deck style (cover page, section headers, formatting) creates a professional, consistent look across all projects and helps stakeholders quickly navigate information.

DECISION LOG TEMPLATE. A centralized, simple log for tracking decisions, approvals, and responsible parties prevents issues from being revisited unnecessarily and clarifies who holds authority.

ROLES & RESPONSIBILITIES. Outlining who is Responsible, Accountable, Consulted, and Informed for each major process provides clarity and avoids duplication of effort.

By streamlining and standardizing processes, OSM can reduce time spent re-creating tools, minimize miscommunication, and ensure that stakeholders are always receiving information in a consistent and clear format. This not only improves internal efficiency but also builds trust and transparency with external partners.

PROGRAM MANAGEMENT PLAN & PROCESSES AND PROCEDURES TO BE PUT IN PLACE IMMEDIATELY

The primary purpose of a Program Management Plan (PMP) is to provide an overview of the Portland Public Schools Jefferson High School Modernization Project and introduce the Program Manager (PgM). The PgM will oversee the daily operations, planning and execution across the entire program, not on a project level.

This PMP outlines the typical sequence of activities for the design and construction phases, provides updates to the schedule and budget models for all projects within the program, and details the management tools that will be utilized. The plan emphasizes strong governance through Board of Education oversight, committee engagement, and community input.

To ensure effective delivery, program management emphasizes budget reconciliation, schedule adherence, cost tracking, and risk management. The scope and prioritization of work are guided by facility condition assessments that identified critical infrastructure needs. Procurement strategies will be designed to encourage business participation and maintain full compliance with state regulations. Throughout the process, technology platforms such as Procore, Egnyte, and Operational Excellence (OPEX) dashboards provide essential support for communication transparency, documentation, and reporting.

OPEX, or Operational Excellence, is a proprietary program developed to serve as the standard for managing every project. It is a comprehensive approach centered on leadership, teamwork, and meticulous processes to achieve project goals effectively. OPEX focuses on safety, quality, schedule, cost, trade partners, and Clients, ensuring that functional goals met throughout the duration of the program.

Design and construction follow structured guidelines for pre-design, schematic design, design development, and contract bidding. Construction employs both traditional and Construction Manager/General Contractor (CM/GC) delivery methods to balance risk and schedule. The closeout process ensures punch list completion, occupancy readiness, and warranty tracking. Financial tracking is integrated into Portland Public Schools' accounting system to ensure transparency and compliance. Finally, the PMP is updated twice annually to provide progress reports, budget updates, and accountability to stakeholders.

PROCESS AND PROCEDURES EXAMPLE

Procedure/Process Name	Description
3rd Party Contract Routing Procedure	Process for submitting and routing contract proposals for approved Spending Authority services.
3rd Party Invoicing Procedure	Process for submitting and processing 3rd party payment requests for approved Spend Authority Services.
AE Change Management	Process for when additional services, reimbursements, or architect contract amendments are required.
AE Invoicing Procedure	Process for submitting and processing requests for payment to an Architect's Fee.
Bond Cashflow Submission & Timeline	Process to establish a submission timeline for periodic cash flow reports to help District prepare for upcoming needs.
Custodial Overtime Request Process	Process for requesting after-hours campus access by contractors for work outside standard custodial schedules.
Design Review Process	Bluebeam project and session requirements when in Design.
FF&E Retainage, Removal & Disposal	Process for evaluating and determining retainage, reuse, or disposal of existing FF&E during bond construction.
FF&E Scope, Procurement & Installation	Process to define, review, and procure FF&E based on project scope and best value criteria.
FWISD Substitution Request Process	Process for contractor requests to substitute non-specified products for A/E and district review.
FWISD Utility Shutdown Process	Process for requesting, approving, and coordinating utility shutdowns on campus to perform construction work.
GC Document Closeout Process	Process for Bond Program Project Closeout.
General Contractor Substantial Completion	Process to confirm construction completion, certify occupancy readiness, and establish contract closeout milestones.
JOC Abatement Routing Procedure	Process for submitting and routing proposals for hazardous material abatement by approved JOC Contractors.
Monthly Schedule Update	Process for maintaining and updating both program & project-level schedules (recurring monthly)
Moving Services & Student Phasing Guidelines	Guideline for coordinating campus moves and student transitions with project teams and movers.
Pay Application Submittal & Processing	Process for submitting and processing monthly payment request for construction and abatement services.
Permit Process	Process for obtaining permits, reviews, inspections, and/or approvals from outside entities.

Note: *Processes and procedures are currently under view and may be updated for the upcoming school year as applicable.*

TEAM & STAKEHOLDER ENGAGEMENT

BOND PROGRAM COMMUNICATION

The PgM believes the most important aspect of a successful program is good communication across everyone engaged in the process. Our PMP suggests establishing recurring meetings between the PROCEDEO staff and PPS to provide a status update on all things related to the bond. The PgM team will develop an agenda and will lead the in-person meeting which is suggested to take place at a location appropriate for the District. When discussing communication, it is important to think of both internal and external communications related to the program.

EXTERNAL COMMUNICATION

We observed external communication challenges for OSM. As directed by the Superintendent, we would recommend a customized approach when communicating with external stakeholders. One way to do this is the creation of a program-specific website for external communication. The website should include an overview, total projects page, vendor opportunities page, and a sub-page for each individual project. This will allows users the ability to track project-specific information such as budget, completion dates, design progress, construction progress, new square footage, renovated square footage, and a project narrative. The team will provide a project update with current photos and a short narrative describing what is happening on-site. This tool will help enhance alignment and consistency in Portland Public Schools' public communications regarding the bond program.

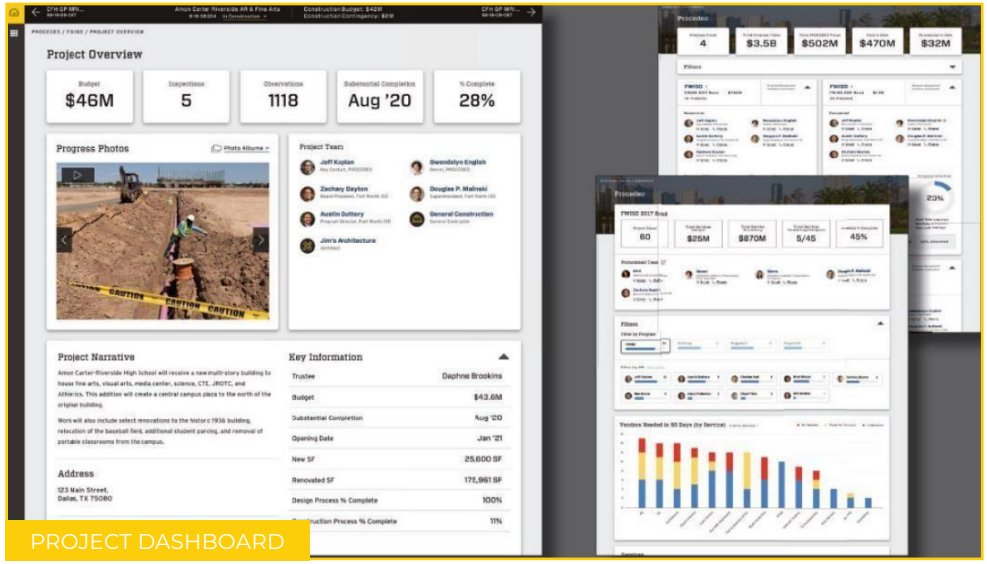

PROJECT DASHBOARD

AGENDA & MEETING MINUTES EXAMPLE

PROCEDEO

Agenda & Meeting Minutes

Topic	JHS	**Subject**	**JHS – New OAC + PPL Kick-Off Meeting**
Date	09/02/2025	**Time**	
Location	Via Teams	**Facilitator**	
Prepared by			

Attendees: Ayana Horn, Ashley Koger, Andrew Colas, Blair Cranston (Level Architecture), Bob Gravely (PacifiCorp), Olivia Austin (PacificCorp), Justin Brainard (PacifiCorp), Bradley Wilson, Brian Reeves, Brian Coffield, Bryce Tolene, Bridget Feitl, Miguel Hidalgo, Jeremy Morris (PacifiCorp), Josh Melu, Kami Calaro, Kiesha Locklear, Lloyd Stoller, Mark Parsons, Rashmi Vasavada, Stephen Effros, Stefee Kknudsen, Stephanie Coyle, Stephen Diffenderfer, Walker Frank

AGENDA AND MEETING MINUTES

ITEM	DISCUSSION ITEMS
Introduction	**Colas/Hoffman CM/GC team with Pacific Power Team**
Colas/ Hoffman Onboarding Process	**Overview of Colas/Hoffman onboarding process** • Start of 100% SD estimating • Update of schedule/construction phasing approach

Pacific Power Process	**Pacific Power Impact Study Status**
	• Olivia (PPS):
	  ○ Study return timeline: Mid-to-late October 2025
	  ○ Evaluating PPL system capacity
	  ▪ Previous load: 5.106MW (diversified) – seems high, but will plan for this in the system
	  ○ Determining if network upgrades are necessary (may be covered by owner's allowance)
	• Walker (Samata): latest calculation = ~8,200 A
	• Steve (PAE): Estimate =~5.6 MW; diversified load ≈ 5.1 MW
	
	Design Coordination (Pacific Power + Design Team)
	• Service Entrances and Metering
	  ○ Current design: 3 separate service entrance on north side of property
	  ○ Walker (Samata): May need to totalize to 1 service, potential need for exterior gear
	  ○ Olivia (PPS):
	  ▪ Current design is workable
	  ▪ Totalizing metering to be confirmed
	  ▪ May include vault with switchgear, upstream protection, and fused risers (TBD)
	  ▪ Network upgrades are pretty set, equipment locations will be finalized during estimating
	• Communication and Site Coordination
	  ○ Bob (PPL):
	  ▪ Email PPL for any construction questions
	  ▪ Workers can visit the site to confirm design, have previously confirmed certain elements (access to meter, etc.)
	  ○ Olivia (PPL): Will align with latest design as much as possible
	  ○ Justin (PPL): final design depends on completion of estimating
	
	Equipment Procurement and Process Timeline
	• Transformer Lead Times
	  ○ Olivia/Justin (PPL): 3-phase transformer on another project has an 84-week lead time
	  ○ Once PPS approves, still need to draft MESA agreement (takes several weeks and requires signature on both sides)
	  ○ Next Steps:
	  ▪ Study results will be delivered October 2025
	  ▪ Steve will revisit MESA agreement with PPS legal counsel
	
	• Transformer Procurement Coordination
	  ○ Brian (Colas-Hoffman): requested process and transformer installation timeline
	  ○ Justin (PPL):
	  ▪ Hard to confirm transformer installation timeline without design
	  ▪ Vault spec will stay the same and can begin laying groundwork
	  ○ Next Steps:
	  ▪ Steve: Will send process timeline information to Colas-Hoffman team and CC Bob
	  ▪ Olivia: will follow up with crews to estimate transformer installation timeline and CC the team.

FWISD 2021 Bond Update

CONTRACT AMENDMENTS

Monthly Reports are recommended to ensure budget reporting, schedule tracking and risk management are in place.

An example of the current contracts 21 executed amendments is shown on the right in one interactive report.

As directed by the Superintendent, the team looked at multiple processes. The monthly report sample shown here is an example of a concise and efficient way to communicate complex information. Currently, this information is housed in three to four different places and it took our team two multi-hour work sessions with multiple team members to create this document.

We recommend standardizing reporting, across all project to create consistence, transparency and efficiency.

PORTLAND PUBLIC SCHOOLS

AE contact report as of Sep. 30, 2025

PROCEDEO

Jefferson High School Modernization - 5531

Contract # ARCH 91616 **Architect: Bora Architects, Inc** **Current Contract Value: $40,081,407**
Original Contract Amount: $149,715
Original Contract Time: Start 8/22/2019, End 6/30/2020 - 161 Calendar Days
Scope of Work: Planning (92%) and Public Participation (8%)

Amendment #	Timeline	Duration/Days	Amount	Scope of Work
1	06/15/2022 - 12/31/2022	199	$1,266,754.00	Pre-Design and Community Meetings
2	07/14/2022 - 12/31/2022	170	$100,778.00	Site Investigation
3	10/11/2022 - 12/31/2022	81	$70,662.00	More Consultants
4	12/02/2022 - 12/31/2022	29	$0	Reduce Consultant Reimbursable
5	01/01/2023 - 02/28/2023	0	$0	
6	02/28/2023 - 12/31/2028	2133	$22,947,420.00	Design expansion and retain 1909 original bldg. (334,410 SF)
7	05/07/2023 - 12/31/2028	2065	$22,947,420.00	Cost Estimating for redesign concept
8	07/31/2023 - 12/31/2028	0	$0	
9	09/05/2023 - 12/31/2028	1944	$553,215.00	Consolidation of two design packages into a single design package.
10	11/16/2023 - 12/31/2028	1872	$158,205.00	Directs BORA Architects to proceed with design scopes of work associated with the South Lot which include but may not be limited to civil, lighting and fields.
11	02/15/2024 - 12/31/2028	1781	$130,000.00	Finish 50% DDS and proceed with closeout
12	02/15/2024 - 12/31/2028	1781	$889,765.00	Concept design keeping students on-site
13	02/27/2024 - 12/31/2028	1769	$27,964.00	BIM Model
14	04/17/2024 - 12/31/2028	1719	$6,909,929.00	New design for 310,926 SF
15	06/09/2024 - 12/31/2028	1666	$373,250.00	Early Baseball Field Package
16	06/09/2024 - 12/31/2028	1666	$-437,600.00	Adjust reimbursables
17	07/17/2024 - 12/31/2028	1628	$1,189,300.00	Cultural Placemaking and enhanced community engagement support.
18	11/25/2024 - 12/31/2028	1497	$-267,374.00	Invoice Reconciliations
19	01/24/2025 - 12/31/2028	1437	$50,000.00	Cost Reduction study phase 1
20	04/01/2025 - 12/31/2028		$512,096.00	Cost reduction study phase 2
21	05/08/2025 - 12/31/2028	1333	$5,329,788	New plan SC
			$40,081,407	

PROPOSED STAFFING PLAN

Organizational structure for K-12 bond program management is meticulously designed to ensure seamless execution and alignment with the unique needs of educational institutions. This multidisciplinary team collaborates closely with school district leadership, architects, and contractors to ensure every phase of the bond program is executed efficiently and transparently. By integrating experienced professionals with backgrounds in construction, procurement, hazardous materials, and educational administration, the PgM creates a cohesive and adaptable framework that prioritizes accountability, cost efficiency, and stakeholder engagement. This structure not only supports the successful delivery of projects but also fosters trust and collaboration with the communities served.

Below you will find a typical staffing plan that has been implemented and successful in other districts similar to Portland Public Schools. These districts are similar in metropolitan location, demographics, number of schools, bond size and equity inclusion.

TYPICAL STAFFING PLAN

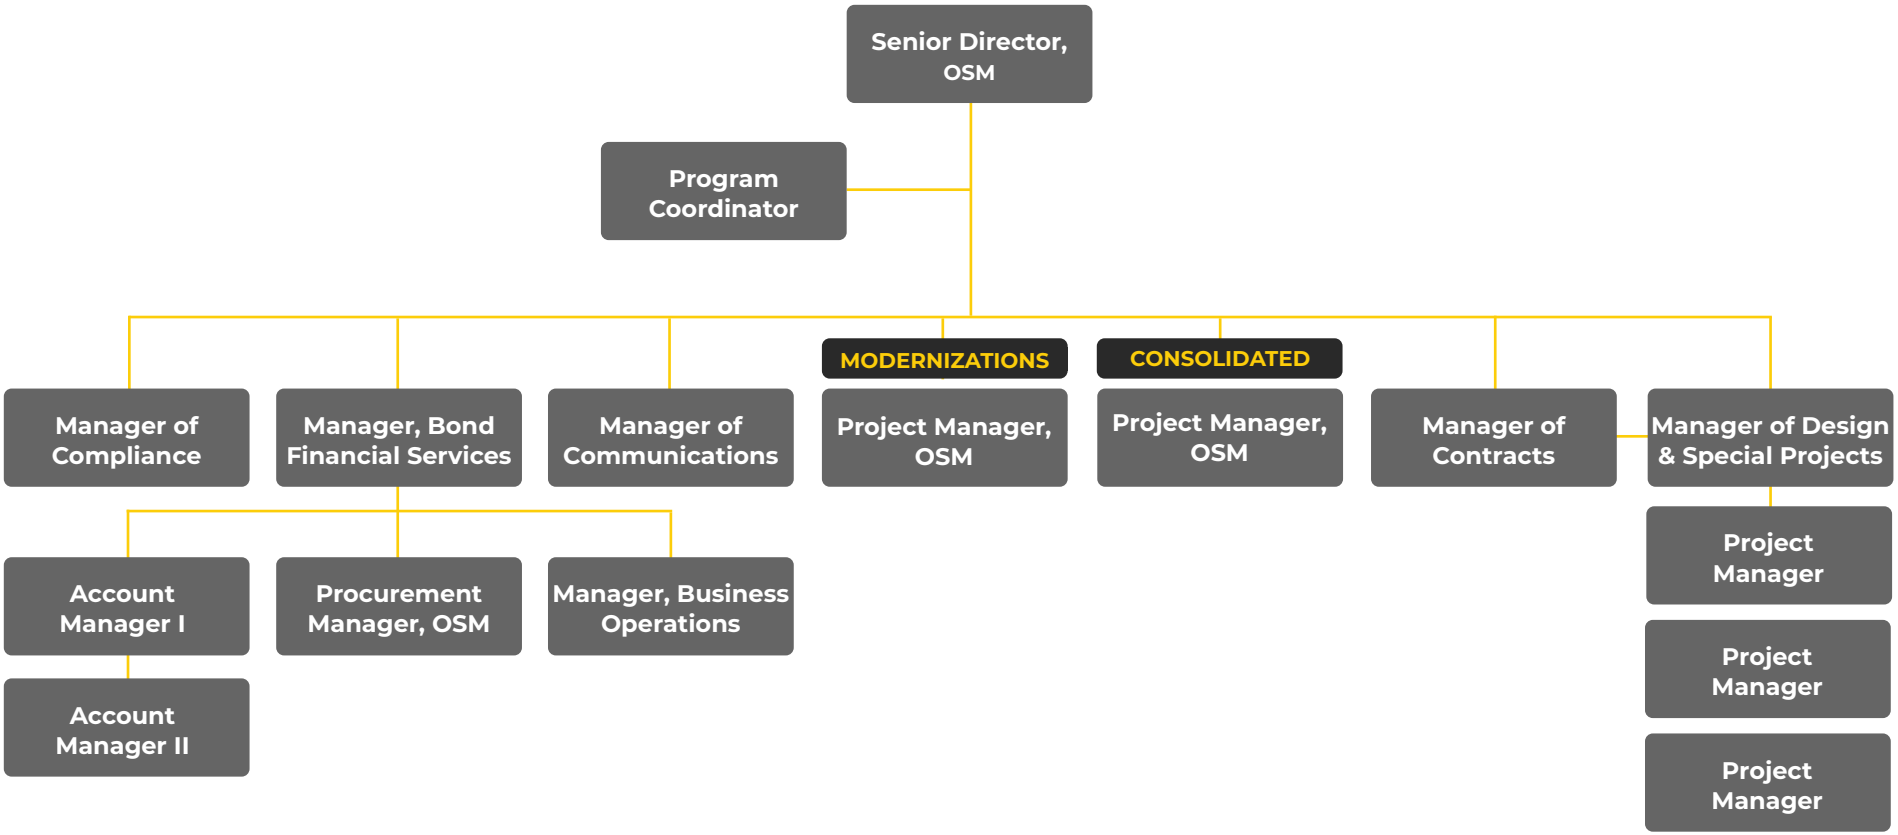

POSSIBLE PROGRAM MANAGEMENT FTE STAFFING PLAN

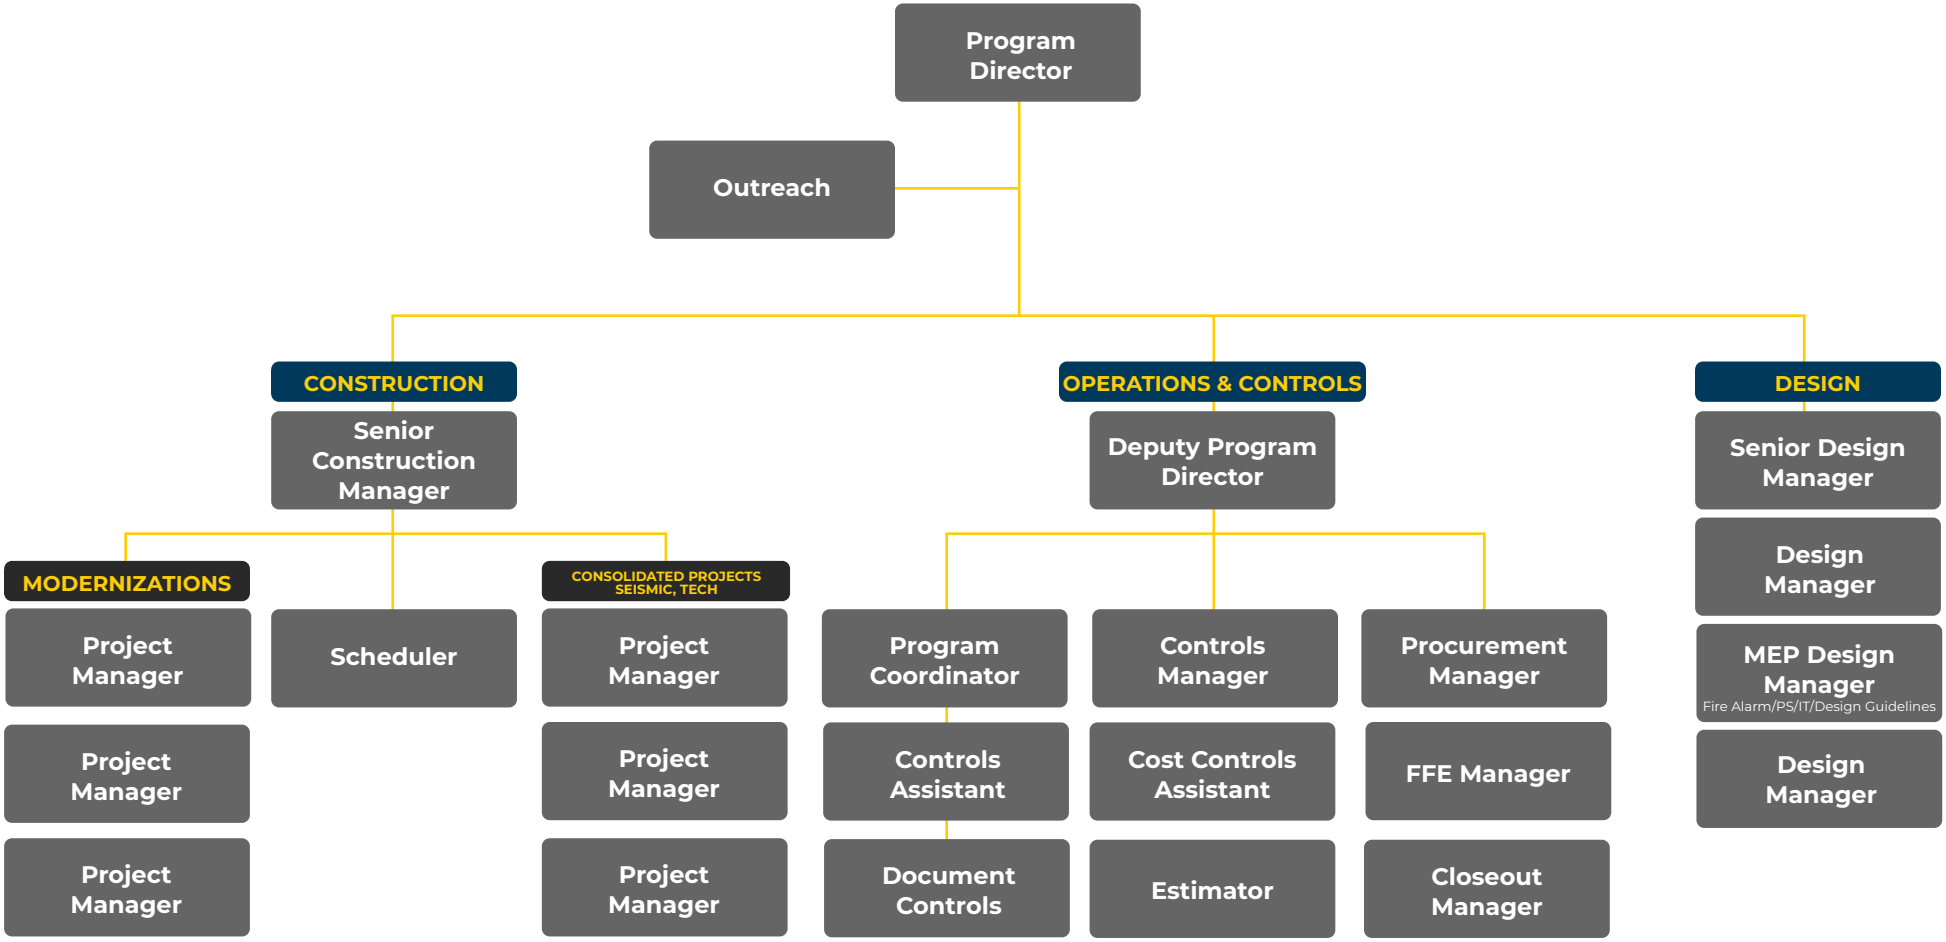

SECTION 03

JEFFERSON HIGH SCHOOL OPTIONS

PROCEDEO

STUDENT MOVE-IN DATE	
1ST AND 2ND FLOOR =	SEPTEMBER 2028
3RD AND 4TH FLOOR =	SEPTEMBER 2029

OPTION 1 | SHELL

Option 1 (SHELL) offers Portland Public Schools an accelerated path that allows **students to begin using the 1st and 2nd floors of the new Jefferson High School building in September 2028**. **The 3rd and 4th floors will be ready for student occupancy in September 2029**. While this approach avoids the need for portables, it requires construction to continue on the upper floors after occupancy. **The total project would still finish by December 2029**, saving about a year overall and reducing cost exposure from extended schedules. Compared to the other options, Option 1 balances earlier access to classrooms with on-site construction challenges that demand strict safety protocols and careful sequencing.

PROPOSED SCHEDULE

PHASE 1: NEW BASEBALL & SOFTBALL FIELDS

PROCESS	START	END	DURATION
DESIGN	4/2025	12/2025	9 Months
PERMITTING	3/2026	6/2026	4 Months
CONSTRUCTION	7/2026	11/2026	5 Months

PHASE 2A: EARLY FOUNDATION TO GRADE - DEMOLITION OF EXISTING TRACK & FIELD

PROCESS	START	END	DURATION
DESIGN	11/2025	2/2026	4 Months
PERMITTING	3/2026	6/2026	4 Months
CONSTRUCTION	7/2026	12/2026	6 Months

PHASE 2B: START NEW JHS BUILDING (1ST & 2ND FLOOR)

PROCESS	START	END	DURATION
DESIGN	4/2025	7/2026	16 Months
PERMITTING	8/2026	11/2026	4 Months
CONSTRUCTION	1/2027	8/2028	20 Months

PHASE 3A: DEMOLITION OF EXISTING JHS BUILDING

PROCESS	START	END	DURATION
DESIGN	3/2027	8/2027	6 Months
PERMITTING	9/2027	2/2028	6 Months
CONSTRUCTION	9/2028	4/2029	8 Months

PHASE 3B: NEW TRACK & FIELD

PROCESS	START	END	DURATION
DESIGN	4/2025	7/2026	16 Months
PERMITTING	9/2027	2/2028	6 Months
CONSTRUCTION	5/2029	12/2029	8 Months

PHASE 3C: COMPLETE NEW JHS BUILDING (SHELL - 3RD & 4TH FLOOR)

PROCESS	START	END	DURATION
DESIGN	4/2025	7/2026	16 Months
PERMITTING	9/2027	2/2028	6 Months
CONSTRUCTION	9/2028	8/2029	12 Months

1 NEW BASEBALL & SOFTBALL FIELDS



2A EARLY FOUNDATION TO GRADE - DEMO OF EXISTING TRACK & FIELD



2B START NEW JHS BUILDING (1ST & 2ND FLOOR)



3A DEMOLITION OF EXISTING JHS BUILDING



3B NEW TRACK & FIELD

3C COMPLETE NEW JHS BUILDING (SHELL - 3RD & 4TH FLOOR)



** All dates are subject to change and require validation from the Architect/Engineer and Construction Manager/General Contractor.*

The images shown were originally produced by BORA Architects and showcased in the Jefferson High School Modernization Community Information Session held on August 20, 2025, and can be found on the Portland Public Schools website (pps.net).

OPTION 2 | PORTABLES

STUDENT MOVE-IN DATE

JANUARY 2029

Option 2 (PORTABLE VILLAGE) provides Portland Public Schools with a plan that keeps students close to home while still accelerating Jefferson High School's modernization timeline. By using a separately designed and built portable village within walking distance of campus, around 400 students can remain in the neighborhood starting in 2026, avoiding the disruption of relocation to a distant site. This option allows for overlapping demolition and construction activities, **enabling students to occupy the new building by January 2029** — while also delivering some site amenities, like the baseball field, sooner. However, it introduces added costs and complexities tied to portables, site safety, temporary facilities for meals and PE, and careful sequencing of portable removal.

PROPOSED SCHEDULE

PHASE 1

PHASE 1A: FAST TRACK - PORTABLE VILLAGE			
PROCESS	START	END	DURATION
DESIGN / BUILD	11/2025	8/2026	9 Months

PHASE 1B: NEW BASEBALL FIELD ONLY			
PROCESS	START	END	DURATION
DESIGN	4/2025	1/2026	9 Months
PERMITTING	3/2026	7/2026	4 Months
CONSTRUCTION	7/2026	12/2026	5 Months

PHASE 2

PHASE 2A: DEMOLITION OF EXISTING JHS BUILDING			
PROCESS	START	END	DURATION
DESIGN	11/2025	5/2026	6 Months
PERMITTING	5/2026	7/2026	2 Months
CONSTRUCTION	7/2026	3/2027	8 Months

PHASE 2B: NEW TRACK & FIELD			
PROCESS	START	END	DURATION
DESIGN	4/2025	8/2026	16 Months
PERMITTING	8/2026	12/2026	4 Months
CONSTRUCTION	4/2027	12/2027	8 Months

PHASE 3

PHASE 3A: EARLY FOUNDATION TO GRADE - DEMOLITION OF EXISTING TRACK & FIELD			
PROCESS	START	END	DURATION
DESIGN	11/2025	2/2026	4 Months
PERMITTING	2/2026	6/2026	4 Months
CONSTRUCTION	6/2026	12/2026	6 Months

PHASE 3B: NEW JHS BUILDING			
PROCESS	START	END	DURATION
DESIGN	4/2025	8/2026	16 Months
PERMITTING	8/2026	12/2026	4 Months
CONSTRUCTION	1/2027	9/2028	20 Months

PHASE 3C: NEW SOFTBALL FIELD / DEMO OF PORTABLE VILLAGE			
PROCESS	START	END	DURATION
CONSTRUCTION	1/2029	8/2030	20 Months

** All dates are subject to change and require validation from the Architect/Engineer and Construction Manager/General Contractor.*

**Removal of portables and building the new softball field may take less than 20 months. The CMGC will need to validate the duration.*

1A FAST TRACK - PORTABLE VILLAGE

1B NEW BASEBALL FIELD ONLY



2A DEMOLITION OF EXISTING JHS BUILDING



2B NEW TRACK & FIELD



3A EARLY FOUNDATION TO GRADE - DEMO OF EXISTING TRACK & FIELD



3B NEW JHS BUILDING



3C NEW SOFTBALL FIELD / DEMO OF PORTABLE VILLAGE



The images shown were originally produced by BORA Architects and showcased in the Jefferson High School Modernization Community Information Session held on August 20, 2025, and can be found on the Portland Public Schools website (pps.net).

STUDENT MOVE-IN DATE

JANUARY 2029

OPTION 3 | SWING

**** PROCEDEO is aware that the Portland Public Schools voting community has previously rejected the "Swing" strategy proposed in Option 3.***

Option 3 (SWING) for the Jefferson High School Modernization Project offers Portland Public Schools a faster and more cost-effective path to completion. By delivering the new building for **student use in January 2029**—seven months earlier than the current plan—it reduces overall construction time by nearly a year. This approach minimizes prolonged disruption on campus, lowers escalation risks, and cuts soft costs associated with extended construction. However, it does require relocating about 400 students to swing space in August 2026 and introduces challenges around tighter sequencing and upfront coordination.

1 NEW BASEBALL & SOFTBALL FIELDS

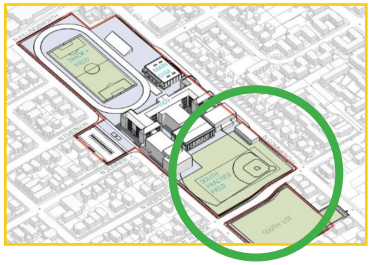

2A DEMOLITION OF EXISTING JHS BUILDING



2B NEW TRACK & FIELD



3A EARLY FOUNDATION TO GRADE - DEMO OF EXISTING TRACK & FIELD

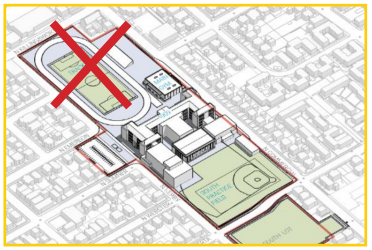

3B NEW JHS BUILDING

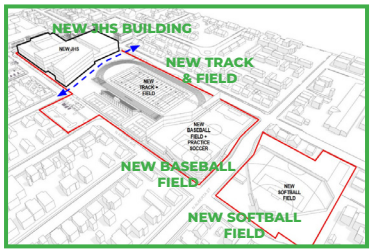

The images shown were originally produced by BORA Architects and showcased in the Jefferson High School Modernization Community Information Session held on August 20, 2025, and can be found on the Portland Public Schools website (pps.net).

PROPOSED SCHEDULE

PHASE 1: NEW BASEBALL & SOFTBALL FIELDS			
PROCESS	START	END	DURATION
DESIGN	4/2025	1/2026	9 Months
PERMITTING	3/2026	7/2026	4 Months
CONSTRUCTION	7/2026	12/2026	5 Months

PHASE 2A: DEMOLITION OF EXISTING JHS BUILDING			
PROCESS	START	END	DURATION
DESIGN	11/2025	5/2026	6 Months
PERMITTING	5/2026	7/2026	2 Months
CONSTRUCTION	7/2026	3/2027	8 Months

PHASE 2B: NEW & TRACK FIELD			
PROCESS	START	END	DURATION
DESIGN	4/2025	8/2026	16 Months
PERMITTING	8/2026	12/2026	4 Months
CONSTRUCTION	4/2027	12/2027	8 Months

PHASE 3A: EARLY FOUNDATION TO GRADE - DEMOLITION OF EXISTING TRACK & FIELD			
PROCESS	START	END	DURATION
DESIGN	11/2025	2/2026	4 Months
PERMITTING	2/2026	6/2026	4 Months
CONSTRUCTION	6/2026	12/2026	6 Months

PHASE 3B: NEW JHS BUILDING			
PROCESS	START	END	DURATION
DESIGN	4/2025	8/2026	16 Months
PERMITTING	8/2026	12/2026	4 Months
CONSTRUCTION	1/2027	9/2028	20 Months

** All dates are subject to change and require validation from the Architect/Engineer and Construction Manager/General Contractor.*

JEFFERSON HIGH SCHOOL OPTIONS

DESIGN, PERMIT, & CONSTRUCTION SCHEDULE COMPARISON

Per our directive from the Superintendent, we were tasked with looking at ways to expedite moving students into the modernized building sooner. The alternative strategies prioritize students by providing earlier access to new learning spaces and athletic facilities. Ultimately, the decision requires weighing the value of earlier access and reduced escalation against the complexity, safety, and community concerns inherent in each alternative. Options such as Swing, Portable Village, or Shell shorten timelines by a year or more, ensuring that Jefferson students benefit from modernized classrooms and programs much sooner. The Superintendent and the community are eager to see real improvements; these proposed options offer a pathway to student-centered choices.

PROPOSED JHS OPTION 1 SHELL

PROS

Earlier occupancy for students – PPS can move into the building Aug 2028.

Accelerated educational benefit – Students gain access to classrooms and key facilities sooner.

Time savings – Overall project is completed by Dec 2029.

Potential cost savings on escalation – Earlier occupancy reduces soft cost exposure compared to a longer, fully sequential project.

CONS

Safety and logistics risk – Students and staff occupy the building while upper floors are under construction, requiring strict safety measures.

Limited access to fully completed facilities – Upper-floor classrooms, labs, and other spaces remain unavailable until Phase 3C is finished. However, accommodating students is achievable without utilizing the 3rd and 4th floors.

Complex construction sequencing – Contractors must carefully manage work around occupied areas, which can increase supervision, logistics, and temporary protections.

Potential for noise/disruption – Construction above or adjacent to occupied spaces can impact learning environment.

Coordination with trades is critical – MEP, elevators, and structural completion must be carefully staged to avoid delays or conflicts with occupied areas.

Phased commissioning challenges – Systems serving the partially occupied building may need temporary setups or repeated testing after upper floors are completed.

PROPOSED JHS OPTION 2 PORTABLE VILLAGE

PROS

Off-site relocation – Students remain in the neighborhood instead of being sent to a distant campus.

Portable village within walking distance – Easy access across the street keeps 400 students connected to their community until construction is complete.

Accelerated overall schedule – Overlapping demo, foundation, and building construction allows new building occupancy Jan 2029, saving ~1 year versus the current plan.

Phased delivery of site amenities – New baseball field completed early; track and other fields delivered later.

Reduced soft cost exposure – Shorter program duration reduces escalation and general condition costs.

Parallel design/build efficiencies – Portable village can be designed and built separately, accelerating construction readiness.

CONS

Portables cost – Procurement, installation, utilities, and maintenance add upfront costs; removal later adds mobilization.

Construction site intensity – Overlapping construction zones on campus while students are present increases safety risks.

Limited early field access – Only the baseball field is available; track, softball, and other fields wont be completed until end of project.

Community/parent perception – Learning in portables may be perceived as temporary or substandard.

Compressed design & permitting schedule – Overlapping windows increase risk of errors or permitting delays.

Portables removal impact – Final removal overlaps with site finishing; sequencing must be carefully managed.

No cafeteria, gymnasium, science labs, or PE area in portables – District must find temporary alternatives for meals, physical education, and lab instruction, adding cost and complexity.

PROPOSED JHS OPTION 3 SWING

PROS

Earlier completion - Full project done Jan 2029, saving 12+ months.

Earlier building use - Students occupy new facility Jan 2029, accelerating educational benefit.

Reduced escalation exposure - Shorter overall timeline limits the impact of material/labor inflation.

Efficient sequencing - Early demo and foundation packages run in parallel with field work, preventing gaps.

Utility/abatement addressed earlier - Early demo package (2A) allows asbestos/abatement to be cleared up front.

Soft cost savings - Fewer mobilizations, less extended general conditions cost.

CONS

Swing space required - Moving students off-site Aug 2026–Jan 2029 requires logistics, transportation, and community buy-in.

Higher upfront complexity - Multiple early packages (demo, foundation, fields) demand close coordination with city permitting.

Potential cost premium - Phased GMPs/early packages may add some contractor markup and overhead.

Compressed design durations - Some design overlaps could create pressure on architects/engineers to deliver faster.

Community perception - Swinging students out temporarily may be unpopular, even if it accelerates the final delivery.

**** PROCEDEO is aware that the Portland Public Schools voting community has previously rejected the "Swing" strategy proposed in Option 3.***

SECTION 04

SCHEDULE ANALYSIS

PROCEDEO

SCHEDULE ANALYSIS

DESIGN, PERMIT, & CONSTRUCTION SCHEDULE COMPARISON

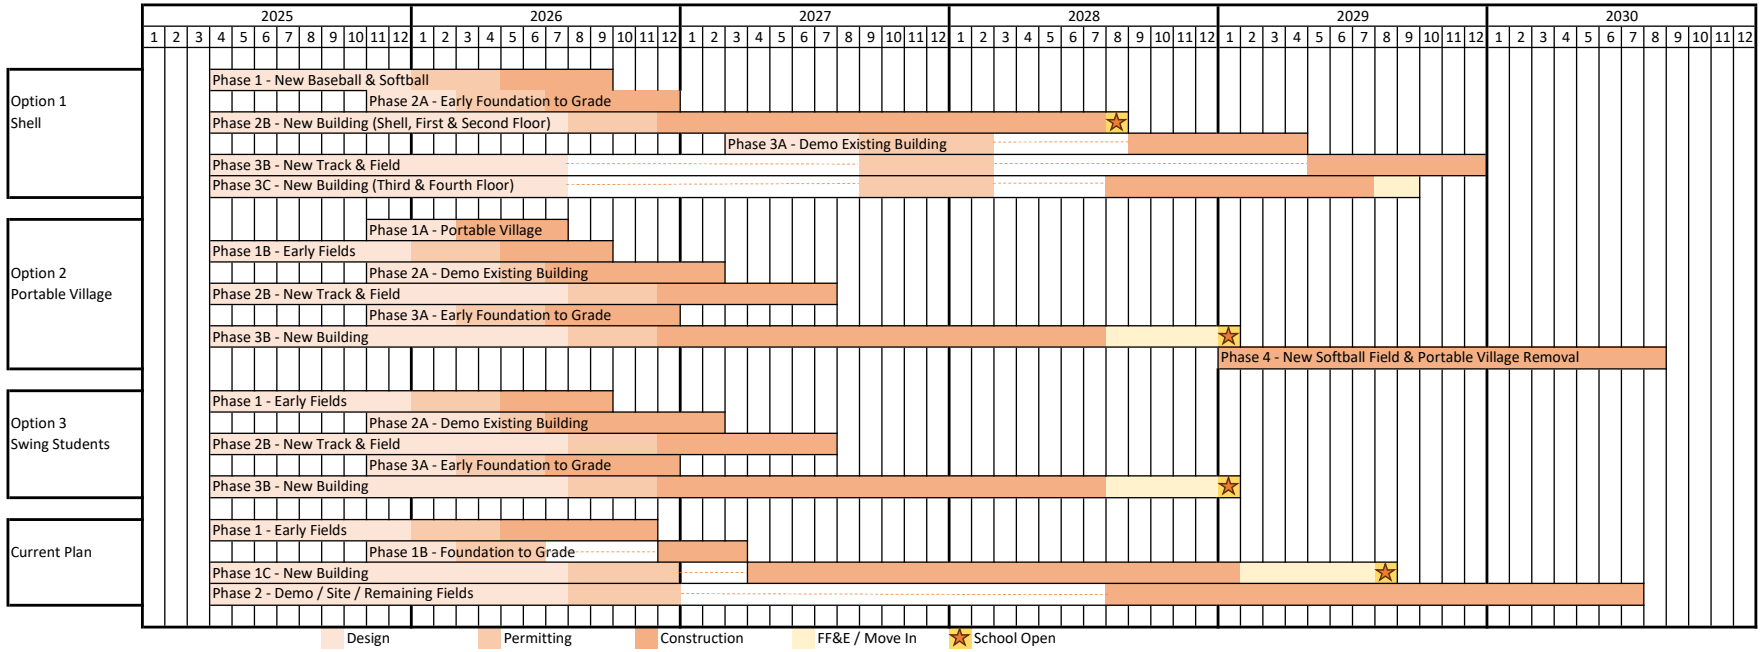

CURRENT PLAN | FINAL COMPLETION JULY 2030

While this phased approach offers benefits such as **early access to athletic fields and reduced design risk**, it ultimately extends the Jefferson High School Modernization Project timeline too far.

Full project completion would not occur until 2030, leaving students and the community to deal with ongoing construction impacts for more than five years.

The prolonged schedule also **increases exposure to cost escalation, permitting delays, and repeated utility challenges**, making this the least efficient and most disruptive option.

OPTION 1 (SHELL) | FINAL COMPLETION DECEMBER 2029

Option 1 delivers student-usable classrooms and facilities **earlier (August 2028)** and compresses the total schedule.

Compared to Option 3, it **achieves earlier occupancy**, but introduces **higher safety, coordination, and operational risks** since construction continues in unoccupied portions of the same building. Compared to Option 2 (portables), it **avoids temporary structures** but relies heavily on careful phasing to keep students safe and minimize disruption.

OPTION 2 (PORTABLES) | FINAL COMPLETION AUGUST 2030

Option 2 will lead to earlier completion and reduced soft costs.

Compared to Option 3, it **keeps students local** and connected to their community while construction is ongoing. The main trade-offs are higher site management complexity and the **need to provide alternatives for cafeteria, PE, and science labs.**

OPTION 3 (SWING) | FINAL COMPLETION JANUARY 2029

Option 3 saves the District one year overall (completion in January 2029 vs. 2030). This also means that students will be in the new building sooner (occupancy in January 2029 vs. August 2029).

Option 3 avoids keeping the campus in major construction mode as long, which reduces escalation risk, soft costs, and prolonged disruption.

That said, Option 3 does introduce **new trade-offs**, mainly around student swing space, more aggressive sequencing, and higher upfront coordination.

**** PROCEDEO is aware that the Portland Public Schools voting community has previously rejected the "Swing" strategy proposed in Option 3.***

JEFFERSON HIGH SCHOOL SCHEDULE

Factor	Current Plan	Option 1 - Shell	Option 2 - On-Site Portables	Option 3 - Off-Site Swing
Full Project Completion	Aug 2030	Aug 2029	Aug 2029	Jan 2029
Student Occupancy	Aug 2029	Aug 2028 (partial access)	Jan 2029	Jan 2029
Student Relocation / Swing Space	None	None	On-site portables	Off-site for 3 years
Construction Disruption / Safety Risk	Medium (long timeline)	High; students occupy lower floors while upper floors under construction	Medium to High; intensive site activity	Low
Field Access	Staggered; some early fields, final track & field later delivery	Staggered; some early fields, final track & field later delivery	Only baseball field early; remaining fields delayed	All fields will be delivered by end 2027
Soft Cost / Escalation Exposure	High (long timeline)	Medium-low	Medium	Medium
Flexibility / Phasing Efficiency	Low	Medium; partial occupancy accelerates use, but requires careful staging	Medium	Medium; requires full swing
Complexity of Management	Low	High; occupied construction requires careful coordination	High; portables + construction overlap	Medium; swing logistics
Community / Student Impact	Long exposure to construction	Partial building occupancy; learning environment affected by ongoing construction. High exposure.	Students remain local; temporary classrooms. High exposure.	Displaced students; full off-site relocation. No exposure to construction
Cost Implications	Baseline	Moderate; cost for logistics	High; portables, utilities, removal	Moderate-high; swing + staging + occupied construction safety measures

SCHEDULE ANALYSIS

OPTION 1 | SHELL

Activity ID	Activity Name	Months	Orig Dur	Rem Dur	Start	Finish
Jefferson High School - Option 1						
New Baseball and Softball Fields - Phase 1						
A1470	Early Fields Design (Baseball & Softball)	9 Months	275	99	01-Apr-25 A	31-Dec-25
A1340	Permits Early Fields	4 Months	122	122	01-Mar-26	30-Jun-26
A1370	Early Fields Construction (Baseball & Softball)	5 Months	153	153	01-Jul-26	30-Nov-26
Early Foundation to Grade - Demo Existing Track and Field - Phase 2A						
A1540	Early Foundation to Grade Design	4 Months	120	120	01-Nov-25*	28-Feb-26
A1550	Permits	4 Months	122	122	01-Mar-26	30-Jun-26
A1560	Construct New Building Foundations & Utilities	6 Months	184	184	01-Jul-26	31-Dec-26
New Building (Shell, First & Second Floor) - Phase 2B						
A1570	New Building Design	16 Months	487	311	01-Apr-25 A	31-Jul-26
A1580	Permits	4 Months	122	122	01-Aug-26	30-Nov-26
A1590	Construct New Building (Shell, First & Second Floor)	20 Months	609	609	01-Jan-27	31-Aug-28
Demo Package Existing Building - Phase 3A						
A1490	Design Documents	6 Months	184	184	01-Mar-27*	31-Aug-27
A1500	Permits	6 Months	182	182	01-Sep-27	29-Feb-28
A1450	Phase 3A Demo Existing Building	8 Months	242	242	01-Sep-28	30-Apr-29
New Track and Field - Phase 3B						
A1510	New Track and Field Design	16 Months	487	311	01-Apr-25 A	31-Jul-26
A1520	Permits	6 Months	182	182	01-Sep-27	29-Feb-28
A1530	Construct New Track and Field	8 Months	245	245	01-May-29	31-Dec-29
New Building (Third & Fourth Floor) - Phase 3C						
A1600	New Building Design	16 Months	487	311	01-Apr-25 A	31-Jul-26
A1610	Permits	6 Months	182	182	01-Sep-27	29-Feb-28
A1620	Construct New Building (Third & Fourth Floor)	12 Months	365	365	01-Sep-28	31-Aug-29
Close-Out						
A1410	OTIS Installation	3 Months	92	92	01-Jun-28	31-Aug-28
A1400	Substantial Completion		0	0		31-Aug-28
A1420	FF&E Installation (First & Second Floor)	1 Month	31	31	01-Sep-28	01-Oct-28
A1430	Move In (First & Second Floor)	1 Month	31	31	01-Sep-28	01-Oct-28
A1440	School Opens		0	0		01-Oct-28*
A1630	FF&E Installation (Third & Fourth Floor)	2 Months	61	61	02-Aug-29	01-Oct-29
A1640	Move In (Third & Fourth Floor)	1 Month	31	31	02-Oct-29	01-Nov-29
A1460	JHS Complete		0	0		31-Dec-29

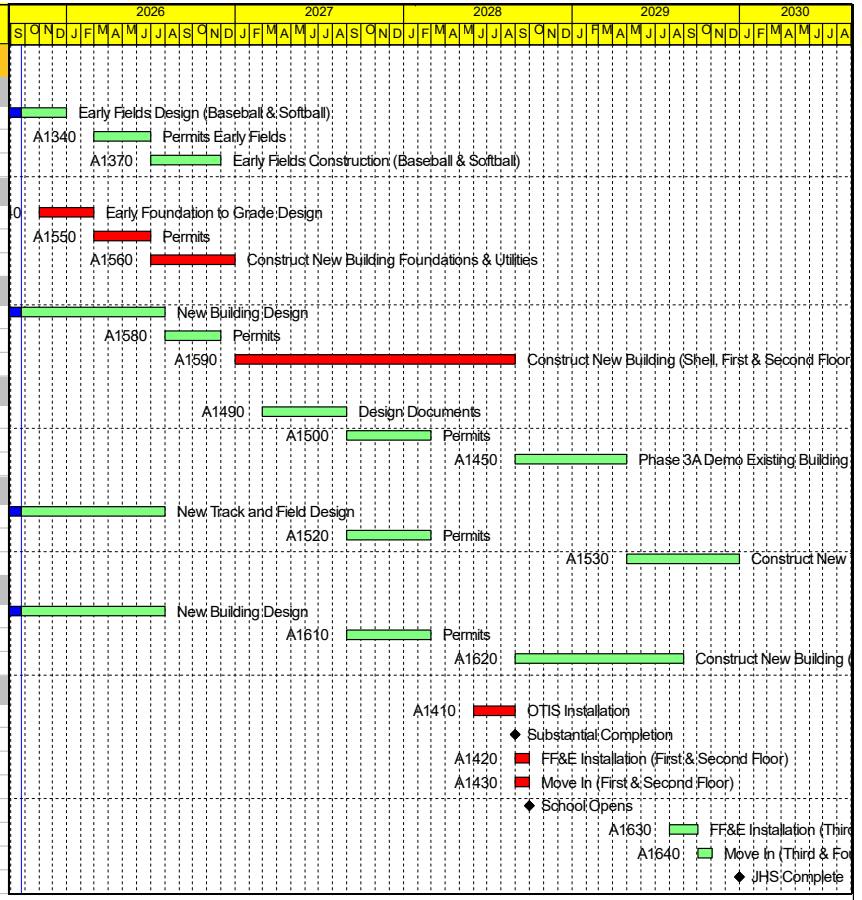

Start Date	01-Apr-25
Finish Date	31-Aug-28
Data Date	24-Sep-25
Run Date	21-Oct-25

Remaining Level of Effort · Critical R... · Actual Level of Effort · Milestone · Previous Baseline · Actual Work · Remaining Work

JHS Options — 1 of 1

Procedeo
Jefferson High School
Option 1 - Shell

PROCEDEO

OPTION 2 | PORTABLE VILLAGE

Activity ID	Activity Name	Months	Orig Dur	Rem Dur	Start	Finish
Jefferson High School - Option 2						
FAST TRACK - Portable Village - Phase 1A						
A1600	Design / Building Portable Village	9 Months	273	273	01-Nov-25*	31-Jul-26
Set A - Early Fields (Only New Baseball Field) - Phase 1B						
A1470	Set A - Early Fields Design	9 Months	183	99	01-Apr-25 A	31-Dec-25
A1340	Set A - Permits Early Field	4 Months	120	120	01-Jan-26	30-Apr-26
A1370	Set A - Early Field (Baseball Field) Construction	5 Months	153	153	01-May-26	30-Sep-26
Set B - Demo Package Existing Building - Phase 2A						
A1490	Set B - Design Documents	6 Months	181	181	01-Nov-25*	30-Apr-26
A1500	Set B - Permits	2 Months	61	61	01-May-26	30-Jun-26
A1450	Set B - Phase 2 Demo Existing Building	8 Months	243	243	01-Jul-26	28-Feb-27
Set D - New Track and Field - Phase 2B						
A1510	Set D - New Track and Field Design	16 Months	333	311	01-Apr-25 A	31-Jul-26
A1520	Set D - Permits	4 Months	122	122	01-Aug-26	30-Nov-26
A1530	Set D - Construct New Track and Field	8 Months	243	243	01-Dec-26	31-Jul-27
Set C - Early Foundation to Grade - Existing Track and Field Demo - Phase 3A						
A1540	Set C - Early Foundation to Grade Design	4 Months	120	120	01-Nov-25*	28-Feb-26
A1550	Set C - Permits	4 Months	122	122	01-Mar-26	30-Jun-26
A1560	Set C - Construct New Building Foundations & Utilities	6 Months	126	126	01-Jul-26	03-Nov-26
Set D - New Building - Phase 3B						
A1570	Set D - New Building Design	16 Months	333	311	21-Apr-25 A	31-Jul-26
A1580	Set D - Permits	4 Months	121	121	01-Aug-26	29-Nov-26
A1590	Set D - Construct New Building	20 Months	610	610	30-Nov-26	31-Jul-28
Set A - New Softball Field & Portable Village Removal - Phase 4						
A1630	Set A - New Softball Field & Portable Village Demo / Removal		608	608	01-Jan-29*	31-Aug-30
Close-Out						
A1400	Substantial Completion		0	0		31-Jul-28
A1410	OTIS Installation	3 Months	92	92	01-Aug-28	31-Oct-28
A1420	FF&E Installation	3 Months	92	92	01-Aug-28	31-Oct-28
A1460	JHS Complete		0	0		31-Oct-28
A1430	Move In	1 Months	31	31	01-Dec-28	31-Dec-28
A1440	School Opens		0	0		01-Jan-29*

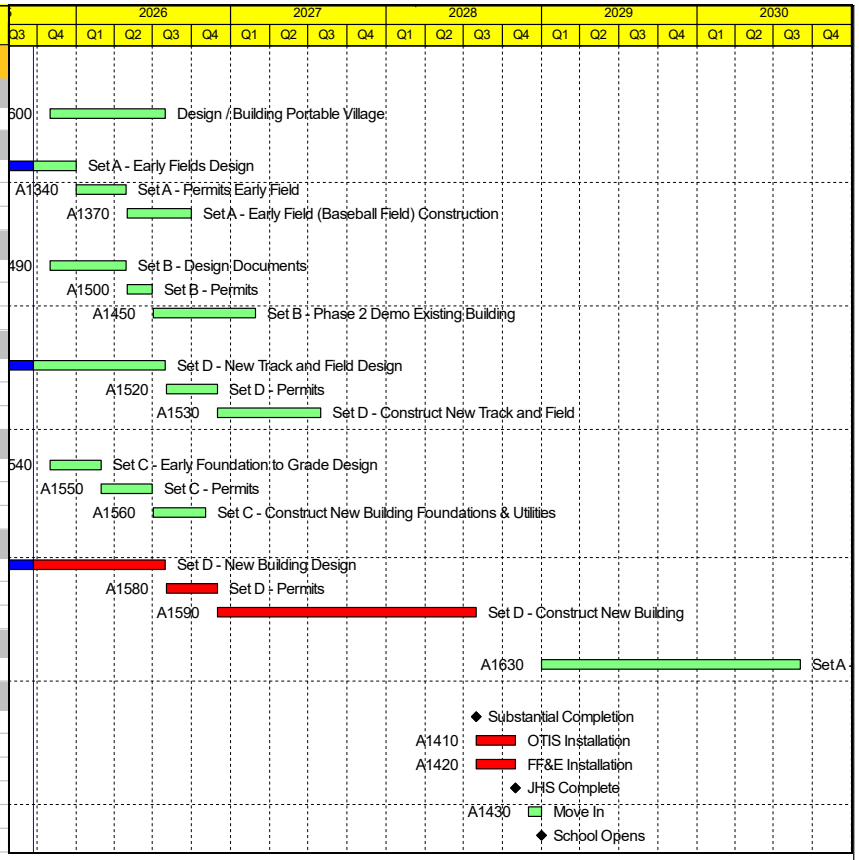

Start Date	01-Apr-25
Finish Date	31-Jul-28
Data Date	24-Sep-25
Run Date	26-Sep-25

Remaining Level of Effort · Critical R... · Actual Level of Effort · Milestone · Previous Baseline · Actual Work · Remaining Work

JHS Options 1 of 1
Procedeo
Jefferson High School
Option 2 - 400 Student On-Site Portables

OPTION 3 | SWING

** PROCEDEO is aware that the Portland Public Schools voting community has previously rejected the "Swing" strategy proposed in Option 3.*

Activity ID	Activity Name	Months	Orig Dur	Rem Dur	Start	Finish
Jefferson High School - OPTION 3						
Set A - Early Fields - Phase 1						
A1470	Set A - Early Fields Design	9 Months	275	99	01-Apr-25 A	31-Dec-25
A1340	Set A - Permits Early Fields	4 Months	120	120	01-Jan-26	30-Apr-26
A1370	Set A - Early Fields Construction	5 Months	153	153	01-May-26	30-Sep-26
A1480	MS- 400 Students Off-Site		0	0	01-Aug-26*	
Set B - Demo Package Existing Building - Phase 2A						
A1490	Set B - Design Documents	6 Months	181	181	01-Nov-25	30-Apr-26
A1500	Set B - Permits	2 Months	61	61	01-May-26	30-Jun-26
A1450	Set B - Phase 2 Demo Existing Building	8 Months	243	243	01-Jul-26	28-Feb-27
Set D - New Track and Field - Phase 2B						
A1510	Set D - New Track and Field Design	16 Months	333	311	01-Apr-25 A	31-Jul-26
A1520	Set D - Permits	4 Months	122	122	01-Aug-26	30-Nov-26
A1530	Set D - Construct New Track and Field	8 Months	243	243	01-Dec-26	31-Jul-27
Set C - Early Foundation to Grade - Existing Track and Field Demo - Phase 3A						
A1540	Set C - Early Foundation to Grade Design	4 Months	120	120	01-Nov-25	28-Feb-26
A1550	Set C - Permits	4 Months	122	122	01-Mar-26	30-Jun-26
A1560	Set C - Construct New Building Foundations & Utilities	6 Months	184	184	01-Jul-26	31-Dec-26
Set D - New Building - Phase 3B						
A1570	Set D - New Building Design	16 Months	333	311	01-Apr-25 A	31-Jul-26
A1580	Set D - Permits	4 Months	122	122	01-Aug-26	30-Nov-26
A1590	Set D - Construct New Building	20 Months	609	609	01-Dec-26	31-Jul-28
Project Completion						
A1460	Substantial Completion		0	0		31-Jul-28
A1600	FF&E Installation	3 Months	92	92	01-Aug-28	31-Oct-28
A1610	OTIS Installation	3 Months	92	92	01-Aug-28	31-Oct-28
A1620	JHS Complete		0	0		31-Oct-28
A1430	Move In	1 Month	31	31	01-Dec-28	31-Dec-28
A1440	School Opens		0	0		01-Jan-29*

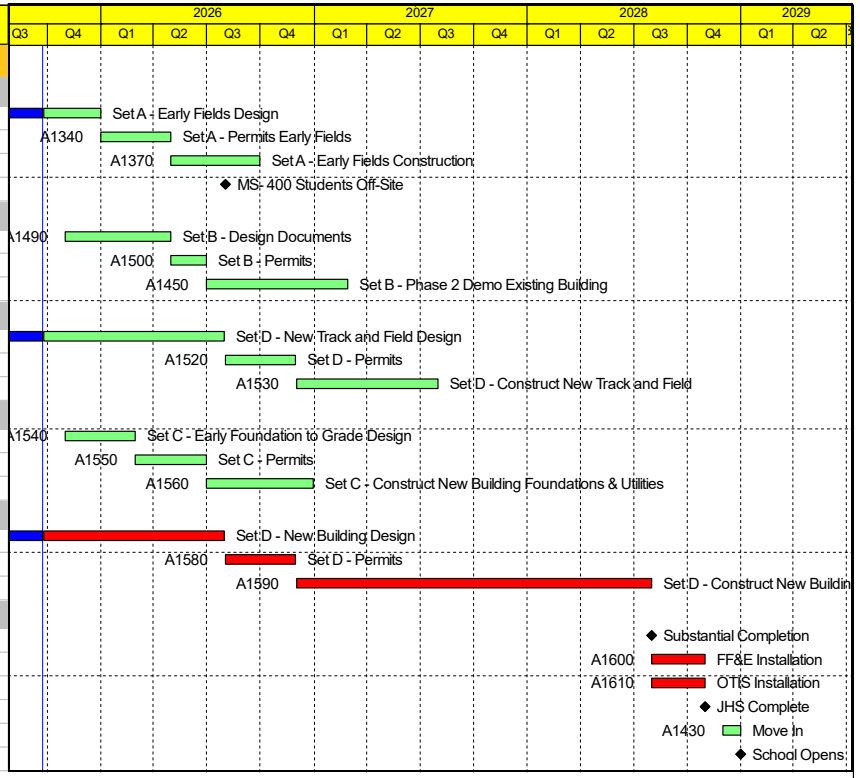

Start Date	01-Apr-25
Finish Date	31-Jul-28
Data Date	24-Sep-25
Run Date	26-Sep-25

Remaining Level of Effort · Critical R...
Actual Level of Effort · Milestone
Previous Baseline
Actual Work
Remaining Work

JHS Options
Procedeo
Jefferson High School
OPTION 3 | SWING

1 of 1

PROCEDEO

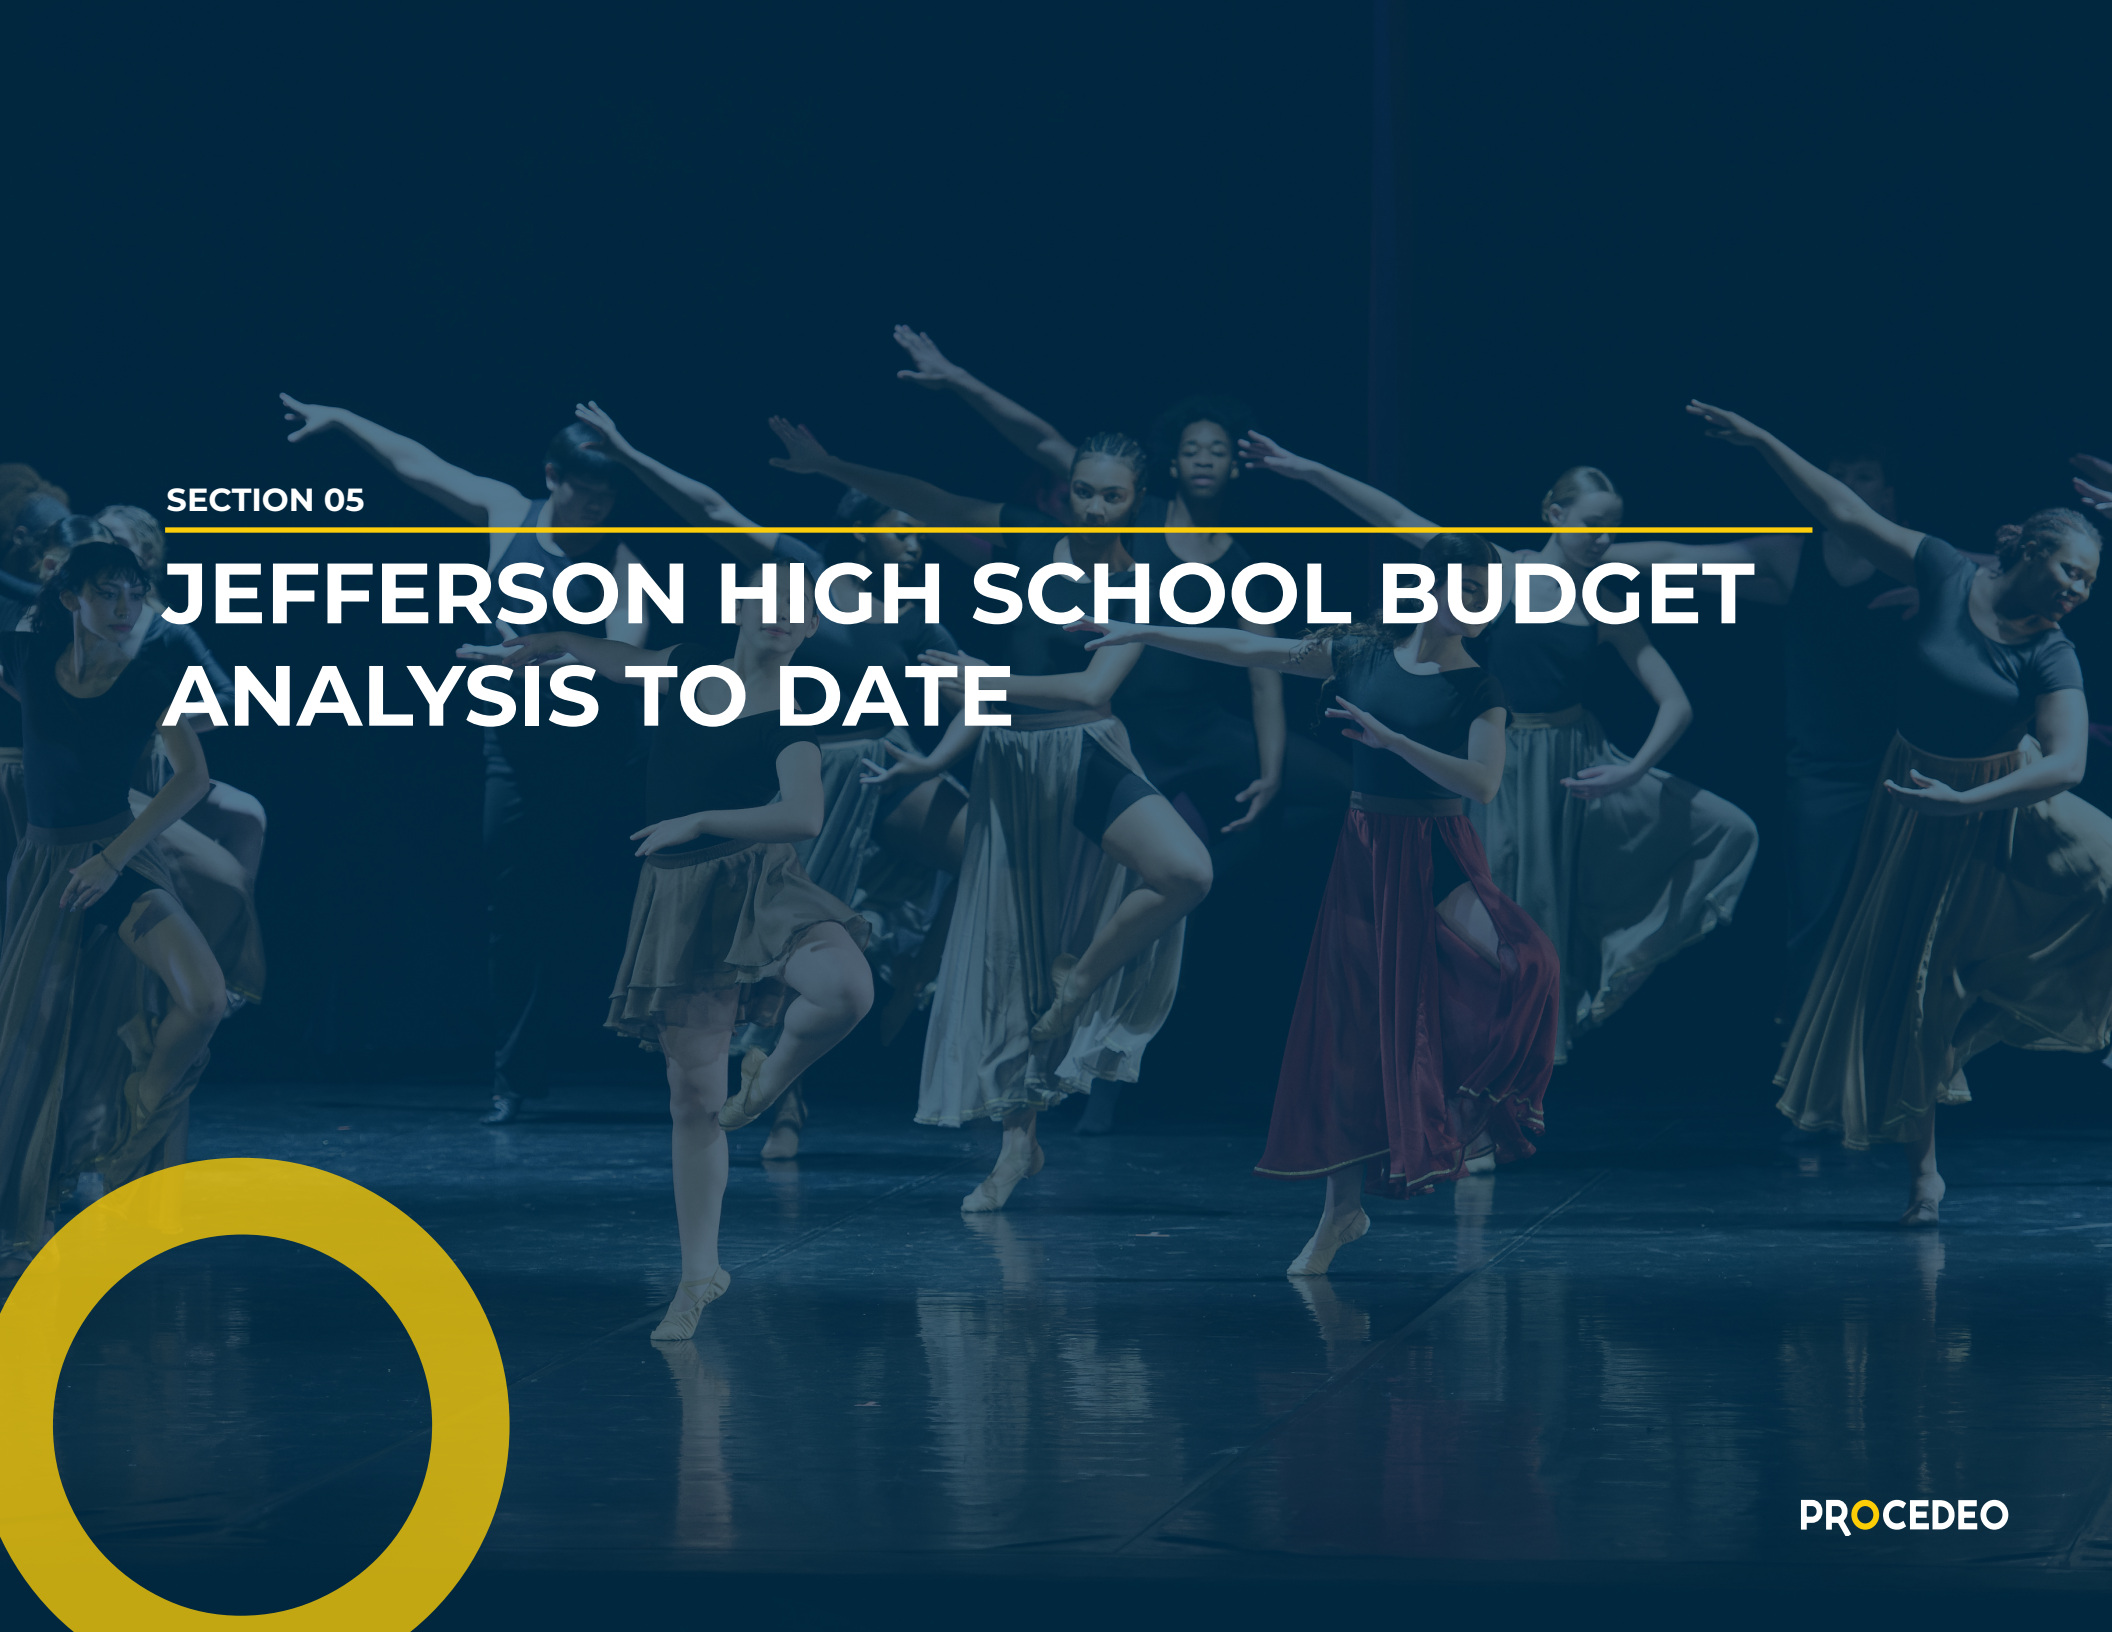

SECTION 05

JEFFERSON HIGH SCHOOL BUDGET ANALYSIS TO DATE

PROCEDEO

JEFFERSON HIGH SCHOOL BUDGET ANALYSIS TO DATE

FINANCIAL MANAGEMENT REPORT AS OF SEPTEMBER 29, 2025

Jefferson HS Modernization	CURRENT					PROJECTIONS		
	Initial Budget	Changes To-Date	Current Budget	Executed / Projected Commitments	Paid-To-Date	Uncommitted Current Budget	Additional Forecasted Commitments	Projected Commitments (Over)/Under
Demolition & Deconstruction	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00
New Construction - Building	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00
Major Renovations > $25k	222,717,203.00	134,884,663.00	357,601,866.00	2,447,973.25	2,214,062.25	355,153,892.75	355,153,892.75	0.00
Minor Alterations < $25k	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00
Ordinary Repairs & Maintenance	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00
Site Improvements (Non-building)	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00
Off-Site Improvements (Non-building)	1,555,000.00	945,000.00	2,500,000.00	0.00	0.00	2,500,000.00	2,500,000.00	0.00
Hazardous Material Abatement	3,110,000.00	(2,610,000.00)	500,000.00	0.00	0.00	500,000.00	500,000.00	0.00
Other Property Services	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00
Utility Costs and Connection Fees - Electric	622,000.00	278,000.00	900,000.00	0.00	0.00	900,000.00	900,000.00	0.00
Land Acquisition	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00
Easements/Rights-of-Way	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00
Total Hard Costs (Category 1)	$228,004,203.00	$133,497,663.00	$361,501,866.00	$2,447,973.25	$2,214,062.25	$359,053,892.75	$359,053,892.75	$0.00
Architectural Design	18,660,000.00	23,478,920.42	42,138,920.42	40,138,920.42	18,435,203.87	2,000,000.00	2,000,000.00	0.00
Professional Engineering Services	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00
Hazardous Materials Consultant Services	311,000.00	(11,000.00)	300,000.00	271,518.00	238,391.02	28,482.00	28,482.00	0.00
Material Testing & Special Inspections	622,000.00	(322,000.00)	300,000.00	28,000.00	28,000.00	272,000.00	272,000.00	0.00
Geotechnical Engineering Services	0.00	300,000.00	300,000.00	216,910.00	189,760.25	83,090.00	83,090.00	0.00
Land Surveyor Services	124,400.00	125,600.00	250,000.00	200,875.00	196,615.00	49,125.00	49,125.00	0.00
Cost Estimating Consultant	31,100.00	(31,100.00)	0.00	0.00	0.00	0.00	0.00	0.00
Building Commissioning Services	622,000.00	78,000.00	700,000.00	645,160.00	45,200.00	54,840.00	54,840.00	0.00
Building Envelope Consultant	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00
Constructability Reviews	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00
Permit/Land Use Consultant Services	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00
Sustainability Consultant	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00
Traffic Engineering Services	311,000.00	(186,000.00)	125,000.00	99,352.00	73,360.00	25,648.00	25,648.00	0.00
3rd Party QA/QC Inspections	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00
Other Design Services	311,000.00	(211,000.00)	100,000.00	71,025.41	70,023.41	28,974.59	28,974.59	0.00
Construction Management - External	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00
Program Management - External	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00
Project Management - External	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00
Legal Services	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00
Total Soft Costs (Category 2)	$20,992,500.00	$23,221,420.42	$44,213,920.42	$41,671,760.83	$19,276,553.55	$2,542,159.59	$2,542,159.59	$0.00
Project Management - Internal	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00
District Administrative Cost	12,440.00	(12,440.00)	0.00	0.00	0.00	0.00	0.00	0.00
Educational Staff	62,200.00	(17,200.00)	45,000.00	0.00	0.00	45,000.00	45,000.00	0.00
Custodial Staff	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00
Other District Staff Costs	7,778,960.00	(7,778,960.00)	0.00	0.00	0.00	0.00	0.00	0.00
Advertising	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00
Printing/Reprographics	0.00	244.44	244.44	7,312.20	244.44	(7,067.76)	(7,067.76)	0.00
Land Use Permitting	62,200.00	(62,200.00)	0.00	0.00	0.00	0.00	0.00	0.00
Permitting	0.00	4,150,000.00	4,150,000.00	203,336.15	203,336.15	3,946,663.85	3,946,663.85	0.00
Facilities Permit Program (FPP)	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00
System Development Charges	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00
Dues & Fees	62,200.00	0.00	62,200.00	627.00	627.00	61,573.00	61,573.00	0.00
Local Meetings	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00
Temporary Facilities & Equipment Rentals	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00
Moving Services	933,000.00	(133,000.00)	800,000.00	13,585.46	6,519.48	786,414.54	786,414.54	0.00
Student Transportation (School Bus)	62,200.00	(62,200.00)	0.00	0.00	0.00	0.00	0.00	0.00
Maintenance Work Orders	12,440.00	(2,440.00)	10,000.00	0.00	0.00	10,000.00	10,000.00	0.00
Office Equipment/Consumable Supplies	12,440.00	12,560.00	25,000.00	4,781.18	4,781.18	20,218.82	20,218.82	0.00
Computers & Peripherals	3,110,000.00	(360,000.00)	2,750,000.00	0.00	0.00	2,750,000.00	2,750,000.00	0.00
Miscellaneous Technology	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00
Fixtures, Furniture and Equipment < $150	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00
Fixtures, Furniture and Equipment $150 < $24	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00
Fixtures, Furniture and Equipment > $2500	7,775,000.00	(25,000.00)	7,750,000.00	0.00	0.00	7,750,000.00	7,750,000.00	0.00
Maintenance Materials	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00
Computer Software	311,000.00	(311,000.00)	0.00	0.00	0.00	0.00	0.00	0.00
Bond Issuance Costs	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00
Bond Assurances/Set-Asides	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00
Builders Risk Insurance (District Held)	1,244,000.00	756,000.00	2,000,000.00	0.00	0.00	2,000,000.00	2,000,000.00	0.00
Transfer to Other Funds	0.00	7,500.00	7,500.00	0.00	0.00	7,500.00	7,500.00	0.00
Total Owners Costs (Category 3)	$21,438,080.00	($3,838,135.56)	$17,599,944.44	$229,641.99	$215,508.25	$17,370,302.45	$17,370,302.45	$0.00
Escalation	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00
Contingency	195,565,217.00	(152,873,447.86)	42,691,769.14	0.00	0.00	42,691,769.14	42,691,769.14	0.00
Total Contingency (Category 4)	$195,565,217.00	($152,873,447.86)	$42,691,769.14	$0.00	$0.00	$42,691,769.14	$42,691,769.14	$0.00
OTHER FUNDING SOURCE								
INTEREST								
Total	**$466,000,000.00**	**$7,500.00**	**$466,007,500.00**	**$44,349,376.07**	**$21,706,124.05**	**$421,658,123.93**	**$421,658,123.93**	**$0.00**
				Commitments Less Paid to Date = Remaining Commitments $22,643,252.02				

CLOSING

We greatly appreciate the opportunity to work alongside the PPS team on this effort. Without their openness and collaboration, this report would not have been possible. We remain committed to providing the leadership and guidance necessary to ensure corrective measures are in place - keeping not only the individual projects, but the overall bond program, on budget and on schedule.

We welcome the opportunity to further discuss any of the observations and recommendations outlined in this report. While our analysis is centered on the Jefferson High School project, many of the findings, concerns, and recommendations are broadly applicable across the bond program. Our goal is to provide actionable insight that supports PPS in strengthening effectiveness, efficiency, and transparency throughout the process.

PROCEDEO

SECTION 06 | APPENDIX

CURRENT PLAN, CONDITIONS, & SCHEDULE

PROCEDEO

CURRENT SITE PLAN AND AERIAL VIEW

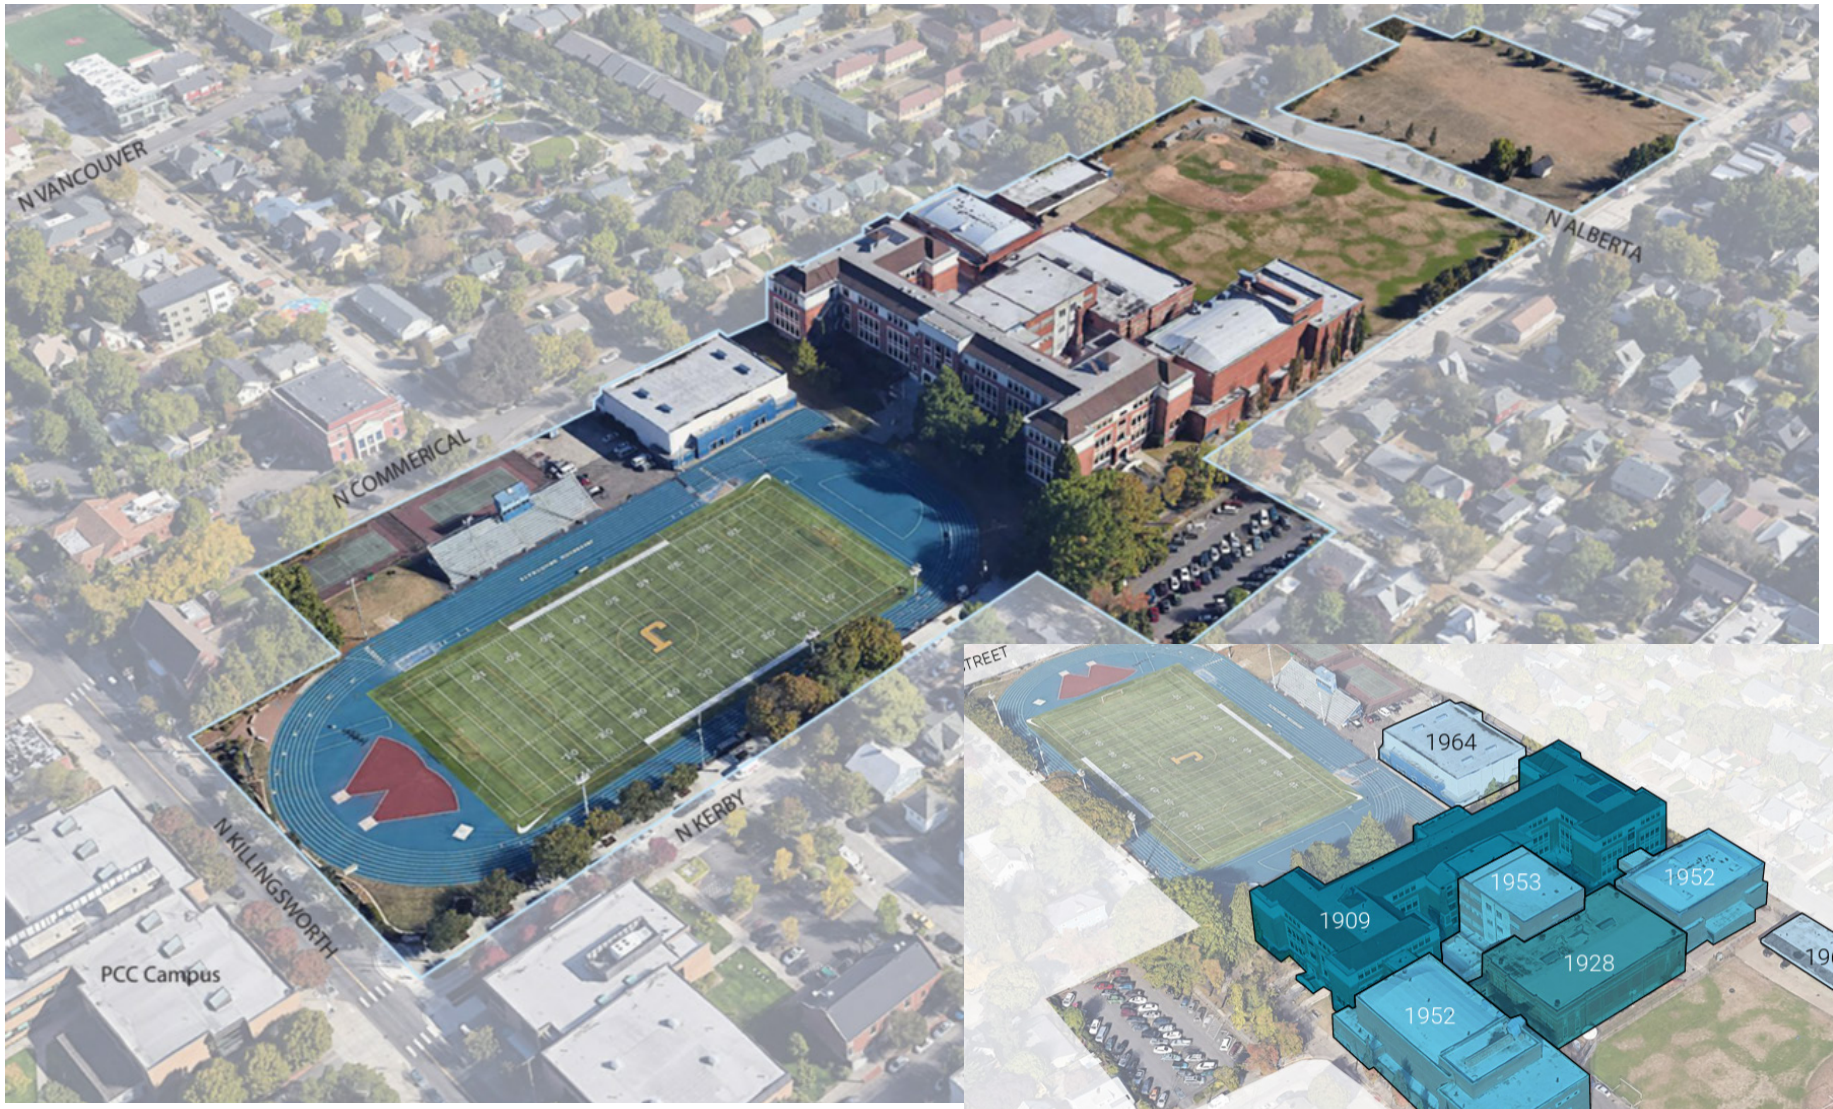

Aerial view from northwest of the existing Jefferson High School campus

The images shown were originally produced by BORA Architects and showcased in the Jefferson High School Conceptual Master Plan Report prepared in January of 2020, and can be found on the Portland Public Schools website (pps.net).

SITE PAIN POINTS

1. **Historic 1909 Building.** The front steps, both inside and outside of the main building, are not accessible but hold symbolic value as a traditional gathering spot. This creates a major challenge to compliance with modern universal design standards, which require equal access for all users. While removal is possible, the design must re-establish a new outdoor "heart" for the school to replace that function.

2. **Building Organization.** Unified building design is preferred: avoid multiple separate buildings. The theater and gym should be easily accessible to the public. All new construction should be located south of the historic 1909 building.

3. **Athletics & Support Spaces.** Scattered fields present connectivity challenges.

4. **Commons & Circulation.** The Student Commons should be positioned close to the main building entrance to maximize accessibility and centrality.

5. **1928 Gymnasium.** While there was interest in reuse, the 1928 Gymnasium should not be retained, as it limits design opportunities elsewhere. Detached building presents security challenges.

6. **Parking.** Existing parking is limited and athletic parking is stationed on the side streets.

In general, the current proposed design by BORA Architects addresses the High School pain points.

SITE INFORMATION

PORTLAND PUBLIC SCHOOLS | District No. 1J, Multnomah County
SITE AREA | 13.5 Acres
GRADES | High School 9th - 12th
STUDENT ENROLLMENT | approx. 402 Students

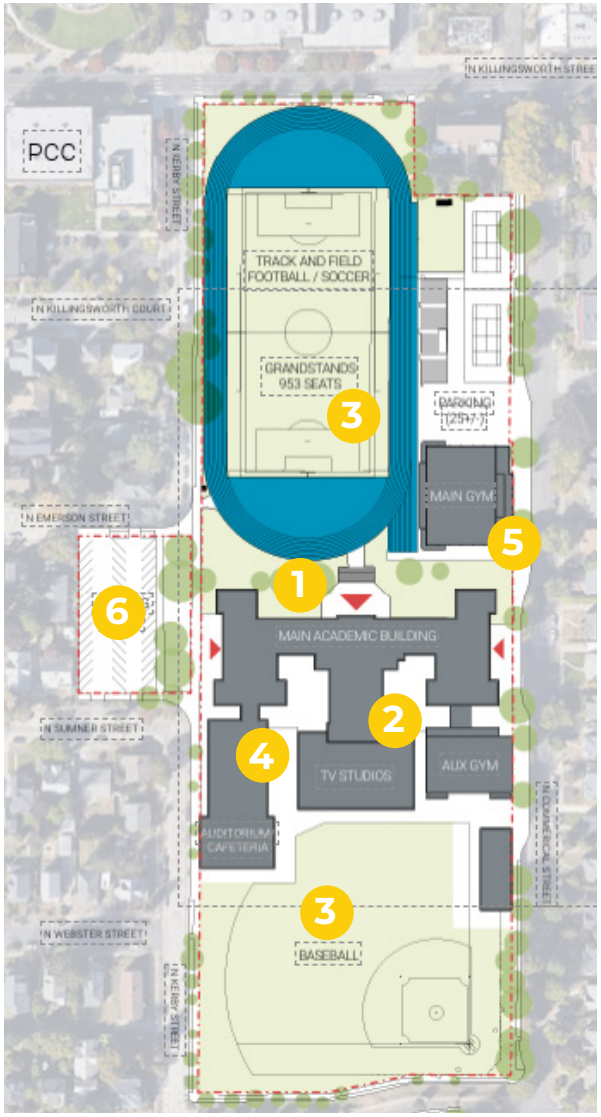

Existing Site Plan

The image shown was originally produced by BORA Architects and showcased in the Jefferson High School Conceptual Master Plan Report prepared in January of 2020, and can be found on the Portland Public Schools website (pps.net).

CURRENT CAMPUS PHOTOS

Original entrance to the building

Existing cafeteria

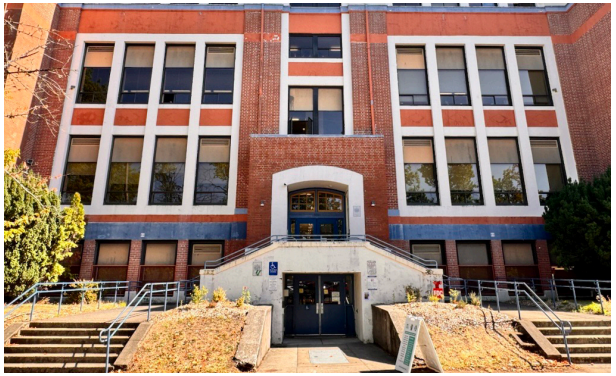

Current entrance to the JHS building by Kerby Ave.



Existing detached gym



Existing main corridor

Existing main corridor

JEFFERSON HIGH SCHOOL OPTIONS

DESIGN, PERMIT, & CONSTRUCTION SCHEDULE COMPARISON

Per our directive from the Superintendent, we were tasked with looking at ways to expedite moving students into the modernized building sooner. The alternative strategies prioritize students by providing earlier access to new learning spaces and athletic facilities. Ultimately, the decision requires weighing the value of earlier access and reduced escalation against the complexity, safety, and community concerns inherent in each alternative. Options such as Swing, Portable Village, or Shell shorten timelines by a year or more, ensuring that Jefferson students benefit from modernized classrooms and programs much sooner. The Superintendent and the community are eager to see real improvements, these proposed options offer a pathway to student-centered choices.

CURRENT PLAN

PROS

New softball and baseball fields to be completed and available first by the beginning of 2027.

Phased delivery reduces risk exposure – breaking work into smaller packages (fields, foundations, building, site) allows issues to be identified and resolved without holding up the entire project.

Early activation of fields – students/community gain access to athletic facilities years before the main building and final site work are completed.

Logical sequencing – foundational work, building, and final demo/site work are staged to minimize overlap and avoid heavy conflicts on campus.

Extended design windows – longer design durations reduce the chance of rushed drawings, errors, or major change orders.

CONS

Very long total duration – the overall program stretches from now to 2030, meaning full completion takes 5+ years from now.

Late delivery of final site/fields – final demo and field work aren't usable until near the end of the decade, leaving partial facilities for an extended period.

High exposure to inflation/escalation – long timeline increases the likelihood of cost overruns due to labor and materials price increases.

Permit dependencies at multiple phases – permitting is required three separate times (for A, B, and C/Phase 2), each creating a potential delay.

Multiple utility coordination points – repeating utility and easement challenges across phases can create bottlenecks.

Extended community/student impact – site remains under construction for years, potentially affecting usability, safety, and perception.

BOARD APPROVED ON OCTOBER 14, 2025

STUDENT MOVE-IN DATE

AUGUST 2029

CURRENT DESIGN STRATEGY

The current plan ensures that students will remain on-site during construction while accommodating up to 1,700 students. The main building will stay on the north side of the property with its primary entrance on Kerby. Athletic fields will remain as designed, with the gym located next to them along Commercial. The plan also activates the Killingsworth building with a new Fine Arts Hall, and provides a required cross-block connection.

Estimated Construction Budget: $355,153,892.75

Estimated All-In Budget: $466,007,500

PROPOSED SCHEDULE

PHASE 1A | SPRING 2026 - WINTER 2026

Construction on new softball field, new baseball field, and new soccer practice field.

PHASE 1B | WINTER 2026 - SPRING 2029

Construction on the new Jefferson High School.

PHASE 1C | SPRING 2029 - FALL 2030

Abatement and demolition to the existing Jefferson High School.

PHASE 2 | FALL 2029 - WINTER 2030

Construction on new track.

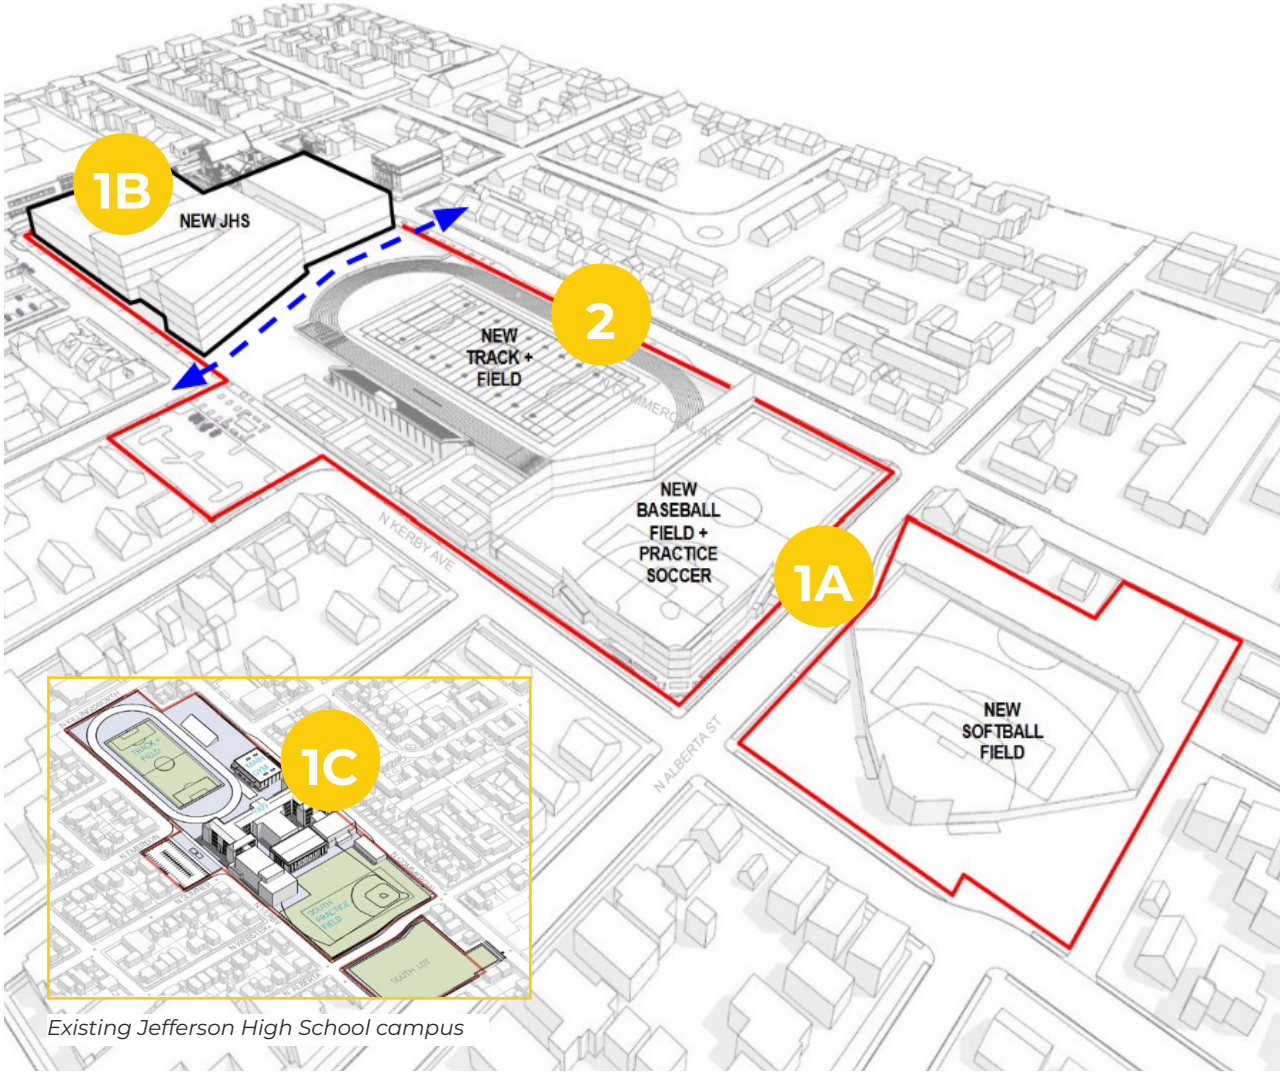

Existing Jefferson High School campus

The image shown was originally produced by BORA Architects, and showcased in the Jefferson High School Modernization Community Information Session held on August 20, 2025, and can be found on the Portland Public Schools website (pps.net).

CURRENT PLAN

Activity ID	Activity Name	Months	Orig Dur	Rem Dur	Start	Finish
Jefferson High School - Current Plan						
Set A - Early Fields - Phase 1A						
A1470	Set A - Early Fields Design	9 Months	275	99	01-Apr-25 A	31-Dec-25
A1340	Set A - Permits Early Fields	4 Months	120	120	01-Jan-26	30-Apr-26
A1370	Set A - Early Fields Construction	7 Months	214	214	01-May-26	30-Nov-26
Set B - Foundation to Grade - Phase 1B						
A1540	Set B - Foundation to Grade Design	9 Months	181	181	01-Nov-25*	30-Apr-26
A1550	Set B - Permits	4 Months	123	123	01-May-26	31-Aug-26
A1560	Set B - Construct New Building Foundations & Utilities	4 Months	121	121	01-Dec-26	31-Mar-27
Set C - New Building - Phase 1C						
A1570	Set C - New Building Design	19 Months	487	311	01-Apr-25 A	31-Jul-26
A1580	Set C - Permits	5 Months	153	153	01-Aug-26	31-Dec-26
A1590	Set C - Construct New Building	25 Months	761	761	01-Apr-27	30-Apr-29
Phase 2 Demo / Site / Remaining Fields						
A1490	Phase 2 - Design Documents	19 Months	487	311	01-Apr-25 A	31-Jul-26
A1500	Phase 2 - Permits	5 Months	153	153	01-Aug-26	31-Dec-26
A1450	Phase 2 - Demo / Site / Remaining Fields	12 Months	365	365	15-Aug-29*	14-Aug-30
Close-Out						
A1400	Substantial Completion		0	0		30-Apr-29
A1410	OTIS Installation	3 Months	92	92	01-May-29	31-Jul-29
A1420	FF&E Installation	3 Months	92	92	01-May-29	31-Jul-29
A1430	Move In	1 Month	31	31	01-Aug-29	31-Aug-29
A1440	School Opens		0	0		31-Aug-29*
A1460	JHS Complete		0	0		15-Aug-30

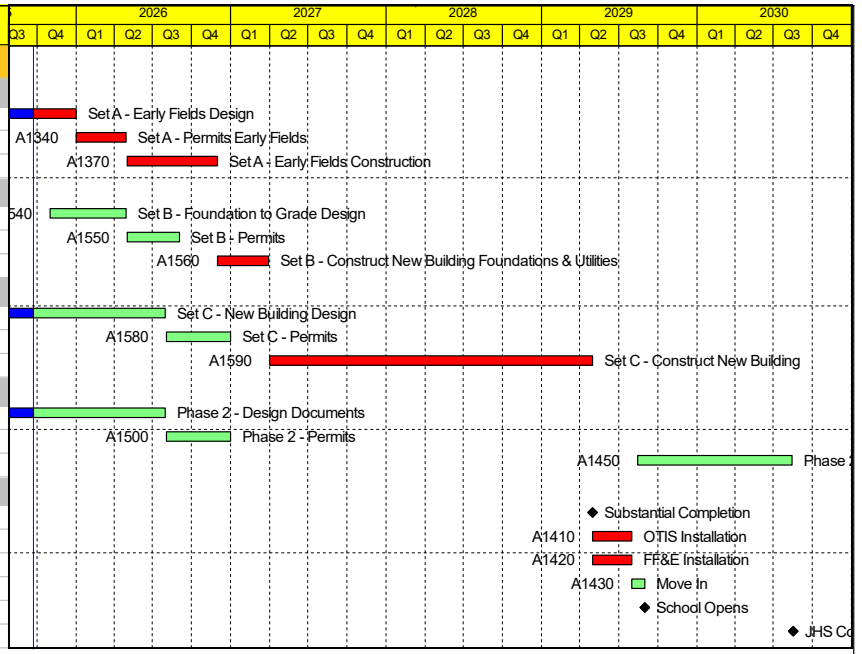

Start Date	01-Apr-25
Finish Date	31-Jan-29
Data Date	24-Sep-25
Run Date	30-Sep-25

Remaining Level of Effort · Critical R...
Actual Level of Effort · Milestone
Previous Baseline
Actual Work
Remaining Work

JHS Options — 1 of 1

Procedeo
Jefferson High School
Current Plan
