# Bond Accountability Committee Update
# Q2 April 29, 2026



PORTLAND
Public Schools

April 29, 2026

# Agenda

| | |
|---|---|
| • Call to Order, Welcome, and Introductions | 5:30pm |
| • Public Comments | 5:40pm |
| • Seismic Update | 5:50pm |
| • Financial Update | 6:10pm |
| • Consolidated Project Updates | 6:40pm |
| • ERP Update | 7:00pm |
| • Charter Update Conclusion | 7:10pm |
| • BAC General Discussion, Updates, and Votes | 7:15pm |
| • Adjourn | 7:30pm |

# Introductions

**Greg DiLoreto,** BAC Committee Chair

**Cara Turano,** BAC Committee Member

**Norm Dowty,** BAC Committee Member

**Ryan Kinsella,** BAC Committee Member

**Jonathan Truitt,** BAC Committee Member

**Chris Dunning,** BAC Committee Member

**Travis George,** BAC Committee Member

**Kelly Wingard,** BAC Committee Member

**Brian Harper,** BAC Committee Member

**Chris Poulsen,** BAC Committee Member

**Director Christy Splitt,** BOE Liaison to the BAC

**Sarah Norman,** Executive Director, RISE, PROCEDEO

**TJ Hopkins,** Senior Director, RISE, PROCEDEO

**Joanna Evenson,** Senior Director, RISE, PPS

**Michelle Morrison,** CFO, PPS

**Maya Litauer Chan,** Financial Operations Manager, PPS

**Jennifer Eggers,** Principal, Holmes

**Eddie Richter,** Project Engineer, Holmes

**Russell Adamson,** Senior Director of IT, PPS

*Presenters will introduce themselves at the time of their presentation.*

# Public Comment

(5:40 pm)

# Seismic Update
(5:50 pm)

# Bond Program Financial Update

(6:10 pm)

# All Bond Programs Dashboard – As of 4/1/26

## PORTLAND PUBLIC SCHOOLS

**Bond Program Dashboard**


| Data Source | Report Name | Date Exported |
|---|---|---|
| eBuilder | 0-PIVOT TABLE - FUNDING - SLS 04.01.2026 06 04 13 AM.xls | 4/1/2026 8:16:5 |
| eBuilder | BAC Data Project Management Cost 04.01.2026 06 30 28 AM.xls | 4/1/2026 8:16:5 |
| eBuilder | BAC Report Dashboard - Copy.pbix | 4/1/2026 10:56: |
| eBuilder | BAC Report Dashboard.pbix | 4/1/2026 8:14:3 |

Bond Measure


Deselect all | 2012 Bond | 2017 Bond | 2020 Bond | 2025 Bond

| Total Funds | Spent to Date | Outstd. Encumbrance | Available Funds | Percent Available |
|---|---|---|---|---|
| 4.7bn | 2.1bn | 182.6M | 2.3bn | 50% |

### Spent to Date and Total Funds

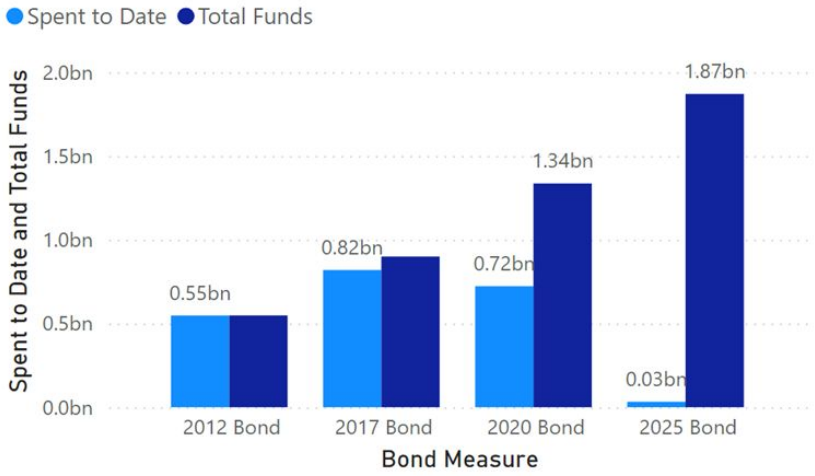


### Spent and Encumbered

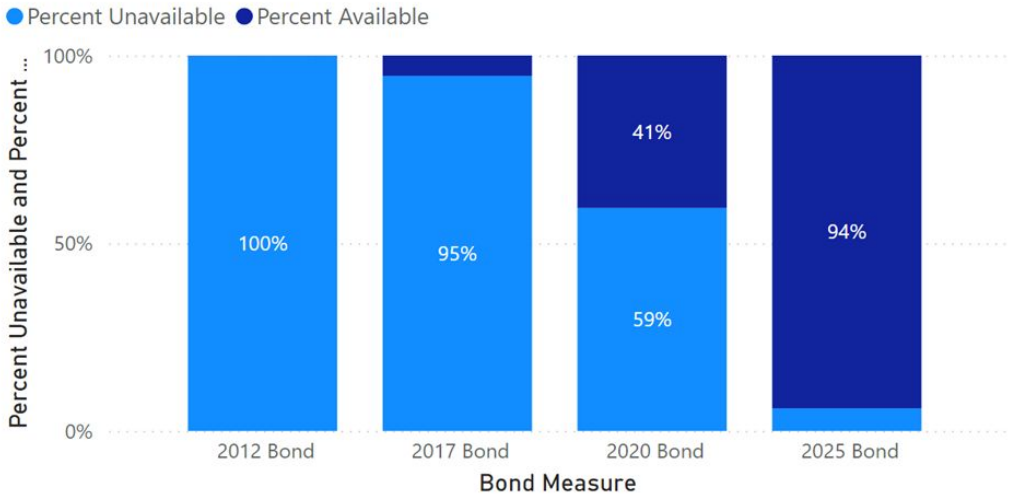

# 2012 Bond Program Dashboard – As of 4/1/26

**PORTLAND PUBLIC SCHOOLS**


**Bond Program Dashboard**


| Data Source | Report Name | Date Exported |
|---|---|---|
| eBuilder | 0-PIVOT TABLE - FUNDING - SLS 04.01.2026 06 04 13 AM.xls | 4/1/2026 8:16:5 |
| eBuilder | BAC Data Project Management Cost 04.01.2026 06 30 28 AM.xls | 4/1/2026 8:16:5 |
| eBuilder | BAC Report Dashboard - Copy.pbix | 4/1/2026 10:56: |
| eBuilder | BAC Report Dashboard.pbix | 4/1/2026 8:14:3 |

Bond Measure

Select all | **2012 Bond** | 2017 Bond | 2020 Bond | 2025 Bond

| Total Funds | Spent to Date | Outstd. Encumbrance | Available Funds | Percent Available |
|---|---|---|---|---|
| 547.8M | 547.4M | 51.0K | 379.4K | 0% |

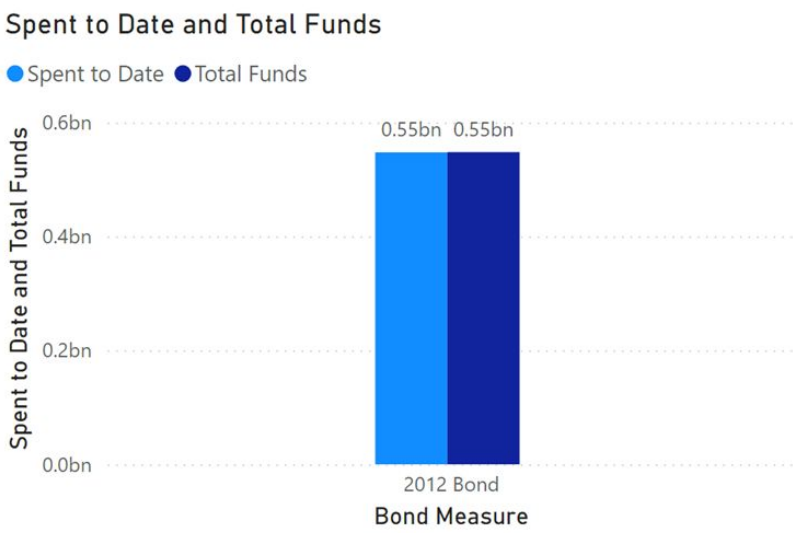
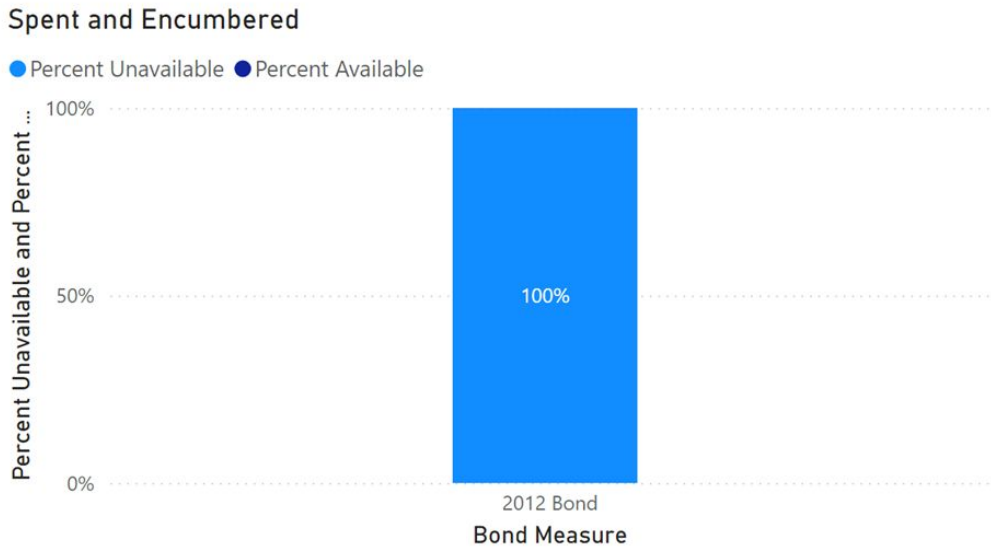
# 2012 Program Financial Status 4/1/2026

| | FUNDING | PROGRESS | | | | | |
|---|---|---|---|---|---|---|---|
| **2012 PROGRAM** | Bond Funds | Actuals To Date | Bond Funds less Actuals to Date | Additional Encumbered | Available (Unspent & Unencumbered) | Forecast From Cash Flow | Variance From Cash Flow |
| Franklin HS Mod | 110,950,414 | 110,950,414 | | - | - | | |
| Grant HS Mod | 155,300,188 | 155,300,188 | | - | - | | |
| Roosevelt HS Mod | 97,128,043 | 97,128,043 | | - | - | | |
| Faubion Replace | 30,653,663 | 30,653,663 | | - | - | | |
| Grant Upper Field | 3,170,988 | 3,170,988 | | - | - | | |
| RHS Phase IV | 6,153,741 | 6,153,741 | | - | - | | |
| Other Projects | 112,710,428 | 112,710,428 | | 0 | (0) | | |
| Grant & Franklin add ons (Active) | 226,663 | 51,279 | 175,384 | 50,989 | 124,395 | 97,594 | (77,791) |
| | | | | *2012 Project Subtotals* | | | |
| Administration | 31,284,018 | 31,284,018 | | - | - | | |
| Contingency | 254,104 | (902) | | - | 255,006 | | |
| | | | | *2012 Program Subtotals* | | | |
| ***Totals*** | *547,832,249* | *547,401,858* | | *50,989* | *379,401* | *97,594* | *(77,791)* |

| Bond Funds | Bond Actuals |
|---|---|
| *547,832,249* | *547,401,858* |

**Modernizations:** Franklin HS, Grant HS, Roosevelt HS, and Faubion PK-8

**Middle School Science Upgrades**

**Consolidated Projects:** Accessibility, Seismic

# 2017 Bond Program Dashboard – As of 4/1/26

## PORTLAND PUBLIC SCHOOLS


**Bond Program Dashboard**


| Data Source | Report Name | Date Exported |
|---|---|---|
| eBuilder | 0-PIVOT TABLE - FUNDING - SLS 04.01.2026 06 04 13 AM.xls | 4/1/2026 8:16:5 |
| eBuilder | BAC Data Project Management Cost 04.01.2026 06 30 28 AM.xls | 4/1/2026 8:16:5 |
| eBuilder | BAC Report Dashboard - Copy.pbix | 4/1/2026 10:56: |
| eBuilder | BAC Report Dashboard.pbix | 4/1/2026 8:14:3 |

Bond Measure

Select all | 2012 Bond | **2017 Bond** | 2020 Bond | 2025 Bond

| Total Funds | Spent to Date | Outstd. Encumbrance | Available Funds | Percent Available |
|---|---|---|---|---|
| 899.5M | 818.9M | 32.0M | 48.6M | 5% |

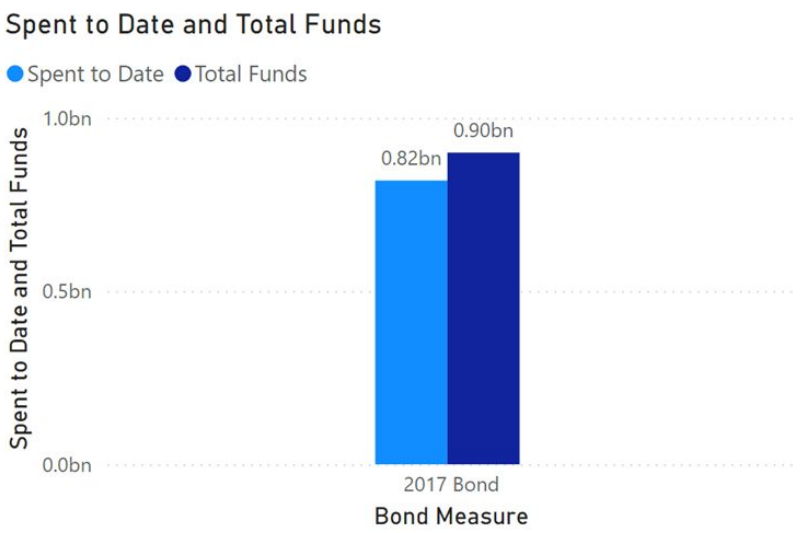
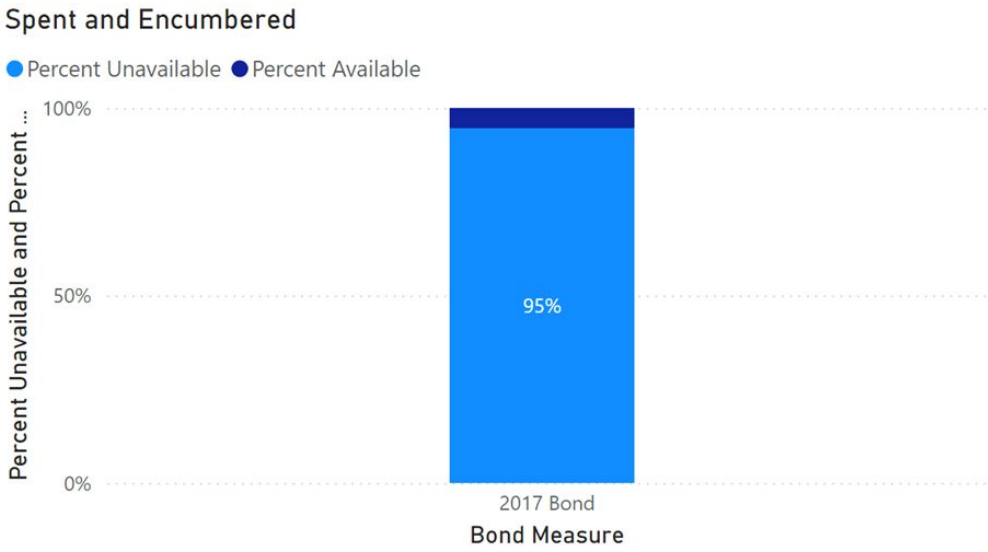
# 2017 Program Financial Status 4/1/2026

| | FUNDING | PROGRESS | | | | | |
|---|---|---|---|---|---|---|---|
| 2017 PROGRAM | Bond Funds | Actuals To Date | Bond Funds less Actuals to Date | Additional Encumbered | Available (Unspent & Unencumbered) | Forecast From Cash Flow | Over/Under From Cash Flow |
| | | | | | | | |
| Benson HS Mod | 146,614,560 | 143,349,657 | 3,264,903 | 140,366.39 | 3,124,536.22 | 3,264,902.61 | - |
| Benson Add Ons | 2,865,020 | 55,715 | 2,809,305 | 1,397,235.90 | 1,412,069.42 | 2,484,305.32 | (325,000) |
| Benson Swings | 12,199,595 | 12,199,595 | - | 0.00 | (0.00) | - | - |
| Lincoln HS Repl | 240,836,448 | 224,096,580 | 16,739,868 | 5,976,291.93 | 10,763,575.81 | - | (16,739,868) |
| Kellogg MS Replace | 57,648,703 | 57,648,703 | - | - | - | - | - |
| McDaniel Mod | 197,000,000 | 196,810,549 | 189,451 | 16,713.50 | 172,737.52 | 189,954.52 | 504 |
| Health & Safety | 165,195,907 | 121,858,490 | 43,337,417 | 23,795,454 | 19,541,963.22 | 41,318,419.12 | (2,018,998) |
| Athletics | 4,895,489 | 2,278,729 | 2,616,760 | 174,034 | 2,442,725.72 | - | (2,616,760) |
| | | | | *2017 Project Subtotals* | | | |
| Administration | 67,862,160 | 60,618,998 | 7,243,162 | 457,995 | 6,785,166.35 | 371,892.80 | (96,510) |
| Contingency | 2,502,859 | - | 2,502,859 | - | 2,502,859.12 | - | (2,502,859) |
| Unallocated H&S | 1,738,723 | - | 1,738,723 | - | 1,738,722.54 | - | - |
| Unalloc Athletics | 104,511 | - | | - | 104,510.84 | | |
| | | | | *2017 Program Subtotals* | | | |
| ***Totals*** | *899,463,975* | *818,917,017* | | *31,958,091* | *48,588,867* | *47,629,474* | *(24,299,491)* |
| | *899,463,975* | Bond Actuals: | | | | | |
| | - | *818,917,017* | | - | | | |

**Modernizations:** Benson Polytechnic, Lincoln, McDaniel, Kellogg Middle School and Multiple Pathways to Graduation

**Consolidated Projects:** Water Quality, Security Upgrades, New Roofs, Asbestos Abatement, Radon Remediation, Lead Paint Stabilization, Life Safety Upgrades, Accessibility, Seismic

# 2017 Consolidated Program Financial Status 4/1/2026

| | FUNDING | PROGRESS | | | | | |
|---|---|---|---|---|---|---|---|
| **2017 HEALTH & SAFETY** | Bond Funds | Actuals To Date | Bond Funds less Actuals to Date | Additional Encumbered | Available (Unspent & Unencumbered) | Forecast From Cash Flow | Over/Under From Cash Flow |
| 2017 ADA | 12,855 | 12,855 | - | - | - | - | - |
| 2017 Asbestos | 13,046,800 | 9,934,749 | 3,112,051 | 162,127.04 | 2,949,924.41 | 2,589,143.82 | (522,908) |
| 2017 Consolidated | 105,976,767 | 75,956,092 | 30,020,675 | 22,542,719.78 | 7,477,954.76 | 29,731,727.41 | (288,947) |
| 2017 Fire | 21,568,613 | 12,390,824 | 9,177,789 | 978,997.71 | 8,198,791.38 | 8,975,547.89 | (202,241) |
| 2017 Lead Paint | 5,209,118 | 4,990,797 | 218,321 | 11,909.19 | 206,412.24 | - | (218,321) |
| 2017 Radon | 514,221 | 192,471 | 321,750 | 99,700.00 | 222,050.00 | 22,000.00 | (299,750) |
| 2017 Security | 7,856,961 | 7,856,961 | - | - | - | - | - |
| 2017 Water Quality | 11,010,572 | 10,523,742 | 486,830 | - | 486,830.43 | - | (486,830) |
| ***Totals*** | *165,195,907* | *121,858,490* | *43,337,417* | *23,795,454* | *19,541,963* | *41,318,419* | *(2,018,998)* |

# 2020 Bond Program Dashboard – As of 4/1/26

**PORTLAND PUBLIC SCHOOLS**


**Bond Program Dashboard**


| Data Source | Report Name | Date Exported |
|---|---|---|
| eBuilder | 0-PIVOT TABLE - FUNDING - SLS 04.01.2026 06 04 13 AM.xls | 4/1/2026 8:16:5 |
| eBuilder | BAC Data Project Management Cost 04.01.2026 06 30 28 AM.xls | 4/1/2026 8:16:5 |
| eBuilder | BAC Report Dashboard - Copy.pbix | 4/1/2026 10:56: |
| eBuilder | BAC Report Dashboard.pbix | 4/1/2026 8:14:3 |

Bond Measure

Select all | 2012 Bond | 2017 Bond | **2020 Bond** | 2025 Bond

| Total Funds | Spent to Date | Outstd. Encumbrance | Available Funds | Percent Available |
|---|---|---|---|---|
| 1.3bn | 722.3M | 70.6M | 542.5M | 41% |

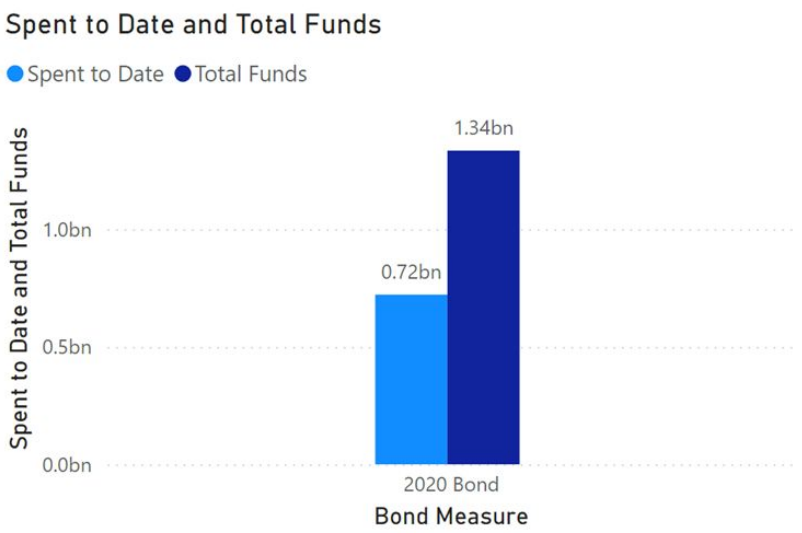
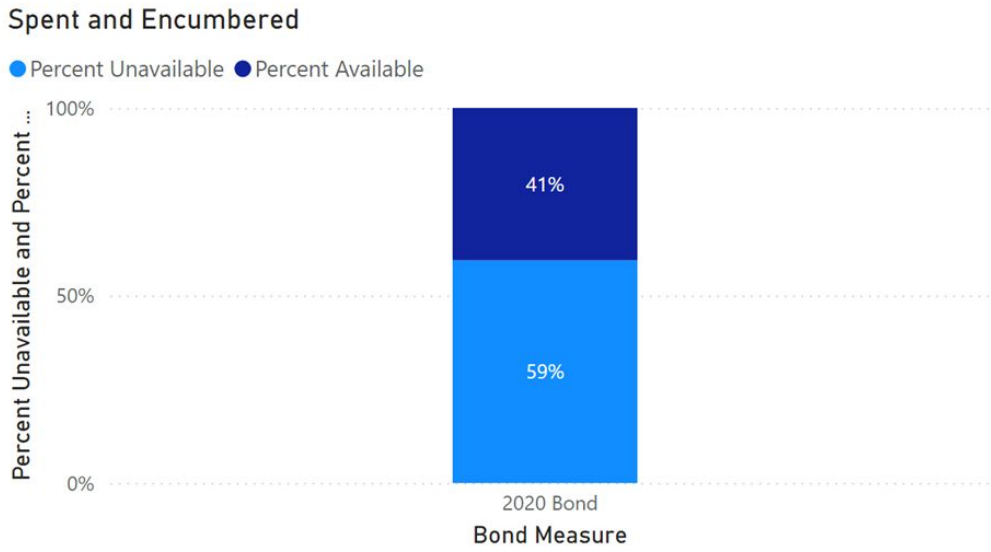
# 2020 Program Financial Status 4/1/2026

| | FUNDING | PROGRESS | | | | | |
|---|---|---|---|---|---|---|---|
| 2020 PROGRAM | Bond Funds (incl. unissued) | Actuals To Date | Bond Funds less Actuals to Date | Additional Encumbered | Available (Unspent & Unencumbered) | Forecast From Cash Flow | Over/Under From Cash Flow |
| Benson 2020 funds | 164,903,890 | 162,293,196 | 2,610,694 | 1,149,080 | 1,461,615 | 2,610,694 | - |
| Jefferson HS Mod | 366,007,500 | 28,208,577 | 337,798,923 | 17,872,208 | 319,926,715 | 337,798,923 | - |
| Jefferson Add Ons | 152,175 | 250 | 151,925 | 149,945 | 1,980 | 151,925 | - |
| CEE | 60,000,000 | 16,222,680 | 43,777,320 | 1,700 | 43,775,620 | 42,959,120 | (818,200) |
| Cleveland HS Design | 25,784,000 | 14,306,646 | 11,477,354 | 10,144,359 | 1,332,995 | 12,089,465 | 612,111 |
| Cleveland Swing Site | 137,500 | 100,155 | 37,345 | 7,300 | 30,045 | 37,345 | - |
| Wells HS Design | 25,318,534 | 16,721,527 | 8,597,007 | 2,883,043 | 5,713,964 | 8,597,007 | - |
| Roosevelt PhV Design | 2,000,000 | 97,625 | 1,902,375 | 1,035 | 1,901,340 | - | (1,902,375) |
| MPG Building | 80,447,075 | 77,947,593 | 2,499,482 | 265,462 | 2,234,021 | - | (2,499,482) |
| Curriculum | 63,319,191 | 54,462,003 | 8,857,188 | 865,342 | 7,991,846 | 4,295,388 | (4,561,800) |
| Technology | 136,100,000 | 86,405,942 | 49,694,058 | 21,093,525 | 28,600,533 | 46,446,187 | (3,247,872) |
| Infra Projects | 260,913,415 | 231,973,916 | 28,939,499 | 14,589,956 | 14,349,543 | 18,320,799 | (10,618,700) |
| | | | | *2020 Project Subtotals* | | | |
| Administration | 64,666,987 | 33,613,864 | 31,053,123 | 1,608,738 | 29,444,385 | 18,648,243 | (85,277,106) |
| 2017 Bond Balance | - | - | | - | - | | |
| Contingency - OSM | 72,872,226 | - | | - | 72,872,226 | | |
| Unalloc Proj Funds | 12,852,629 | - | | - | 12,852,629 | | |
| | | | | *2020 Project Subtotals* | | | |
| ***Totals*** | *1,335,475,122* | *722,353,971* | | *70,631,693* | *542,489,457* | *491,955,097* | *(108,313,425)* |
| | | Bond Actuals: | | | | | |
| | *1,335,467,622* | *722,353,971* | | - | | | |
| | *1,335,467,622* | | | | | | |
| | 7,500 | *Difference between sum of projects and 2020 Bond/458,459,460 fund sums caused by ETO Funding (U0228) | | | | | |

**Modernizations:** Jefferson HS, Pre-Planning/Design Ida B Wells and Cleveland HS, The Center of Black Excellence, Roosevelt (added capacity), and Benson

**Consolidated Projects:** Curriculum Materials, New Technology for classroom and distance learning, Health & Safety, Seismic, Security, Re-Roofing

# 2020 Consolidated Program Financial Status 4/1/2026

| | FUNDING | PROGRESS | | | | | |
|---|---|---|---|---|---|---|---|
| **2020 INFRA PROJECTS** | Bond Funds | Actuals To Date | Bond Funds less Actuals to Date | Additional Encumbered | Available (Unspent & Unencumbered) | Forecast From Cash Flow | Over/Under From Cash Flow |
| 2020 Capacity | 48,086,590 | 45,459,926 | 2,626,664 | 1,044,679.10 | 1,581,985.04 | (61,916.00) | (2,688,580) |
| 2020 Seismic | 17,199,982 | 12,567,699 | 4,632,283 | 1,170,775.02 | 3,461,507.70 | 4,475,992.12 | (156,291) |
| 2020 Roofing | 63,027,250 | 63,001,985 | 25,265 | 7,830.00 | 17,435.00 | - | (25,265) |
| 2020 Mechanical | 61,564,344 | 45,603,756 | 15,960,588 | 12,099,854.82 | 3,860,733.15 | 13,720,148.83 | (2,240,439) |
| 2020 ADA | 44,897,229 | 44,134,018 | 763,210 | 19,886.42 | 743,323.85 | 61,696.05 | (701,514) |
| 2020 SPED | 4,478,497 | 4,297,864 | 180,633 | 47,465.25 | 133,167.55 | - | (180,633) |
| 2020 Security | 21,659,524 | 16,908,668 | 4,750,856 | 199,465.45 | 4,551,390.88 | 124,878.08 | (4,625,978) |
| ***Totals*** | *260,913,415* | *231,973,916* | *28,939,499* | *14,589,956* | *14,349,543* | *18,320,799* | *(10,618,700)* |

# 2025 Bond Program Dashboard – As of 4/1/26

**PORTLAND PUBLIC SCHOOLS**


**Bond Program Dashboard**


| Data Source | Report Name | Date Exported |
|---|---|---|
| eBuilder | 0-PIVOT TABLE - FUNDING - SLS 04.01.2026 06 04 13 AM.xls | 4/1/2026 8:16:5 |
| eBuilder | BAC Data Project Management Cost 04.01.2026 06 30 28 AM.xls | 4/1/2026 8:16:5 |
| eBuilder | BAC Report Dashboard - Copy.pbix | 4/1/2026 10:56: |
| eBuilder | BAC Report Dashboard.pbix | 4/1/2026 8:14:3 |

Bond Measure

Select all | 2012 Bond | 2017 Bond | 2020 Bond | **2025 Bond**

| Total Funds | Spent to Date | Outstd. Encumbrance | Available Funds | Percent Available |
|---|---|---|---|---|
| 1.9bn | 32.6M | 80.0M | 1.8bn | 94% |

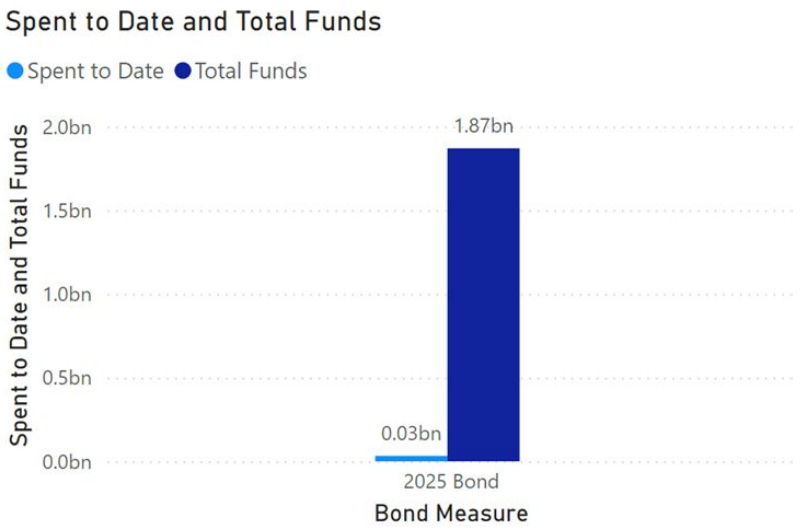
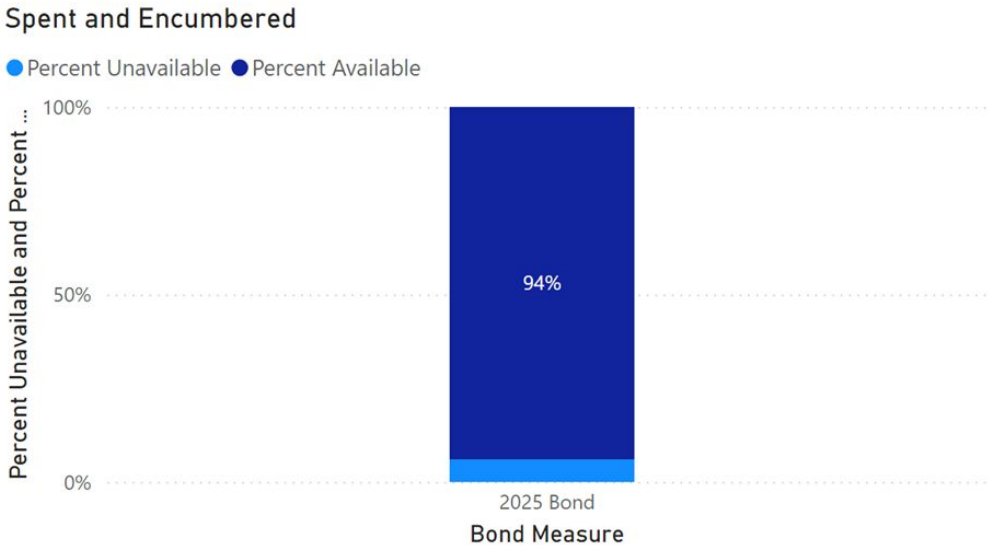
# 2025 Program Financial Status 4/1/2026

| | FUNDING | PROGRESS | | | | | |
|---|---|---|---|---|---|---|---|
| 2025 PROGRAM | Bond Funds (ind. unissued) | Actuals To Date | Bond Funds less Actuals to Date | Additional Encumbered | Available (Unspent & Unencumbered) | Forecast From Cash Flow | Variance From Cash Flow |
| | | | | | | | |
| Jefferson 2025 Funds | 100,000,000 | - | 100,000,000 | - | 100,000,000 | 99,944,129 | (55,871) |
| Cleveland HS Modernization | 447,699,868 | 99,568 | 447,600,300 | 9,815,079 | 437,785,221 | 445,962,149 | (1,638,151) |
| Wells HS Modernization | 432,000,000 | - | 432,000,000 | 487,900 | 431,512,100 | 432,000,000 | - |
| Curriculum | 56,000,000 | - | 56,000,000 | - | 56,000,000 | 56,416,685 | 416,685 |
| Technology | 176,000,000 | 26,118,260 | 149,881,740 | 3,916,460 | 145,965,280 | 150,629,082 | 747,342 |
| Athletics Projects | 20,111,069 | 568,958 | 19,542,111 | 2,721,847 | 16,820,264 | 1,235,157 | (18,306,955) |
| Seismic Projects | 3,947,382 | 73,113 | 3,874,269 | 3,310,227 | 564,042 | 3,906,443 | 32,174 |
| Priority Facilities | 110,000 | 73,113 | 36,887 | - | 36,887 | - | - |
| | | | | | | | |
| Administration | 83,050,000 | 5,691,791 | 77,358,209 | 59,732,226 | 17,625,983 | 78,899,360 | 1,541,151 |
| Contingency | 125,956,806 | - | | - | 125,956,806 | | |
| Unalloc Elementary & MS | 170,300,132 | - | 170,300,132 | - | 170,300,132 | - | (170,300,132) |
| Unalloc Priority Facilities | 89,890,000 | - | 89,890,000 | - | 89,890,000 | 85,000,000 | (4,890,000) |
| Unalloc Physical Education | 10,000,000 | - | 10,000,000 | - | 10,000,000 | 10,000,000 | - |
| Unalloc Athletics | 58,888,931 | - | 58,888,931 | - | 58,888,931 | 65,588,681 | 6,699,750 |
| Unalloc Seismic | 96,052,618 | - | 96,052,618 | - | 96,052,618 | 89,900,000 | (6,152,618) |
| | | | | | | | |
| ***Totals*** | *1,870,006,806* | *32,624,802* | | *79,983,739* | *1,757,398,264* | *1,519,481,685* | *(191,906,625)* |
| | | Bond Actuals: | | | | | |
| | *1,870,006,806* | *32,551,689* | | 73,113 | | | |
| | | *Added $43M in bond proceeds in March 2026. | | | | | |

**Modernizations:** Cleveland HS, Ida B Wells HS, and Jefferson

**Consolidated Projects:** Security Upgrades, Seismic, Technology, Improvements for Roosevelt, Lincoln, Franklin, and Grant, and New Athletic Hub Facilities at Jackson MS and Marshall Campuses

# **Consolidated Projects** (6:40 pm)

# Consolidated Projects - Seismic

**2026 Construction**

**Roofing with Seismic**

- Contractor bids complete and contracts executed for Summer 2026 work
  - Woodmere
  - Cesar Chavez
  - Marshall
  - Vestal

**Seismic Parts**

- Construction bids due May 7th
  - Vernon
  - Winterhaven
  - Marysville Ph 3

# Consolidated Projects - Seismic

**<u>Anticipated 2027 Construction</u>**

**Seismic Parts and Partial Roof**

- Richmond
  - Design Contract in final stages and anticipated to be in front of board on 4/28
- Capitol Hill
  - Design Contract in final stages and anticipated to be in front of board on 4/28
  - Anticipated Summer 2027 and 2028 construction

**Seismic Parts**

- Ainsworth and Kelly: Design Contracts anticipated to be in front of board in May

**Full Seismic**

- Beverly Cleary: Design in progress. Anticipated Summer ‘27-’28 construction

# Consolidated Projects - Seismic

**Anticipated 2028 and 2029 Construction**

**Seismic Parts and Partial Roof**

- Beach
  - Anticipated Summer 2028 construction

- Rose City Park
  - Full Seismic and roof
  - Contract expected to be before the Board in May 2026
  - Anticipated Summer 2028 and 2029 construction

# Consolidated Projects - Athletics

**Grant Bowl Lighting**

- Construction start April 15
- Directional boring for new electrical service across the road
- Light pole installation the week of April 20
- Electrical gear installation and connect in the first half of May

**Marshall Track/Field and Tennis Courts**

- Turf installation is complete; Track installation complete on April 25
- Tennis Court upgrade in progress and ahead of schedule

**Jackson Athletic Hub**

- Phase 0: Upper Field is nearing design completion with construction anticipated to start in June
- Phase 1: Multi-Use Field has completed SD Review

# Consolidated Projects - Curriculum

**Device Refresh**

- New computers for ALL PPS students
- 41,500 devices will be deployed
- Pilot deployments at six schools begins on April 20
- All schools will have newly deployed devices by the beginning of the 26-27 school year
- Ongoing deployment support during the beginning of school year

# Consolidated Projects – Mechanical, Health & Safety

**DDC Controls Upgrades – changing pneumatic systems to DDC**

- Allows better control of the systems resulting in more energy efficiency and better comfort control
- School group phases
  - Ph 1 – 9 schools – Complete
  - Ph 2A - 6 schools – Construction Complete
  - Ph 2B – 6 schools – In construction
  - Ph 2C – In design for Summer 2026 construction

**Fire Alarm Upgrades – upgrade fire alarm panels and devices**

- Projects out to bid with multiple campuses in each project
- Construction anticipated Summer 2026

# Consolidated Projects – Facility Improvements

**Complete**

- Wilcox HVAC System Replacement
- Marshall Water Main Replacement

**Summer 2026**

- Franklin Condenser Replacement – Anticipated
- Buckman
  - Cafeteria Truss Replacement, Dance Studio Truss Repairs, Caf. Flooring Replacement
- Boise Elliot – Repaint majority of school
- Capitol Hill – Flooring abatement, subfloor repairs, new flooring
- Jefferson – Stage rigging repairs
- Sitton – Truss repair/replacement
- Rose City Park – Boiler re-tubing
- Vestal – Built-in cafeteria table replacement

# Consolidated - Technology/ERP Update

# Charter Update
(7:10 pm)

# Draft Charter

# BAC General Discussion, Updates, and Votes

(7:15 pm)

# Votes

- Q1 Meeting Minutes

- Charter Discussion Meeting Minutes

# Adjourn

# Next Meeting:

TBD (July 2026)
(In-Person or Virtual – TBD)
