Bond Program Update



PORTLAND
Public Schools

April 28, 2026


Agenda

- Program Status Update
- Schedule Update
- Program Budget Update
- Project Updates

Program Status Update

2012 Bond Program Project Status

Total Projects	Pre-Planning	Design Phase	Construction	Post Construction	Completed
33	0	0	8	2	23

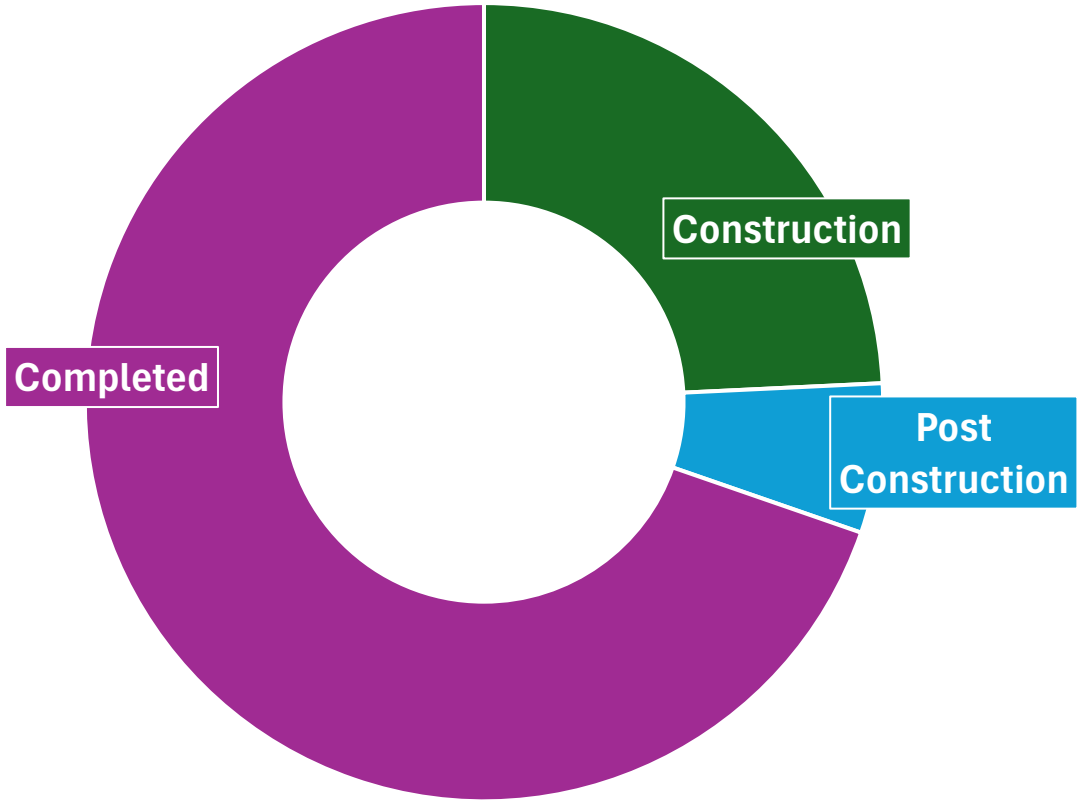


NOTE: source data: Ebuilder reports by bond measure, sorted by project status.

Audit of Project Completion and Closeout statuses is currently ongoing.

2017 Bond Program Project Status

Total Projects	Pre-Planning	Design Phase	Construction	Post Construction	Completed
175	0	0	48	17	110

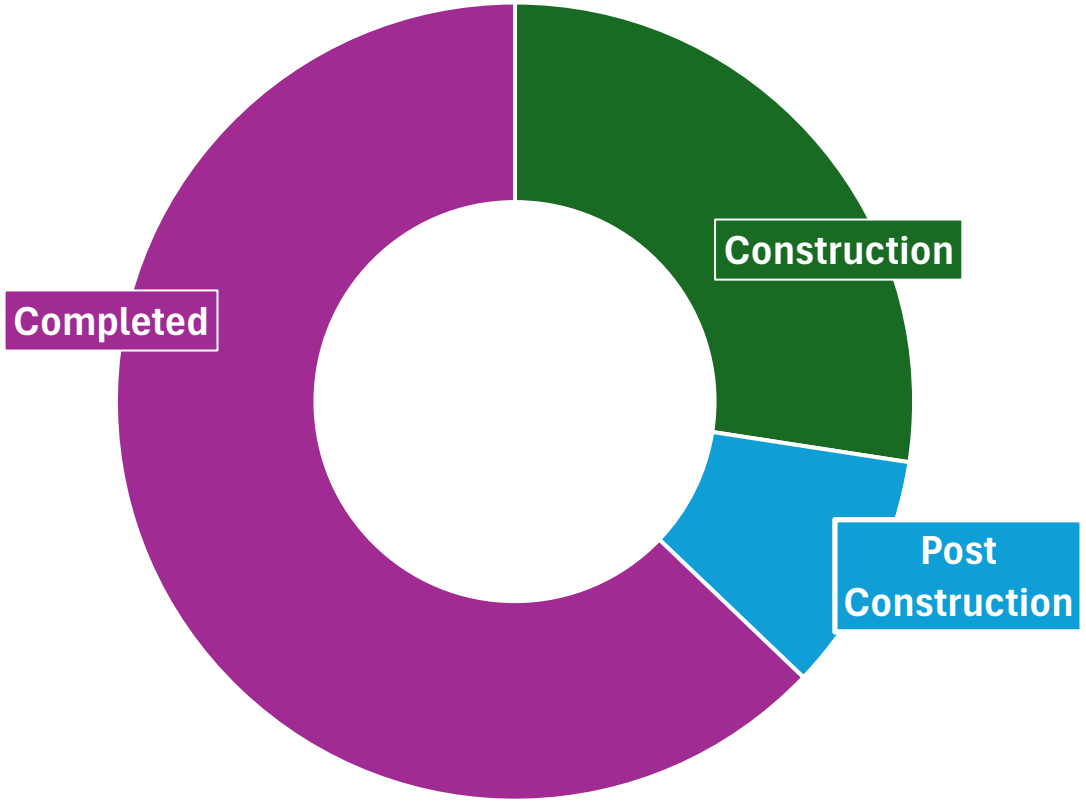


NOTE: source data: Ebuilder reports by bond measure, sorted by project status.

Audit of Project Completion and Closeout statuses is currently ongoing.

2020 Bond Program Project Status

Total Projects	Pre-Planning	Design Phase	Construction	Post Construction	Completed
103*	1	0	61	2	39

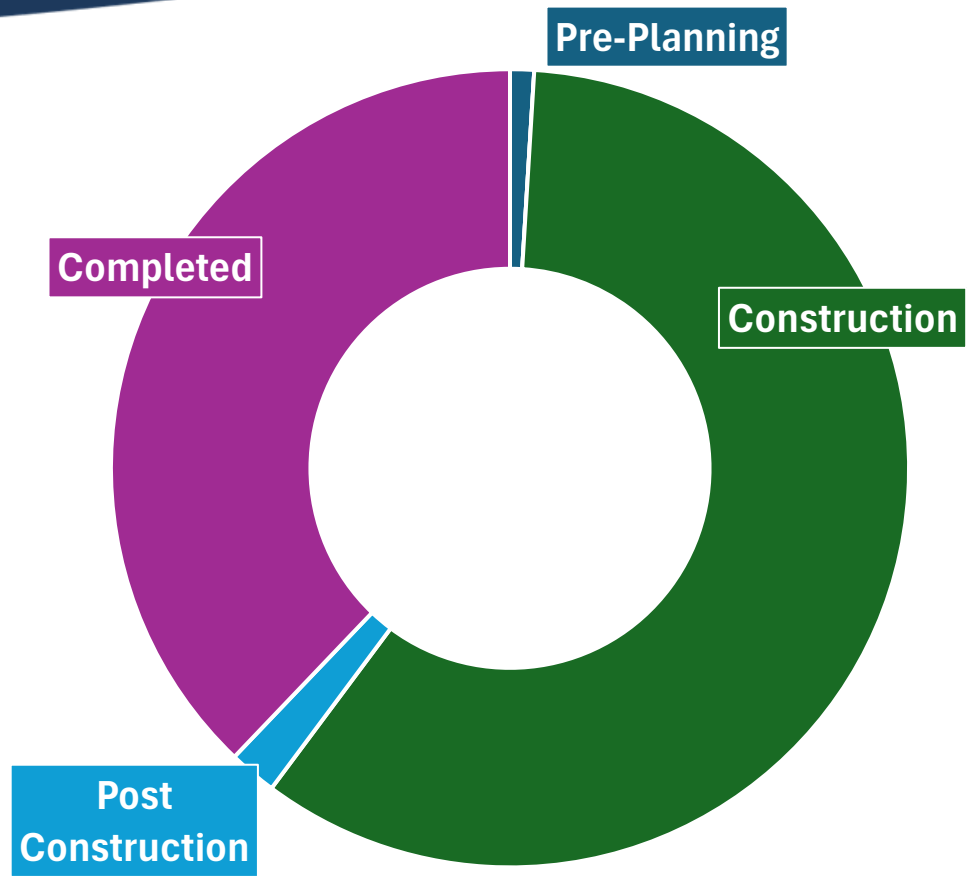


**Approximately $542 M remaining to be scheduled for 2020 Bond.*

NOTE: source data: Ebuilder reports by bond measure, sorted by project status.

Audit of Project Completion and Closeout statuses is currently ongoing.

2025 Bond Program Project Status


Total Projects	Pre-Planning	Design Phase	Construction	Post Construction	Completed
14*	9	5	0	0	0

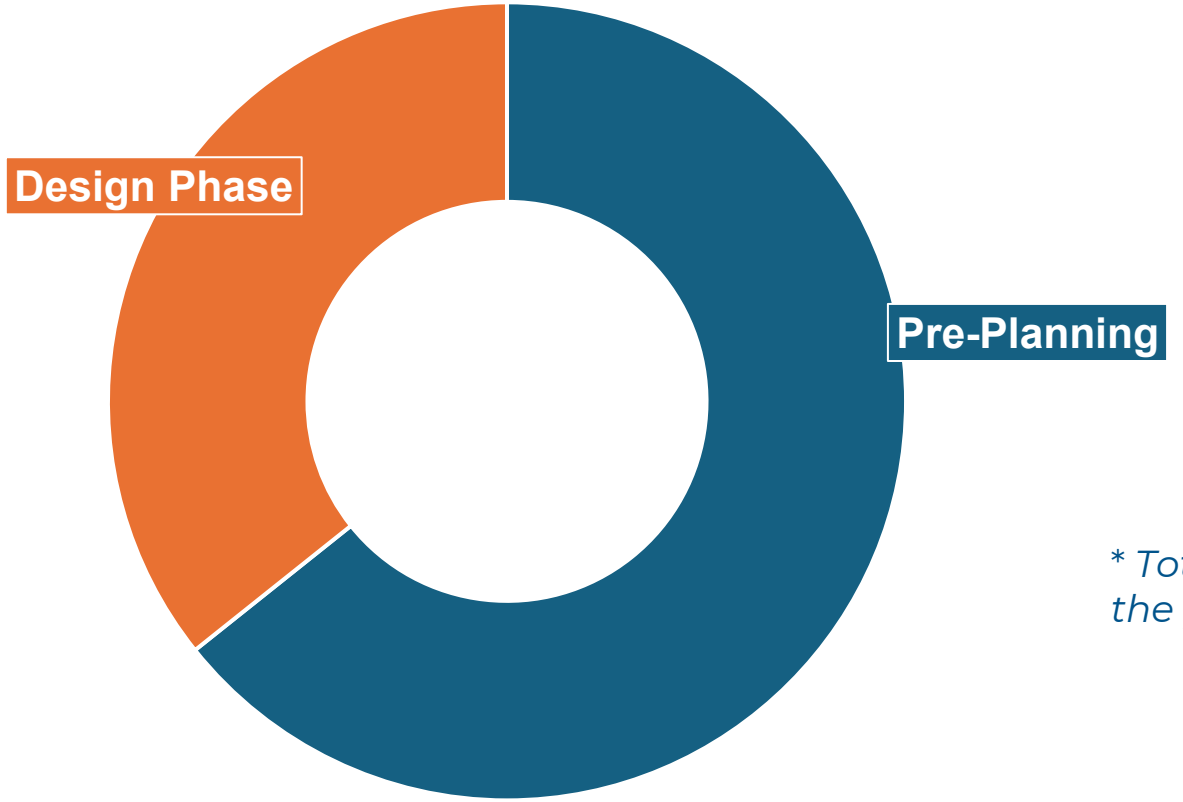

** Total projects will increase as the program progresses.*

Schedule and Budget Update

2025 Bond Schedule

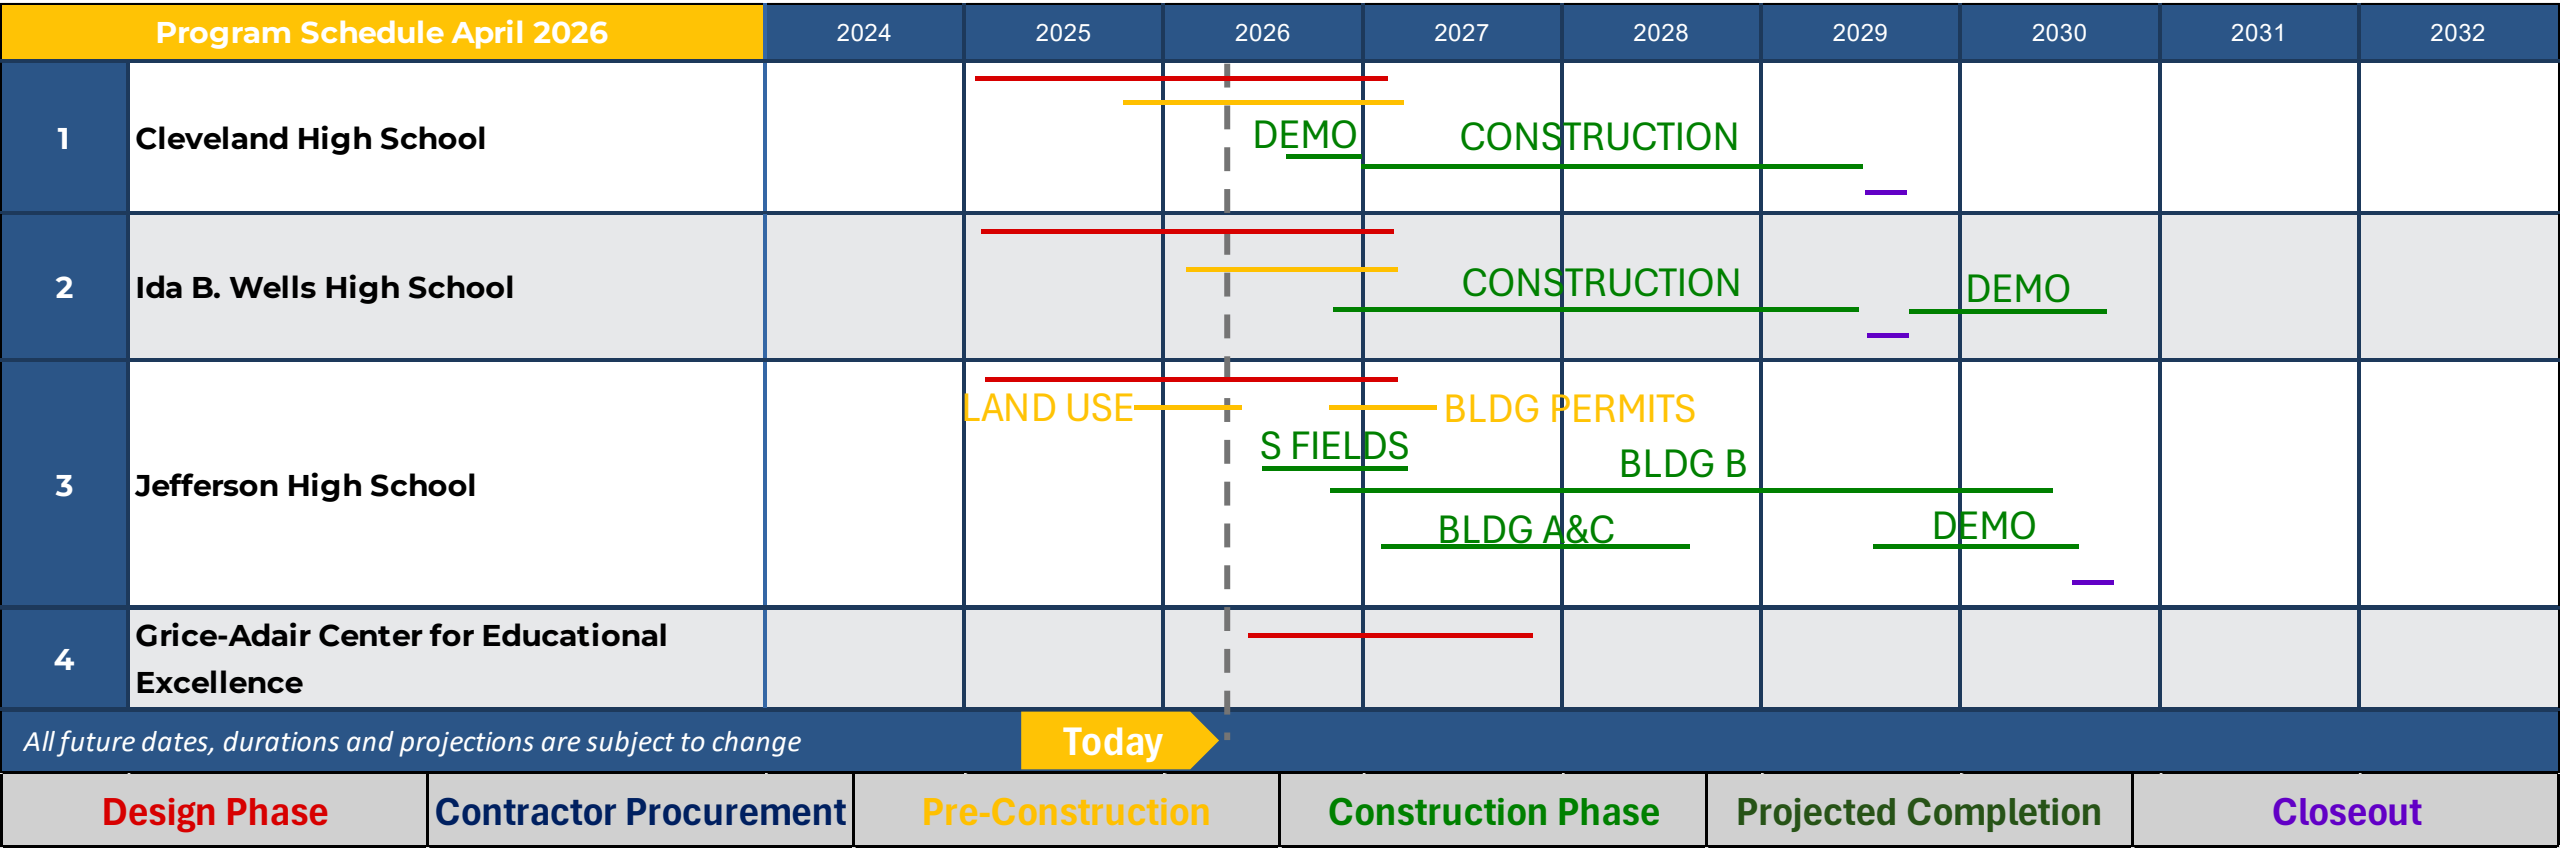

PORTLAND PUBLIC SCHOOLS

Bond Program Dashboard


Data Source	Report Name	Date Exported
eBuilder	0-PIVOT TABLE - FUNDING - SLS 04.01.2026 06 04 13 AM.xls	4/1/2026 8:16:5
eBuilder	BAC Data Project Management Cost 04.01.2026 06 30 28 AM.xls	4/1/2026 8:16:5
eBuilder	BAC Report Dashboard - Copy.pbix	4/1/2026 10:56:
eBuilder	BAC Report Dashboard.pbix	4/1/2026 8:14:3

Bond Measure


Deselect all | 2012 Bond | 2017 Bond | 2020 Bond | 2025 Bond

Total Funds	Spent to Date	Outstd. Encumbrance	Available Funds	Percent Available
4.7bn	2.1bn	182.6M	2.3bn	50%

Spent to Date and Total Funds

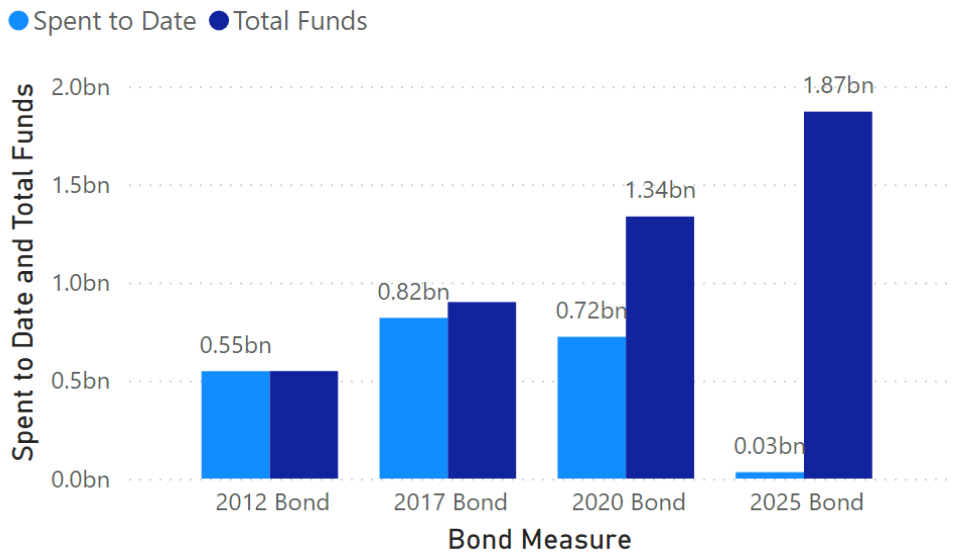


Spent and Encumbered

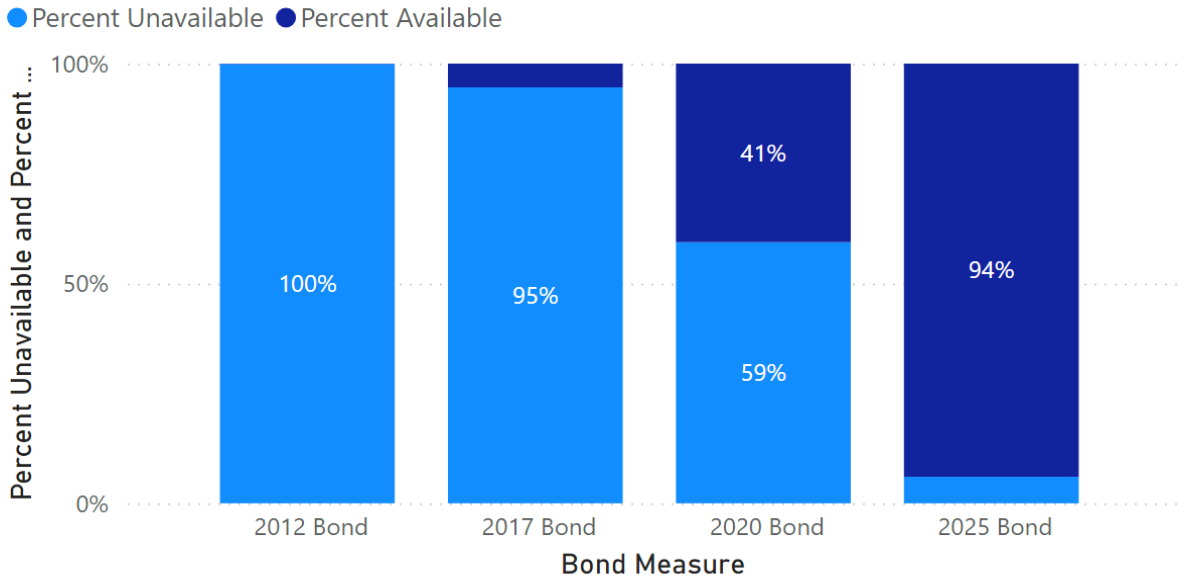

2012 Bond Program Status – Budget Update - Overview

Modernizations: Franklin HS, Grant HS, Roosevelt HS, and Faubion PK-8
Middle School Science Upgrades
Consolidated Projects: Accessibility, Seismic

Project	Budget	Outstanding Encumbrance	Amount Paid to Date	Remaining Balance
Franklin HS Mod	$110,950,414	$0	$110,950,414	$0
Grant HS Mod	$155,300,188	$0	$155,300,188	$0
Roosevelt HS Mod	$97,128,043	$0	$97,128,043	$0
Faubion Replace	$30,653,663	$0	$30,653,663	$0
Grant Upper Field	$3,170,988	$0	$3,170,988	$0
RHS Phase IV	$6,153,741	$0	$6,153,741	$0
Other Projects	$112,710,428	$0	$112,710,428	$0
Grant & Franklin Add Ons	$226,663	$50,989	$51,279	$124,395
Administration	$31,284,018	$0	$31,284,018	$0
Contingency	$254,104	$0	$902	$253,201
PPS 2012 Bond Program Total	**$547,832,249**	**$50,989**	**$547,403,663**	**$377,596**

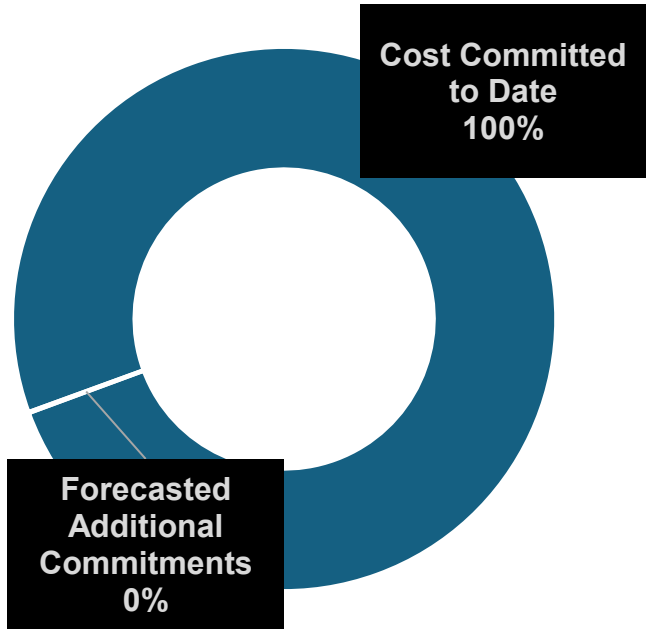


*as of 4/1/26

2017 Bond Program Status – Budget Update - Overview

Modernizations: Benson Polytechnic, Lincoln, McDaniel, Kellogg Middle School and Multiple Pathways to Graduation
Consolidated Projects: Water Quality, Security Upgrades, New Roofs, Asbestos Abatement, Radon Remediation, Lead Paint Stabilization, Life Safety Upgrades, Accessibility, Seismic

Project	Budget	Outstanding Encumbrance	Amount Paid to Date	Remaining balance
Benson HS Mod	$146,614,560	$140,366	$143,349,657	$3,124,536
Benson Add Ons	$2,865,020	$1,397,236	$55,715	$1,412,069
Benson Swings	$12,199,595	$0	$12,199,595	$0
Lincoln HS Repl	$240,836,448	$5,976,292	$224,096,580	$10,763,576
Kellogg MS Replace	$57,648,703	$0	$57,648,703	$0
McDanial Mod	$197,000,000	$16,714	$196,810,549	$172,738
Health & Safety	$166,849,630	$23,787,304	$121,858,490	$21,203,836
Athletics	$5,000,000	$174,034	$2,278,729	$2,547,237
Administration	$67,862,160	$457,995	$60,618,998	$6,785,166
Contingency	$2,502,859	$0	$0	$2,502,859
PPS 2017 Bond Program Total	**$899,378,975**	**$31,949,941**	**$818,917,017**	**$48,512,017**

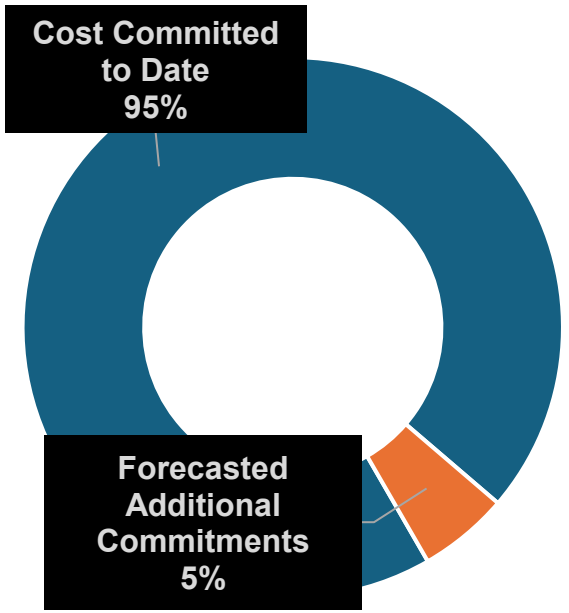


*as of 4/1/26

2020 Bond Program Status – Budget Update - Overview

Modernizations: Jefferson HS, Pre-Planning/Design Ida B Wells and Cleveland HS, The Center of Black Excellence, Roosevelt (added capacity), and Benson
Consolidated Projects: Curriculum Materials, New Technology for classroom and distance learning, Health & Safety, Seismic, Security, Re-Roofing

Project	Budget Managed by PROCEDEO	Budget Managed by PPS	Outstanding Encumbrance	Amount Paid to Date	Remaining Balance
Benson 2020 Funds		$164,903,890	$1,149,080	$162,293,196	$1,461,615
Jefferson HS	$366,152,175		$18,022,153	$28,201,327	$319,928,695
CEE	$60,000,000		$1,700	$16,222,680	$43,775,620
Cleveland HS – Design	$25,784,000		$10,144,359	$14,306,646	$1,332,995
Cleveland Swing Site	$137,500		$7,300	$100,155	$30,045
Wells HS – Design	$25,318,534		$2,883,043	$16,721,527	$5,713,964
Roosevelt PhV – Design		$2,000,000	$1,035	$97,625	$1,901,340
MPG Building		$80,447,075	$265,462	$77,947,593	$2,234,021
Curriculum		$63,319,191	$865,342	$54,462,003	$7,991,846
Technology		$136,100,000	$21,093,525	$86,405,942	$28,600,533
Infra Projects		$260,748,415	$14,623,843	$231,973,916	$14,150,656
Administration		$64,666,987	$1,608,738	$33,613,864	$29,444,385
2017 Bond Balance		$0	$0	$0	$0
Contingency – OSM		$72,872,226	$0	$0	$72,872,226
Unallocated Funds		$12,852,629	$0	$0	$12,852,629
PPS 2020 Bond Program Total	**$477,392,209**	**$857,910,413**	**$70,665,580**	**$722,346,471**	**$542,290,570**

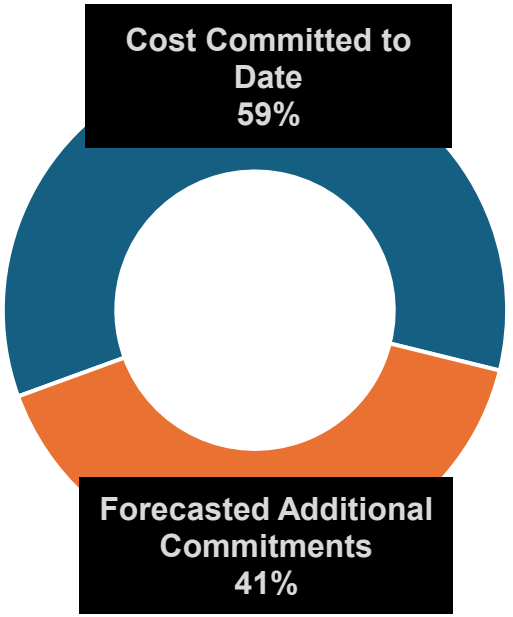


*as of 4/1/26

2025 Bond Program Status – Budget Update - Overview

Modernizations: Cleveland HS, Ida B Wells HS, and Jefferson
Consolidated Projects: Security Upgrades, Seismic, Technology, Improvements for Roosevelt, Lincoln, Franklin, and Grant, and New Athletic Hub Facilities at Jackson MS and Marshall Campuses

Project	Budget Managed by PROCEDEO	Budget Managed by PPS	Outstanding Encumbrance	Amount Paid to Date	Remaining Balance
Priority Scope		$189,890,000	$3,310,227	$73,113	$186,506,660
Athletics		$79,000,000	$2,721,847	$568,958	$75,709,195
Technology		$176,000,000	$3,916,460	$26,118,260	$145,965,280
Physical Education		$10,000,000	$0	$0	$10,000,000
Curriculum		$56,000,000	$0	$0	$56,000,000
Jefferson HS Modernization	$100,000,000		$0	$0	$100,000,000
Cleveland HS Modernization	$447,699,868		$9,815,079	$99,568	$437,785,221
Ida B Wells HS Modernization	$432,000,000		$487,900	$0	$431,512,100
Elementary & Middle Schools		$170,300,132	$0	$0	$170,300,132
Admin		$83,050,000	$59,732,226	$5,691,791	$17,625,983
Contingency		$125,956,806	$0	$0	$125,956,806
PPS 2025 Bond Program Total	**$979,699,868**	**$890,196,938**	**$79,983,739**	**$32,551,689**	**$1,757,361,377**

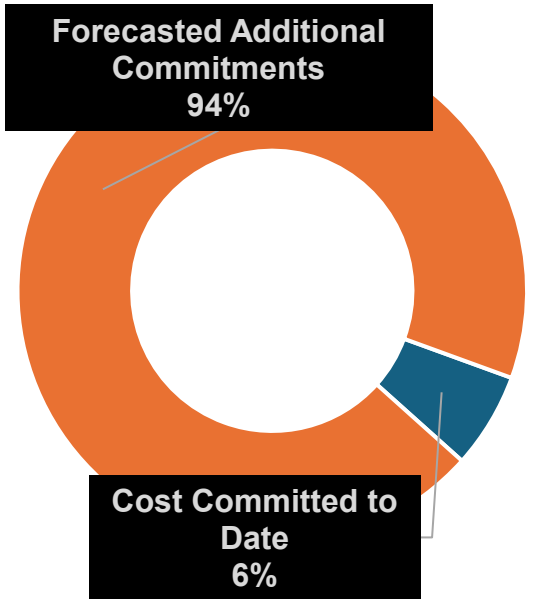

*as of 4/1/26

Project Updates

Cleveland HS Modernization

3400 SE 26th Ave, Portland, OR 97202

Senior CM
Drew Schott

Contractor (CMGC)
Skanska

PPS Zone 6
Stephanie Engelsman

Architect
Mahlum

Project Budget

Total Budget	CMGC GMP
$472,553,760	GMP: TBD

Project Overview

Current Phase: In Design
Scope: New Facility
New Facility: 297,000 SF
Construction Start: Summer 2026
Student Move-In: 29-30 School Yr
Tentative Sub Com: Summer 2029
GMP Construction Timeline: TBD

General Scope

- ✓ 2 new four-story buildings connected by a skybridge
- ✓ Dynamic outdoor courtyard
- ✓ New arts theater, black box theater, 2 gyms, and dance and wrestling studios
- ✓ Improvements to track and athletic fields

Project Status

Design Procurement
100%

Design
75%

CDs In Progress

Construction
0%

Construction NTP
Pending

Project Update

1	Marshall improvements began on 4/6 and will be substantially complete in early August.
2	Groundbreaking at 1pm on June 12, 2026.
3	Halfway through the Construction Documentation phase on May 11th!

Project Floor Plan

See next slide for floor plans


PROCEDEO | PORTLAND Public Schools

Cleveland HS

Floor Plans Levels 1-4

L01

- FLEX LEARNING
- SPED + LRC
- CTE
- VISUAL + PERFORMING ARTS
- WRAP-AROUND SERVICES
- GYM + ATHLETICS
- MISCELLANEOUS
- CUSTODIAL

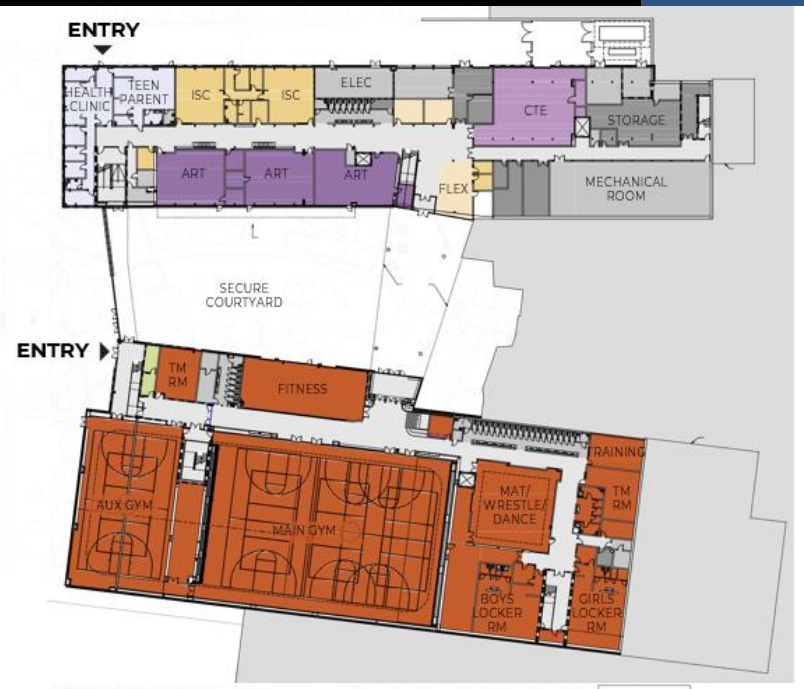

L02

- ADMIN / STUDENT SPACE
- COUNSELING / CAREER
- FLEX LEARNING
- SPED + LRC
- GENERAL CLASSROOMS
- VISUAL + PERFORMING ARTS
- STUDENT COMMONS
- GYM + ATHLETICS
- MISCELLANEOUS
- CUSTODIAL



L03

- ADMIN / STUDENT SPACE
- LIBRARY / MEDIA CENTER
- FLEX LEARNING
- SPED + LRC
- GENERAL CLASSROOMS
- CTE
- VISUAL + PERFORMING ARTS
- MISCELLANEOUS
- CUSTODIAL



L04

- ADMIN / STUDENT SPACE
- FLEX LEARNING
- SPED + LRC
- GENERAL CLASSROOMS
- CTE
- MISCELLANEOUS
- CUSTODIAL




Cleveland HS

Conceptual Rendering of Exterior



In Design

Cleveland HS

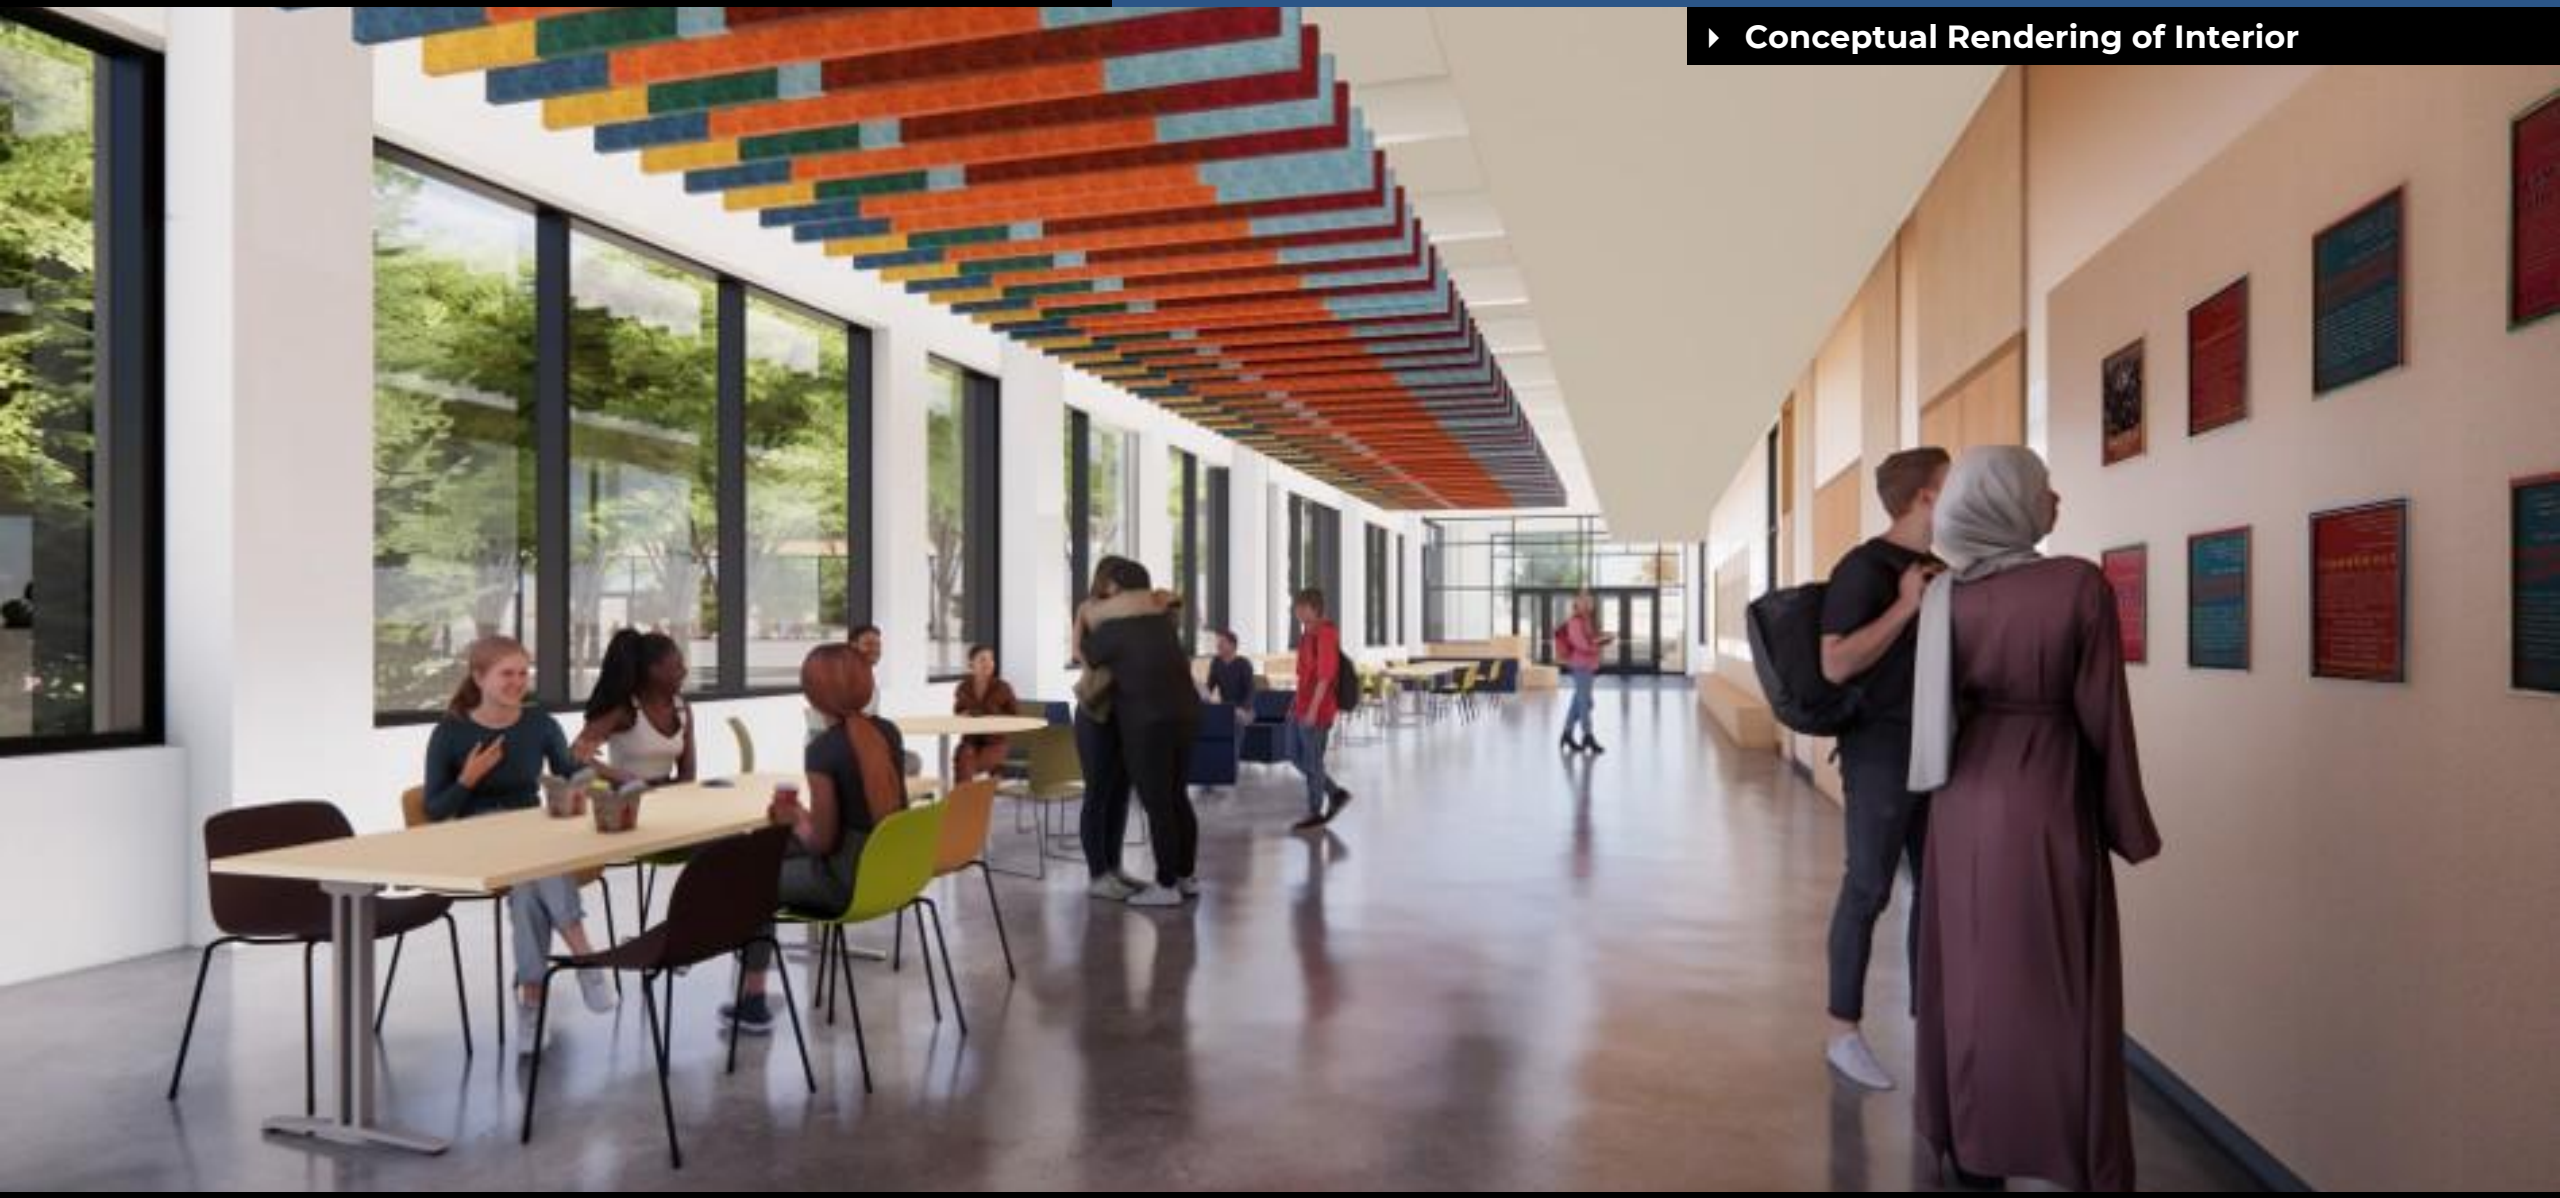

Conceptual Rendering of Interior

In Design

Jefferson HS Modernization

5210 N Kerby Ave, Portland, OR 97217

Senior CM
Drew Schott

Contractor (CMGC)
Colas Hoffman

PPS Zone 2
Michelle DePass

Architect
BORA & LEVER

Project Budget

Total Budget	CMGC GMP
$466,007,500	GMP: $TBD

Project Overview

Current Phase: In Design
Scope: New Facility
New Facility: 299,485 SF
Construction Start: Spring 2026
Student Move-In: 29-30 School Yr
Tentative Sub Com: Fall 2030
GMP Construction Timeline: TBD

General Scope

- ✓ New all-electric multi-story building
- ✓ Includes a theater, health center, teen parent center, and dance studios
- ✓ Track and field relocated to the site of the current structure
- ✓ New softball field and baseball/soccer multiuse field

Project Status

Design Procurement
100%

Design
70%

CDs In Progress

Construction
0%

Construction NTP
Pending

Project Update

1	Contractor has brought on trade partners to provide pre-con input
2	Groundbreaking: 10am on May 29, 2026
3	Community Info Session: May 6, 2026

Project Floor Plan

See next slide for floor plans

PROCEDEO | PORTLAND Public Schools

Jefferson HS


Floor Plans Levels 1-4



Level 1



Level 2

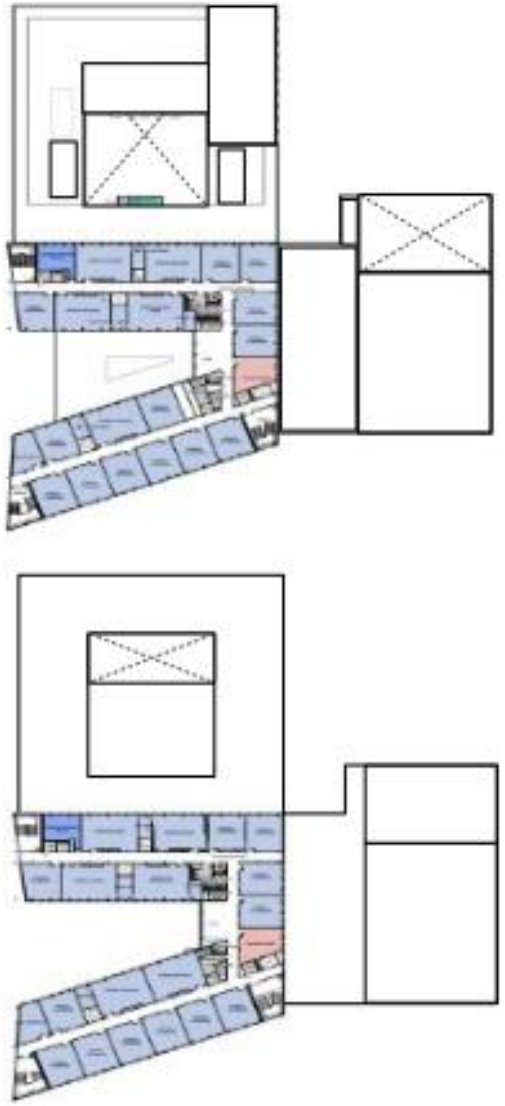

Levels 3-4

Jefferson HS



Conceptual Rendering of Exterior

In Design

Jefferson HS

Conceptual Rendering of Dance Studio



In Design

Ida B Wells HS Modernization

1151 SW Vermont St, Portland, OR 97219

Senior CM
Drew Schott

Contractor (CMGC)
Hoffman Construction

PPS Zone 1
Christy Splitt

Architect
BORA Architects

Project Budget

Total Budget	CMGC GMP
$449,350,000	GMP: $TBD

Project Overview

Current Phase: In Design
Scope: New Facility
New Facility: 283,867 SF
Construction Start: Winter 2026
Student Move-In: 29-30 School Yr
Tentative Sub Com: Fall 2030
GMP Construction Timeline: TBD

General Scope

- ✓ New four-story building including instructional spaces for Career Technical Education programs
- ✓ New performing arts, commons, and outdoor spaces
- ✓ Full complement of athletic fields and upgrade of existing fields on the Rieke side
- ✓ The existing pool is not in the scope, but a new pool support building is included

Project Status

Design Procurement
100%

Design
75%

CDs In Progress

Construction
0%

Construction NTP
Pending

Project Update

1	100% DD Reviews are complete. The Design Team has moved into the CD Phase.
2	Land Use application has been submitted


Project Floor Plan

See next slide for floor plans


Ida B Wells HS

Floor Plans Levels 0-3


LEVEL 0

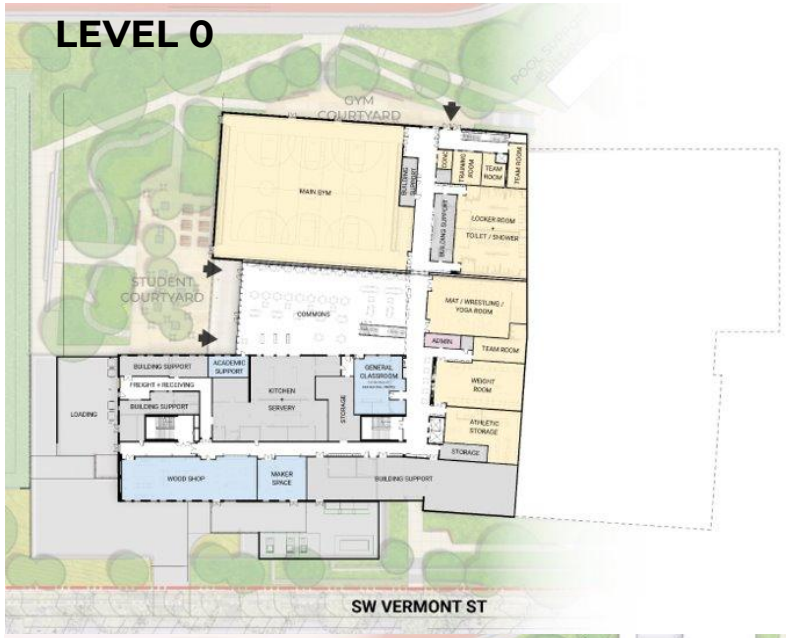

LEVEL 1 (Main Entrance)

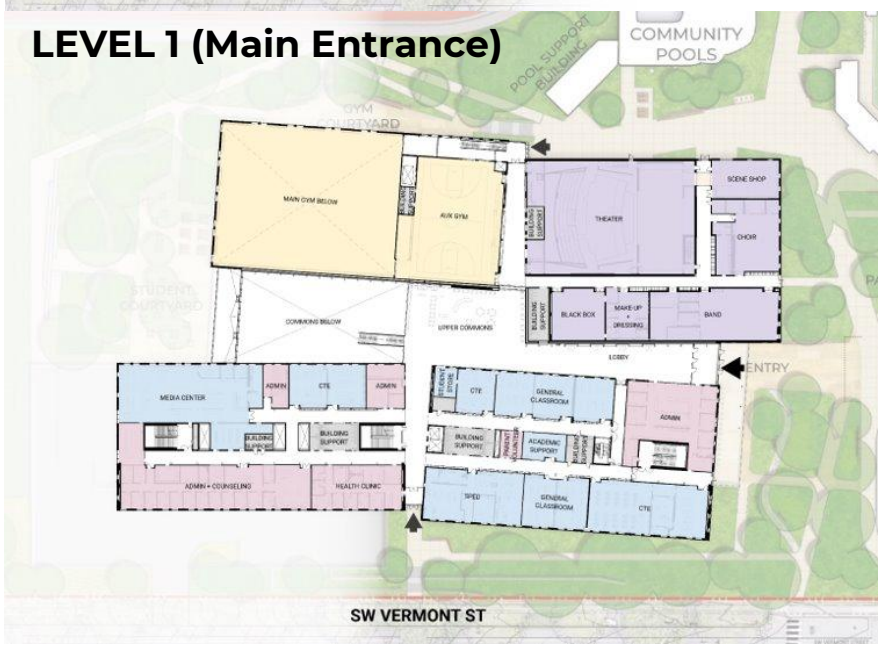

LEVEL 2

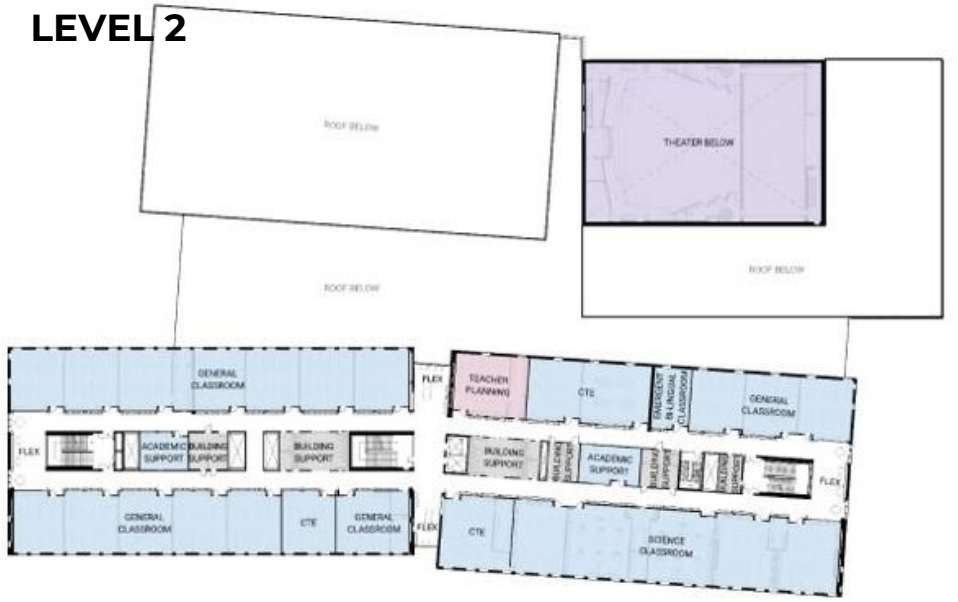

LEVEL 3



Ida B Wells HS

- Conceptual Rendering of Exterior



In Design

Ida B Wells HS

- Conceptual Rendering of Interior



In Design

Grice-Adair Center for Educational Excellence

1 N. Fremont St, Portland, OR 97227

Senior CM
Drew Schott

Contractor (CMGC)
TBD

Architect
TBD

Project Budget

Total Budget	CMGC GMP
$60,000,000	GMP: $TBD

Project Overview

Current Phase: Planning
Scope: Renovations
Renovations: TBD
Construction Start: TBD
Tentative Sub Com: TBD
GMP Construction Timeline: TBD

General Scope

✓ TBD

Project Status

Design Procurement
100%

Design
0%

Construction
0%

Construction NTP
Pending


Project Update

1	6 Architect Engineering firms approved by the Board on 4/14
2	Programming upon architectural award
3	Pre-Planning kick-off meeting anticipated within the next 30 days

Grice-Adair Center

Exterior



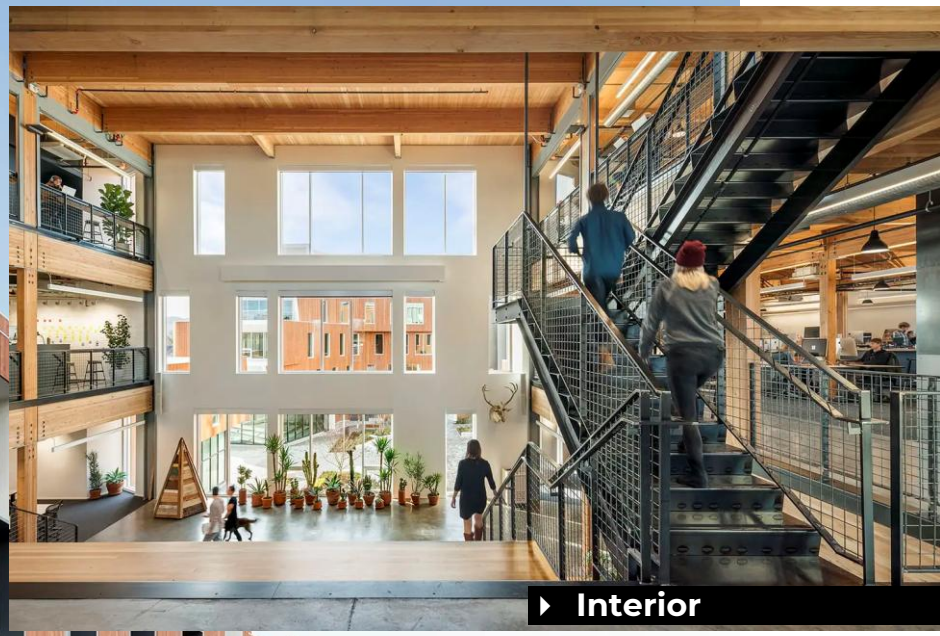


Interior

Planning

Grice-Adair Center

Courtyard Exterior

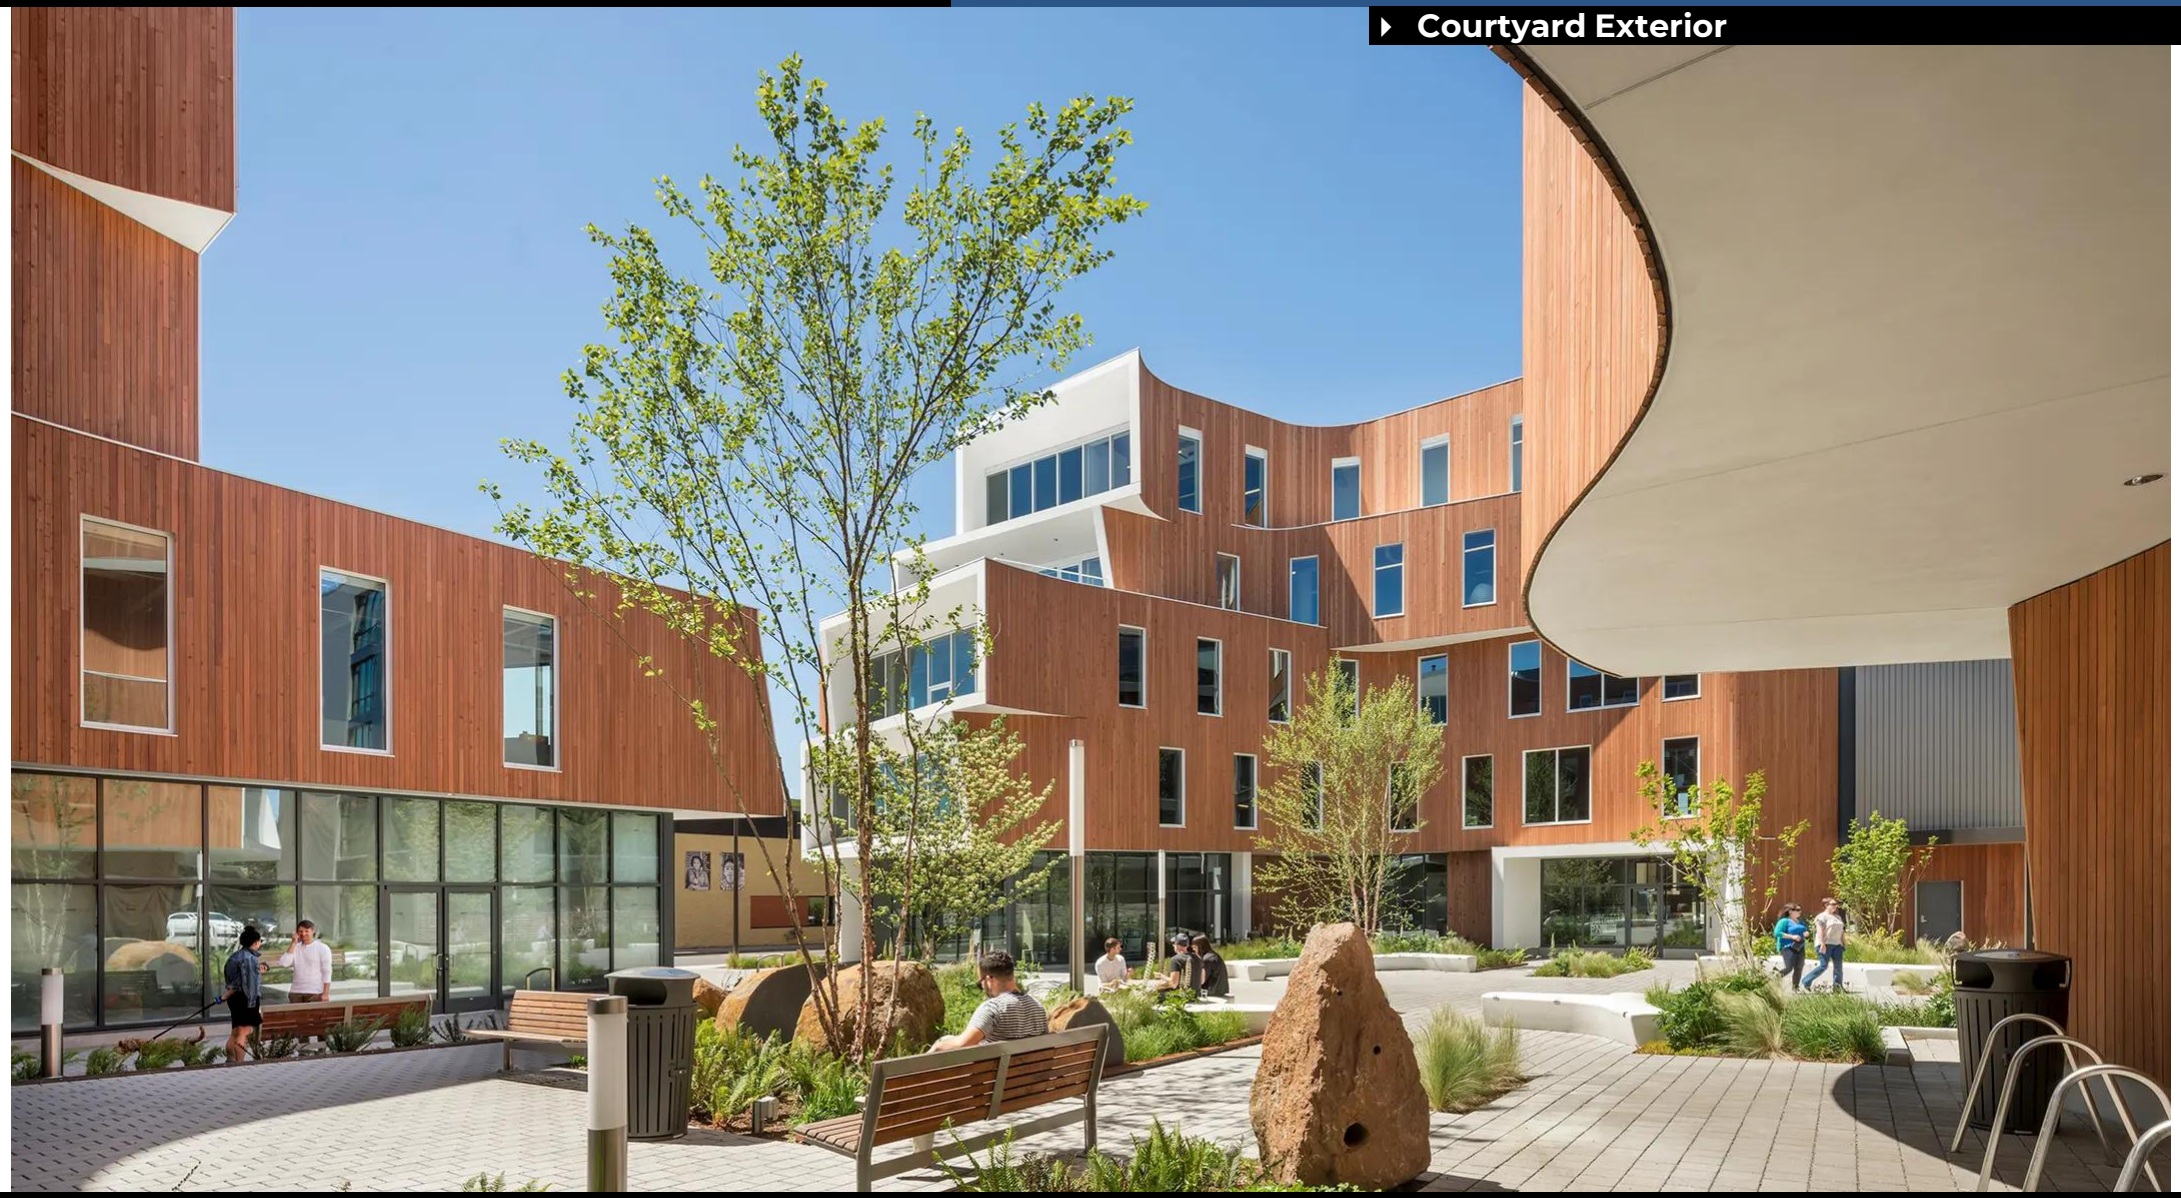

Consolidated Projects - Seismic

2026 Construction

Roofing with Seismic

- Contractor bids complete and contracts executed for Summer 2026 work
  - Woodmere
  - Cesar Chavez
  - Marshall
  - Vestal

Seismic Parts

- Construction bids due May 7th
  - Vernon
  - Winterhaven
  - Marysville (Ph 3)

Consolidated Projects - Seismic

Anticipated 2027 Construction

Seismic Parts and Partial Roof

- Richmond
  - Design Contract in final stages and anticipated to be in front of board on 4/28
- Capitol Hill
  - Design Contract in final stages and anticipated to be in front of board on 4/28
  - Anticipated Summer 2027 and 2028 construction

Seismic Parts

- Ainsworth and Kelly: Design Contracts anticipated to be in front of board in May

Full Seismic

- Beverly Cleary: Design in progress. Anticipated Summer ‘27-’28 construction

Consolidated Projects - Seismic

Anticipated 2028 and 2029 Construction

Seismic Parts and Partial Roof

- Beach
  - Anticipated Summer 2028 construction

- Rose City Park
  - Full Seismic and roof
  - Contract expected to be before the Board in May 2026
  - Anticipated Summer 2028 and 2029 construction

Consolidated Projects - Athletics

Grant Bowl Lighting

- Construction start April 15
- Directional boring for new electrical service across the road
- Light pole installation the week of April 20
- Electrical gear installation and connect in the first half of May

Marshall Track/Field and Tennis Courts

- Turf installation is complete; Track installation complete on April 25
- Tennis Court upgrade in progress and ahead of schedule

Jackson Athletic Hub

- Phase 0: Upper Field is nearing design completion with construction anticipated to start in June
- Phase 1: Multi-Use Field has completed SD Review

Consolidated Projects - Curriculum

Device Refresh

- New computers for ALL PPS students
- 41,500 devices will be deployed
- Pilot deployments at six schools begins on April 20
- All schools will have newly deployed devices by the beginning of the 26-27 school year
- Ongoing deployment support during the beginning of school year

Consolidated Projects – Mechanical, Health & Safety

DDC Controls Upgrades – changing pneumatic systems to DDC

- Allows better control of the systems resulting in more energy efficiency and better comfort control
- School group phases
  - Ph 1 – 9 schools – Complete
  - Ph 2A – 6 schools – Construction Complete
  - Ph 2B – 6 schools – In construction
  - Ph 2C – In design for Summer 2026 construction

Fire Alarm Upgrades – upgrade fire alarm panels and devices

- Projects out to bid with multiple campuses in each project
- Construction anticipated Summer 2026

Consolidated Projects – Facility Improvements

Complete

- Wilcox HVAC System Replacement
- Marshall Water Main Replacement

Summer 2026

- Franklin Condenser Replacement – Anticipated
- Buckman
  - Cafeteria Truss Replacement, Dance Studio Truss Repairs, Caf. Flooring Replacement
- Boise Elliot – Repaint majority of school
- Capitol Hill – Flooring abatement, subfloor repairs, new flooring
- Jefferson – Stage rigging repairs
- Sitton – Truss repair/replacement
- Rose City Park – Boiler re-tubing
- Vestal – Built-in cafeteria table replacement

Questions
Thank You



Contact us

PPS.NET pubinfo@pps.net (503) 916-2000 501 N Dixion, Portland, OR 97227



PORTLAND
Public Schools
