Bond Program Update



PORTLAND
Public Schools

May 26, 2026


Agenda

- Program Status Update
- Schedule Update
- Program Budget Update
- Project Updates

Program Status Update

2012 Bond Program Project Status

Total Projects	Pre-Planning	Design Phase	Construction	Post Construction	Completed
33	0	0	2	7	24

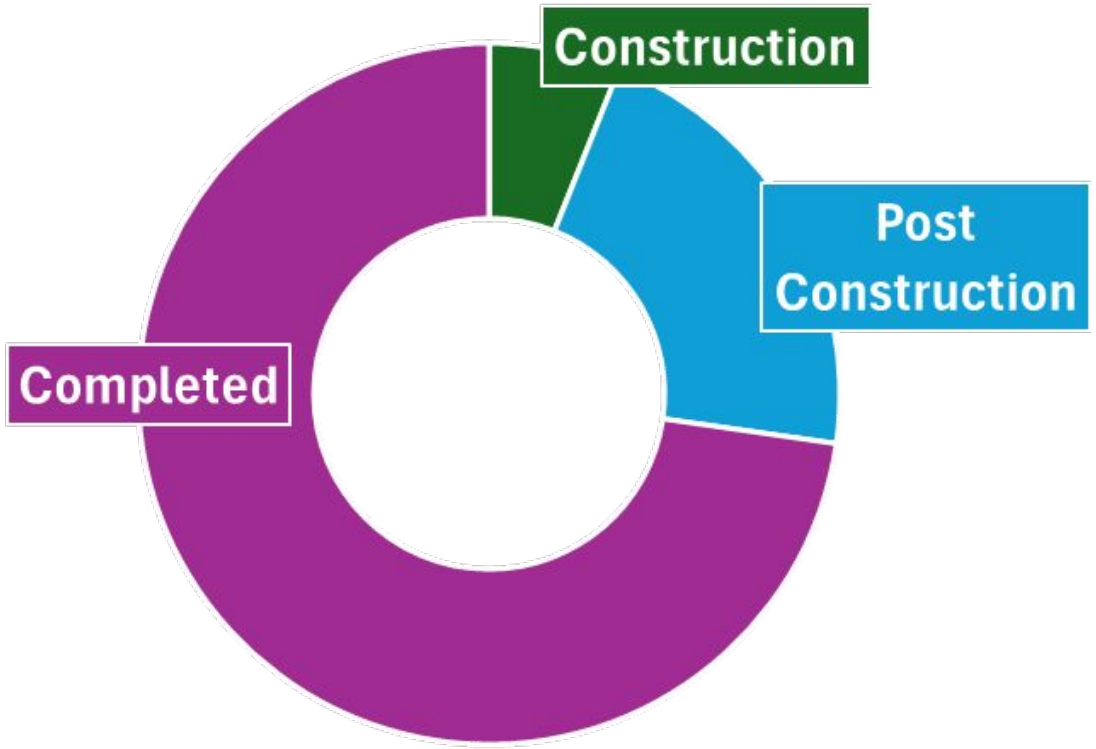


NOTE: source data: Ebuilder reports by bond measure, sorted by project status.

Audit of Project Completion and Closeout statuses is currently ongoing.

2017 Bond Program Project Status

Total Projects	Pre-Planning	Design Phase	Construction	Post Construction	Completed
179	3	7	15	50	104

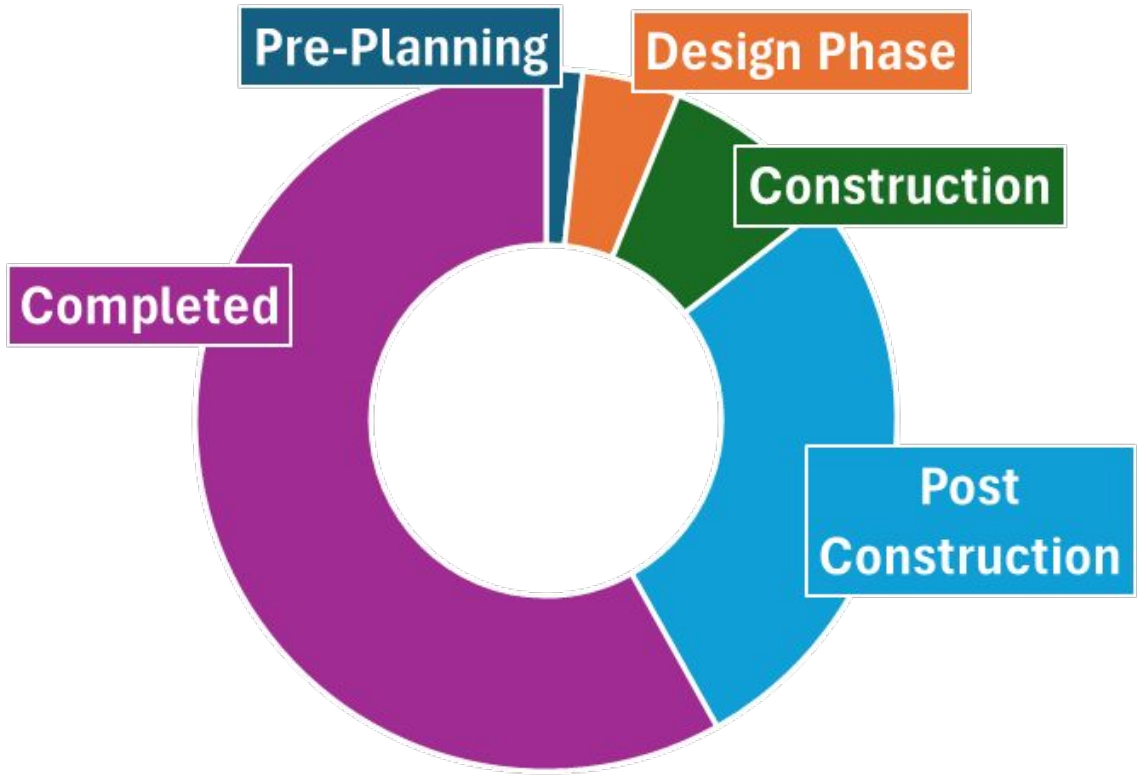


NOTE: source data: Ebuilder reports by bond measure, sorted by project status.

Audit of Project Completion and Closeout statuses is currently ongoing.

2020 Bond Program Project Status

Total Projects	Pre-Planning	Design Phase	Construction	Post Construction	Completed
112*	2	5	30	31	44

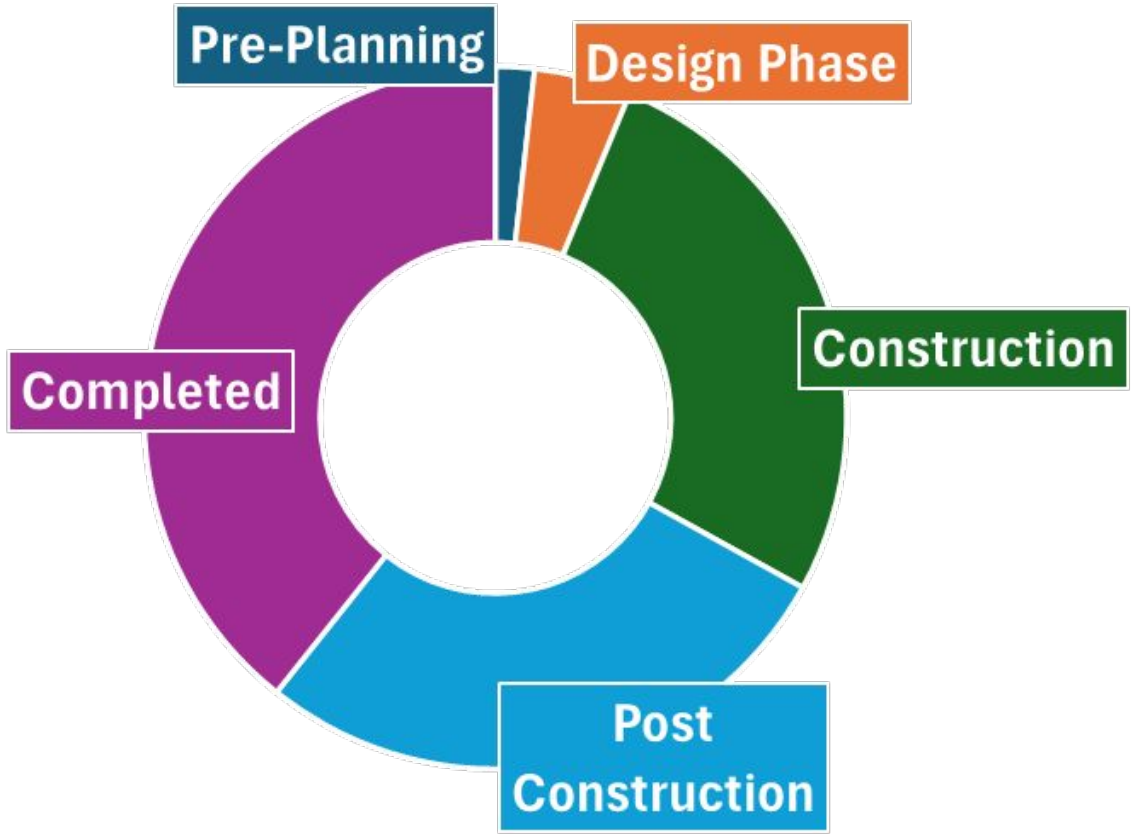


**Approximately $512 M remaining to be scheduled for 2020 Bond.*

NOTE: source data: Ebuilder reports by bond measure, sorted by project status.

Audit of Project Completion and Closeout statuses is currently ongoing.

2025 Bond Program Project Status



Total Projects	Pre-Planning	Design Phase	Construction	Post Construction	Completed
22*	12	5	2	3	0

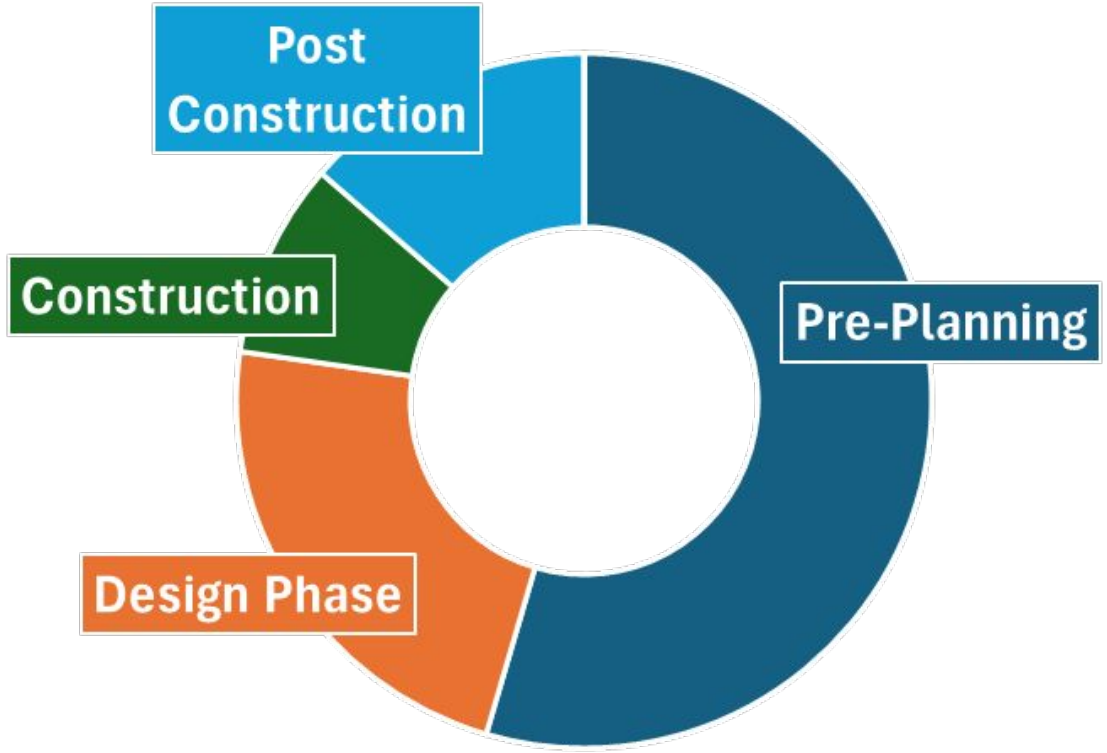

** Total projects will increase as the program progresses.*


Schedule and Budget Update

Program Schedule Update


Program Schedule May 2026		2026	2027	2028	2029	2030
1	Jefferson High School					
2	Cleveland High School					
3	Ida B. Wells High School					
4	Grice-Adair Center for Educational Excellence					
All future dates, durations and projections are subject to change						

Design Phase	Procurement	Land Use	Permitting	Construction Phase	Closeout


JHS Overall Project Schedule

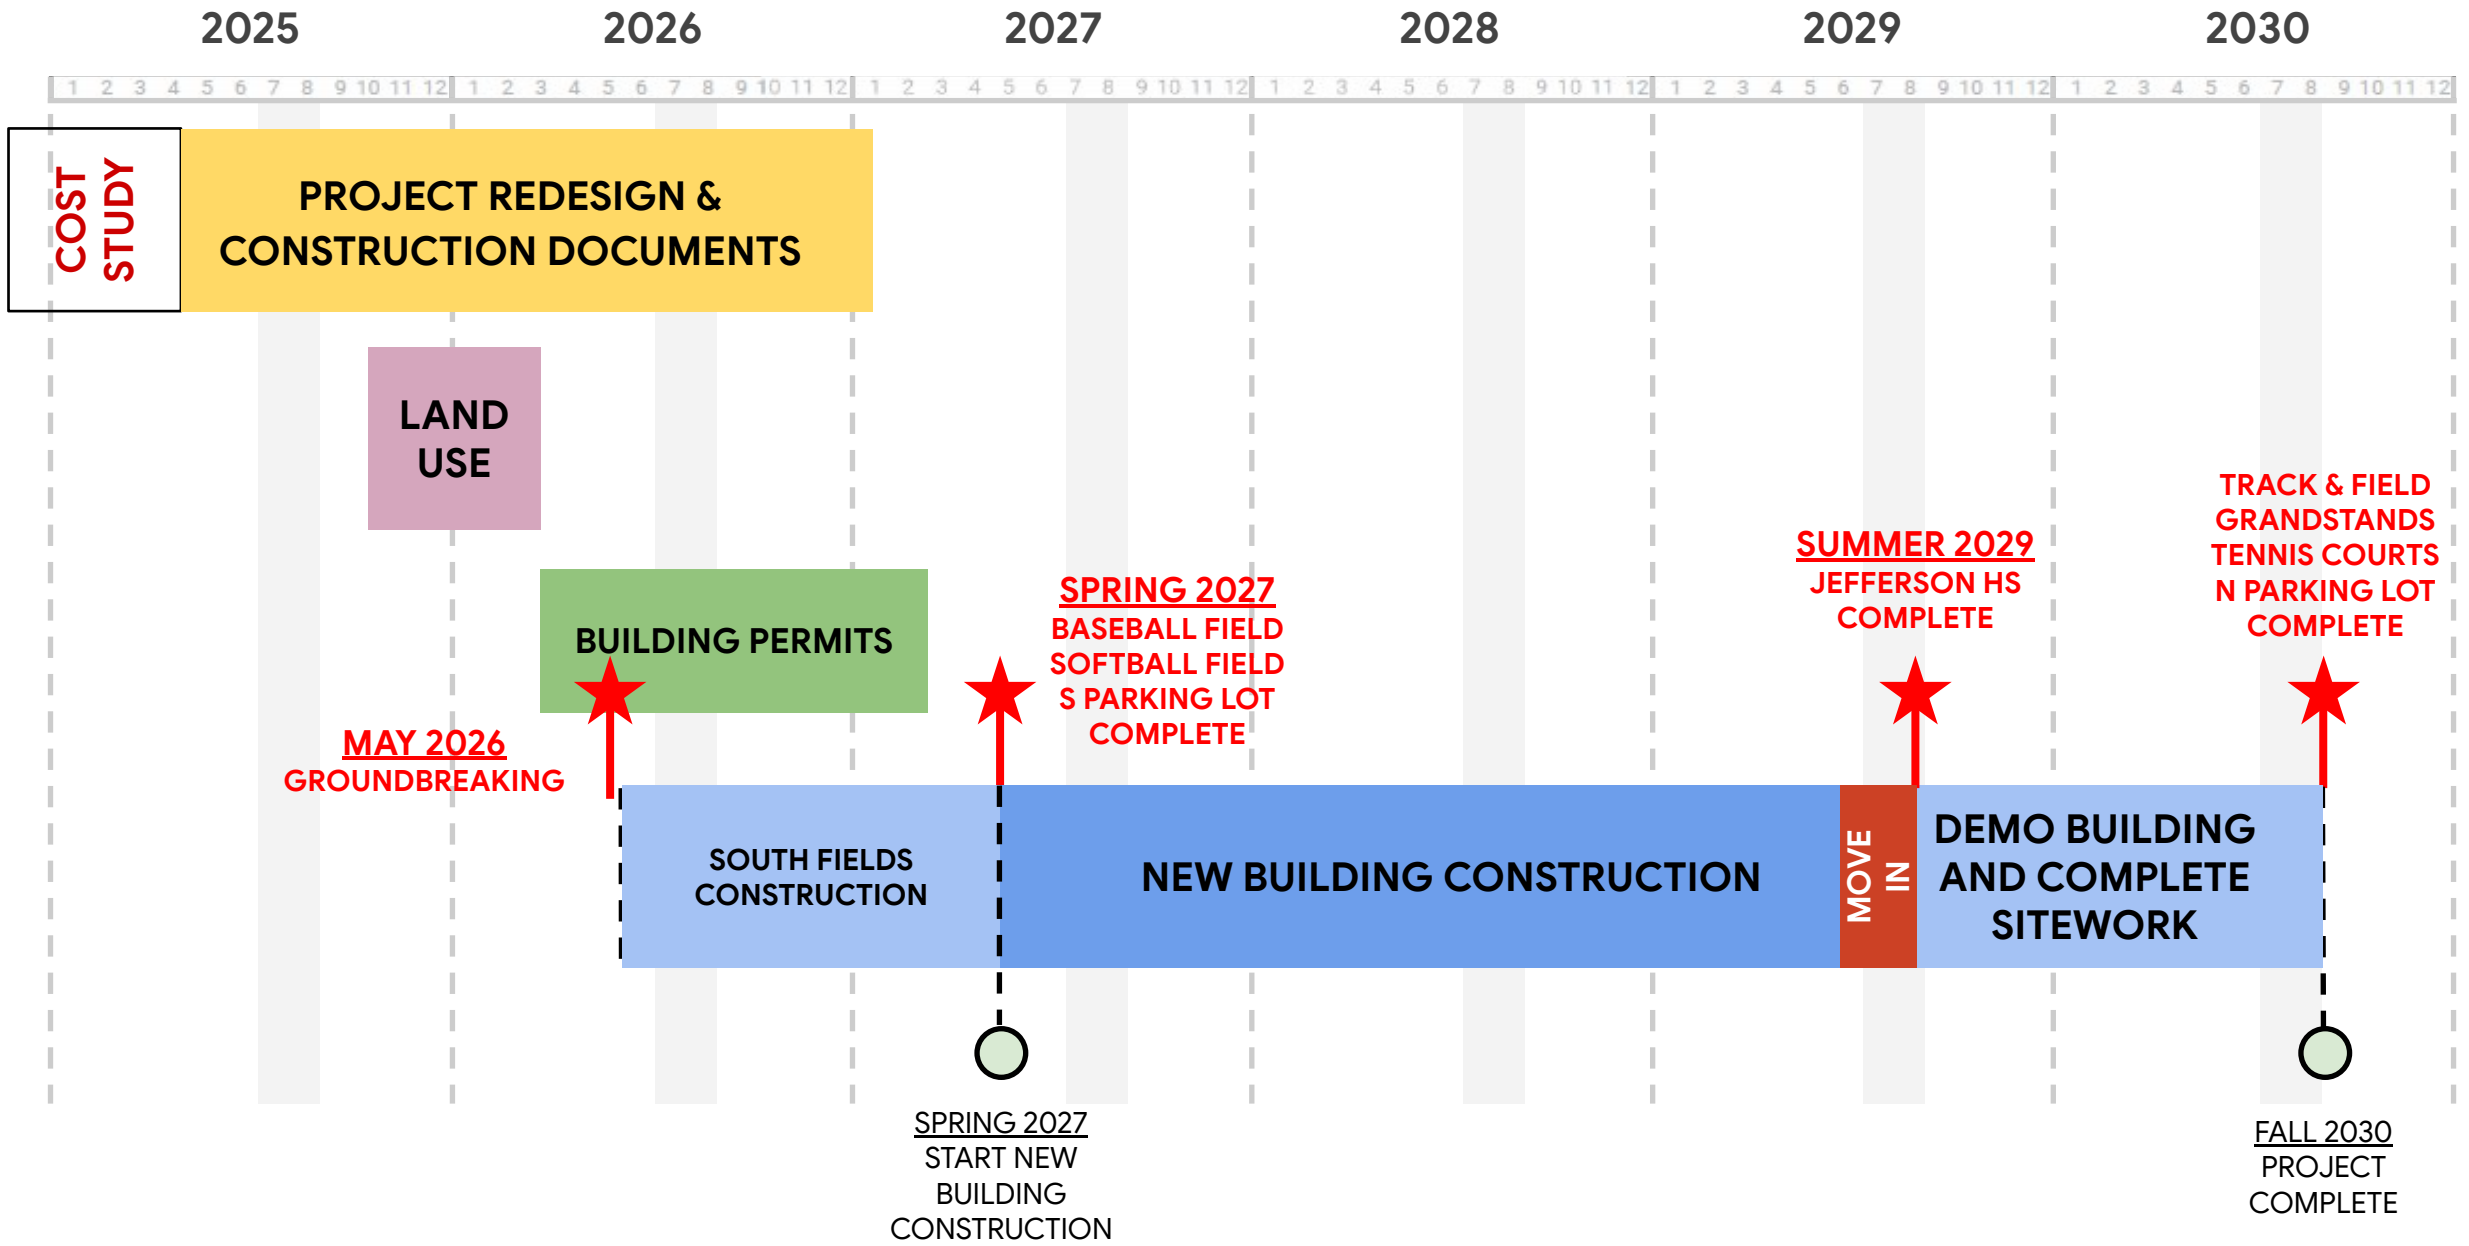

CHS Overall Project Schedule

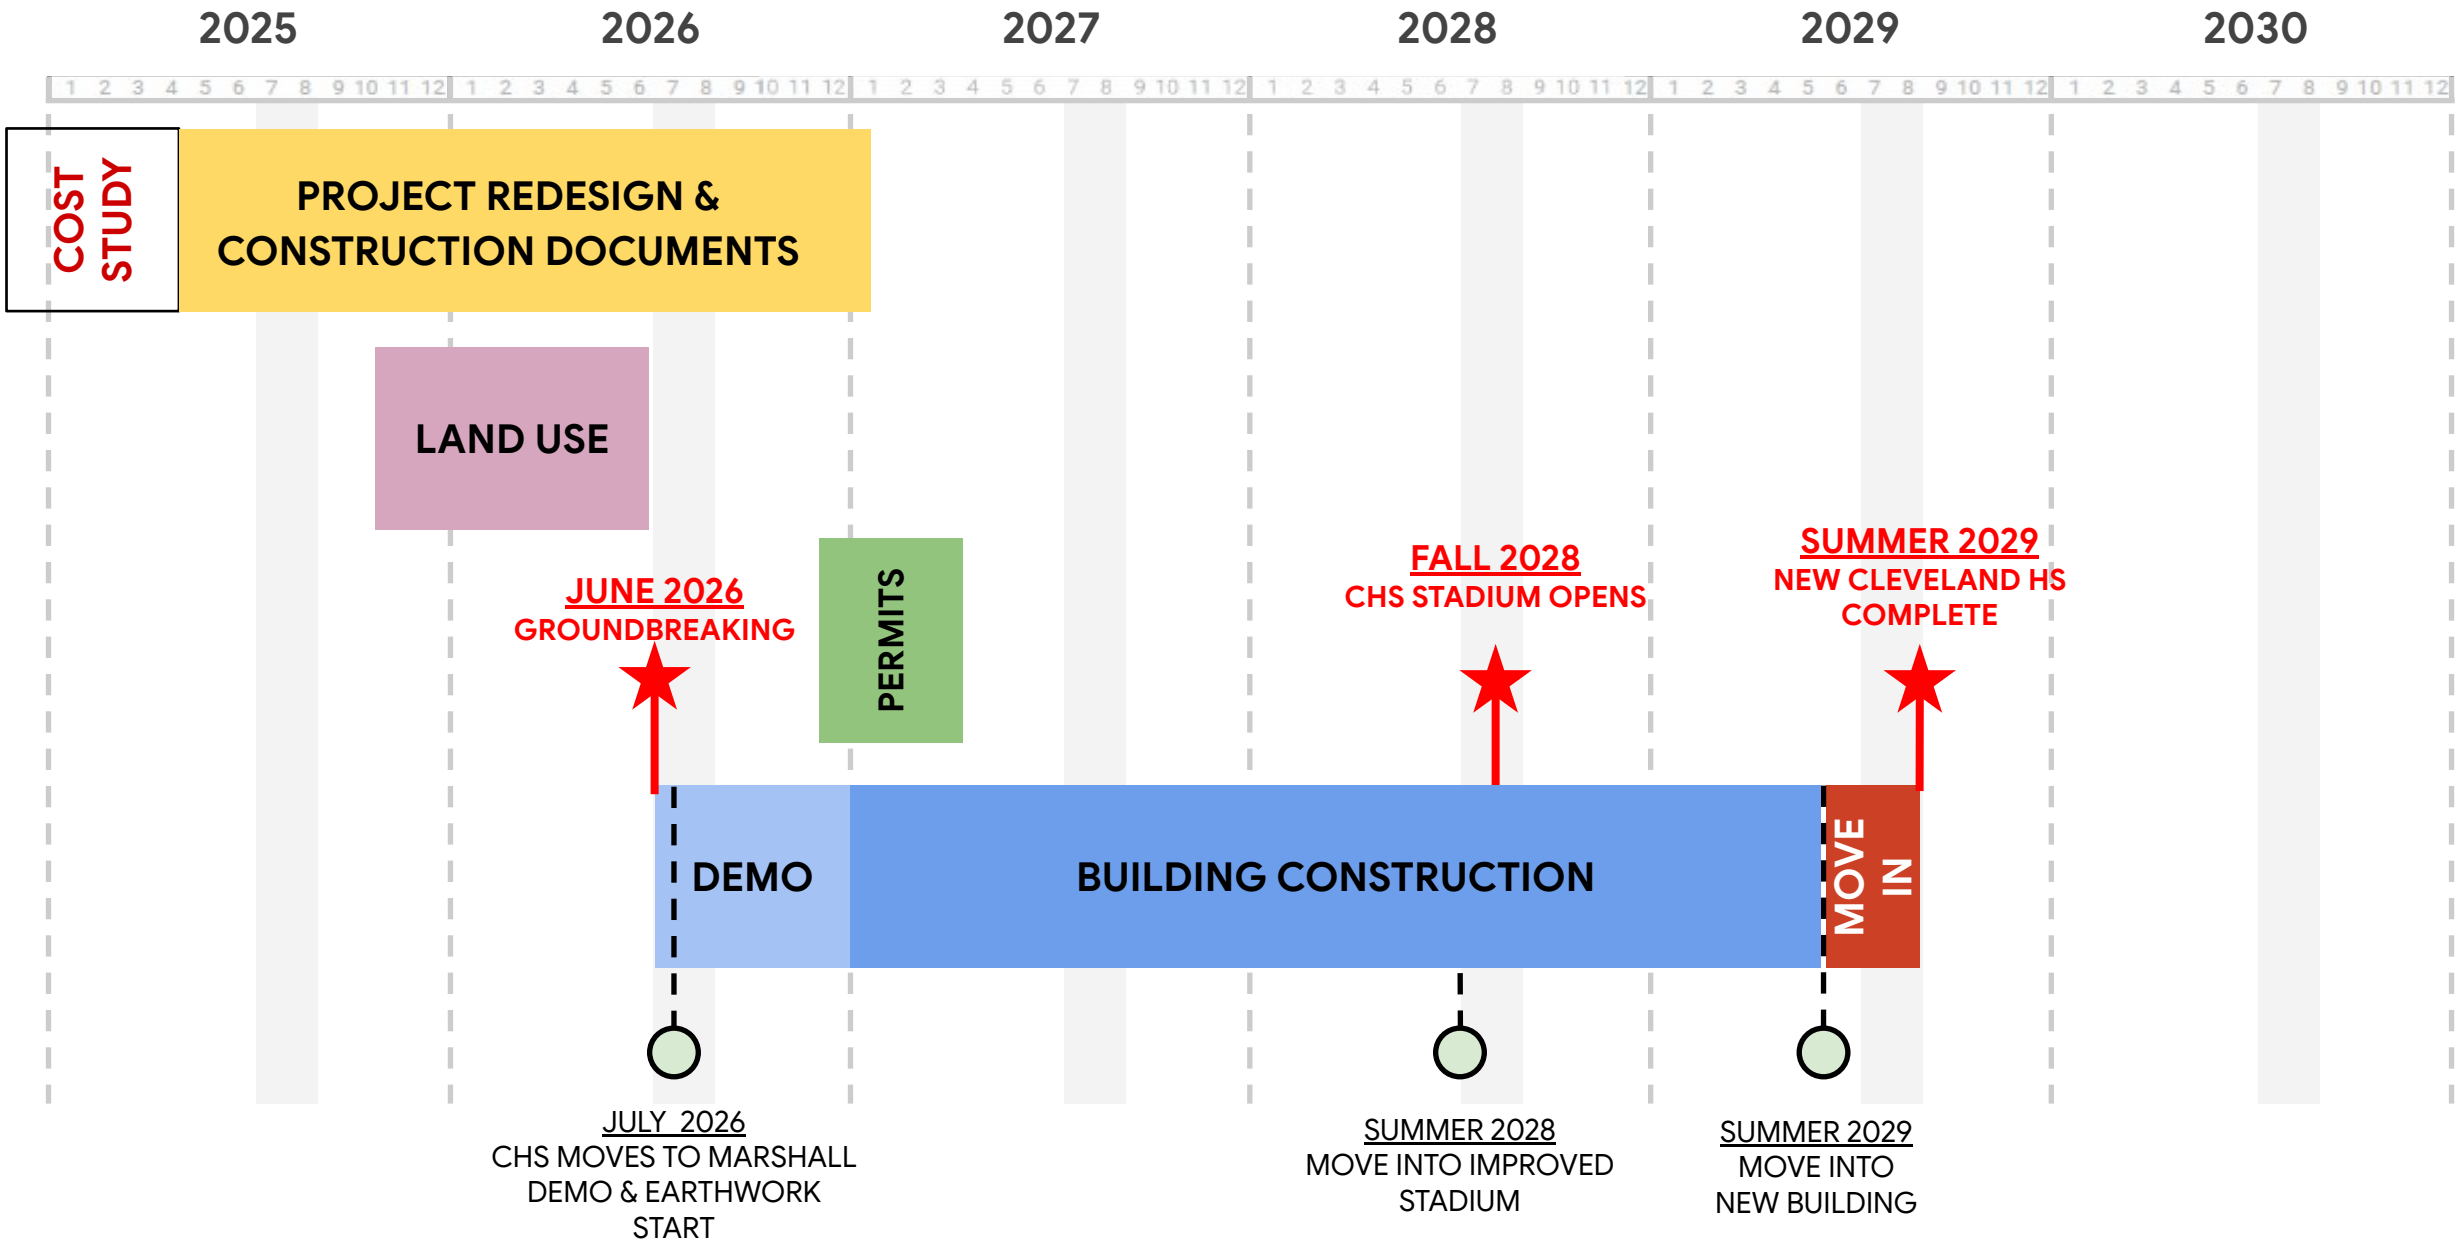

IBW Overall Project Schedule

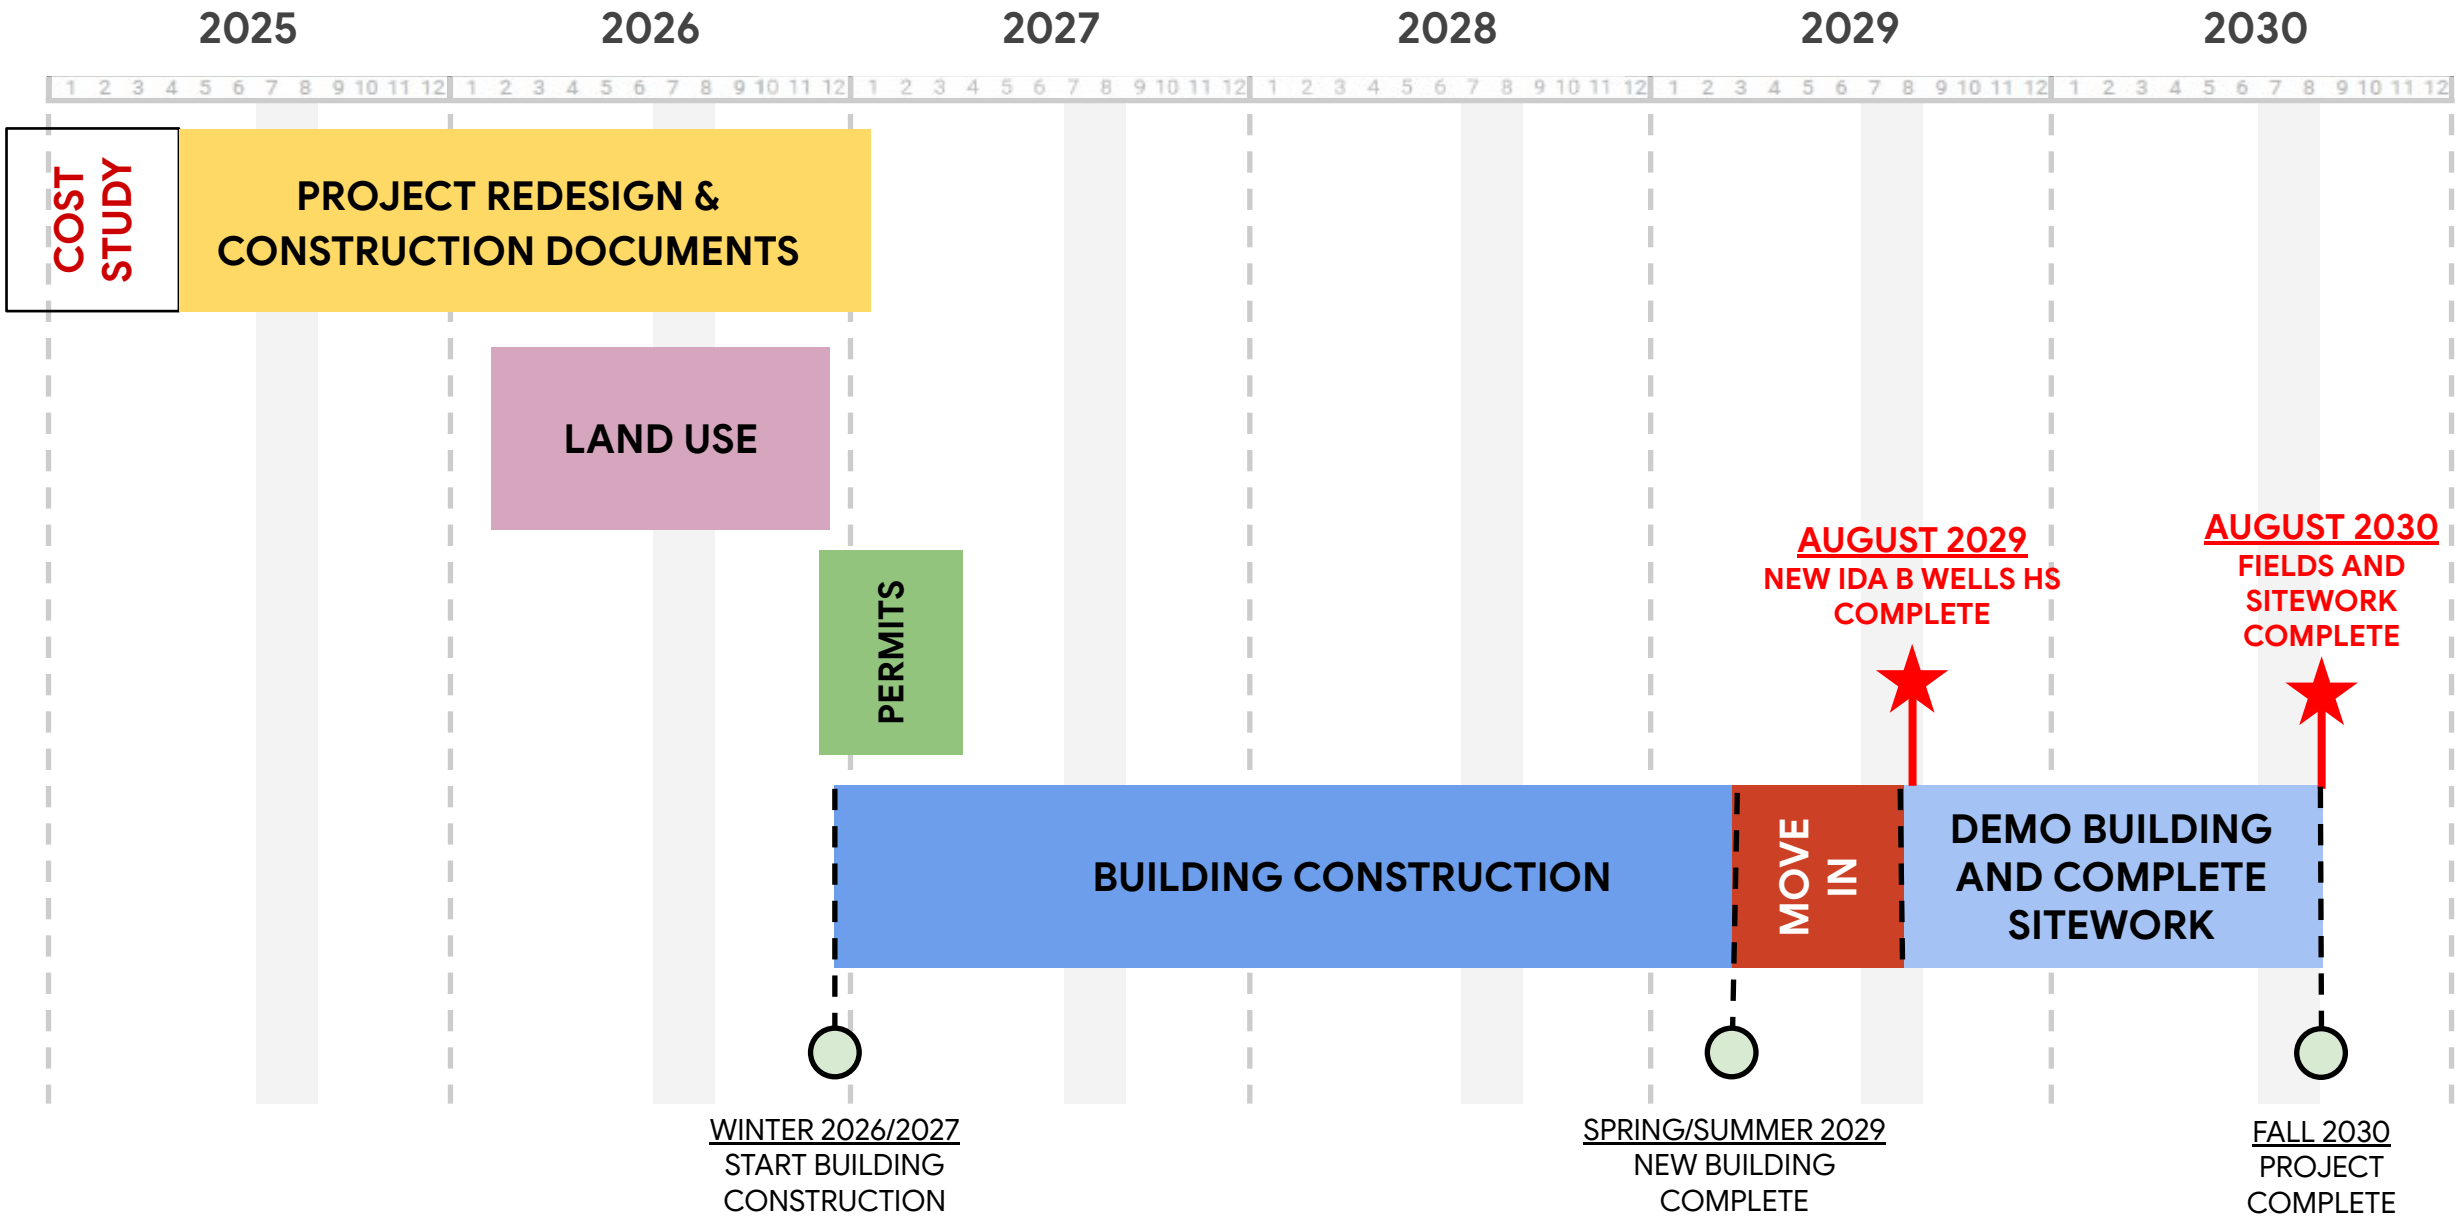

PORTLAND PUBLIC SCHOOLS

Bond Program Dashboard


Data Source	Report Name	Date Export
eBuilder	0-PIVOT TABLE - FUNDING - SLS 05.01.2026 06 04 52 AM.xls	5/8/2026 3:4
eBuilder	BAC Data Project Management Cost 05.01.2026 06 30 43 AM (1).xls	5/8/2026 3:4
eBuilder	BAC Report Dashboard.pbix	5/7/2026 3:5
eBuilder	Commitment Funding Items 05.01.2026 06 30 15 AM (1).xls	5/8/2026 3:4

Bond Measure


Deselect all | 2012 Bond | 2017 Bond | 2020 Bond | 2025 Bond

Total Funds	Spent to Date	Outstd. Encumbrance	Available Funds	Percent Available
4.6bn	2.1bn	231.4M	2.3bn	49%

Spent to Date and Total Funds

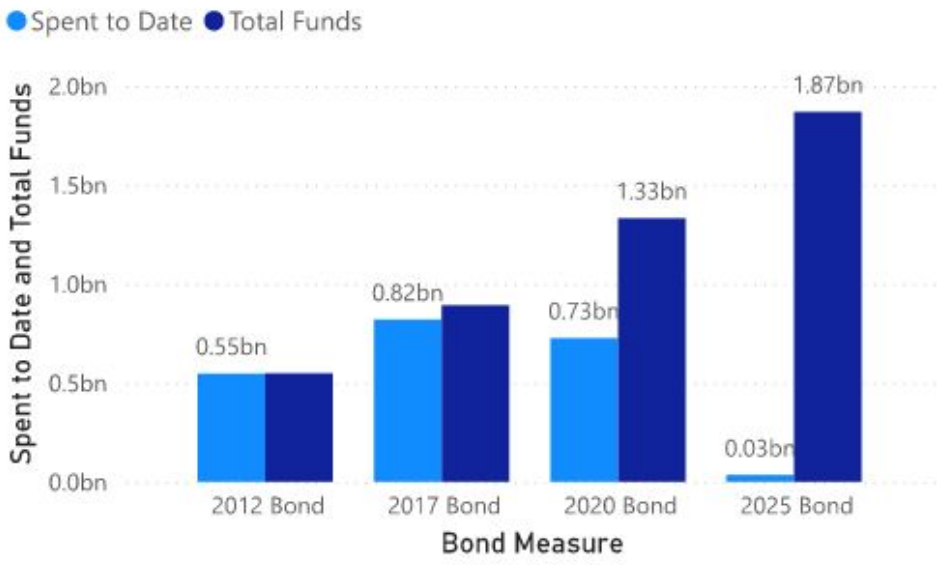


Spent and Encumbered

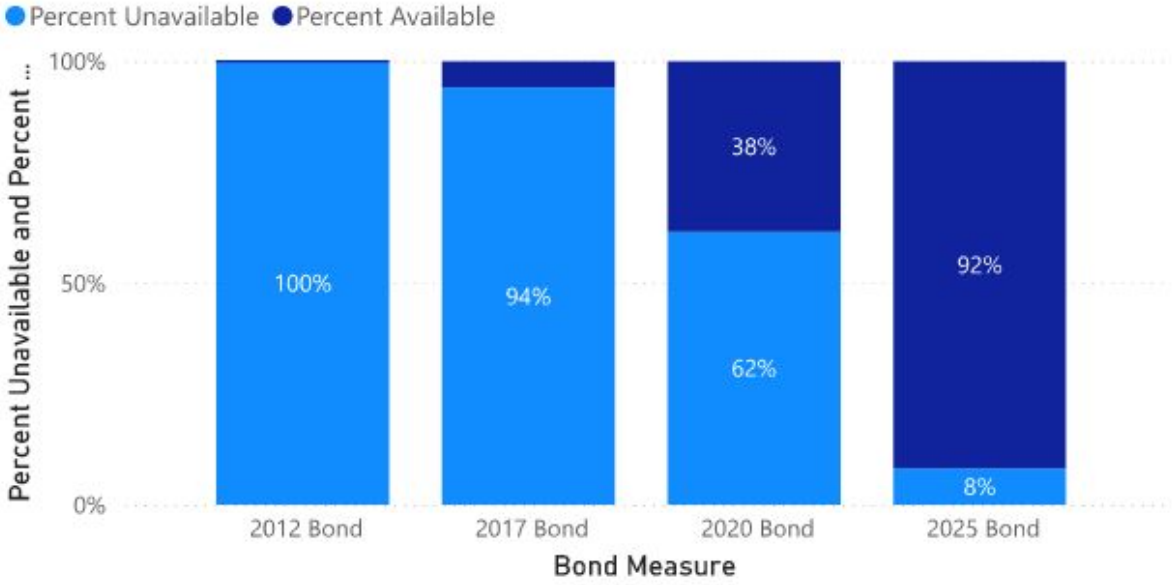

2012 Bond Program Status – Budget Update - Overview

Modernizations: Franklin HS, Grant HS, Roosevelt HS, and Faubion PK-8
Middle School Science Upgrades
Consolidated Projects: Accessibility, Seismic

Project	Budget	Outstanding Encumbrance	Amount Paid to Date	Remaining Balance
Franklin HS Mod	$110,950,414	$0	$110,950,414	$0
Grant HS Mod	$155,300,188	$0	$155,300,188	$0
Roosevelt HS Mod	$97,128,043	$0	$97,128,043	$0
Faubion Replace	$30,653,663	$0	$30,653,663	$0
Grant Upper Field	$3,170,988	$0	$3,170,988	$0
RHS Phase IV	$6,153,741	$0	$6,153,741	$0
Other Projects	$112,710,428	$0	$112,710,428	$0
Grant & Franklin Add Ons	$326,663	$58,912	$72,164	$195,587
Administration	$31,284,018	$0	$31,284,018	$0
Contingency	$154,104	$0	-$902	$155,006
PPS 2012 Bond Program Total	**$547,832,249**	**$30,504**	**$547,422,744**	**$350,593**

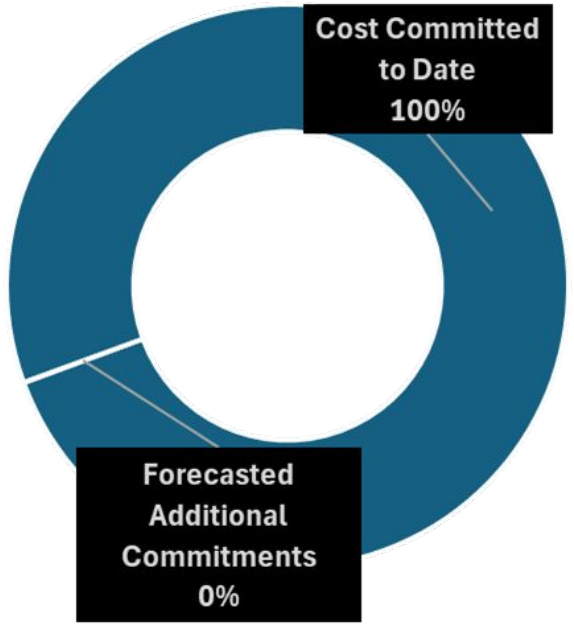

*as of 5/1/26

2012 Bond Spend Down

- The 2012 Bond needs to be closed as the remaining projects wrap up
- There will be approximately $46k left in contingency after requests at Grant and Franklin
- The plan for allocating the remaining $46k will be developed in the coming months


Project Name	Funding Source	Amount Requested
Grant - Flooring Abatement and Replacement - Bond - 6467 - FY25	Grant Add-Ons	$41,000.00
Franklin/Roosevelt blinds	Franklin Add-Ons	$40,000.00
Franklin playground	Franklin Add-Ons	$25,000.00
Grant boiler	Grant Add-Ons	$30,000.00
Total		$136,000.00
Remaining to Spend Down		$45,812.05

2017 Bond Program Status – Budget Update - Overview

Modernizations: Benson Polytechnic, Lincoln, McDaniel, Kellogg Middle School and Multiple Pathways to Graduation

Consolidated Projects: Water Quality, Security Upgrades, New Roofs, Asbestos Abatement, Radon Remediation, Lead Paint Stabilization, Life Safety Upgrades, Accessibility, Seismic

Project	Budget	Outstanding Encumbrance	Amount Paid to Date	Remaining balance
Benson HS Mod	$146,614,560	$158,943	$143,420,606	$3,035,011
Benson Add Ons	$2,865,020	$1,393,148	$60,727	$1,411,144
Benson Swings	$12,199,595	$0	$12,199,595	$0
Lincoln HS Repl	$240,836,448	$28,738	$224,096,580	$16,711,130
Kellogg MS Replace	$57,648,703	$0	$57,648,703	$0
McDaniel Mod	$197,000,000	$13,942	$196,817,745	$168,312
Health & Safety	$157,493,215	$15,985,854	$122,427,460	$19,079,901
Athletics	$4,895,489	$174,034	$2,278,729	$2,442,726
Administration	$61,087,401	$362,789	$60,714,205	$10,408
Contingency	$901,208	$0	$0	$901,208
PPS 2017 Bond Program Total	**$881,541,640**	**$18,117,448**	**$819,664,351**	**$43,759,840**

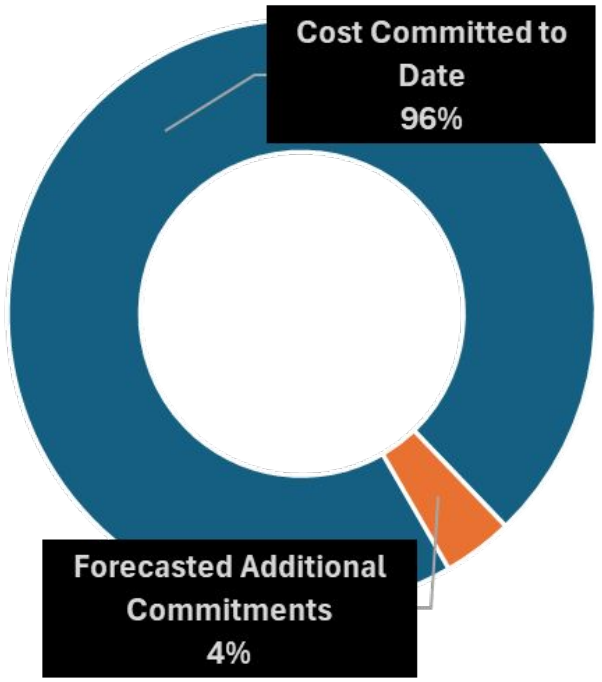

*as of 5/1/26

2020 Bond Program Status – Budget Update - Overview

Modernizations: Jefferson HS, Pre-Planning/Design Ida B Wells and Cleveland HS, The Center of Black Excellence, Roosevelt (added capacity), and Benson

Consolidated Projects: Curriculum Materials, New Technology for classroom and distance learning, Health & Safety, Seismic, Security, Re-Roofing

Project	Budget Managed by PROCEDEO	Budget Managed by PPS	Outstanding Encumbrance	Amount Paid to Date	Remaining Balance
Benson 2020 Funds		$164,903,890	$1,149,080	$162,801,948	$952,863
Jefferson HS Mod	$366,007,500		$35,067,620	$29,140,229	$301,799,651
Jefferson Add Ons	$152,175		$149,945	$250	
CEE	$60,000,000		$1,700	$16,222,680	$43,775,620
Cleveland HS – Design	$23,679,515		$9,255,919	$14,428,328	-$4,732
Cleveland Swing Site	$137,500		$1,800	$105,905	$29,795
Wells HS – Design	$20,000,000		$2,805,861	$17,207,827	-$13,689
Roosevelt PhV – Design		$2,000,000	$1,035	$97,625	$1,901,340
MPG Building		$80,447,075	$275,317	$77,947,593	$2,224,166
Curriculum		$63,319,191	$1,258,555	$54,603,348	$7,457,287
Technology		$136,100,000	$19,721,614	$87,985,972	$28,392,414
Infra Projects		$269,230,017	$22,505,873	$232,639,288	$14,084,856
Administration		$50,706,072	$1,262,019	$34,070,310	$15,373,743
2017 Bond Balance		$0	$0	$0	$0
Contingency – OSM		$80,451,360	$0	$0	$80,451,360
Unallocated Funds		$15,893,767	$0	$0	$15,893,767
PPS 2020 Bond Program Total	**$469,976,690**	**$853,734,488**	**$84,249,677**	**$727,251,302**	**$512,318,442**




*as of 5/1/26

2025 Bond Program Status – Budget Update - Overview

Modernizations: Cleveland HS, Ida B Wells HS, and Jefferson

Consolidated Projects: Security Upgrades, Seismic, Technology, Improvements for Roosevelt, Lincoln, Franklin, and Grant, and New Athletic Hub Facilities at Jackson MS and Marshall Campuses

Project	Budget Managed by PROCEDEO	Budget Managed by PPS	Outstanding Encumbrance	Amount Paid to Date	Remaining Balance
Priority Scope		$189,867,000	$10,685,685	$137,997	$179,043,318
Athletics		$79,000,000	$2,628,454	$764,969	$75,606,577
Technology		$176,000,000	$3,916,460	$26,173,417	$145,910,123
Physical Education		$10,000,000	$0	$0	$10,000,000
Curriculum		$56,000,000	$0	$0	$56,000,000
Jefferson HS Modernization	$100,000,000		$0	$0	$100,000,000
Cleveland HS Modernization	$448,911,745		$12,196,815	$337,342	$436,377,588
Ida B Wells HS Modernization	$429,350,000		$29,359,062	$0	$399,990,938
Elementary & Middle Schools		$171,738,255	$0	$0	$171,738,255
Admin		$83,050,000	$59,733,554	$6,630,838	$16,685,608
Contingency		$125,956,806	$0	$0	$125,956,806
PPS 2025 Bond Program Total	**$978,261,745**	**$891,612,061**	**$118,520,030**	**$34,044,564**	**$1,717,309,212**

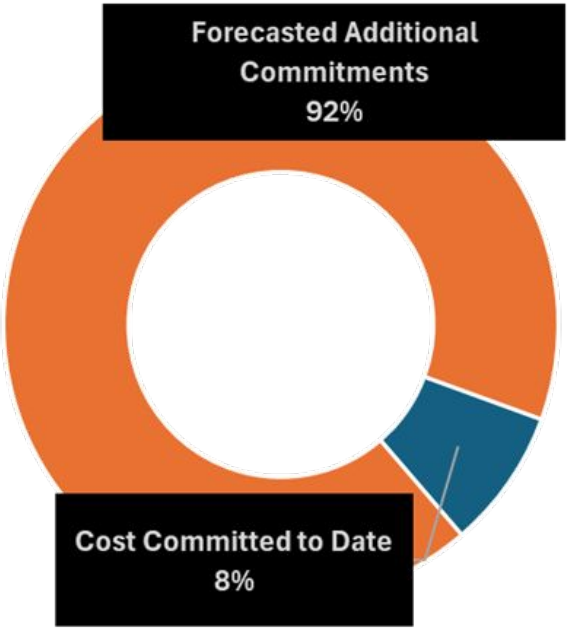

*as of 5/1/26

Project Updates

Jefferson HS Modernization

5210 N Kerby Ave, Portland, OR 97217

Senior CM
Drew Schott

Contractor (CMGC)
Colas Hoffman

PPS Zone 2
Michelle DePass

Architect
BORA & LEVER

Project Budget

Total Budget	CMGC GMP
$466,007,500	GMP: $TBD

Project Overview

Current Phase: In Design
Scope: New Facility
New Facility: 299,485 SF
Construction Start: Spring 2026
Student Move-In: 29-30 School Yr
Tentative Sub Com: Fall 2030
GMP Construction Timeline: TBD

General Scope

- ✔ New all-electric multi-story building
- ✔ Includes a theater, health center, teen parent center, and dance studios
- ✔ Track and field relocated to the site of the current structure
- ✔ New softball field and baseball/soccer multiuse field

Project Status

Design Procurement
100%

Design
75%

50% CDs In Progress

Construction
0%

Construction NTP
Pending

Project Update

1	Beginning early procurement of critical materials such as steel and timber
2	Prep underway for start of construction of baseball and softball fields this Spring
3	Groundbreaking: 12pm on May 29, 2026

Project Floor Plan

See next slide for floor plans

PROCEDEO | PORTLAND Public Schools


> Floor Plans Levels 1-4



Level 1



Level 2

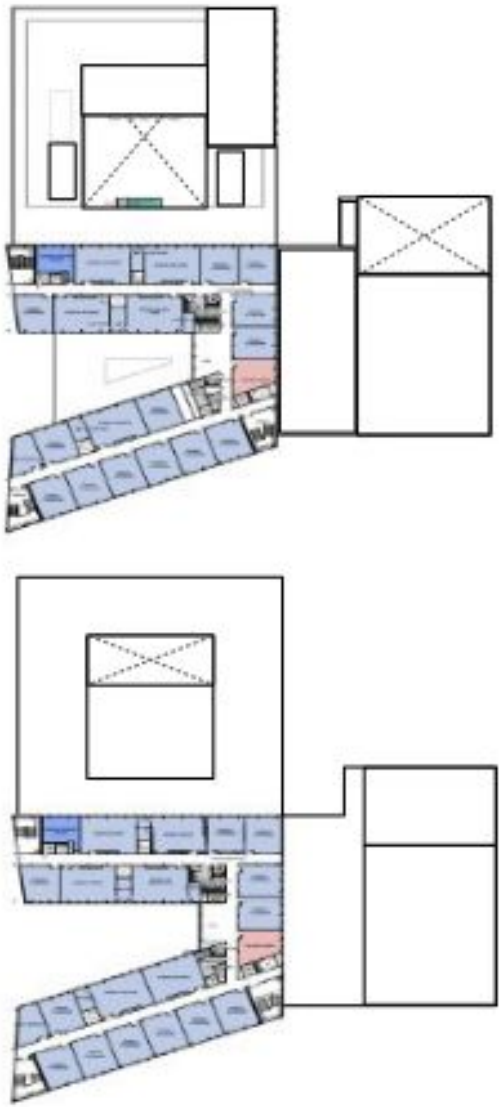

Levels 3-4

Cleveland HS Modernization

3400 SE 26th Ave, Portland, OR 97202

Senior CM
Drew Schott

Contractor (CMGC)
Skanska

PPS Zone 6
Stephanie Engelsman

Architect
Mahlum

Project Budget

Total Budget	CMGC GMP
$472,553,760	GMP: TBD

Project Overview

Current Phase: In Design
Scope: New Facility
New Facility: 297,000 SF
Construction Start: Summer 2026
Student Move-In: 29-30 School Yr
Tentative Sub Com: Summer 2029
GMP Construction Timeline: TBD

General Scope

- ✔ 2 new four-story buildings connected by a skybridge
- ✔ Dynamic outdoor courtyard
- ✔ New arts theater, black box theater, 2 gyms, and dance and wrestling studios
- ✔ Improvements to track and athletic fields

Project Status

Design Procurement
100%

Design
80%

50% CDs In Review

Construction
0%

Construction NTP
Pending

Project Update

1	Marshall improvements are scheduled to be substantially complete in early August.
2	Groundbreaking at 1pm on June 12, 2026.
3	- Cleveland Youth Track, Wrestling, and Saturday Youth Events will shift to the Marshall fields. - All other Youth Programs will use the MS sites or Portland Parks - PIL has coordinated these efforts

Project Floor Plan


See next slide for floor plans

PROCEDEO | PORTLAND Public Schools

> Floor Plans Levels 1-4

L01

- FLEX LEARNING
- SPED + LRC
- CTE
- VISUAL + PERFORMING ARTS
- WRAP-AROUND SERVICES
- GYM + ATHLETICS
- MISCELLANEOUS
- CUSTODIAL

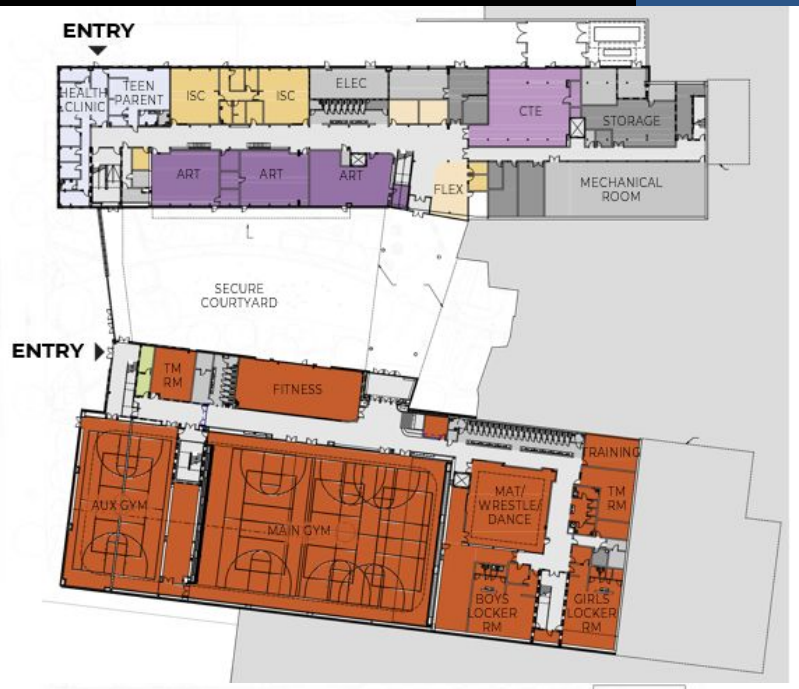


L03

- ADMIN / STUDENT SPACE
- LIBRARY / MEDIA CENTER
- FLEX LEARNING
- SPED + LRC
- GENERAL CLASSROOMS
- CTE
- VISUAL + PERFORMING ARTS
- MISCELLANEOUS
- CUSTODIAL



L02

- ADMIN / STUDENT SPACE
- COUNSELING / CAREER
- FLEX LEARNING
- SPED + LRC
- GENERAL CLASSROOMS
- VISUAL + PERFORMING ARTS
- STUDENT COMMONS
- GYM + ATHLETICS
- MISCELLANEOUS
- CUSTODIAL

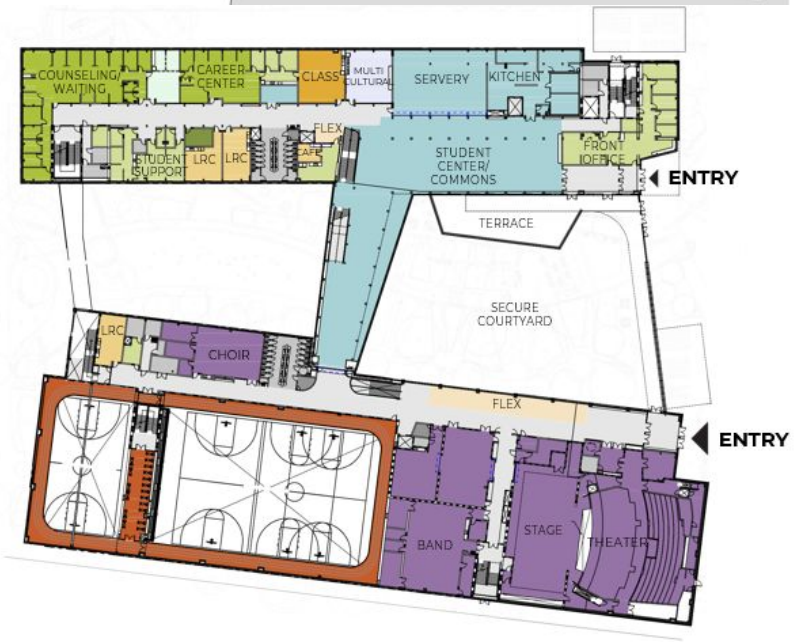


L04


- ADMIN / STUDENT SPACE
- FLEX LEARNING
- SPED + LRC
- GENERAL CLASSROOMS
- CTE
- MISCELLANEOUS
- CUSTODIAL



> Marshall Interior

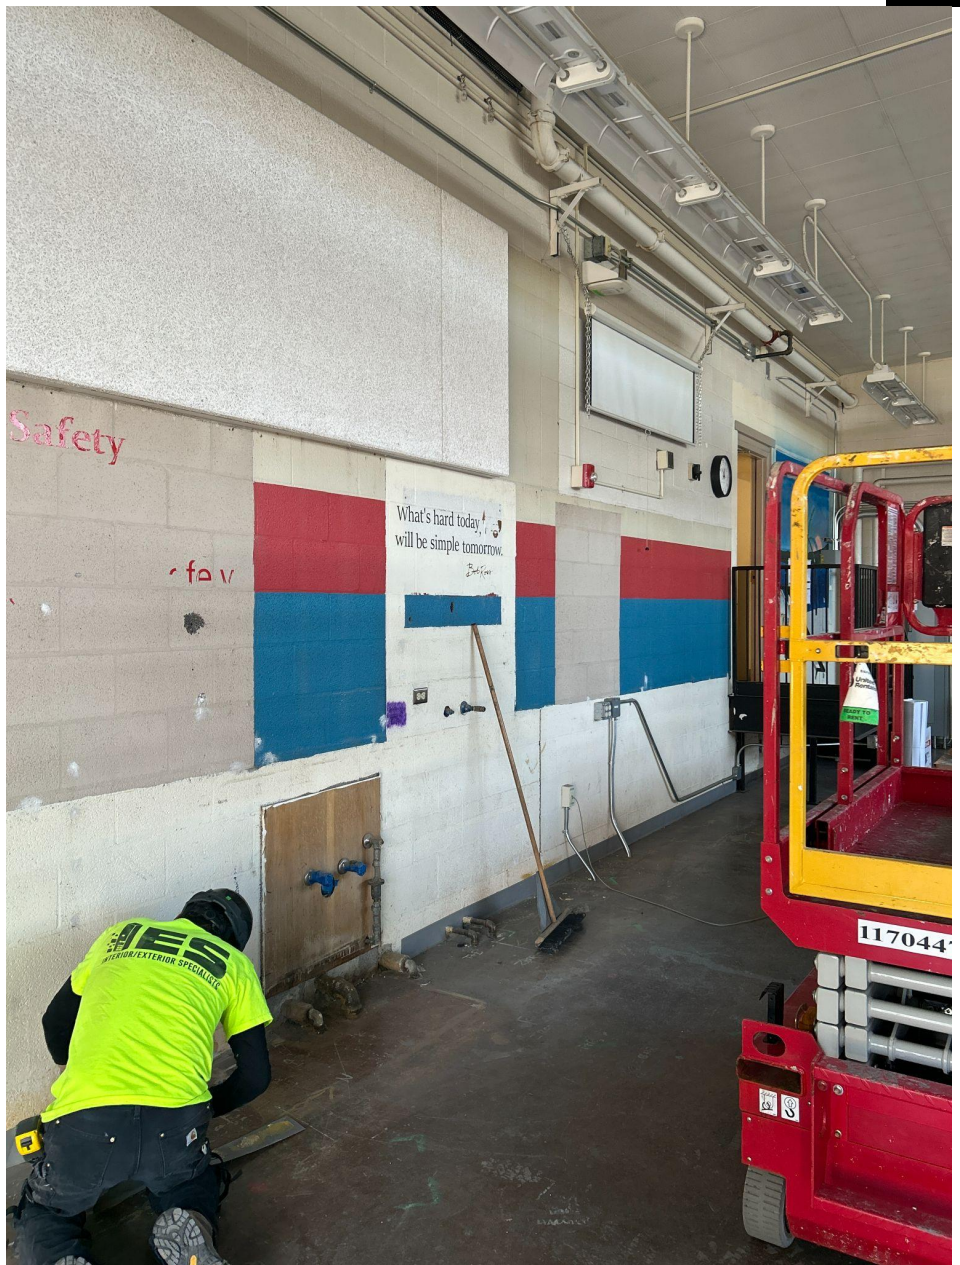

> Marshall Interior

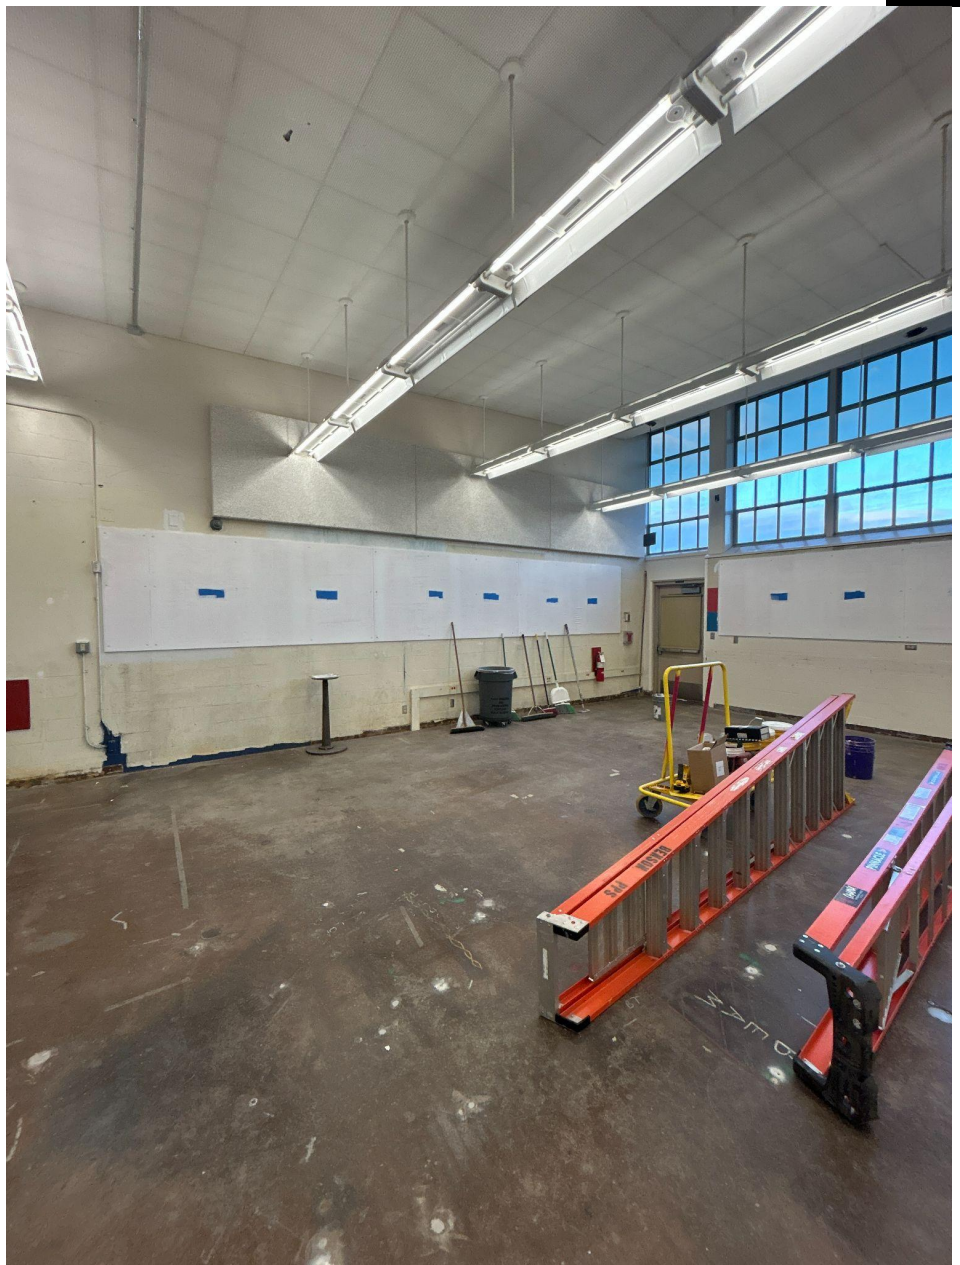

> Marshall Interior



Ida B Wells HS Modernization

1151 SW Vermont St, Portland, OR 97219

Senior CM
Drew Schott

Contractor (CMGC)
Hoffman Construction

PPS Zone 1
Christy Splitt

Architect
BORA Architects

Project Budget

Total Budget	CMGC GMP
$449,350,000	GMP: $TBD

Project Overview

Current Phase: In Design
Scope: New Facility
New Facility: 283,867 SF
Construction Start: Winter 2026
Student Move-In: 29-30 School Yr
Tentative Sub Com: Fall 2030
GMP Construction Timeline: TBD

General Scope

- ✔ New four-story building including instructional spaces for Career Technical Education programs
- ✔ New performing arts, commons, and outdoor spaces
- ✔ Full complement of athletic fields and upgrade of existing fields on the Rieke side
- ✔ The existing pool is not in the scope, but a new pool support building is included

Project Status

Design Procurement
100%

Design
75%

50% CDs In Progress

Construction
0%

Construction NTP
Pending

Project Update


1	Next submittal will be the 50% CD review
2	Coordinating site safety plan with the stakeholders
3	Coordinating with PBOT on planned safe sidewalk closures

Project Floor Plan


See next slide for floor plans

> Floor Plans Levels 0-3


LEVEL 0

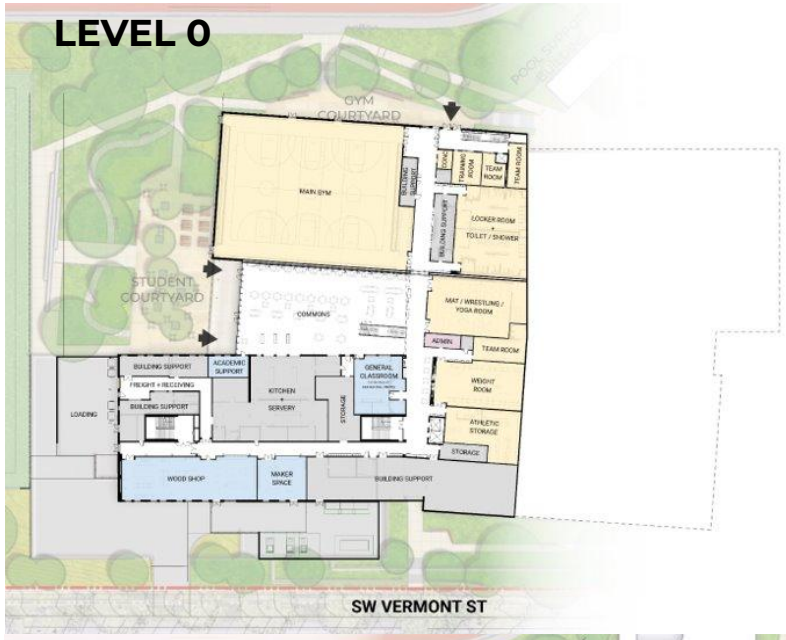

LEVEL 1 (Main Entrance)

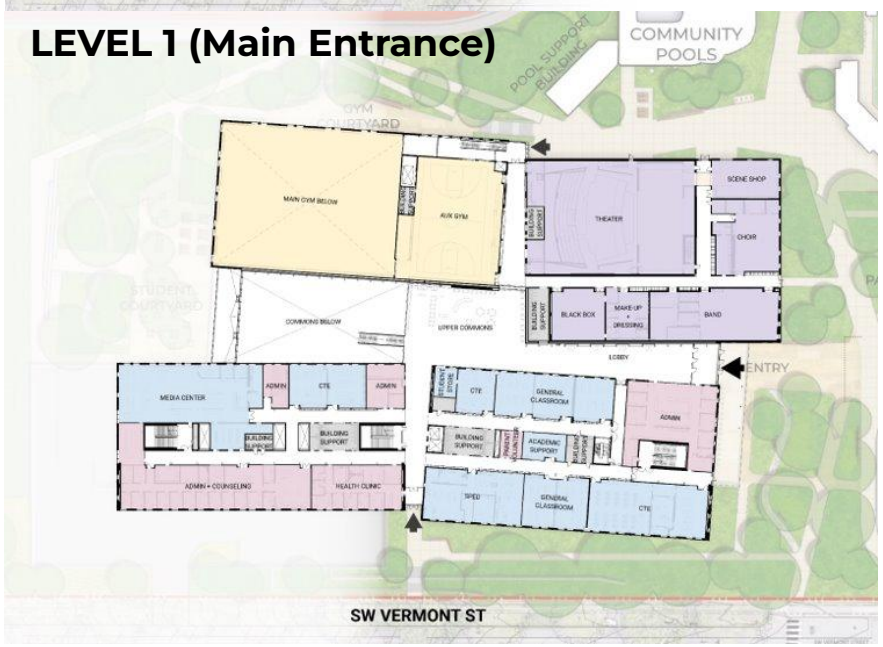

LEVEL 2

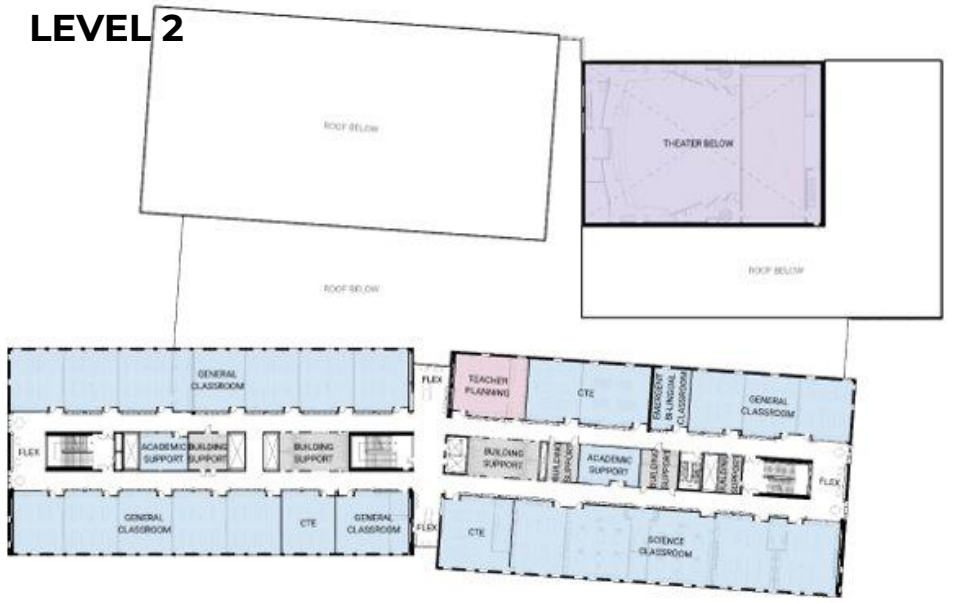

LEVEL 3



Grice-Adair Center for Educational Excellence

1 N. Fremont St, Portland, OR 97227

Senior CM
Drew Schott

Contractor (CMGC)
TBD

Architect
TBD

Project Budget

Total Budget	CMGC GMP
$60,000,000	GMP: $TBD

Project Overview

Current Phase: Planning
Scope: Renovations
Renovations: TBD
Construction Start: TBD
Tentative Sub Com: TBD
GMP Construction Timeline: TBD

General Scope

✔ TBD

Project Status

Design Procurement
100%

Design
0%

Construction
0%


Construction NTP
Pending

Project Update

1	Work is assigned to an AE, Task Order is in progress
2	Program development documents are complete and submitted to AE for proposal
3	Kickoff meeting for programming between PPS and AE is scheduled in June 2026

> Exterior



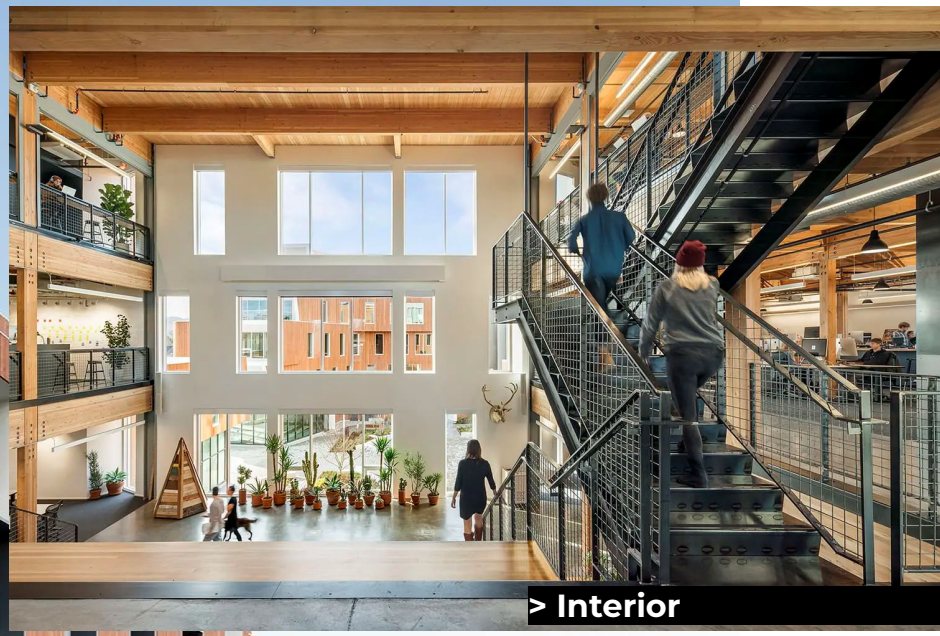

> Interior

Planning

> Courtyard Exterior



Planning

Consolidated Projects - Curriculum

Device Refresh

- New computers for ALL PPS students
- 41,500 devices will be deployed
- Pilot deployments at six schools is complete
- All schools will have newly deployed devices by the beginning of the 26-27 school year

Existing Device Reuse

- Chromebooks currently in circulation will be collected over the summer and will be assessed and graded by our partner vendor (Micro K12).
  - Grading System
    - A grade - will stay with PPS as safety stock
    - B grade - will be donated to other school districts where possible or kept for parts.
    - C grade - will be donated to a local charity such as FreeGeek.

Consolidated Projects - Seismic/Roofing

<u>Summer 2026 Construction</u>

Roofing with Seismic

- Contractor contracts executed for Summer 2026 work
  - Woodmere
  - Cesar Chavez
  - Marshall
  - Vestal

Seismic Parts

- Construction bids received, contracts anticipated to be in front of board in late May
  - Vernon
  - Winterhaven
  - Marysville (Ph 3)

Consolidated Projects - Seismic/Roofing

Anticipated 2027 Construction Start

Seismic Parts and Partial Roof

- Design Contract executed
  - Richmond
  - Capitol Hill

Seismic Parts

- Design Contracts anticipated to be in front of board in May
  - Ainsworth and Kelly

Full Seismic

- Design in progress
  - Beverly Cleary

Anticipated 2028 and 2029 Construction

Seismic Parts and Partial Roof

- Beach

Full Seismic and roof


- Rose City Park
  - Contract expected to be before the Board in May 2026

Consolidated Projects – Facility Improvements

Summer 2026 Construction




- Franklin Condenser Replacement – Anticipated
- Buckman -Dance Studio Truss Replacement, Cafeteria Flooring Replacement
- Boise Elliot – Repaint majority of school
- Capitol Hill – Flooring abatement, subfloor repairs, new flooring
- Jefferson – Stage rigging repairs
- Sitton – Truss repair/replacement
- Rose City Park – Boiler re-tubing
- Vestal – Built-in cafeteria table replacement
- DDC Controls Upgrades - Multiple Sites
- Fire Alarm Upgrades - Multiple Sites

Program Athletics Schedule Update

Athletics Schedule May 2026		2026	2027	2028	2029	2030
1	Grant Bowl Lights					
2	Marshall Hub - Field, Track & Tennis					
3a	Jackson Hub - Phase 1					
3b	Jackson Hub - Phase 2					
All future dates, durations and projections are subject to change						


Design	Procurement	Land Use	Permitting	Construction Phase	Closeout

Program Athletics Schedule Update

Athletics Schedule May 2026		2026	2027	2028	2029	2030
1	Roosevelt					
2	Franklin					
3	West Sylvan					
4	Grant Seating					
All future dates, durations and projections are subject to change						

Design Programming	Procurement	Land Use	Permitting	Construction Phase	Closeout

Program Athletics Schedule Update

Athletics Schedule May 2026		2026	2027	2028	2029	2030
1	Marshall Hub - Upper Field					
2	Powell Park					
3	Jefferson Field					

All future dates, durations and projections are subject to change

Design Programming	Procurement	Land Use	Permitting	Construction Phase	Closeout

Consolidated Projects - Athletics

Grant Bowl Lighting

- Electrical gear installation and Substantial Completion at end of May
- Ribbon Cutting Ceremony planned in June

Jackson Athletic Hub

- Phase 1: Upper Field is nearing design completion with construction anticipated to start in June
  - Track & Field completion Fall 2026
- Phase 2: Design on Multi-Use Field is expected to be complete in July 2026
  - Multi-Use completion Spring 2027

Powell Park Multi-Use Field, Lighting, and Support Buildings

- Continuing discussions with Parks for use agreement

Land Use Application in Progress

- W Sylvan, Franklin, Roosevelt, Grant HS Seating


Grant Bowl Lighting



Consolidated Projects - Athletics

Marshall Athletic Improvements

- Substantially complete, with punch list in progress
  - Targeting availability for first week of June
  - Track
  - Field
  - Tennis Courts
- Gym
  - Targeting availability for use in mid-June
- Weight Room
  - Painting and equipment relocation from Cleveland scheduled for June
  - Targeting availability for use in early July

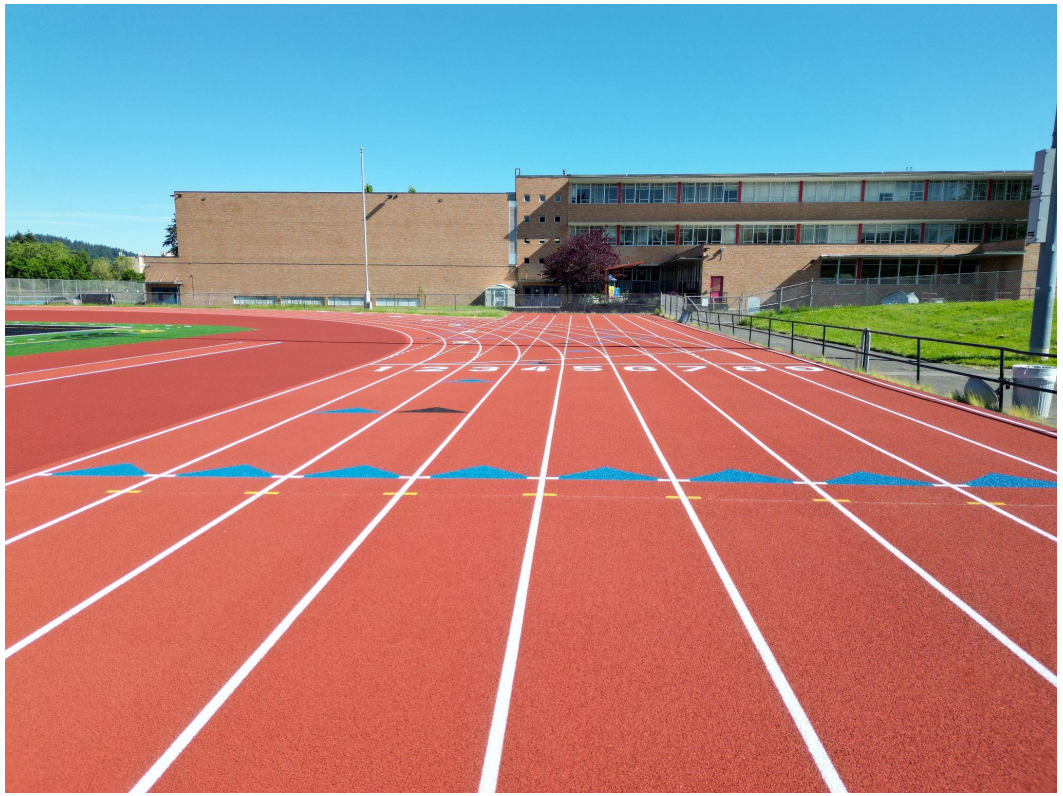


PORTLAND
PORTLAND

PORTLAND
PORTLAND


AND
10
20
9
8
7
6
5
4
3
2
1



Questions
Thank You



Contact us

PPS.NET pubinfo@pps.net (503) 916-2000 501 N Dixion, Portland, OR 97227



PORTLAND
Public Schools
