# Bond Program Update



PORTLAND
Public Schools

June 23, 2026


# Agenda

- Program Statuses
- Schedules
- Program Budget
- Project Updates

# Program Status Update

# 2012 Bond Program Project Status

| Total Projects | Pre-Planning | Design Phase | Construction | Post Construction | Completed |
|---|---|---|---|---|---|
| 33 | 0 | 0 | 2 | 7 | 24 |

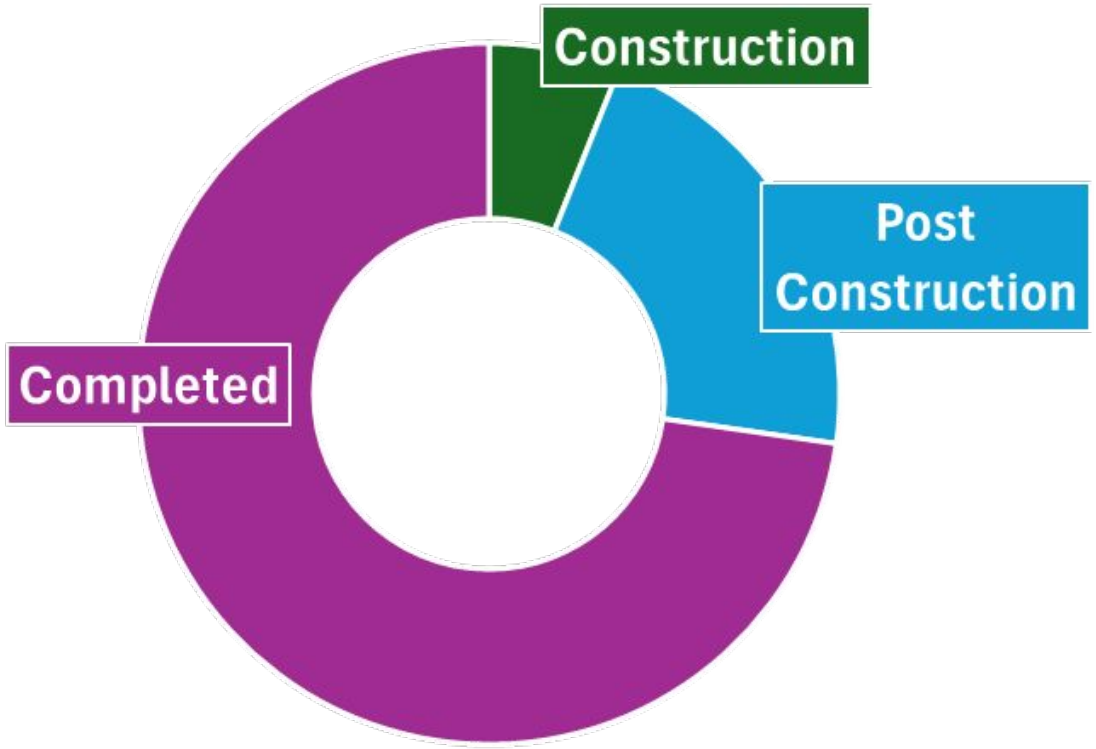



*NOTE: source data: Ebuilder reports by bond measure, sorted by project status.*

*Audit of Project Completion and Closeout statuses is currently ongoing.*

# 2017 Bond Program Project Status

| Total Projects | Pre-Planning | Design Phase | Construction | Post Construction | Completed |
|---|---|---|---|---|---|
| 179 | 3 | 7 | 15 | 50 | 104 |

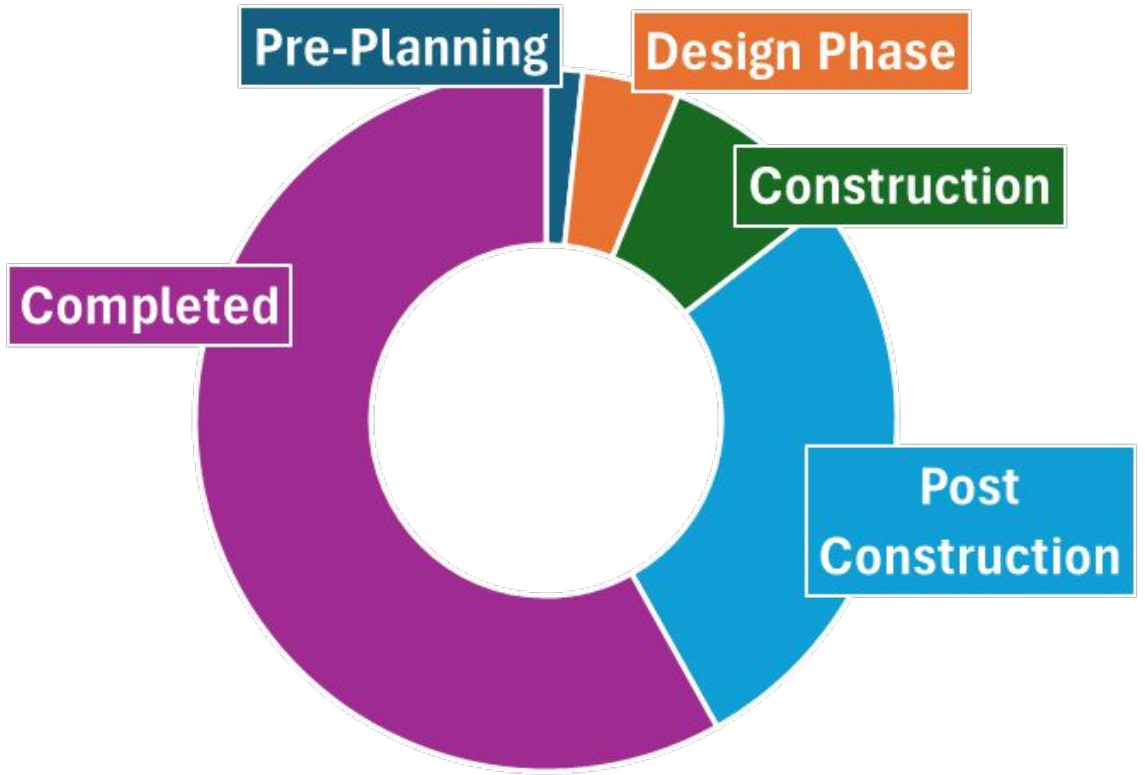



*NOTE: source data: Ebuilder reports by bond measure, sorted by project status.*

*Audit of Project Completion and Closeout statuses is currently ongoing.*

# 2020 Bond Program Project Status

| Total Projects | Pre-Planning | Design Phase | Construction | Post Construction | Completed |
|---|---|---|---|---|---|
| 112* | 2 | 5 | 30 | 31 | 44 |

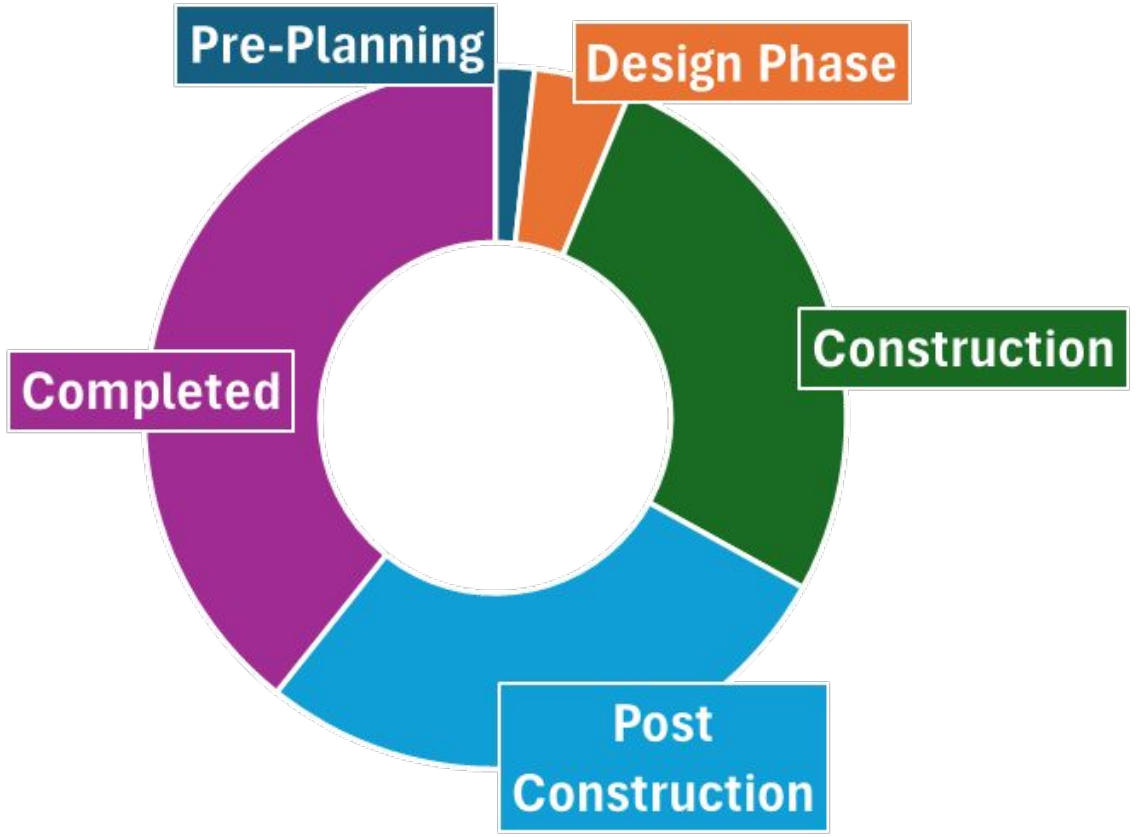



**Approximately $512 M remaining to be scheduled for 2020 Bond.*

*NOTE: source data: Ebuilder reports by bond measure, sorted by project status.*

*Audit of Project Completion and Closeout statuses is currently ongoing.*

# 2025 Bond Program Project Status


| Total Projects | Pre-Planning | Design Phase | Construction | Post Construction | Completed |
|---|---|---|---|---|---|
| 22* | 12 | 5 | 2 | 3 | 0 |

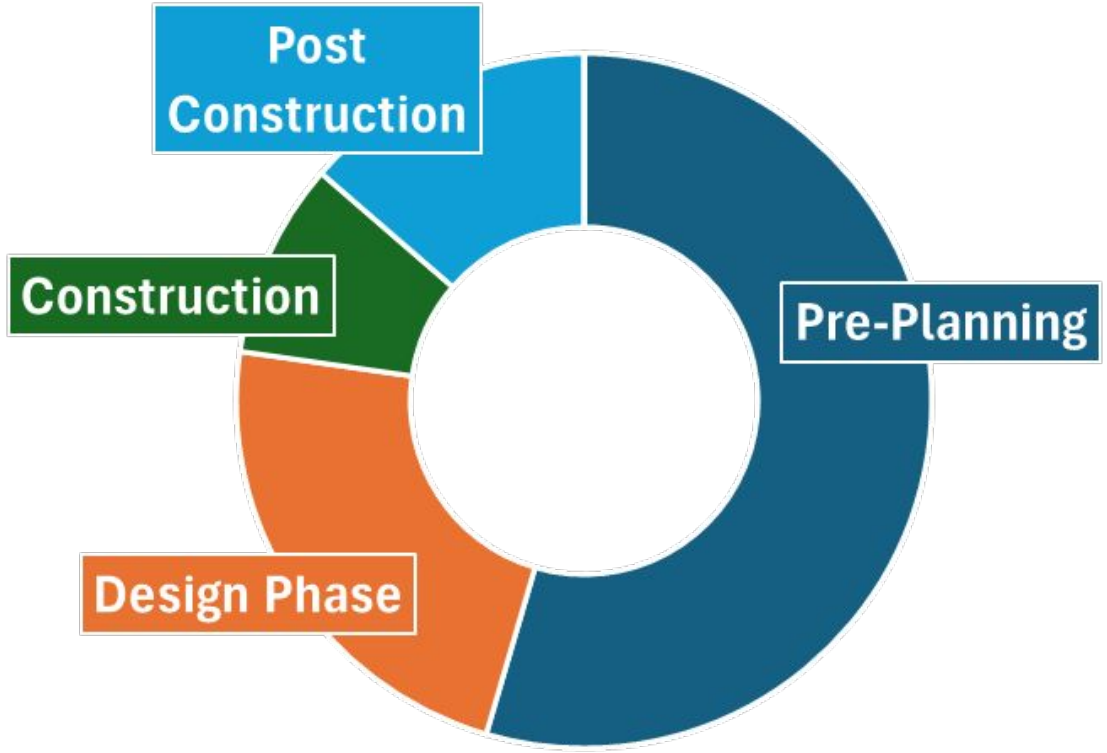



** Total projects will increase as the program progresses.*

# Schedule and Budget Update


# Program Schedule Update

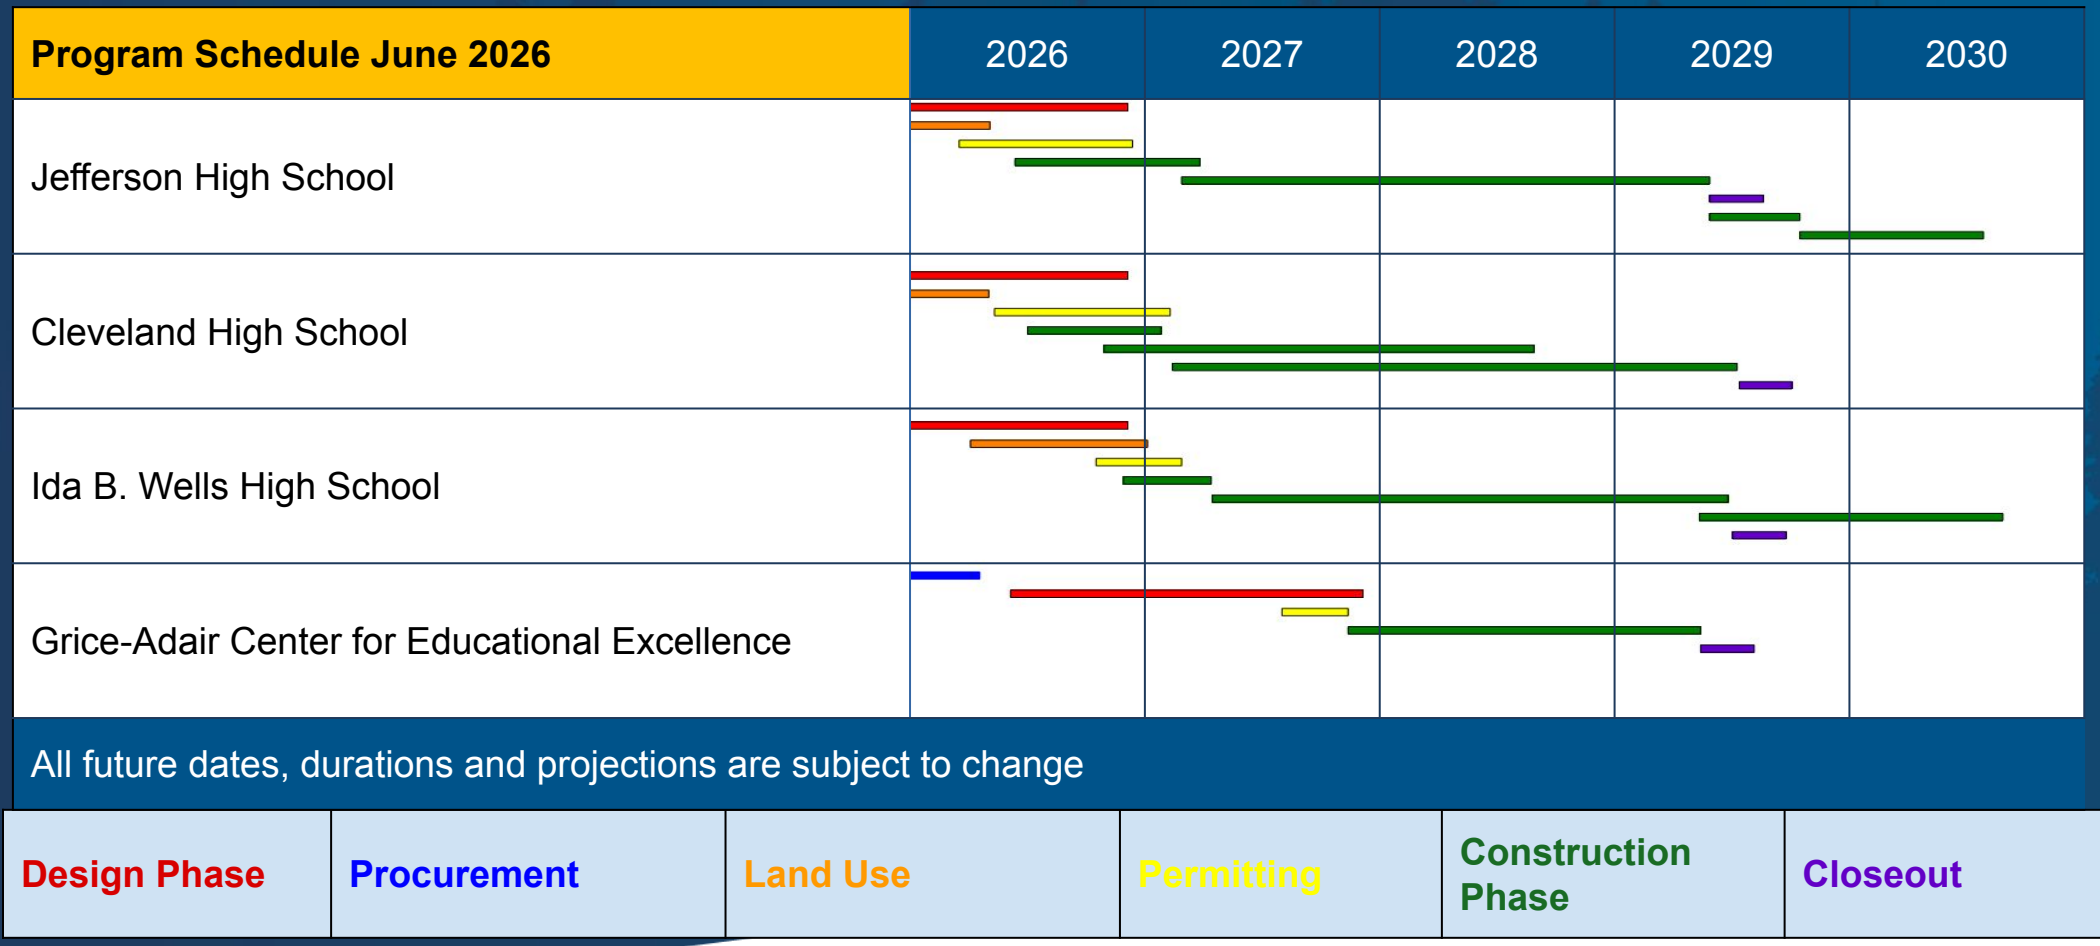


# JHS Overall Project Schedule

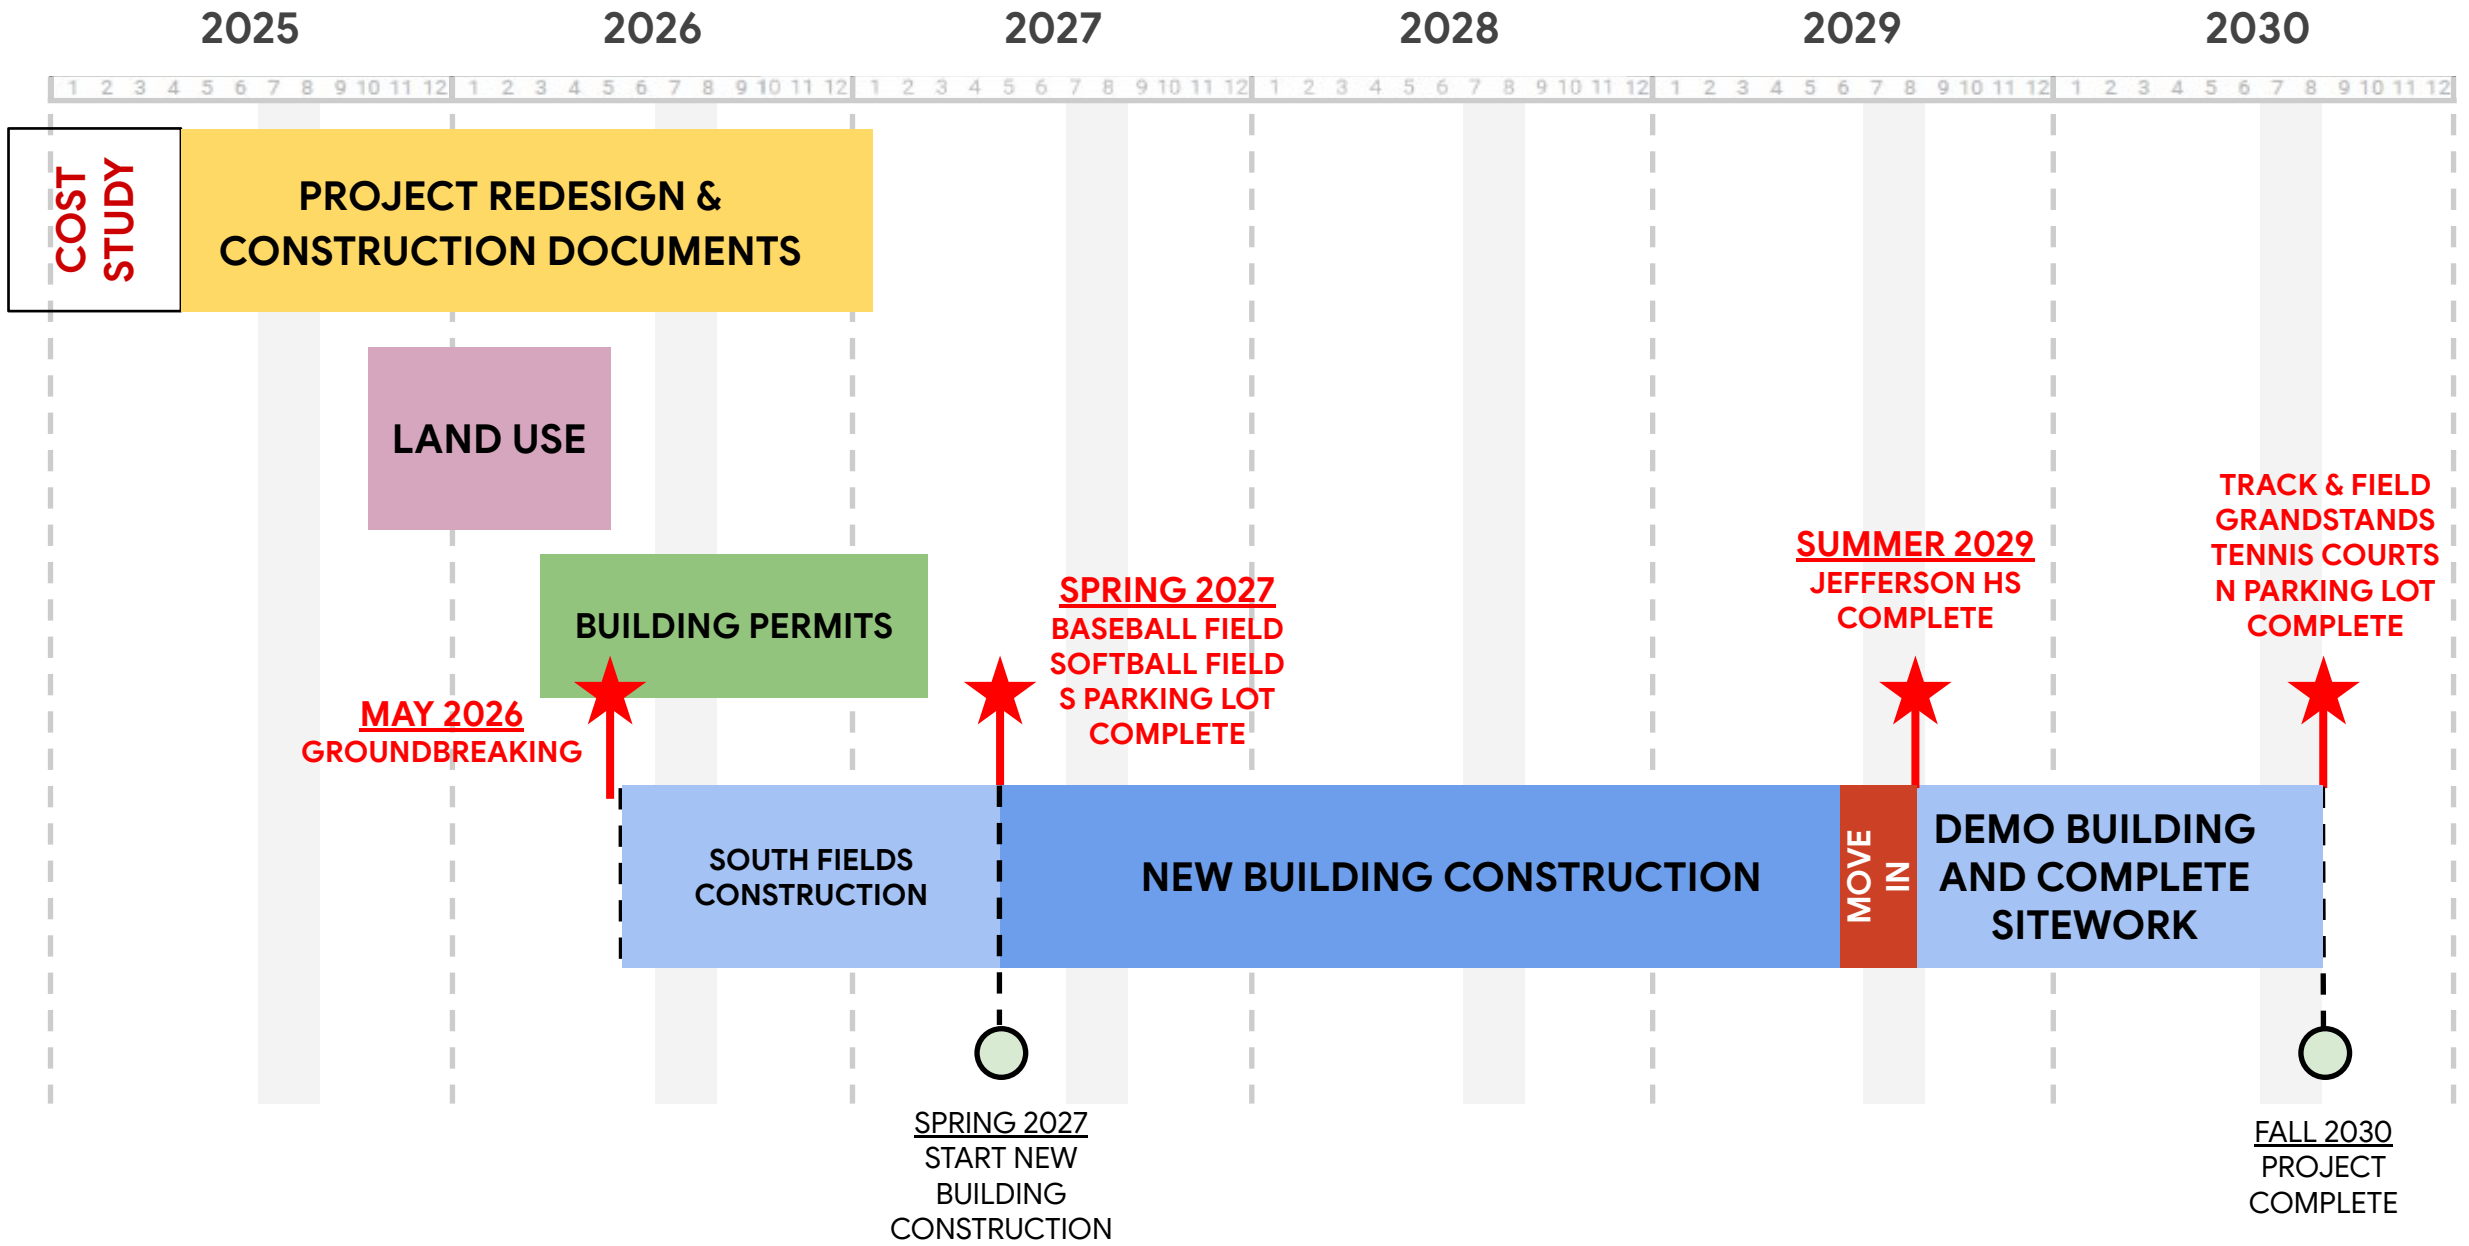

# CHS Overall Project Schedule

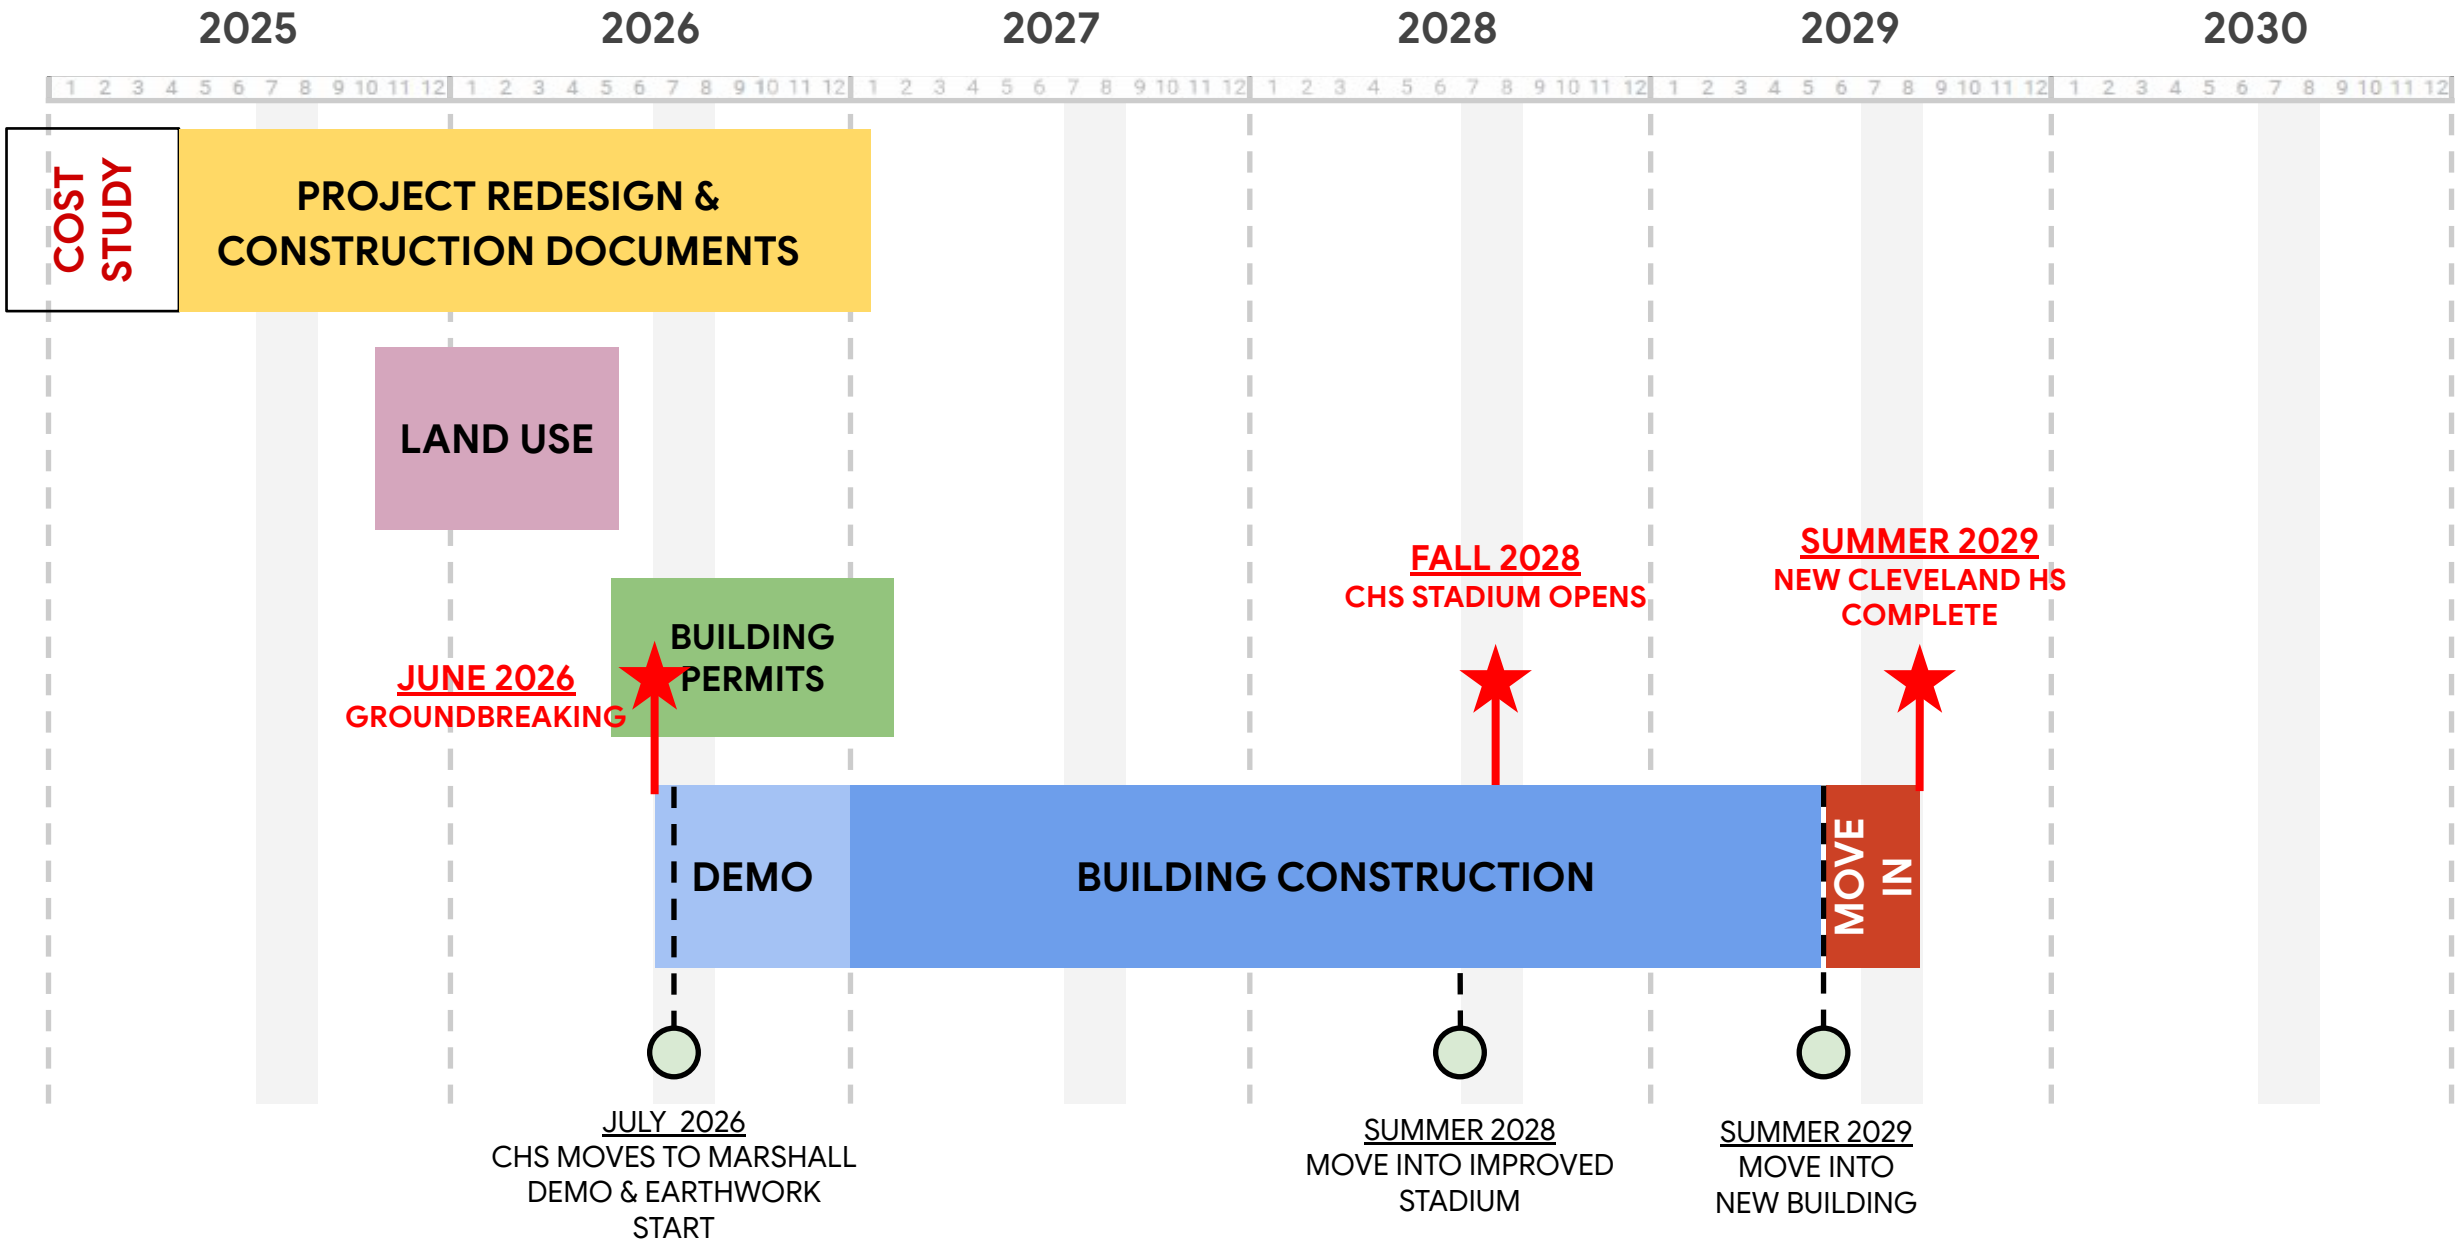

# IBW Overall Project Schedule

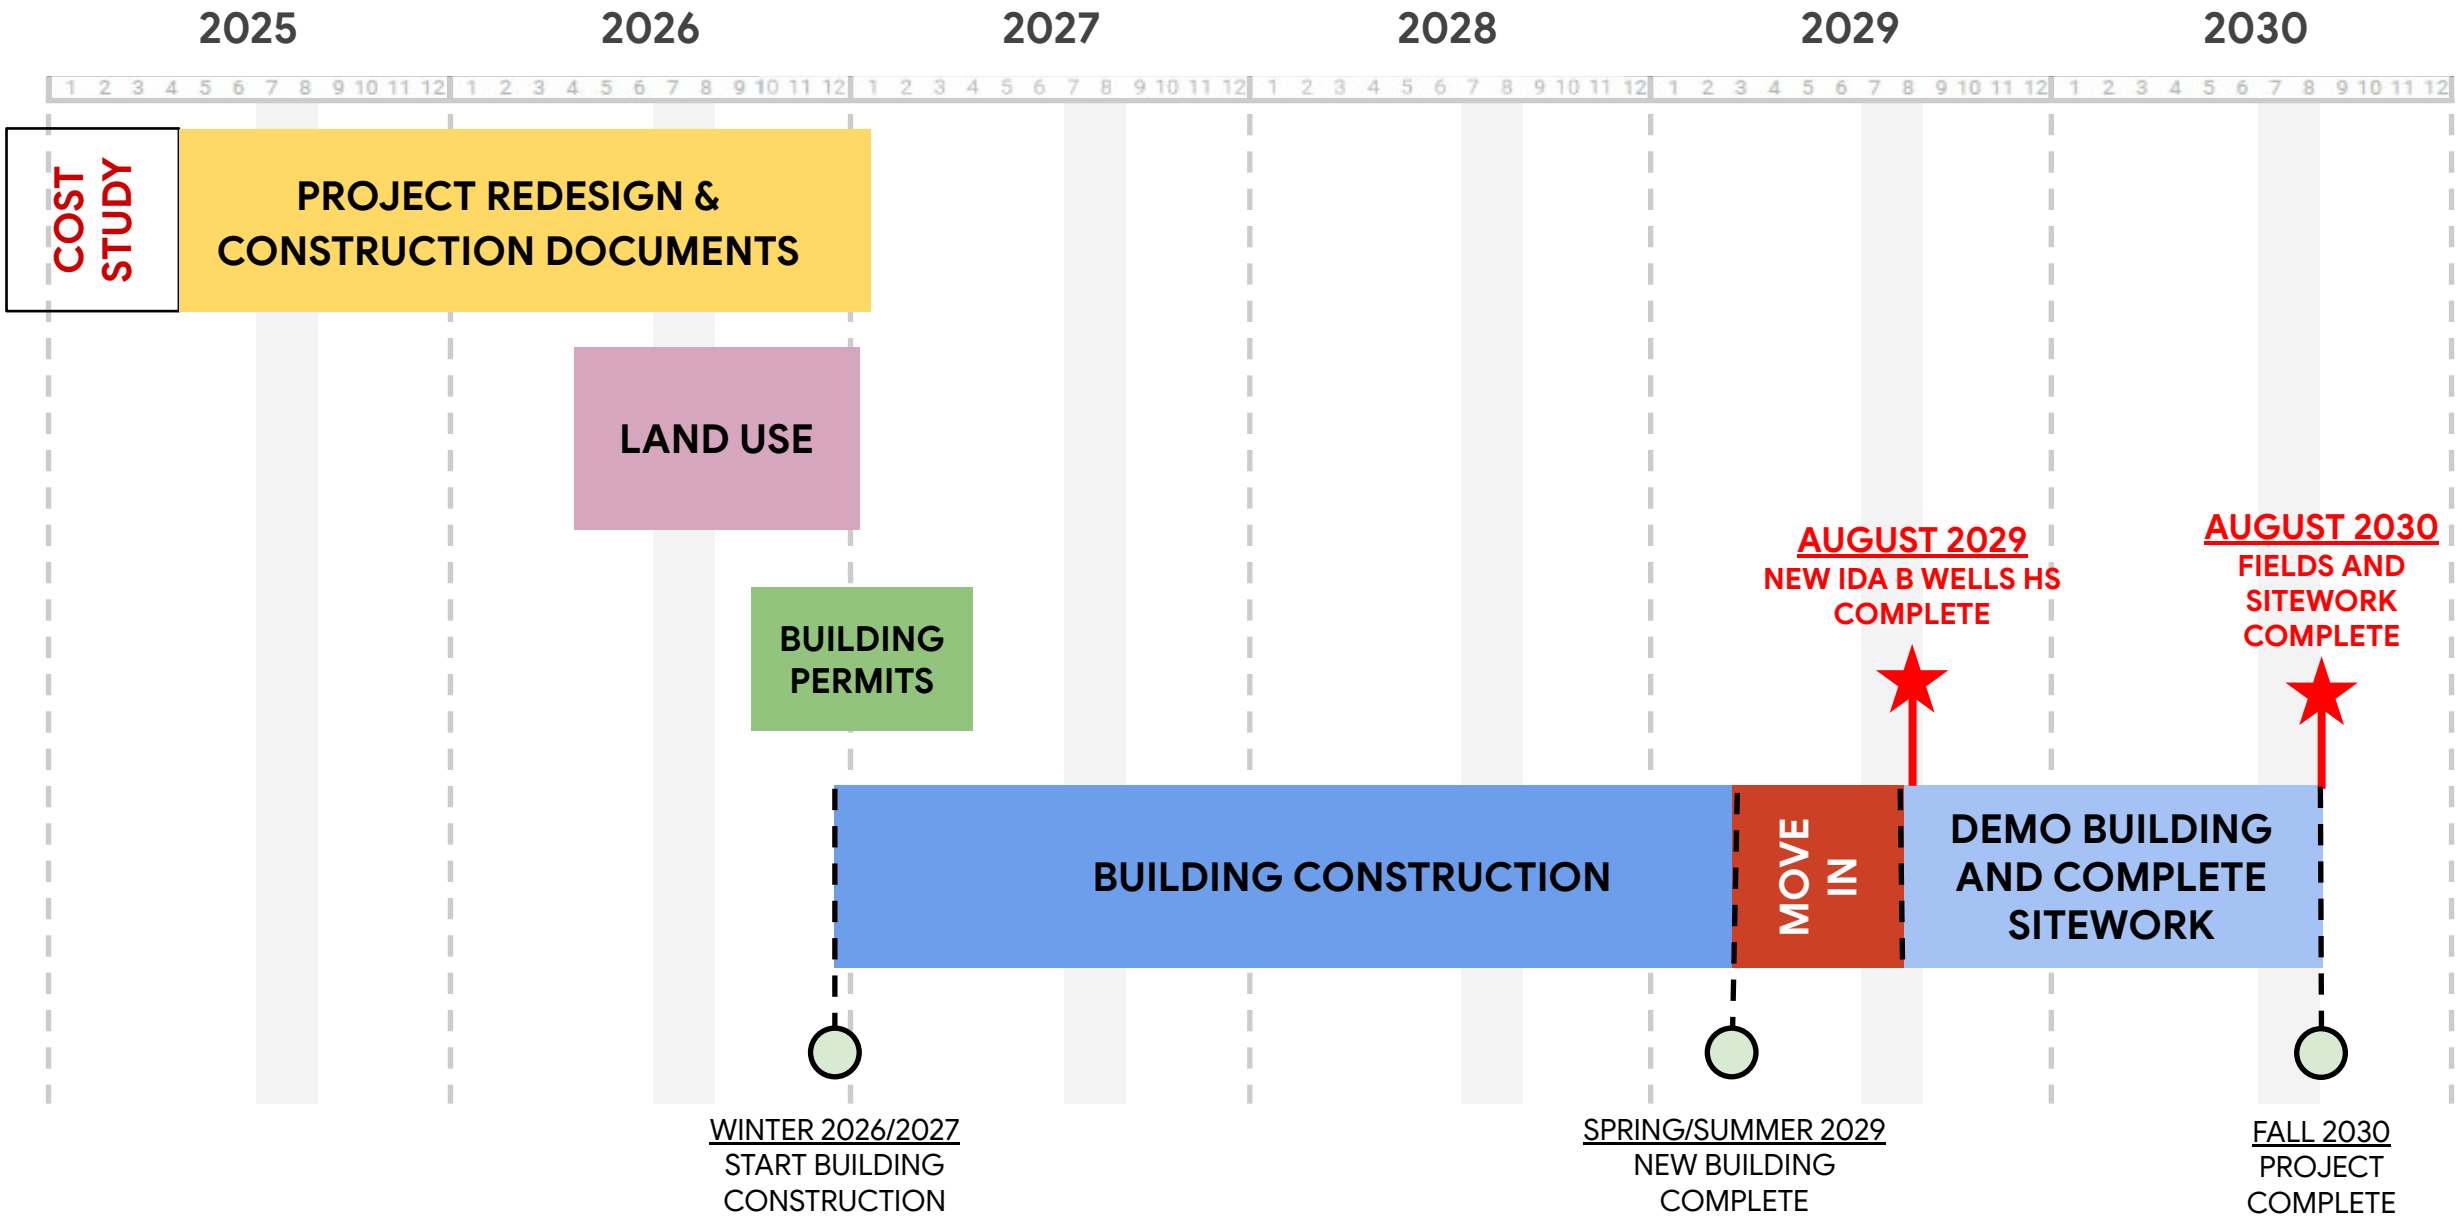

# PORTLAND PUBLIC SCHOOLS

**Bond Program Dashboard**


| Data Source | Report Name | Date Exported |
|---|---|---|
| eBuilder | 0-PIVOT TABLE - FUNDING - SLS 06.01.2026 07 00 12 AM.xls | 6/1/2026 4:30: |
| eBuilder | BAC Data Project Management Cost 06.01.2026 07 17 44 AM (1).xls | 6/1/2026 4:30: |
| eBuilder | Commitment Funding Items 06.01.2026 07 12 31 AM (1).xls | 6/1/2026 4:30: |
| eBuilder | PS Reconcile Export 06.01.2026 06 38 43 AM.xls | 6/1/2026 4:30: |

Bond Measure


Deselect all | 2012 Bond | 2017 Bond | 2020 Bond | 2025 Bond

| Total Funds | Spent to Date | Outstd. Encumbrance | Available Funds | Percent Available |
|---|---|---|---|---|
| 4.6bn | 2.1bn | 228.9M | 2.3bn | 49% |

## Spent to Date and Total Funds

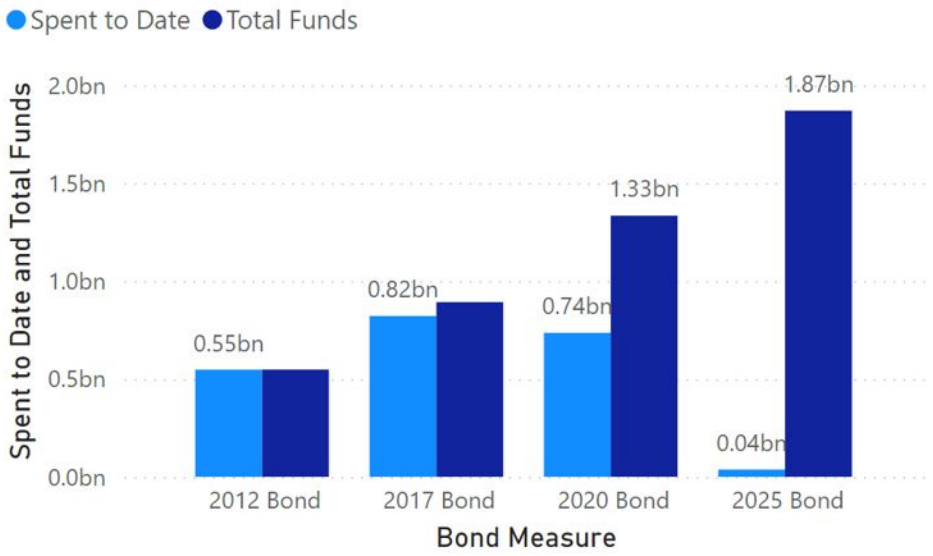


## Spent and Encumbered

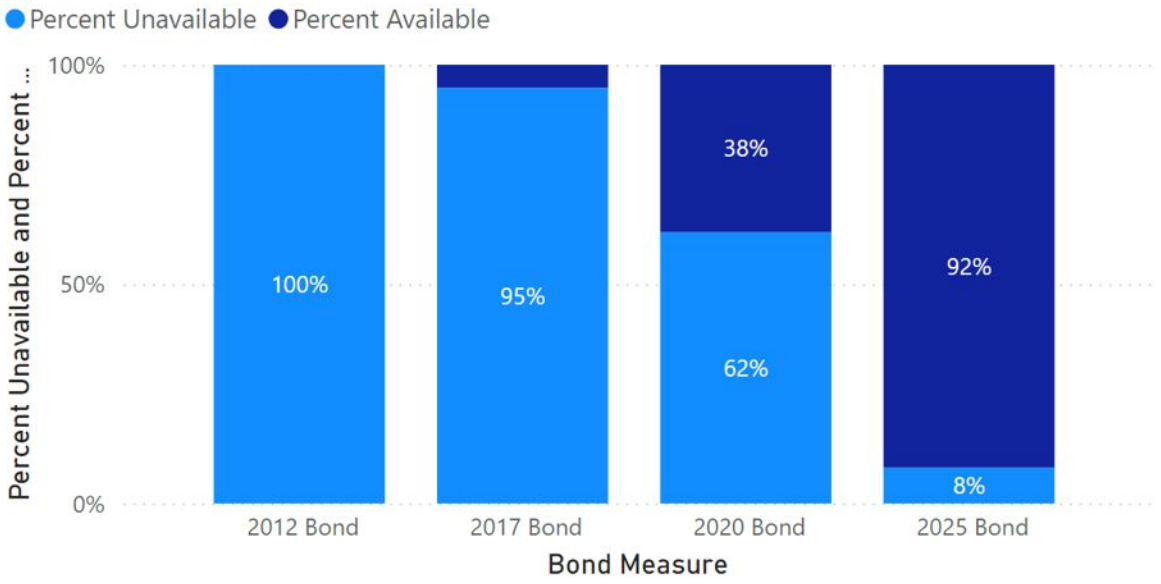

# 2012 Bond Program Status – Budget Update - Overview

**Modernizations:** Franklin HS, Grant HS, Roosevelt HS, and Faubion PK-8
**Middle School Science Upgrades**
**Consolidated Projects:** Accessibility, Seismic

| Project | Budget | Outstanding Encumbrance | Amount Paid to Date | Remaining Balance |
|---|---|---|---|---|
| Franklin HS Mod | $110,950,414 | $0 | $110,950,414 | $0 |
| Grant HS Mod | $155,300,188 | $0 | $155,300,188 | $0 |
| Roosevelt HS Mod | $97,128,043 | $0 | $97,128,043 | $0 |
| Faubion Replace | $30,653,663 | $0 | $30,653,663 | $0 |
| Grant Upper Field | $3,170,988 | $0 | $3,170,988 | $0 |
| RHS Phase IV | $6,153,741 | $0 | $6,153,741 | $0 |
| Other Projects | $112,740,428 | $8,100 | $112,710,428 | $21,900 |
| Grant & Franklin Add Ons | $367,663 | $92,879 | $72,164 | $202,620 |
| Administration | $31,284,018 | $0 | $31,284,018 | $0 |
| Contingency | $83,104 | $0 | -$902 | $84,006 |
| **PPS 2012 Bond Program Total** | **$547,832,249** | **$100,979** | **$547,422,744** | **$308,526** |






*as of 6/1/26

# 2017 Bond Program Status – Budget Update - Overview

**Modernizations:** Benson Polytechnic, Lincoln, McDaniel, Kellogg Middle School and Multiple Pathways to Graduation

**Consolidated Projects:** Water Quality, Security Upgrades, New Roofs, Asbestos Abatement, Radon Remediation, Lead Paint Stabilization, Life Safety Upgrades, Accessibility, Seismic

| Project | Budget | Outstanding Encumbrance | Amount Paid to Date | Remaining balance |
|---|---|---|---|---|
| Benson HS Mod | $146,614,560 | $158,943 | $143,508,637 | $2,946,980 |
| Benson Add Ons | $2,865,020 | $417,585 | $1,092,198 | $1,355,237 |
| Benson Swings | $12,199,595 | $0 | $12,199,595 | $0 |
| Lincoln HS Repl | $240,836,448 | $28,738 | $224,096,580 | $16,711,130 |
| Kellogg MS Replace | $57,648,703 | $0 | $57,648,703 | $0 |
| McDaniel Mod | $197,000,000 | $39,657 | $196,817,745 | $142,598 |
| Health & Safety | $169,256,030 | $23,133,634 | $122,993,632 | $23,128,764 |
| Athletics | $4,895,489 | $174,034 | $2,278,729 | $2,442,726 |
| Administration | $61,087,401 | $203,184 | $60,873,810 | $10,407 |
| Contingency | $42,039 | $0 | $0 | $42,039 |
| **PPS 2017 Bond Program Total** | **$892,445,285** | **$24,155,774** | **$821,509,629** | **$46,779,882** |







*as of 6/1/26

# 2020 Bond Program Status – Budget Update - Overview

**Modernizations:** Jefferson HS, Pre-Planning/Design Ida B Wells and Cleveland HS, Grice-Adair Center for Educational Excellence, Roosevelt (added capacity), and Benson

**Consolidated Projects:** Curriculum Materials, New Technology for classroom and distance learning, Health & Safety, Seismic, Security, Re-Roofing

| Project | Budget Managed by PROCEDEO | Budget Managed by PPS | Outstanding Encumbrance | Amount Paid to Date | Remaining Balance |
|---|---|---|---|---|---|
| Benson 2020 Funds | | $164,903,890 | $640,328 | $162,803,433 | $1,460,129 |
| Jefferson HS Mod | $366,007,500 | | $38,429,302 | $30,053,013 | $297,525,185 |
| Jefferson Add Ons | $152,175 | | $149,945 | $250 | $1,980 |
| CEE | $60,000,000 | | $34,238 | $16,222,680 | $43,743,082 |
| Cleveland HS – Design | $23,679,515 | | $8,412,380 | $15,270,600 | -$3,465 |
| Cleveland Swing Site | $137,500 | | $1,800 | $105,905 | $29,795 |
| Wells HS – Design | $20,000,000 | | $2,404,163 | $17,584,080 | $11,757 |
| Roosevelt PhV – Design | | $2,000,000 | $1,035 | $97,625 | $1,901,340 |
| MPG Building | | $80,447,075 | $267,192 | $77,947,593 | $2,232,290 |
| Curriculum | | $63,319,191 | $1,255,550 | $54,617,744 | $7,445,897 |
| Technology | | $136,100,000 | $16,660,493 | $91,534,529 | $27,904,978 |
| Infra Projects | | $268,153,105 | $19,787,893 | $235,023,435 | $13,341,777 |
| Administration | | $51,706,045 | $1,239,513 | $34,440,015 | $16,026,517 |
| 2017 Bond Balance | | $0 | $0 | $0 | $0 |
| Contingency – OSM | | $79,451,387 | $0 | $0 | $79,451,387 |
| Unallocated Funds | | $17,649,899 | $0 | $0 | $17,649,899 |
| **PPS 2020 Bond Program Total** | **$469,976,690** | **$863,730,592** | **$89,283,832** | **$735,700,902** | **$508,722,548** |

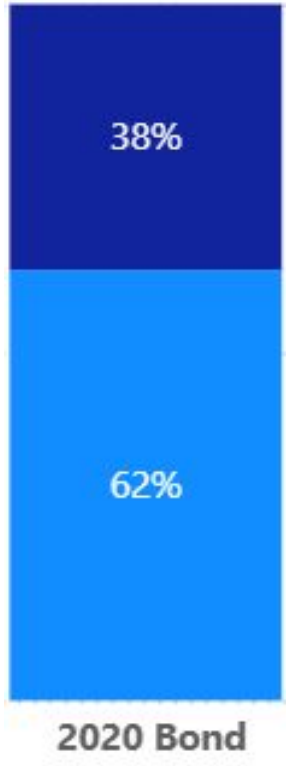




*as of 6/1/26

# 2025 Bond Program Status – Budget Update - Overview

**Modernizations:** Cleveland HS, Ida B Wells HS, and Jefferson

**Consolidated Projects:** Security Upgrades, Seismic, Technology, Improvements for Roosevelt, Lincoln, Franklin, and Grant, and New Athletic Hub Facilities at Jackson MS and Marshall Campuses

| Project | Budget Managed by PROCEDEO | Budget Managed by PPS | Outstanding Encumbrance | Amount Paid to Date | Remaining Balance |
|---|---|---|---|---|---|
| Priority Scope | | $190,000,000 | $10,622,793 | $344,233 | $179,032,974 |
| Athletics | | $79,000,000 | $1,347,024 | $2,047,435 | $75,605,541 |
| Technology | | $176,000,000 | $3,916,460 | $26,452,579 | $145,630,961 |
| Physical Education | | $10,000,000 | $0 | $0 | $10,000,000 |
| Curriculum | | $56,000,000 | $0 | $0 | $56,000,000 |
| Jefferson HS Modernization | $100,000,000 | | $0 | $0 | $100,000,000 |
| Cleveland HS Modernization | $448,911,745 | | $12,273,030 | $393,615 | $436,245,100 |
| Ida B Wells HS Modernization | $429,350,000 | | $29,359,062 | $507,760 | $399,483,178 |
| Elementary & Middle Schools | | $171,738,255 | $0 | $0 | $171,738,255 |
| Admin | | $83,050,000 | $57,898,825 | $7,570,008 | $17,581,167 |
| Contingency | | $125,956,806 | $0 | $0 | $125,956,806 |
| **PPS 2025 Bond Program Total** | **$978,261,745** | **$891,745,061** | **$115,417,194** | **$37,315,630** | **$1,717,273,982** |






*as of 6/1/26

# Project Updates

# Jefferson HS Modernization

5210 N Kerby Ave, Portland, OR 97217

**PPS PM**
Steve Effros

**Contractor (CMGC)**
Colas Hoffman

**PPS Zone 2**
Michelle DePass

**Architect**
BORA & LEVER

## Project Budget

| Total Budget | CMGC GMP |
|---|---|
| $466,007,500 | GMP: $TBD |

## Project Overview

**Current Phase:** In Construction
**Scope:** New Facility
**New Facility:** 299,485 SF
**Construction Start:** Spring 2026
**Student Move-In:** 29-30 School Yr
**Tentative Sub Com:** Fall 2030
**GMP Construction Timeline:** TBD

## General Scope

- ✔ New all-electric multi-story building
- ✔ Includes a theater, health center, teen parent center, and dance studios
- ✔ Track and field relocated to the site of the current structure
- ✔ New softball field and baseball/soccer multiuse field

## Project Status

**Design Procurement**
100%

**Design**
75%
**50% CDs In Progress**

**Construction**
0%
**Construction NTP**
6/15/26

## Project Update

| | |
|---|---|
| 1 | Agreement finalized with Pacific Power to bring new service to all-electric building |
| 2 | Construction staging underway for softball and baseball fields |
| 3 | Construction Impact meeting for neighbors/community on Saturday June 6th |

## > JHS Groundbreaking



# > JHS Groundbreaking



## > JHS Groundbreaking



## > JHS Groundbreaking



# Cleveland HS Modernization

3400 SE 26th Ave, Portland, OR 97202

**PPS PM**
Erik Gerding

**Contractor (CMGC)**
Skanska

**PPS Zone 6**
Stephanie Engelsman

**Architect**
Mahlum

## Project Budget

| Total Budget | CMGC GMP |
|---|---|
| $472,553,760 | GMP: TBD |

## Project Overview

**Current Phase:** In Construction
**Scope:** New Facility
**New Facility:** 297,000 SF
**Construction Start:** Summer 2026
**Student Move-In:** 29-30 School Yr
**Tentative Sub Com:** Summer 2029
**GMP Construction Timeline:** TBD

## General Scope

- ✔ 2 new four-story buildings connected by a skybridge
- ✔ Dynamic outdoor courtyard
- ✔ New arts theater, black box theater, 2 gyms, and dance and wrestling studios
- ✔ Improvements to track and athletic fields

## Project Status

**Design Procurement**
100%

**Design**
80%

**50% CDs In Review**

**Construction**
2%

**Construction**
Marshall Swing Start - 3/30/26
Demo Start - 7/7/26

## Project Update

| | |
|---|---|
| 1 | Moving to Marshall this month |
| 2 | Skanska beginning abatement and demo on 7/6 |
| 3 | Construction Impact meeting for neighbors/community on Thursday June 11th |



PROCEDEO | PORTLAND Public Schools

## > CHS Groundbreaking



## > CHS Groundbreaking




## > CHS Groundbreaking




## > Marshall Exterior



## > Marshall Interior

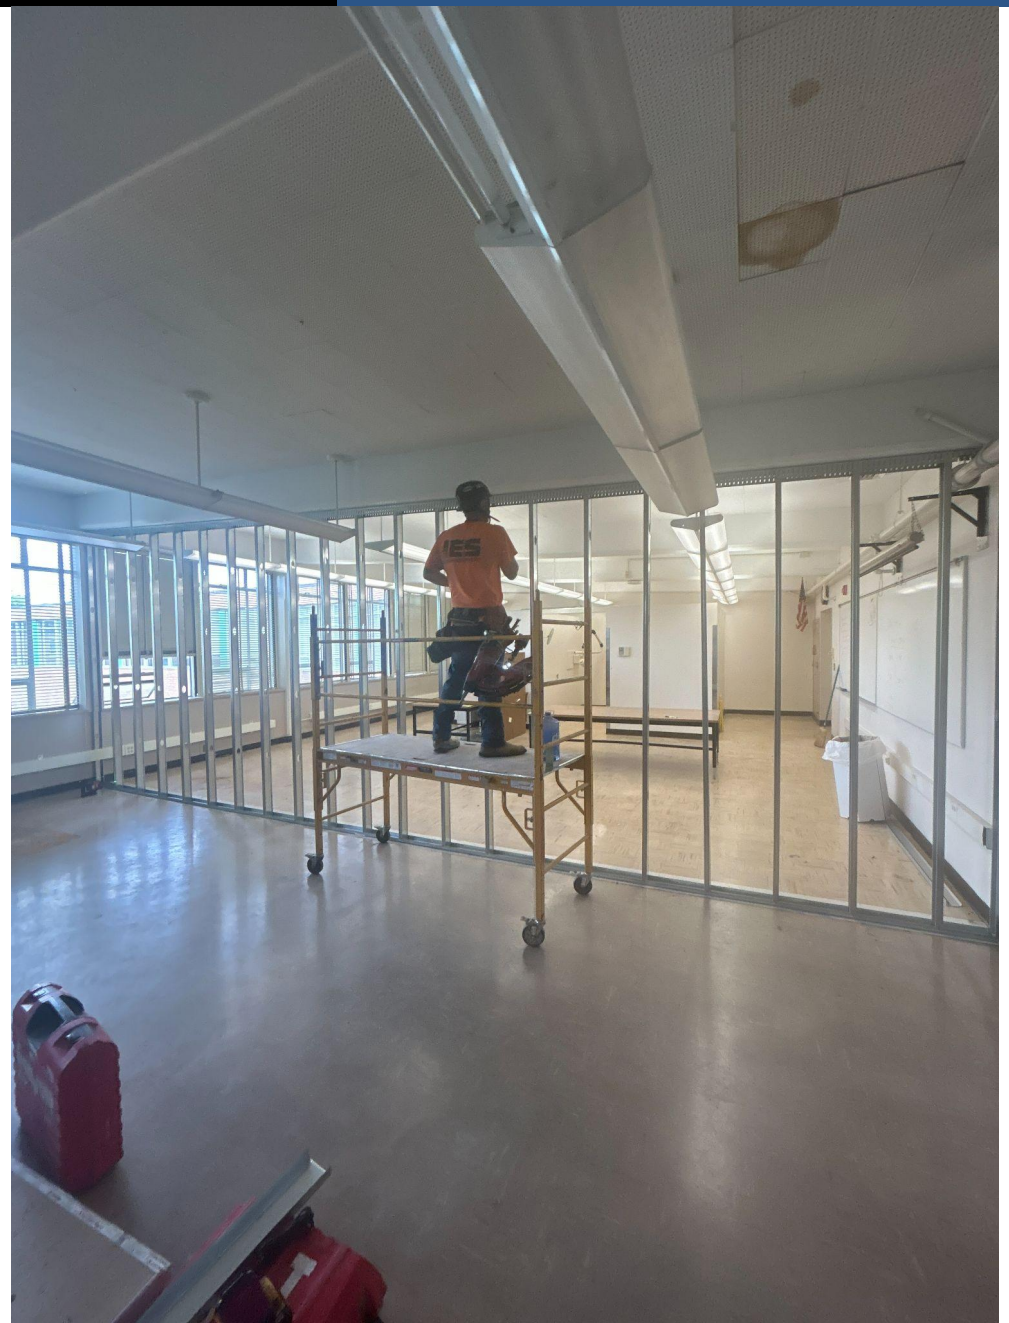

## > Marshall Interior

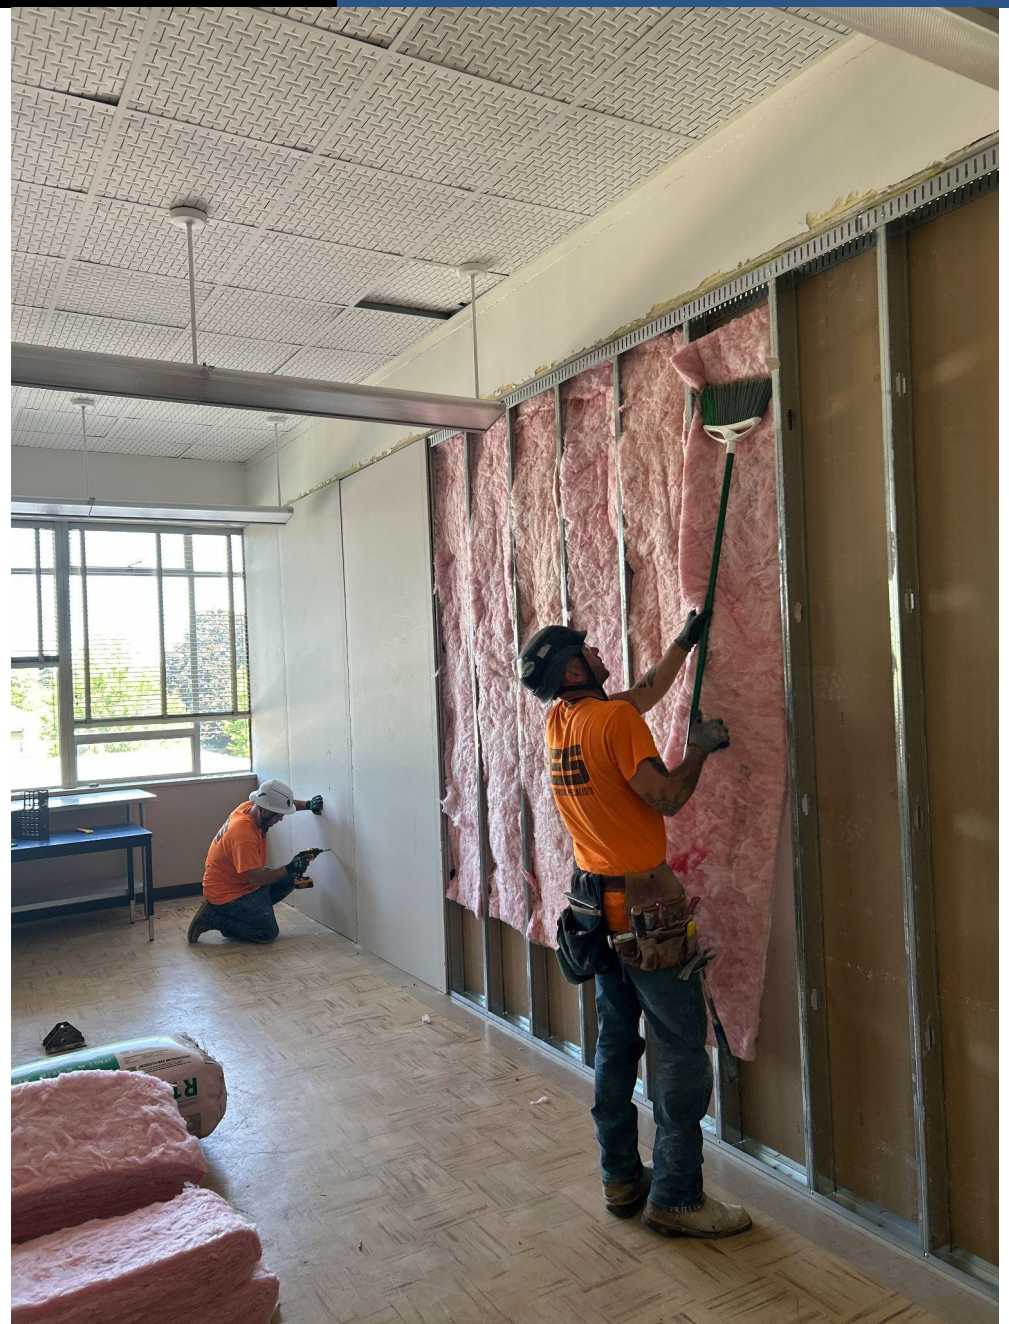

# Ida B Wells HS Modernization

1151 SW Vermont St, Portland, OR 97219

**PROCEDEO PM**
Gabe Asch

**Contractor (CMGC)**
Hoffman Construction

**PPS Zone 1**
Christy Splitt

**Architect**
BORA Architects

## Project Budget

| Total Budget | CMGC GMP |
|---|---|
| $449,350,000 | GMP: $TBD |

## Project Overview

**Current Phase:** In Design
**Scope:** New Facility
**New Facility:** 283,867 SF
**Construction Start:** Winter 2026
**Student Move-In:** 29-30 School Yr
**Tentative Sub Com:** Fall 2030
**GMP Construction Timeline:** TBD

## General Scope

- ✔ New four-story building including instructional spaces for Career Technical Education programs
- ✔ New performing arts, commons, and outdoor spaces
- ✔ Full complement of athletic fields and upgrade of existing fields on the Rieke side
- ✔ The existing pool is not in the scope, but a new pool support building is included

## Project Status

**Design Procurement**
100%

**Design**
75%

**50% CDs In Progress**

**Construction**
0%

**Construction NTP**
Pending

## Project Update

| | |
|---|---|
| 1 | 50% CD submittal due August 10, 2026 |
| 2 | Conditional Use hearing set for July 22, 2026 |
| 3 | Stakeholder engagement continues |

# Grice-Adair Center for Educational Excellence

1 N. Fremont St, Portland, OR 97227

**PROCEDEO PM**
Khalil Rivera

**Contractor (CMGC)**
TBD

**Architect**
DLR

## Project Budget

| Total Budget | CMGC GMP |
|---|---|
| $60,000,000 | GMP: $TBD |

## Project Overview

**Current Phase:** Planning
**Scope:** Renovations
**Renovations:** TBD
**Construction Start:** TBD
**Tentative Sub Com:** TBD
**GMP Construction Timeline:** TBD

## General Scope

✔ TBD

## Project Status

**Design Procurement**
100%

**Design**
0%

**Design NTP**
6/12/26

**Construction**
0%

## Project Update

| | |
|---|---|
| 1 | DLR has been brought on as the Architect |
| 2 | Site walks are underway |
| 3 | Kickoff meeting for programming occurred on 5/28 |



PROCEDEO | PORTLAND Public Schools

## > Grice-Adair Ste 400



## > Grice-Adair Ste 400



# Consolidated Projects

- There have been no significant changes to the Consolidated projects since the last presentation
- Our project teams are finalizing schedules and materials for this summer's projects
- Continuing land use preparation for athletic fields

# Questions
# Thank You



# Contact us

PPS.NET pubinfo@pps.net (503) 916-2000 501 N Dixion, Portland, OR 97227



PORTLAND
Public Schools
