Bond Program Update



PORTLAND
Public Schools

September 15, 2026


Agenda

- Program Status
- Schedule
- Program Budgets
- Project Updates

Program Status Update

2012 Bond Program Project Status

Total Projects	Pre-Planning	Design Phase	Construction	Post Construction	Completed
34	1	1	1	1	31

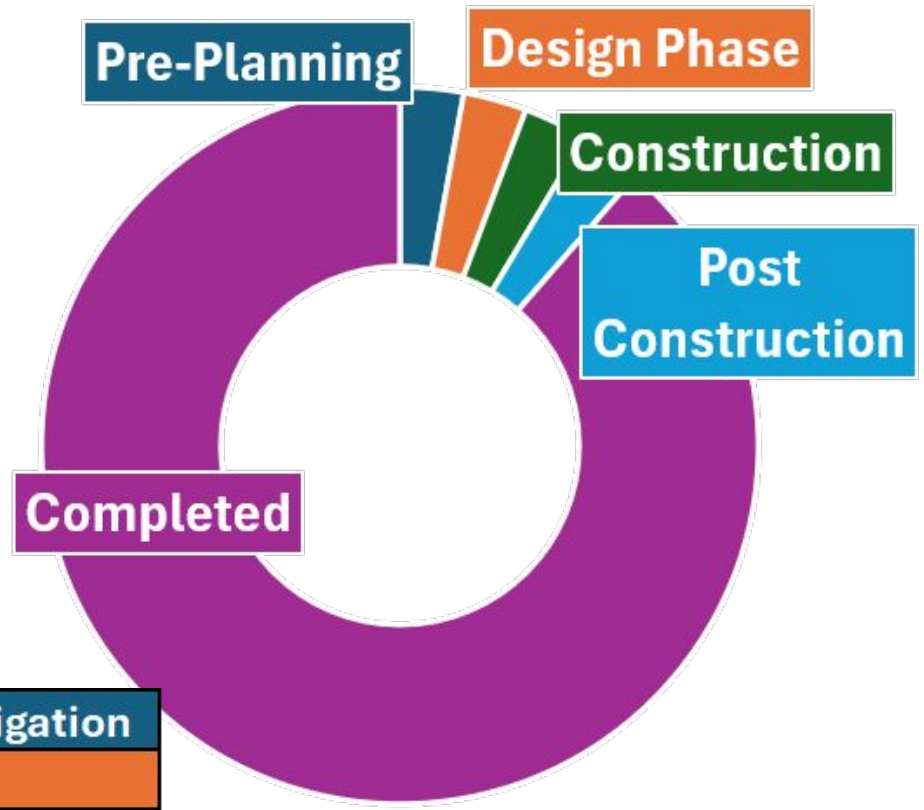


Pre-Planning	Grant Plumbing Investigation
Design Phase	Grant Boiler
Construction	Franklin Safety
Post Construction	Franklin External Flashing

NOTE: source data: Ebuilder reports by bond measure, sorted by project status.

Audit of Project Completion and Closeout statuses is currently ongoing.

2017 Bond Program Project Status

Total Projects	Pre-Planning	Design Phase	Construction	Post Construction	Completed
191	4	7	16	53	111

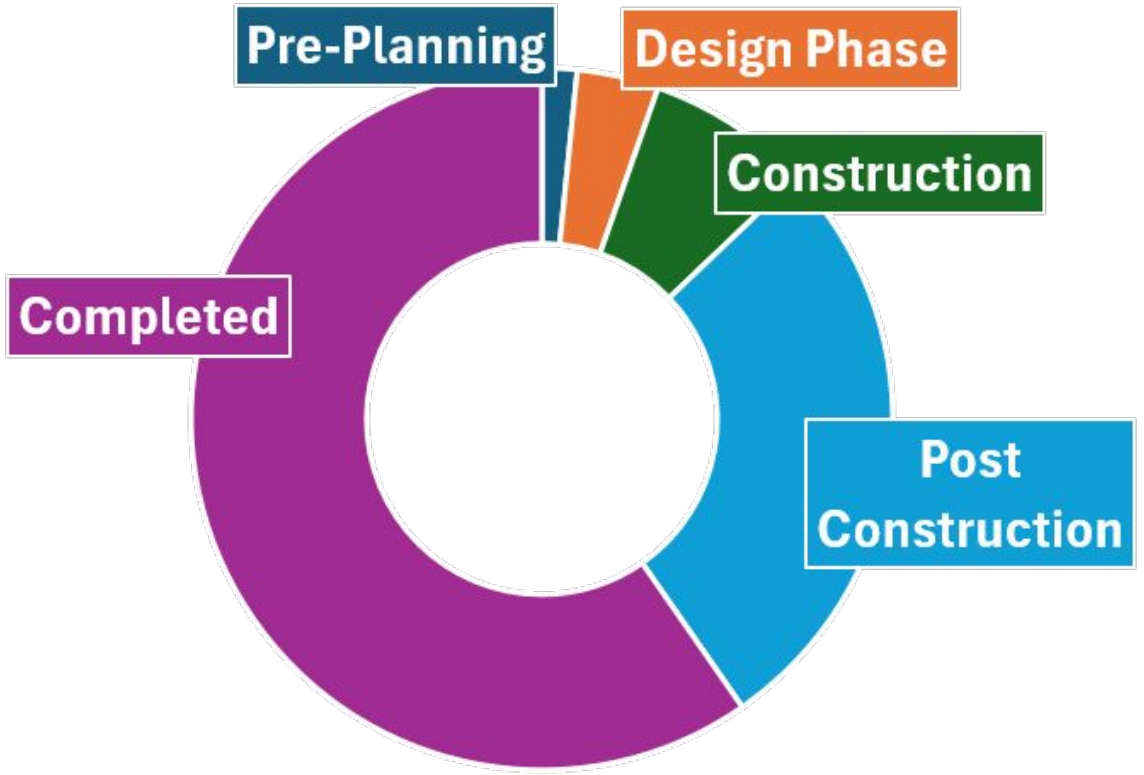


NOTE: source data: Ebuilder reports by bond measure, sorted by project status.

Audit of Project Completion and Closeout statuses is currently ongoing.

2020 Bond Program Project Status

Total Projects	Pre-Planning	Design Phase	Construction	Post Construction	Completed
116*	4	5	30	32	45

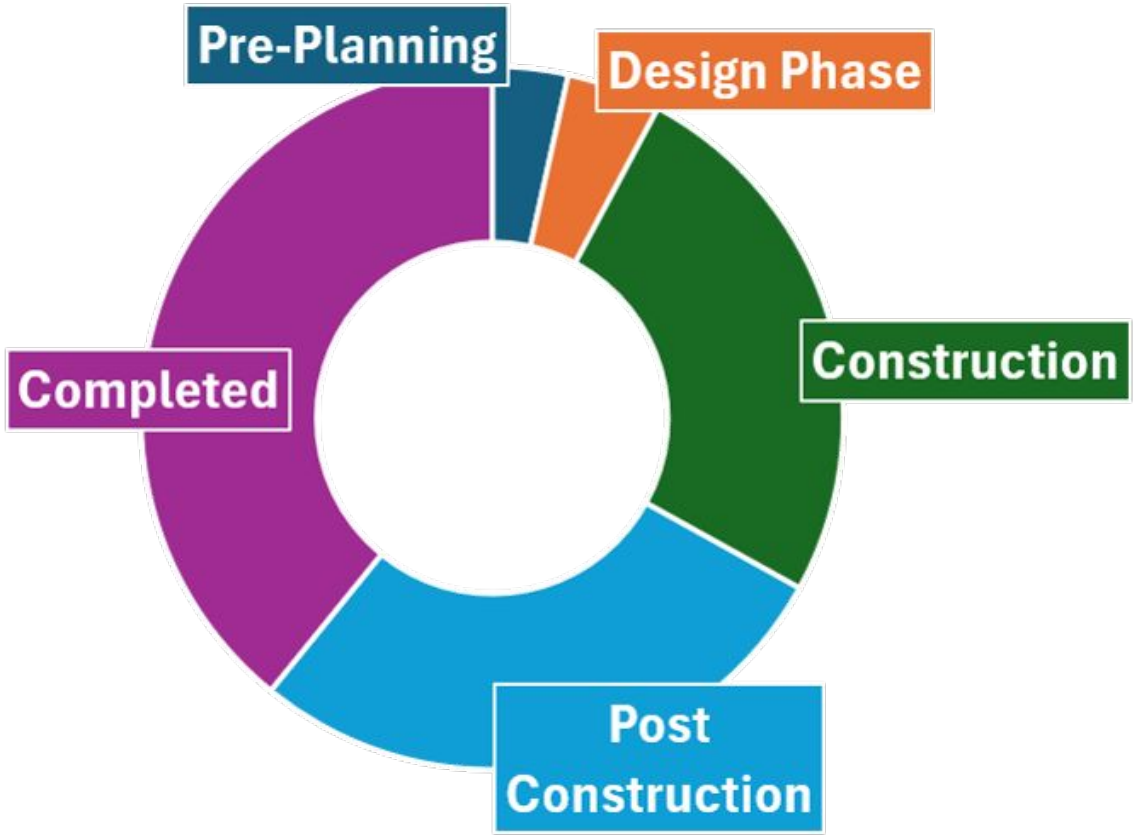

**Approximately $512 M remaining to be scheduled for 2020 Bond.*


NOTE: source data: Ebuilder reports by bond measure, sorted by project status.

Audit of Project Completion and Closeout statuses is currently ongoing.

Construction
7 of 30 are Curriculum Projects

2025 Bond Program Project Status

Total Projects	Pre-Planning	Design Phase	Construction	Post Construction	Completed
27*	16	5	1	5	0

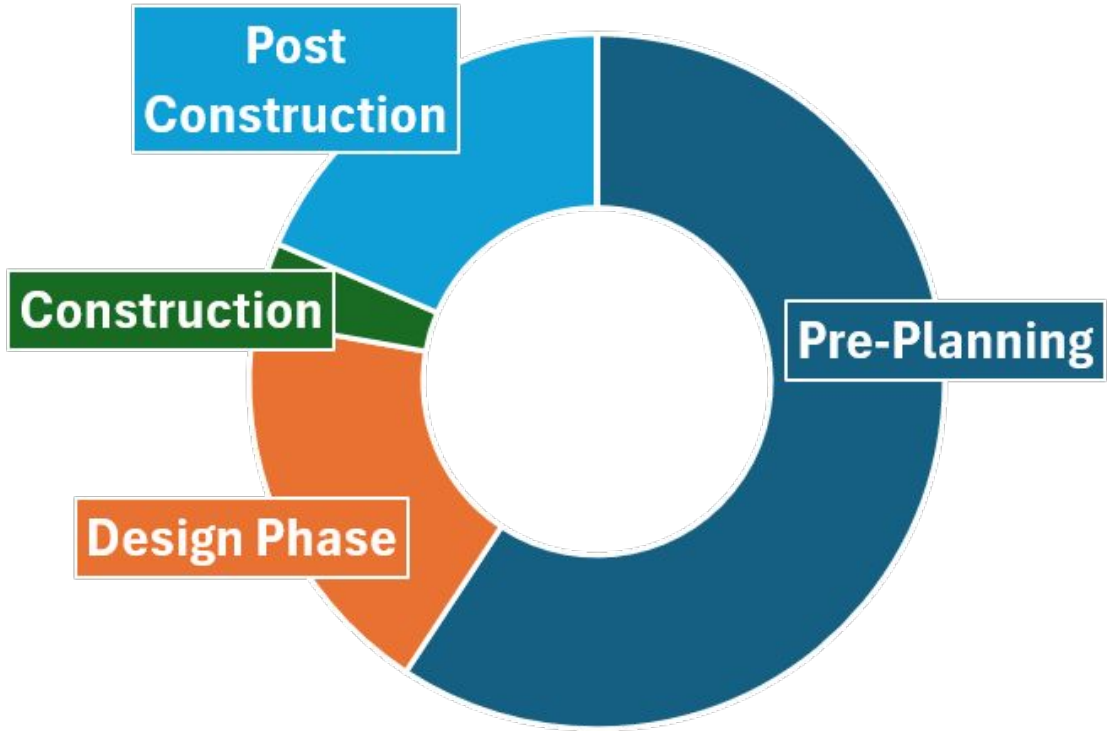


** Total projects will increase as the program progresses.*


Pre-Planning
8 of 16 are Curriculum Projects

Schedule and Budget Update


Program Schedule Update

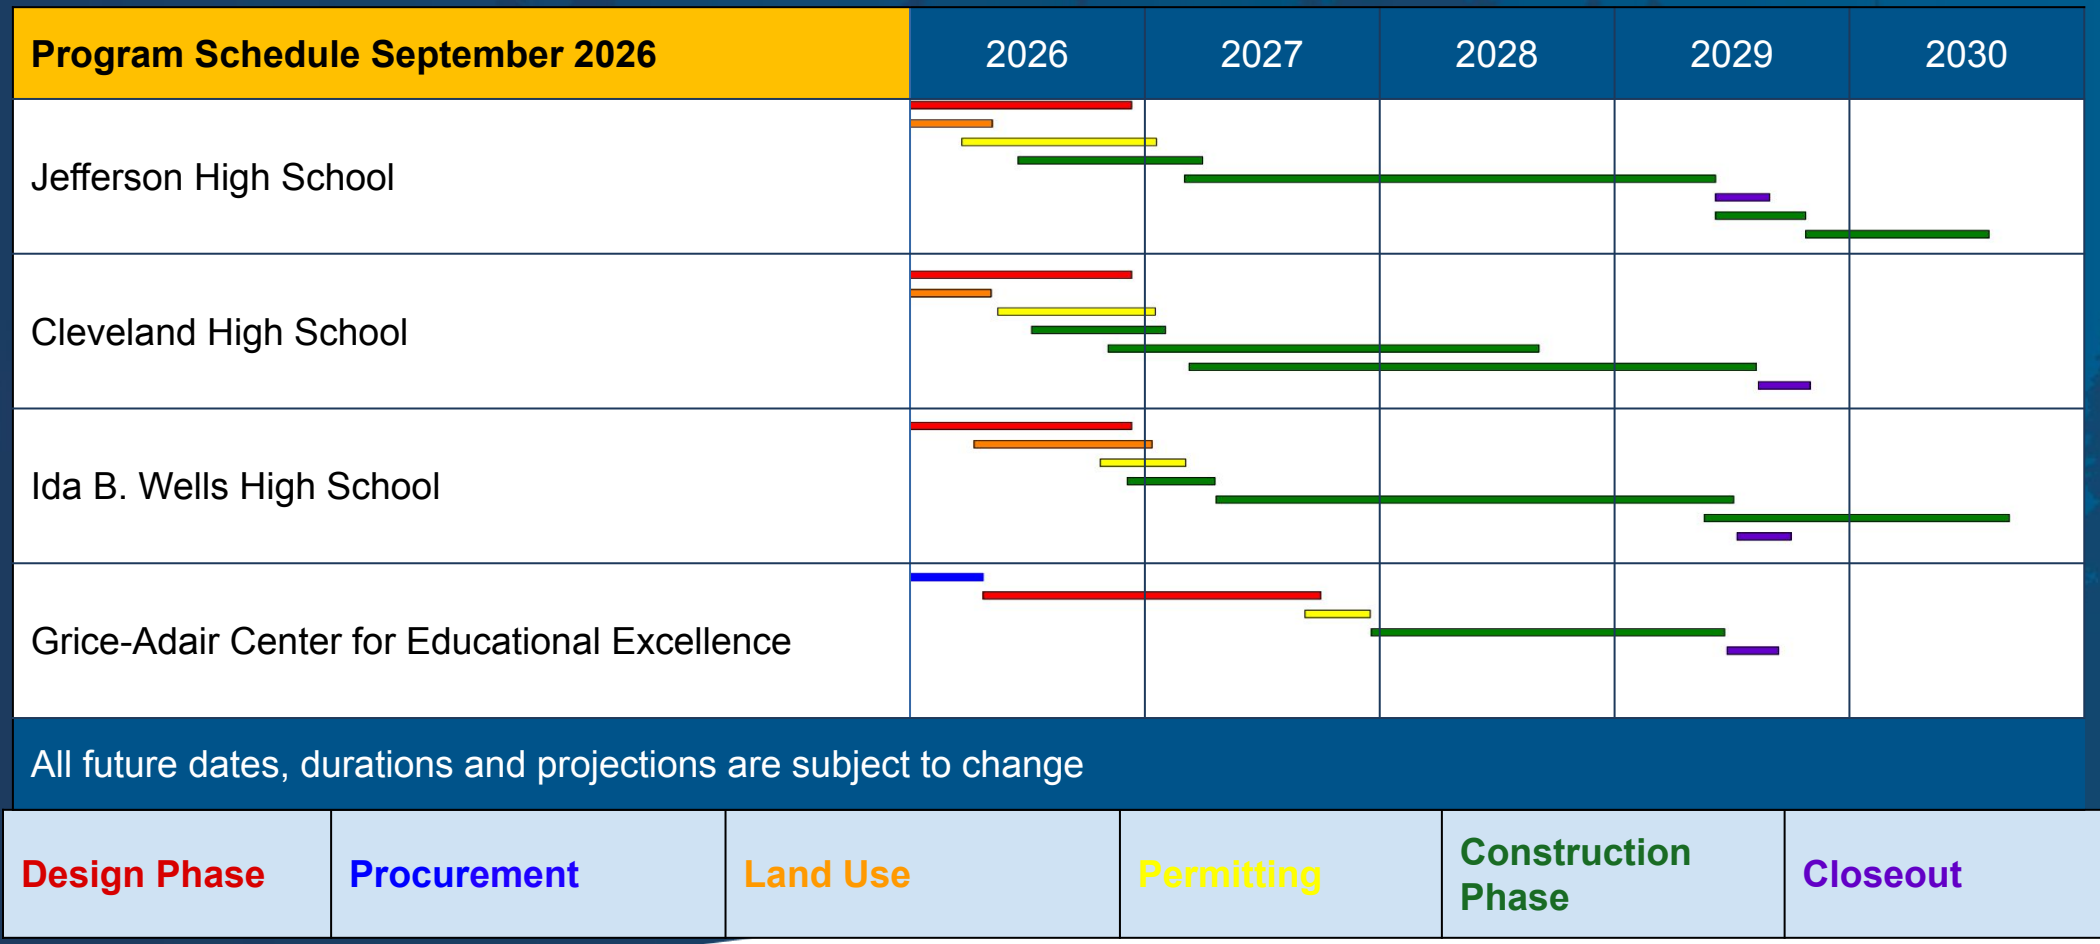


JHS Overall Project Schedule

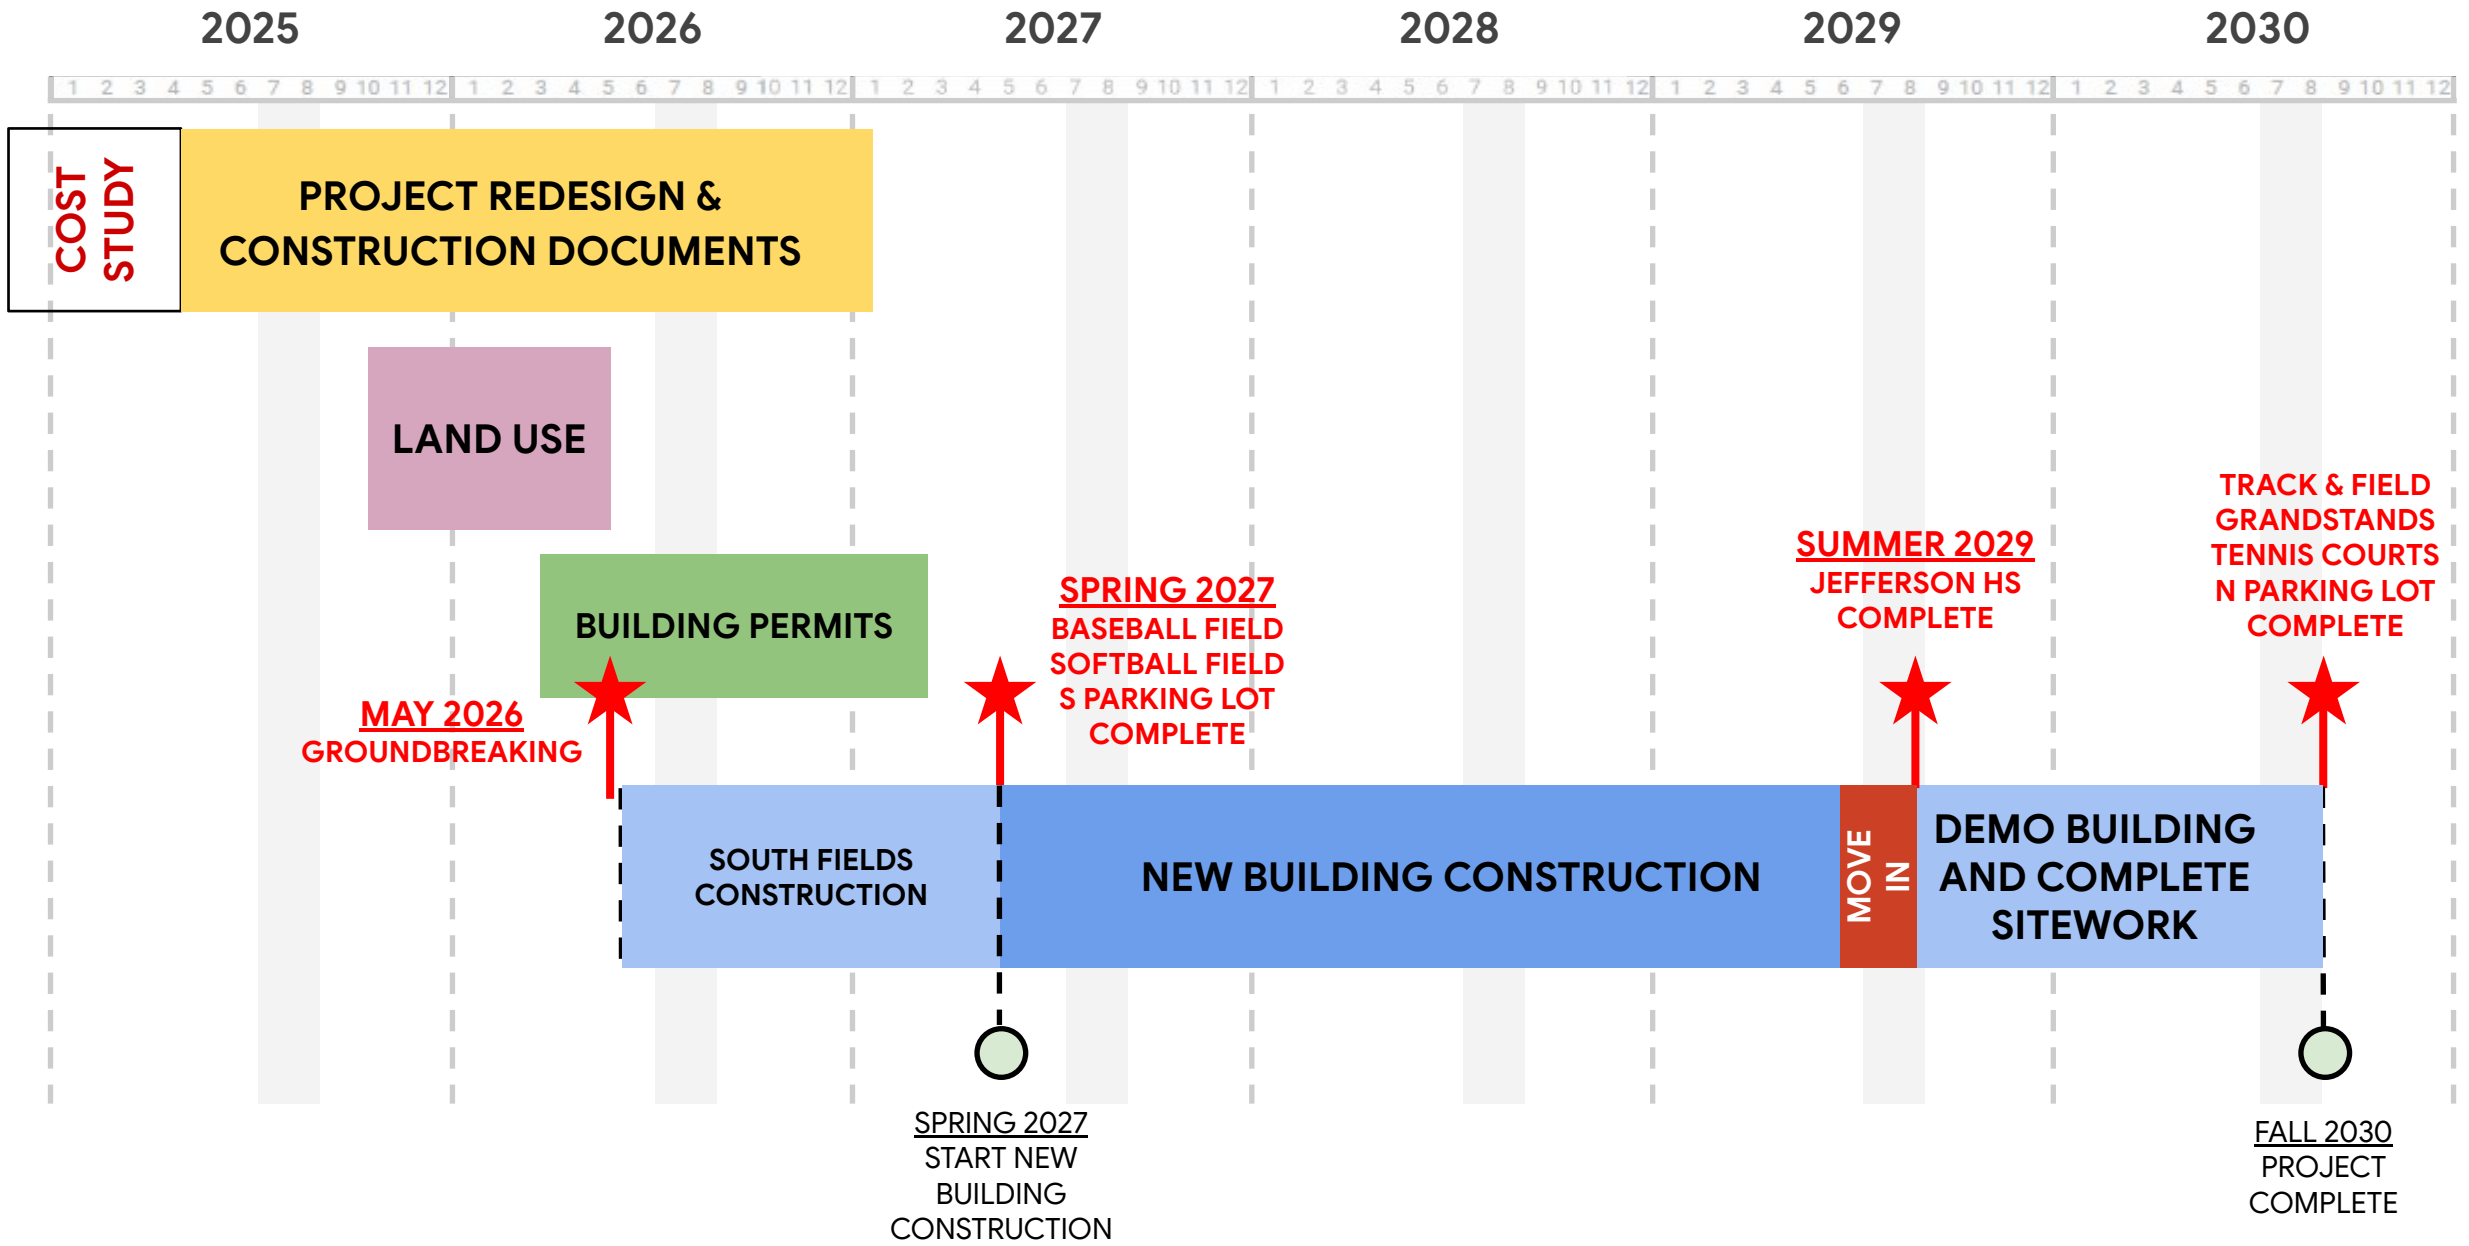

CHS Overall Project Schedule

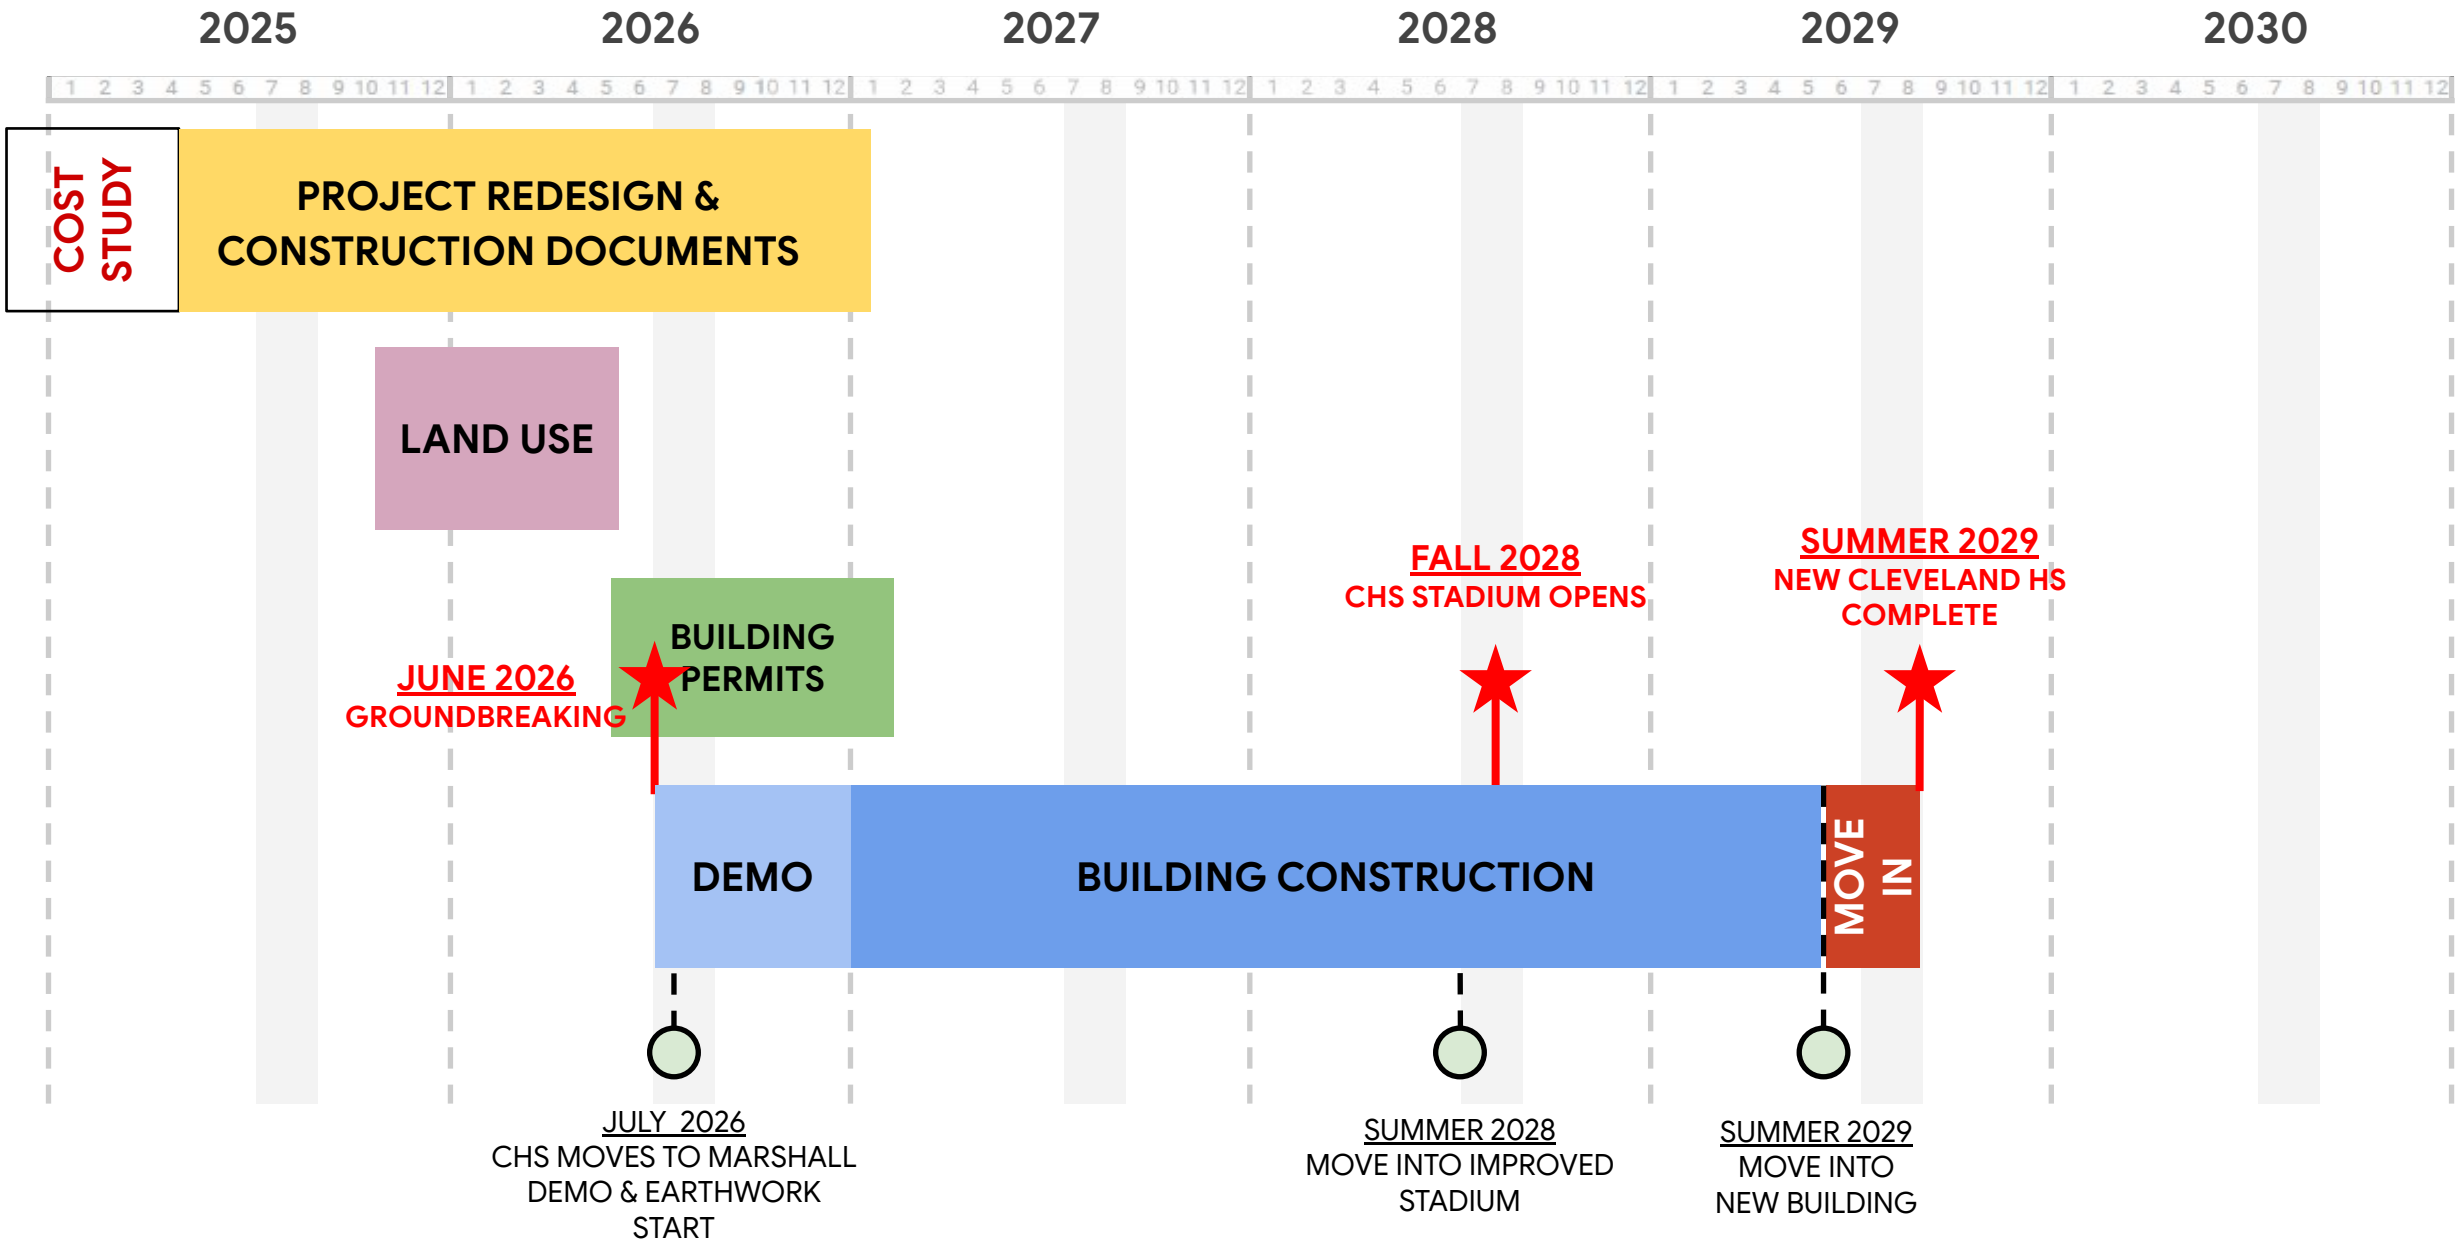

IBW Overall Project Schedule

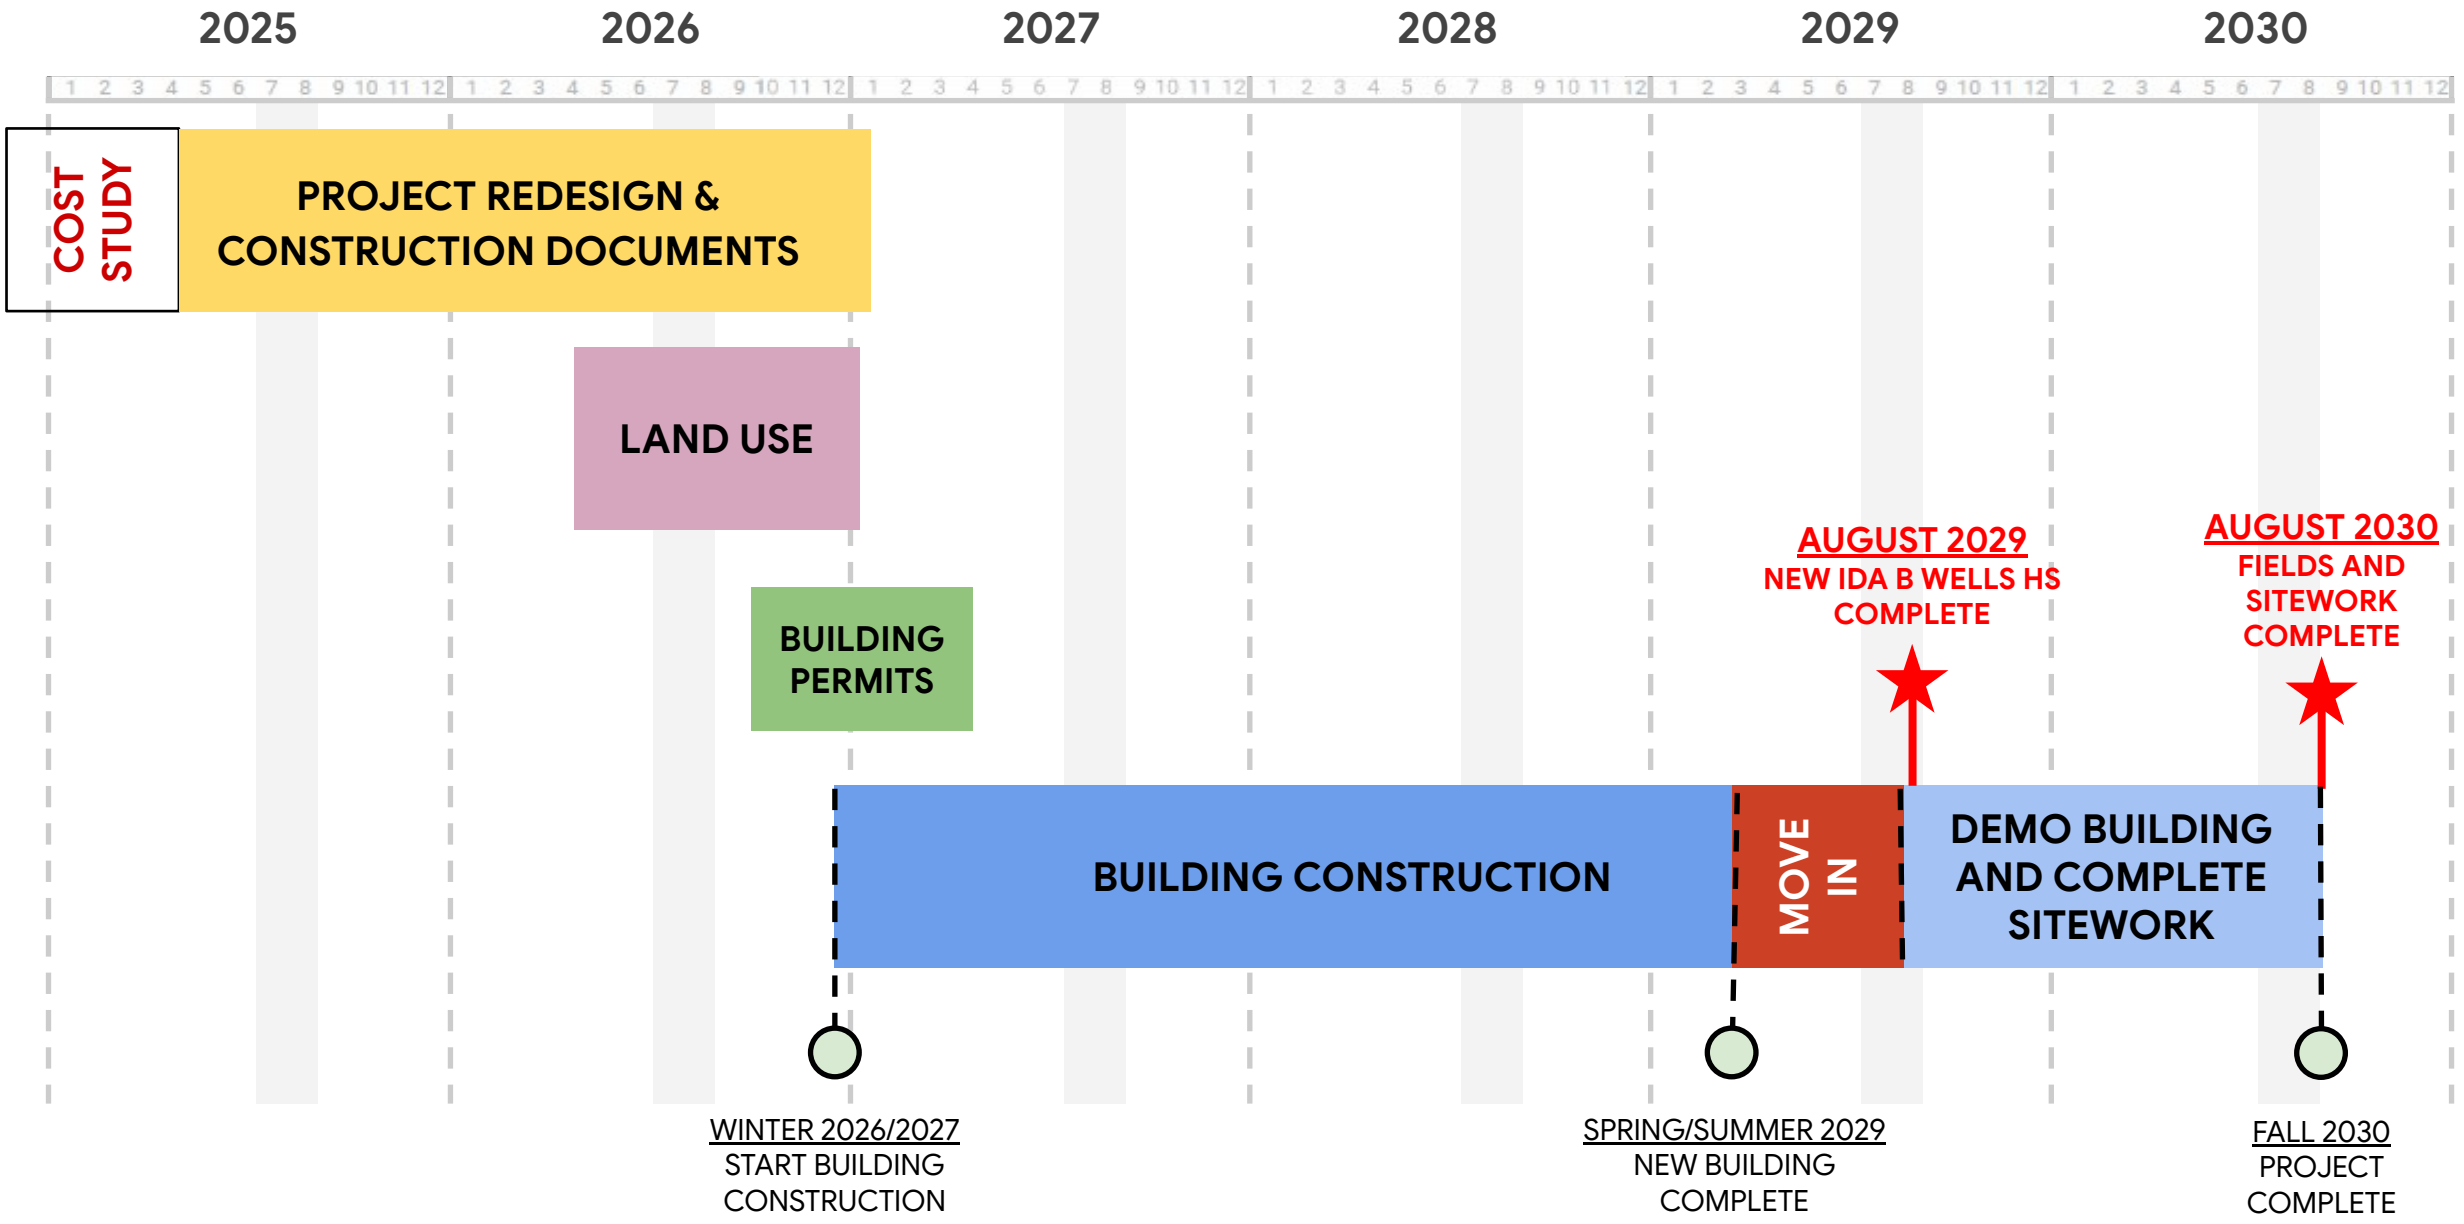

PORTLAND PUBLIC SCHOOLS

Bond Program Dashboard


Data Source	Report Name	Date Exported
eBuilder	0-PIVOT TABLE - FUNDING - SLS 07.01.2026 06 02 26 AM.xls	7/2/2026 3:25:13
eBuilder	BAC Data Project Management Cost 07.01.2026 06 30 23 AM.xls	7/2/2026 3:25:14
eBuilder	Commitment Funding Items 07.01.2026 06 30 09 AM (1).xls	7/2/2026 3:25:14
eBuilder	PS Reconcile Export 07.01.2026 06 00 58 AM.xls	7/2/2026 3:25:13

Bond Measure


Deselect all | 2012 Bond | 2017 Bond | 2020 Bond | 2025 Bond

Total Funds	Spent to Date	Outstd. Encumbrance	Available Funds	Percent Available
4.6bn	2.2bn	318.6M	2.1bn	46%

Spent to Date and Total Funds

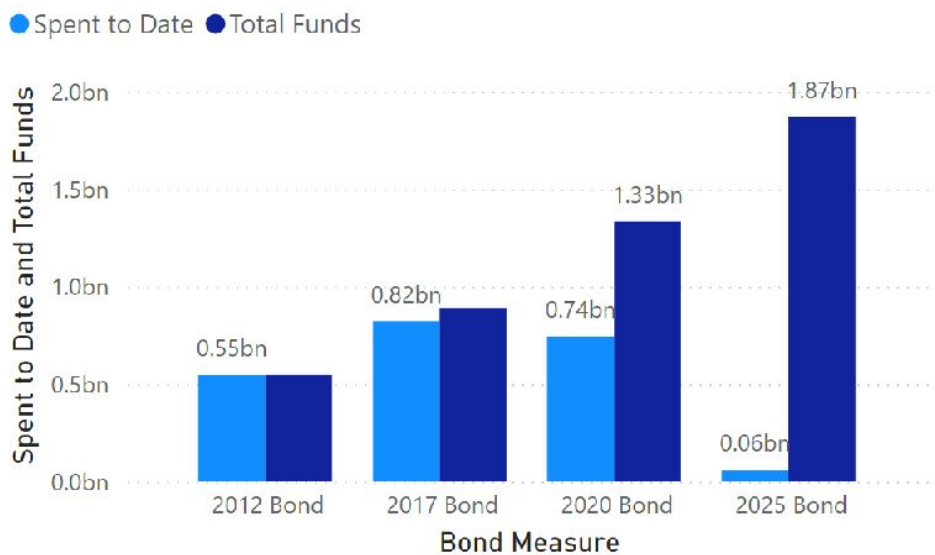

Spent and Encumbered

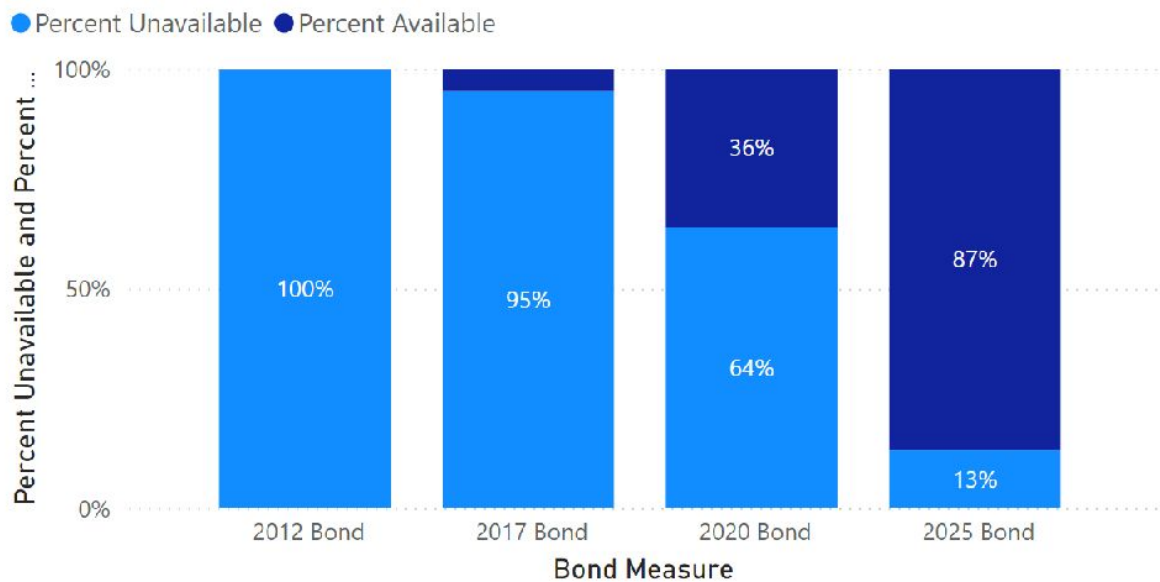

2012 Program Financial Status 7/1/2026

Project	Budget	Outstanding Encumbrance	Amount Paid to Date	Remaining Balance
Franklin HS Mod	$110,950,414	$0	$110,950,414	$0
Grant HS Mod	$155,300,188	$0	$155,300,188	$0
Roosevelt HS Mod	$97,128,043	$0	$97,128,043	$0
Faubion Replace	$30,653,663	$0	$30,653,663	$0
Grant Upper Field	$3,170,988	$0	$3,170,988	$0
RHS Phase IV	$6,153,741	$0	$6,153,741	$0
Other Projects	$112,740,428	$8,100	$112,710,428	$21,900
Grant & Franklin Add Ons	$367,663	$92,107	$75,464	$200,092
Administration	$31,284,018	$0	$31,284,018	$0
Contingency	$83,104	$0	-$902	$84,006
PPS 2012 Bond Program Total	**$547,832,249**	**$100,207**	**$547,426,043**	**$305,998**



Modernizations: Franklin HS, Grant HS, Roosevelt HS, and Faubion PK-8
Middle School Science Upgrades
Consolidated Projects: Accessibility, Seismic

Current balance of $242k as of 9/1/26

2017 Program Financial Status 7/1/2026

Project	Budget	Outstanding Encumbrance	Amount Paid to Date	Remaining balance
Benson HS Mod	$146,614,560	$378,357	$143,715,501	$2,520,702
Benson Add Ons	$2,865,020	$232,666	$1,266,243	$1,366,111
Benson Swings	$12,199,595	$0	$12,199,595	$0
Lincoln HS Repl	$240,836,448	$28,738	$224,096,580	$16,711,130
Kellogg MS Replace	$57,648,703	$0	$57,648,703	$0
McDaniel Mod	$197,000,000	$48,407	$196,817,745	$133,848
Health & Safety	$168,865,686	$22,536,517	$124,615,088	$21,714,081
Athletics	$4,734,678	$174,034	$2,278,729	$2,281,914
Administration	$61,087,401	$168,934	$60,908,060	$10,408
Contingency	$593,194	$0	$0	$593,194
PPS 2017 Bond Program Total	**$892,445,285**	**$23,567,653**	**$823,546,245**	**$45,331,387**




Modernizations: Benson Polytechnic, Lincoln, McDaniel, Kellogg Middle School and Multiple Pathways to Graduation

Consolidated Projects: Water Quality, Security Upgrades, New Roofs, Asbestos Abatement, Radon Remediation, Lead Paint Stabilization, Life Safety Upgrades, Accessibility, Seismic

2020 Program Financial Status 7/1/2026

Project	Budget Managed by PROCEDEO	Budget Managed by PPS	Outstanding Encumbrance	Amount Paid to Date	Remaining Balance
Benson 2020 Funds		$164,903,890	$640,328	$162,803,433	$1,460,129
Jefferson HS Mod	$366,007,500		$38,429,302	$30,053,013	$297,525,185
Jefferson Add Ons	$152,175		$149,945	$250	$1,980
CEE	$60,000,000		$34,238	$16,222,680	$43,743,082
Cleveland HS – Design	$23,679,515		$8,412,380	$15,270,600	-$3,465
Cleveland Swing Site	$137,500		$1,800	$105,905	$29,795
Wells HS – Design	$20,000,000		$2,404,163	$17,584,080	$11,757
Roosevelt PhV – Design		$2,000,000	$1,035	$97,625	$1,901,340
MPG Building		$80,447,075	$267,192	$77,947,593	$2,232,290
Curriculum		$63,319,191	$1,255,550	$54,617,744	$7,445,897
Technology		$136,100,000	$16,660,493	$91,534,529	$27,904,978
Infra Projects		$268,153,105	$19,787,893	$235,023,435	$13,341,777
Administration		$51,706,045	$1,239,513	$34,440,015	$16,026,517
2017 Bond Balance		$0	$0	$0	$0
Contingency – OSM		$79,451,387	$0	$0	$79,451,387
Unallocated Funds		$17,649,899	$0	$0	$17,649,899
PPS 2020 Bond Program Total	**$469,976,690**	**$863,730,592**	**$89,283,832**	**$735,700,902**	**$508,722,548**

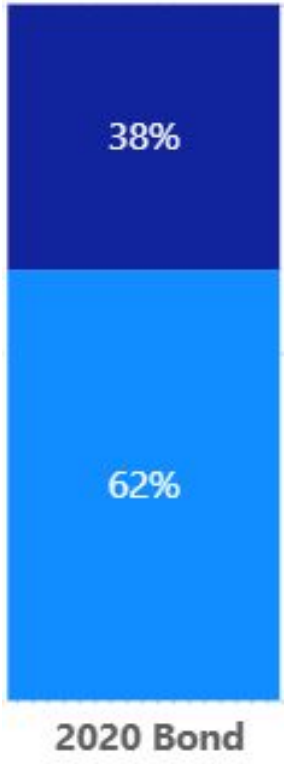


Modernizations: Jefferson HS, Pre-Planning/Design Ida B Wells and Cleveland HS, The Center of Black Excellence, Roosevelt (added capacity), and Benson

Consolidated Projects: Curriculum Materials, New Technology for classroom and distance learning, Health & Safety, Seismic, Security, Re-Roofing

2025 Program Financial Status 7/1/2026

Project	Budget Managed by PROCEDEO	Budget Managed by PPS	Outstanding Encumbrance	Amount Paid to Date	Remaining Balance
Priority Scope		$190,000,000	$10,622,793	$344,233	$179,032,974
Athletics		$79,000,000	$1,347,024	$2,047,435	$75,605,541
Technology		$176,000,000	$3,916,460	$26,452,579	$145,630,961
Physical Education		$10,000,000	$0	$0	$10,000,000
Curriculum		$56,000,000	$0	$0	$56,000,000
Jefferson HS Modernization	$100,000,000		$0	$0	$100,000,000
Cleveland HS Modernization	$448,911,745		$12,273,030	$393,615	$436,245,100
Ida B Wells HS Modernization	$429,350,000		$29,359,062	$507,760	$399,483,178
Elementary & Middle Schools		$171,738,255	$0	$0	$171,738,255
Admin		$83,050,000	$57,898,825	$7,570,008	$17,581,167
Contingency		$125,956,806	$0	$0	$125,956,806
PPS 2025 Bond Program Total	**$978,261,745**	**$891,745,061**	**$115,417,194**	**$37,315,630**	**$1,717,273,982**

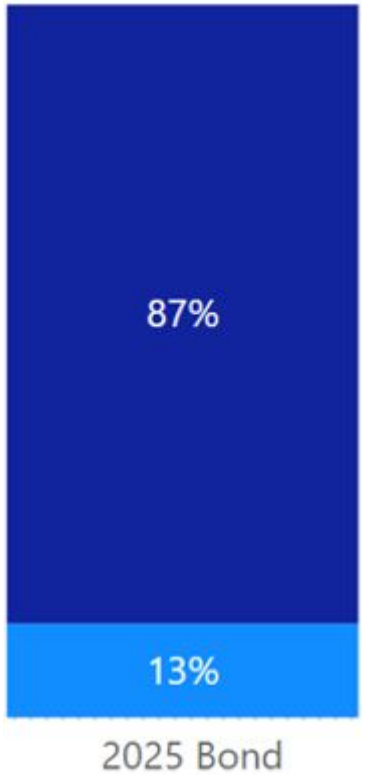

Modernizations: Cleveland HS, Ida B Wells HS, and Jefferson

Consolidated Projects: Security Upgrades, Seismic, Technology, Improvements for Roosevelt, Lincoln, Franklin, and Grant, and New Athletic Hub Facilities at Jackson MS and Marshall Campuses

Project Updates

Jefferson HS Modernization

5210 N Kerby Ave, Portland, OR 97217

PPS PM
Steve Effros

Contractor (CMGC)
Colas Hoffman

PPS Zone 2
Michelle DePass

Architect
BORA & LEVER

Project Budget

Total Budget	CMGC GMP
$466,007,500	GMP: $TBD

Project Overview

Current Phase: In Construction
Scope: New Facility
New Facility: 299,485 SF
Construction Start: Spring 2026
Student Move-In: 29-30 School Yr
Tentative Sub Com: Fall 2030
GMP Construction Timeline: TBD

General Scope

- ✔ New all-electric multi-story building
- ✔ Includes a theater, health center, teen parent center, and dance studios
- ✔ Track and field relocated to the site of the current structure
- ✔ New softball field and baseball/soccer multiuse field

Project Status

Design Procurement
100%

Design
80%

50% CD Review Complete

Construction
5%

Construction NTP
6/15/26

Project Update

1	50% CD Review Session complete, estimate reconciliation & review are underway
2	Permits issued for for baseball & softball fields, construction is ongoing
3	Project team met with JHS staff to provide overview of current and future on-site construction phases and allow for questions & answers

PROCEDEO | PORTLAND Public Schools

> JHS Field Construction - 8/21/26



> JHS Field Construction - 8/28/26



Cleveland HS Modernization

3400 SE 26th Ave, Portland, OR 97202

PROCEDEO PM
Scott Mears

Contractor (CMGC)
Skanska

PPS Zone 6
Stephanie Engelsman

Architect
Mahlum

Project Budget

Total Budget	CMGC GMP
$472,553,760	GMP: TBD

Project Overview

Current Phase: In Construction
Scope: New Facility
New Facility: 297,000 SF
Construction Start: Summer 2026
Student Move-In: 29-30 School Yr
Tentative Sub Com: Summer 2029
GMP Construction Timeline: TBD

General Scope

- ✔ 2 new four-story buildings connected by a skybridge
- ✔ Dynamic outdoor courtyard
- ✔ New arts theater, black box theater, 2 gyms, and dance and wrestling studios
- ✔ Improvements to track and athletic fields

Project Status

Design Procurement
100%

Design
80%

Permit 2 Set In Review

Construction
5%

Construction
Marshall Swing Start - 3/30/26
Demo Start - 7/7/26

Project Update

1	The Marshall site is complete and students have moved in for the school year
2	Abatement and demo is underway. Salvage of exterior masonry and interior materials is nearing completion.
3	Building Permit 1 is currently in review with the City

> CHS Bldg Demo - 8/13/26



Ida B Wells HS Modernization

1151 SW Vermont St, Portland, OR 97219

PROCEDEO PM
Gabe Asch

Contractor (CMGC)
Hoffman Construction

PPS Zone 1
Christy Splitt

Architect
BORA Architects

Project Budget

Total Budget	CMGC GMP
$449,350,000	GMP: $TBD

Project Overview

Current Phase: In Design
Scope: New Facility
New Facility: 283,867 SF
Construction Start: Winter 2026
Student Move-In: 29-30 School Yr
Tentative Sub Com: Fall 2030
GMP Construction Timeline: TBD

General Scope

- ✔ New four-story building including instructional spaces for Career Technical Education programs
- ✔ New performing arts, commons, and outdoor spaces
- ✔ Full complement of athletic fields and upgrade of existing fields on the Rieke side
- ✔ The existing pool is not in the scope, but a new pool support building is included

Project Status

Design Procurement
100%

Design
78%
50% CDs In Review

Construction
0%
Construction NTP
Pending

Project Update

1	50% CD Review Session started on 8/12/26
2	Land Use approved on 8/28
3	Permitting submitted to the City and is under review
4	Groundbreaking scheduled for November 13th

PROCEDEO | PORTLAND Public Schools

Grice-Adair Center for Educational Excellence

1 N. Fremont St, Portland, OR 97227

PROCEDEO PM
Khalil Rivera

Contractor (CMGC)
TBD

Architect
DLR

Project Budget

Total Budget	CMGC GMP
$60,000,000	GMP: $TBD

Project Overview

Current Phase: In Design
Scope: Renovations
Renovations: TBD
Construction Start: TBD
Tentative Sub Com: TBD
GMP Construction Timeline: TBD

General Scope

- ✔ Renovation of buildings into PPS Managed Community Center, supporting programs for students of all ages and families with space for Study, Connection, Learning, and Movement
- ✔ A portion of the upper floors of the West Building will remain and be leased to Community Partner Organizations
- ✔ Space allocated for PPS and Community Partner Administration, as well as Community Gathering and an Outdoor Courtyard

Project Status

Design Procurement
100%

Design
20%

SDs in Progress

Construction
0%

Project Update

1	Scope to Budget (STB) review session completed on 8/28, A/E approved to begin work on SDs
2	Initial cost estimate received and is within budget
3	AE site walks and facility assessments have been completed

PROCEDEO | PORTLAND Public Schools

Seismic/Roofing - 2026

Summer 2026 Construction

Roofing with Seismic

- Scheduled for 2026 Fall completion
  - Woodmere
  - Cesar Chavez
  - Marshall
  - Vestal

Seismic Parts

- Scheduled for 2026 Fall completion
  - Vernon
  - Winterhaven
  - Marysville (Ph 3)



YOUR BOND DOLLARS AT WORK!

2026 SUMMER CONSTRUCTION:

$29.4M

Seismic/Roofing - 2027 and Beyond

<u>Anticipated 2027 Construction Start</u>

Seismic Parts and Partial Roof

- In Design
  - Richmond (DD Phase)
  - Capitol Hill (DD Phase)

Seismic Parts

- In Design
  - Ainsworth (SRGP awarded, DD phase)
  - Kelly (DD phase)

Full Seismic

- Design in progress
  - Beverly Cleary (CD mid-Sept)

<u>Anticipated 2028 and 2029 Construction</u>

Seismic Parts and Partial Roof

- Beach
  - Pre-Design docs due mid-Sept

Full Seismic and roof

- Rose City Park
  - Pre-Design docs due Aug 31st

Facility Improvement Projects

Summer 2026 Construction

- Bridger - Mechanical Upgrades
- Buckman - Cafeteria Flooring Abatement and Replacement
- Buckman - Sidewalk Replacement
- Boise Elliot – Repaint majority of school
- Capitol Hill - Flooring abatement, structural repairs, new flooring
- George - Boiler Room Roof Beam Replacement
- Jefferson – Stage rigging repairs
- Kelly - Mechanical Upgrades
- Lent - Mechanical Upgrades
- Classroom Technology Upgrades - Gray, Markham, West Sylvan, Mt. Tabor , Harrison Park, Laurelhurst, Hosford, Buckman, MLC, Davinci, Chavez, MLK, Roseway Hts, Alameda, Ainsworth, Sellwood
- Roosevelt – Science Chemical Storage
- Rose City Park - Boiler Retube
- Sabin – Restroom Pipe Replacement
- Sitton – Truss repair/replacement
- Vestal – Built-in cafeteria table replacement
- DDC Controls Upgrades - Alameda, Beach, Chavez, James John, Brentwood, Roseway Hts, Sellwood, Sitton, West Sylvan
- Fire Alarm Upgrades - Glencoe, Marshall Campus, Woodlawn

YOUR BOND DOLLARS AT WORK!

2026 SUMMER CONSTRUCTION:

$16M

Athletic Sites

Grant Bowl Lighting

- “Flip the Switch” celebration on September 1st

Jackson Athletic Hub

- Phase 1: Track & Field construction began in June and anticipated to be operationally accessible by Fall 2026
- Phase 2: Multi-Use Field entering Permitting Phase August 2026
  - Multi-Use completion Spring 2027

Powell Park Multi-Use Field, Lighting, and Support Buildings

- Continuing discussions with Parks for use agreement - meeting 9/8


Land Use Application Planning in Progress

- West Sylvan, Franklin, Roosevelt, Grant Seating

Athletic Sites

Marshall Athletic Improvements

- Completed:
  - Light Retrofit
  - Track
  - Field
  - Tennis Courts
  - Gym
  - Weight Room

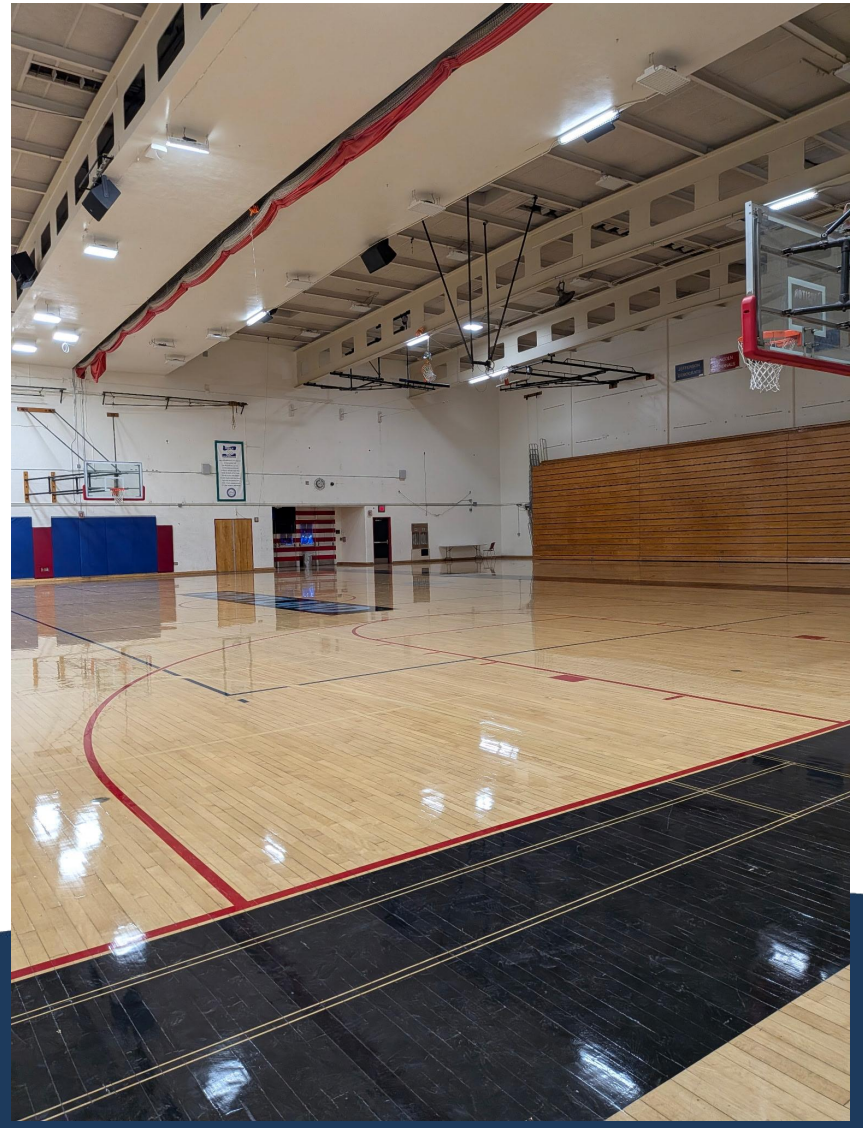

> Grant Flip the Switch - 9/1/26



> Grant Wins 2-0! - 9/1/26



Fall 2026 Look Ahead

A round of applause to all of the teams who successfully completed large amounts of work over the summer. Our work does not stop here. We are continuously planning, designing, and implementing the work of the district.

Modernizations - Continued field work and demolition, finalizing designs and construction planning.

Facility Improvements - Planning and design for next summer projects, and ongoing facility improvements that can be done during winter break

Athletics/PE - Continued work on the Jackson hub, and land use planning for other sites

Security - Planning and implementation of smaller projects to enhance school security

Technology - Continue updated technology deployments to classrooms, and the start of the ERP modernization moving to our new platform

Current PPS Betterment Savings

Recognized within the first 6-month of PROCEDEO Contract

Total Realized Savings: $20,839,680

Total PROCEDEO Fee Paid to Date

$6.4M

Return on Investment

Current ROI

225%

Owner Betterment Savings Breakdown

Realized/Reallocated Savings

- Reallocation of funds in 2012 Bond into Projects
- Savings recognized by new processes no need for temporary labor
- FF&E Coordination Repetitive SOW Corrected
- Negotiated Street Closure Fee Cap with ODOT
- Worked with ODOE to document effort for GET

For Every $1 PPS has invested in PROCEDEO we have returned $2.25 in identified saving to the bond program

Questions
Thank You



Contact us

PPS.NET pubinfo@pps.net (503) 916-2000 501 N Dixon, Portland, OR 97227



PORTLAND
Public Schools
