School Improvement Bond Update

Bond Accountability Committee Meeting

August 23, 2023

Agenda

• Welcome & Introductions	5:30 – 5:40 pm
• Public Comment	5:40 – 5:45 pm
• Program Administration Updates	5:45 – 6:00 pm
• Modernization Project Updates	6:00 – 7:30 pm
• Adjourn	7:30 pm

Public Comment

(public comments received via email prior to the meeting will be read aloud)

Business Equity Utilization Data Constraints

Business equity utilization data from the B2GNow software system represents a point in time and may not fully represent actual payments received by Certified Businesses. The accuracy of the utilization data is contingent on several factors:

- PPS's payment data from Peoplesoft is uploaded into B2GNow monthly and reflects all payments from PPS to prime contractors during the prior month.
- Accurate data on payments to subcontractors is contingent on prime contractors or upper tier subs entering their subcontractors in B2GNow and subsequently self-reporting their monthly payments to each subcontractor in a timely and accurate manner.
- If prime contractors (or first tier subs) enter payments to first tier or subsequent tier subs in a timely manner, the total equity utilization calculation can be expected to accurately reflect contract expenditures as of approximately one to two months prior to the report date.
- If prime contractors (or first tier subs) do not enter payments to first tier or subsequent tier subs in a timely manner, accurate equity utilization data will be delayed, at times significantly. Even closed contracts may be updated later if PPS learns of new subcontractor payments that were made months or even years prior.

Program Administration Updates

Bond Program Administration

Office of School Modernization - Program
August 2023

STATUS AT A GLANCE

Legend:

	As planned: no concerns
	Caution: requires attention
	Impacts: impacts occurring

	As Planned	Caution	Impacts
Budget	X		
Equity		X	
Overall	X		

EQUITY

		BUSINESS EQUITY							WORKFORCE EQUITY					
		MBE	WBE	SDVBE	ESB	N-C	**TOTAL**	*goal*	MIN	*goal*	FEM	*goal*	**APPR**	*req*
Cumulative	Current	4.58%	8.49%	0.05%	2.45%	0.79%	**16.36%**	*18%*	**30%**	*25%*	**5%**	*14%*	**23%**	*20%*
	Prior Report	4.63%	8.56%	0.05%	2.62%	0.80%	16.66%		**29%**		5%		**24%**	
12 Month	Current	4.26%	11.80%	0.00%	1.77%	1.10%	**18.93%**	*18%*						
	Prior Report	3.82%	13.69%	0.00%	2.88%	1.16%	21.55%							

Percent of payments made to Certified owned businesses, cumulative and 12-month rolling; Percent of labor hours of apprenticeable trades, cumulative

BUDGET

	BUDGET		FUNDING		PROGRESS		FORECAST	
2012 PROGRAM	Original Budget	**Current Budget**	Bond Funds	Other Funds	Actuals To Date	Additional Encumbered	**Estimate At Completion**	*Over/Under*
Franklin HS Mod	81,585,655	**113,022,577**	111,040,922	1,981,656	113,022,577	-	**113,022,577**	-
Grant HS Mod	88,336,829	**158,993,225**	155,772,451	3,220,774	158,698,039	166,896	**158,864,685**	(128,540)
Roosevelt HS Mod	68,418,695	**101,631,108**	97,127,989	4,503,119	101,631,108	-	**101,631,108**	-
Faubion Replace	27,035,537	**50,115,627**	34,109,383	16,006,244	50,028,171	-	**50,115,627**	-
Grant Upper Field	-	**3,246,600**	3,246,600	-	3,170,988	11,130	**3,246,600**	-
RHS Phase IV	-	**6,157,969**	6,153,741	4,228	6,157,969	-	**6,157,969**	-
Other Projects	123,441,923	**118,273,603**	113,293,283	4,980,319	118,273,603	-	**118,273,603**	-
							2012 Project Subtotals	*(128,540)*
Administration	68,117,563	**31,483,210**	31,279,728	203,482	31,483,210	-	**31,483,210**	-
Contingency	25,063,798	**332,368**	332,368	-	-	-	**-**	(332,368)
							2012 Program Subtotals	*(332,368)*
Totals	*482,000,000*	***583,256,288***	*552,356,466*	*30,899,822*	*582,465,666*	*178,026*	***582,795,380***	*(460,908)*

2012 Budget Notes

99% Spent

- Staff are working through closing out all non-active 2012 commitments and projects, and returning unspent funds to the Program.
- Any remaining 2012 funding will go towards prior add-on project requests at 2012 modernizations (such as additional security cameras at Franklin and Grant).
- Remaining program contingency is being shown for transparency but, as noted above, will go to prior add-on project requests once all other funding sources and expenditures have been reconciled.

Bond Program Administration

Office of School Modernization - Program
August 2023

2017 PROGRAM	BUDGET		FUNDING		PROGRESS		FORECAST	
	Original Budget	**Current Budget**	Bond Funds	Other Funds	Actuals To Date	Additional Encumbered	**Estimate At Completion**	*Over/Under*
Benson HS Mod	202,000,000	**155,484,185**	141,550,081	13,934,104	104,498,221	66,123,742	**156,800,995**	1,316,810
Benson Swings	-	**13,550,089**	13,544,288	5,801	12,205,396	27,883	**12,233,279**	(1,316,810)
Lincoln HS Repl	187,000,000	**242,619,558**	242,500,000	119,558	218,103,628	12,539,386	**231,228,186**	(11,391,371)
Kellogg MS Replace	45,000,000	**57,941,414**	57,697,500	243,914	57,685,008	195,193	**57,941,414**	-
McDaniel Mod	146,000,000	**202,717,847**	199,000,000	3,717,847	199,957,917	529,456	**200,669,506**	(2,048,342)
Health & Safety	-	**154,286,174**	136,268,544	18,017,630	143,689,266	2,285,347	**154,286,174**	-
						2017 Project Subtotals		*(13,439,713)*
Administration	40,000,000	**59,948,787**	59,832,096	116,690	47,010,502	5,581,630	**55,487,129**	(4,461,658)
Contingency	20,000,000	**16,047,249**	16,047,249	-	-	-	**16,047,249**	-
Unallocated H&S	150,000,000	**21,731,456**	21,731,456	-	-	-	**21,731,456**	-
						2017 Program Subtotals		*(4,461,658)*
Totals	*790,000,000*	***924,326,758***	*888,171,214*	*36,155,543*	*783,149,939*	*87,282,636*	***906,425,387***	*(17,901,371)*

2017 Budget Notes

85% spent

- Benson HS Modernization funding is split between 2017 and 2020. The 2017 Benson HS Modernization information shown above reflects 2017 funding and budget only, with actuals and additional encumbered specific to the 2017 funding as well. The Benson Swings shares total budget/funding with Benson HS Modernization, so the "under" amount of budget in the Benson Swings project will be applied to the Benson HS Modernization and is therefore shown as an "over" amount in the Benson HS Modernization line.
- The McDaniel Modernization project has funds being held in the project until all project scope has been finalized and completed. The netting repair project is already included in the Estimate at Completion. The Lincoln Modernization project is forecasting roughly $11.4M under budget during Phase 2 of construction.
- OSM continues to forecast full use of 2017 Program Contingency at this time but anticipates the full amount will not be needed for risk mitigation of existing projects. Once the Lincoln HS Modernization project has completed, OSM will review Program Contingency and Bond Administration budgets in coordination with review of unneeded budget from Lincoln and McDaniel, for discussion regarding potential additional 2017 Bond-funded projects.
- As the 2017 Health & Safety projects wind down, OSM is also reviewing to ensure that any Health & Safety funds not needed to complete certain categories of H&S scope get reallocated to other H&S categories, to ensure that the full $150M dedicated to Health & Safety projects by the 2017 Bond measure is utilized as such.

Bond Program Administration

Office of School Modernization - Program
August 2023

2020 PROGRAM	BUDGET		FUNDING		PROGRESS		FORECAST	
	Original Budget	**Current Budget**	Bond Funds	Other Funds	Actuals To Date	Additional Encumbered	**Estimate At Completion**	*Over/Under*
Benson 2020 funds	-	**164,903,890**	164,903,890	-	92,057,894	48,008,081	**164,903,890**	-
Jefferson HS Mod	311,000,000	**366,007,500**	366,000,000	7,500	5,888,991	22,749,069	**366,007,500**	-
CBSE	60,000,000	**60,000,000**	60,000,000	-	-	-	**60,000,000**	-
Cleveland HS Design	20,000,000	**20,000,000**	20,000,000	-	-	-	**20,000,000**	-
Wilson HS Design	20,000,000	**20,000,000**	20,000,000	-	-	-	**20,000,000**	-
Roosevelt PhV Desigr	2,000,000	**2,000,000**	2,000,000	-	-	-	**2,000,000**	-
MPG Building	64,000,000	**80,476,726**	80,447,075	29,651	34,296,468	42,237,109	**80,476,726**	-
Curriculum	53,444,000	**53,444,000**	53,444,000	-	35,141,529	10,357,500	**53,444,000**	-
Technology	128,200,000	**143,503,600**	128,200,000	15,303,600	73,111,380	12,160,221	**143,503,600**	-
Infra Projects	-	**215,653,893**	210,596,028	5,057,866	54,891,791	116,133,167	**215,653,893**	-
							2020 Project Subtotals	-
Administration	63,098,640	**63,104,808**	63,098,640	6,168	10,920,518	757,011	**63,104,808**	-
2017 Bond Balance	152,000,000	-	-	-	-	-	-	-
Contingency - OSM	93,257,360	**52,818,164**	52,818,164	-	-	-	**52,818,164**	-
Unalloc Proj Funds	241,000,000	**58,749,561**	58,749,561	-	-	-	**58,749,561**	-
							2020 Project Subtotals	-
Totals	*1,208,000,000*	***1,300,662,142***	*1,280,257,358*	*20,404,785*	*306,308,571*	*252,402,158*	***1,300,662,142***	-

2020 Budget Notes

24% spent

- PPS held their second 2020 Bond sale in April 2023. $420M in bonds were sold, gaining a premium of $44.8M. This was added to Contingency above.
- OSM transferred $4M in 2020 Program Contingency to the MPG project, due to large increases in costs for material inspections, permitting, and addressing costs associated with an extraordinarily large number of hidden drywells underground. As noted in previous reports, the GMP amount was already $2.5M over the previously established budget, due to extreme inflationary pressures. The project team had hoped to be able to find savings in other areas of the budget, but over the course of the last several months, it became clear that was not possible.
- Consistent with prior reporting, the project to convert Harrison Park to a middle school has required use of program contingency funds to fully fund the project. The budget of this complex project is now fully funded with 2020 Bond funds from Capacity, Mechanical, Security, ADA, Technology and Program Contingency, consistent with the respective scopes of work. After all other fund sources were added, OSM transferred in $25M in program contingency to make up the remainder of the budget for this critical project. As discussed in the May 2023 BAC meeting, while the need for this project was anticipated in the 2020 Bond measure with a set-aside of Capacity funds, the exact amount of funding was unknown at that time; the bond measure instead included a significant Program Contingency to address unknowns such this.
- Curriculum reporting in the Bond Programs Report shows Bond funds only. Non-bond funds related to planned bond scope were tracked in eBuilder for a short period of time only. For a full report of non-Bond funds used for planned bond scope, please see the Curriculum Project Status report in the February 2023 BAC update. The next Curriculum Project Status report will be presented at the November 2023 BAC update.

Modernization Project Updates

Definitions

STATUS DEFINITIONS

	As Planned	Caution	Impacts
Budget	Pre-50% const: > 10% Project Contingency	Pre-50% const: 0% - 10% Project Contingency	Pre-50% const: < 0% Project Contingency
	Post-50% const: > 5% Project Contingency	Post-50% const: 0% - 5% Project Contingency	Post-50% const: < 0% Project Contingency
Equity	certified business participation > 18% ***and*** workforce equity > 20%	certified business participation 10% - 18% ***or*** workforce equity 10% - 20%	certified business participation < 10% or workforce equity < 10%
Schedule	0 or less weeks delay to SC	0+ up to 4 weeks delay to SC	greater than 4 weeks delay to SC
Overall	budget, equity and schedule are all green	at least one category is yellow	at least one category is red

EQUITY CATEGORIES

MBE = Minority-owned Business Enterprise

WBE = Woman-owned Business Enterprise

SDVBE = Service Disabled Veteran-owned Business Enterprise

ESB = Emerging Small Business

N-C = Non-Certified, counted for credit from a Certified Business that "graduated" out or did not reapply for certification

Lincoln HS Replacement

Lincoln HS Modernization
August 2023

PPS Team Lead: Erik Gerding
Design: Bora Architects
Construction: Hoffman Pacificmark

STATUS AT A GLANCE

Legend:

- As planned: no concerns
- Caution: requires attention
- Impacts: impacts occurring

	As Planned	Caution	Impacts
Budget	X		
Equity	X		
Schedule	X		
Overall	X		

BUDGET

BUDGET		FUNDING		PROGRESS		FORECAST		CONTINGENCY IN CONTEXT	
Original Budget	**Current Budget**	Bond Funds	Other Funds	Actuals to Date	Additional Encumbered	**Estimate At Completion**	*Over/Under*	Work Complete / %	Contingency Remain / %
242,500,000	**242,619,558**	242,500,000	119,558	218,103,628	12,539,386	**231,228,186**	(11,391,371)	98%	5.21%

EQUITY

Percent of payments made to Certified owned businesses, percent of labor hours of apprenticeable trades; cumulative

	MBE	WBE	SDVBE	ESB	N-C	**TOTAL**	*goal*	MIN	*goal*	FEM	*goal*	**APPR**	*req*
Consultants	0.94%	5.51%	0.00%	2.32%	0.00%	**8.76%**	*18%*						
Contractors	2.45%	15.14%	0.04%	1.03%	1.42%	**20.08%**	*18%*						
Overall	2.32%	14.27%	0.04%	1.14%	1.29%	**19.06%**	*18%*						
Workforce								35%	*25%*	4%	*14%*	**22%**	*20%*

SCHEDULE

NEXT MILESTONE: School Opening On Track? Yes

PROJECT PHASE	2020				2021				2022				2023			
Planning																
Design																
Construction															☆	
School Opening(s)																

Baseline — Planning — Design — Construction — School Opening

Lincoln HS Modernization

Lincoln High School Replacement Design and Construction Schedule

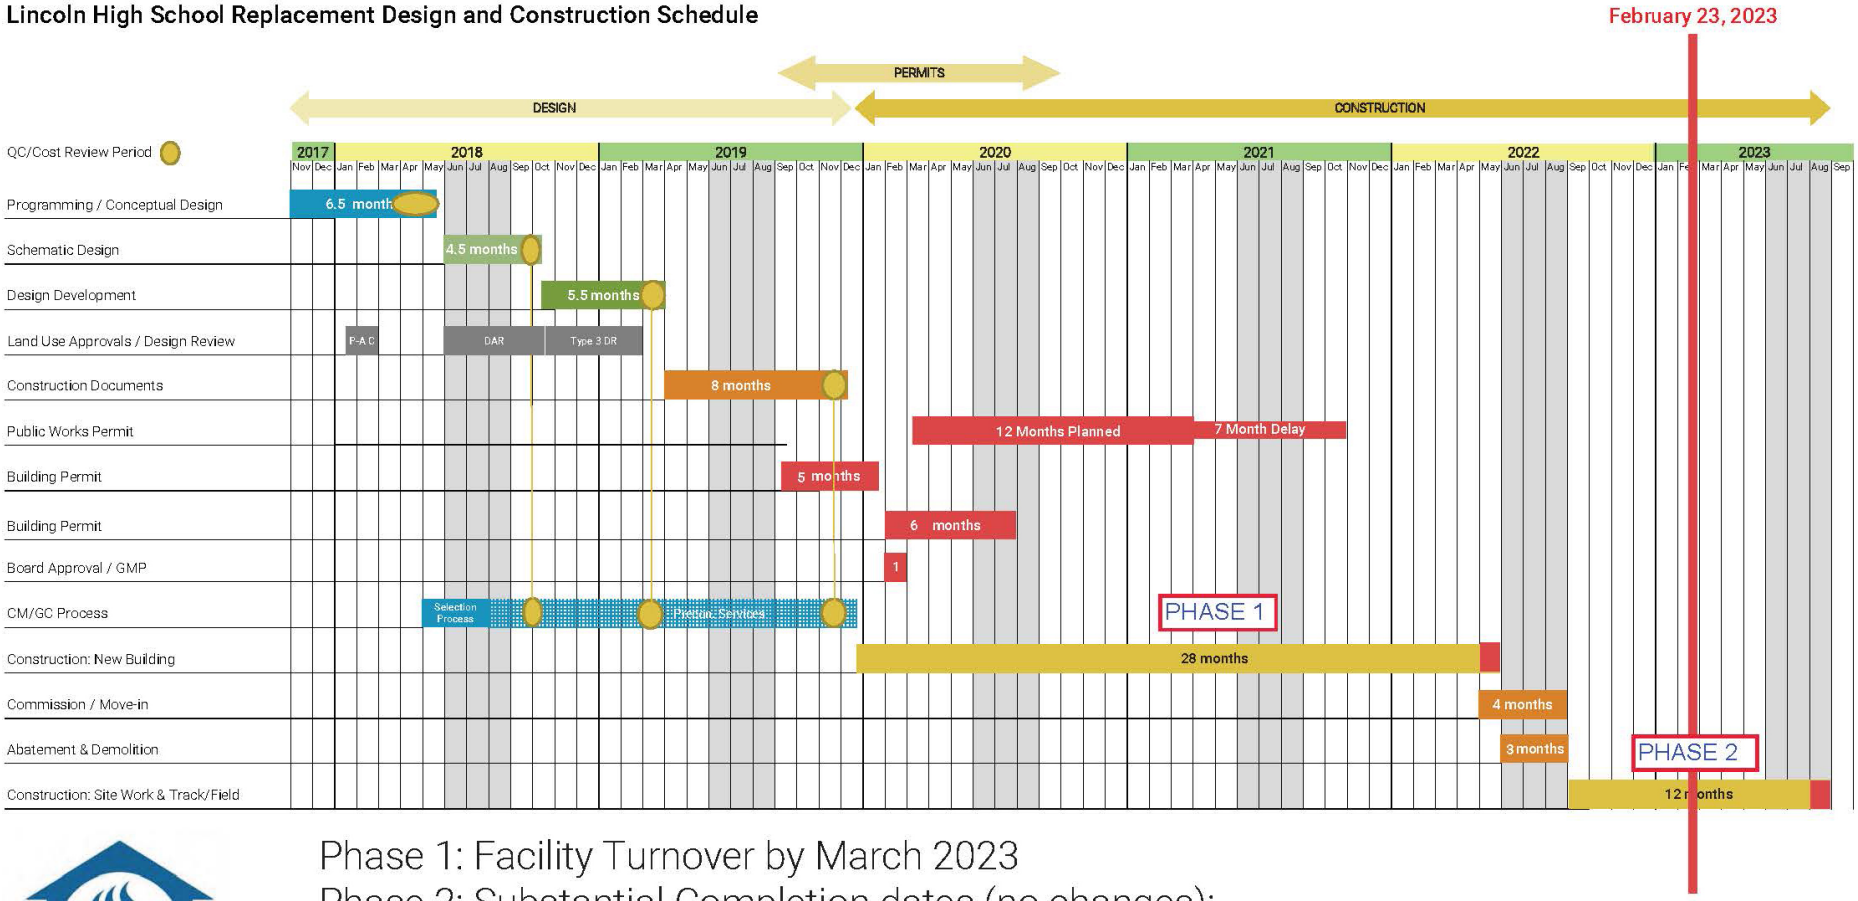

Phase 1: Facility Turnover by March 2023

Phase 2: Substantial Completion dates (no changes):

-Track & Field, Concessions Building, Parking Lot, Site Work- July 17, 2023.

-Teen Parent Center & Field Service Building - August 2, 2023.

-Grand Opening September 2023

Lincoln HS Modernization

Site Plan

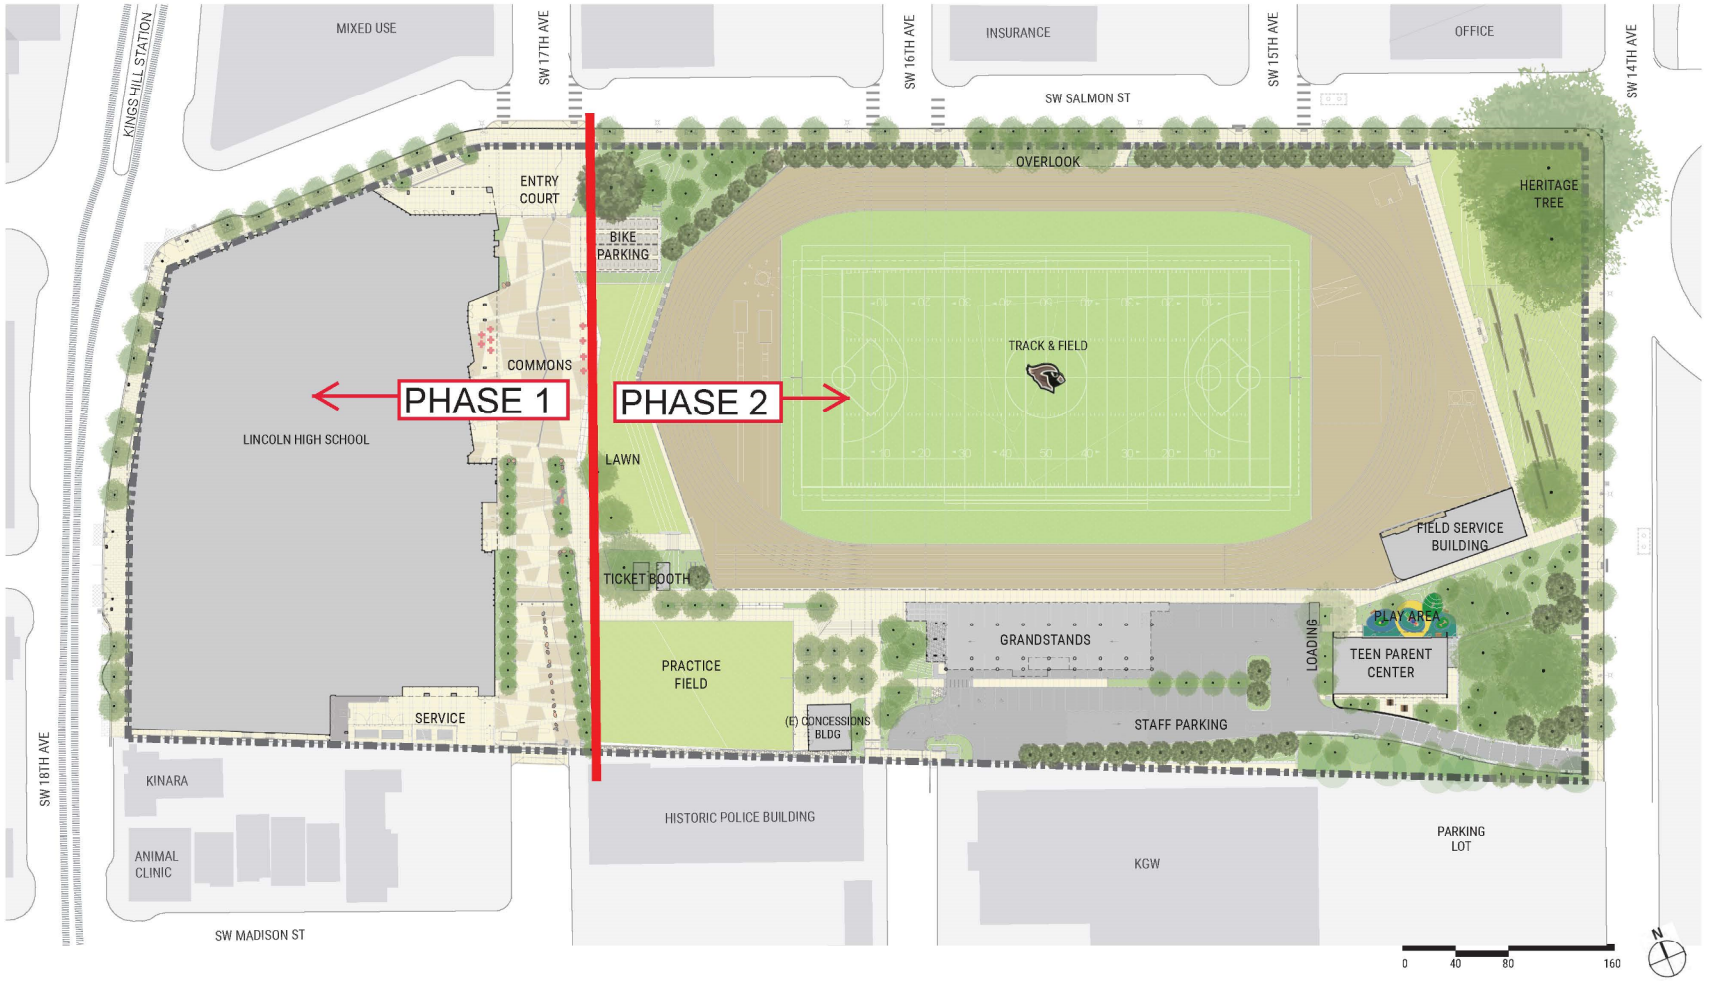

LINCOLN HIGH SCHOOL ACCESSORY BUILDINGS DR, OCTOBER 2021

Mayer/Reed BORA

Lincoln HS Modernization

AERIAL PHOTO – Phase 1 - July 2023

Lincoln HS Modernization

AERIAL PHOTO – August 2023

Lincoln HS Modernization

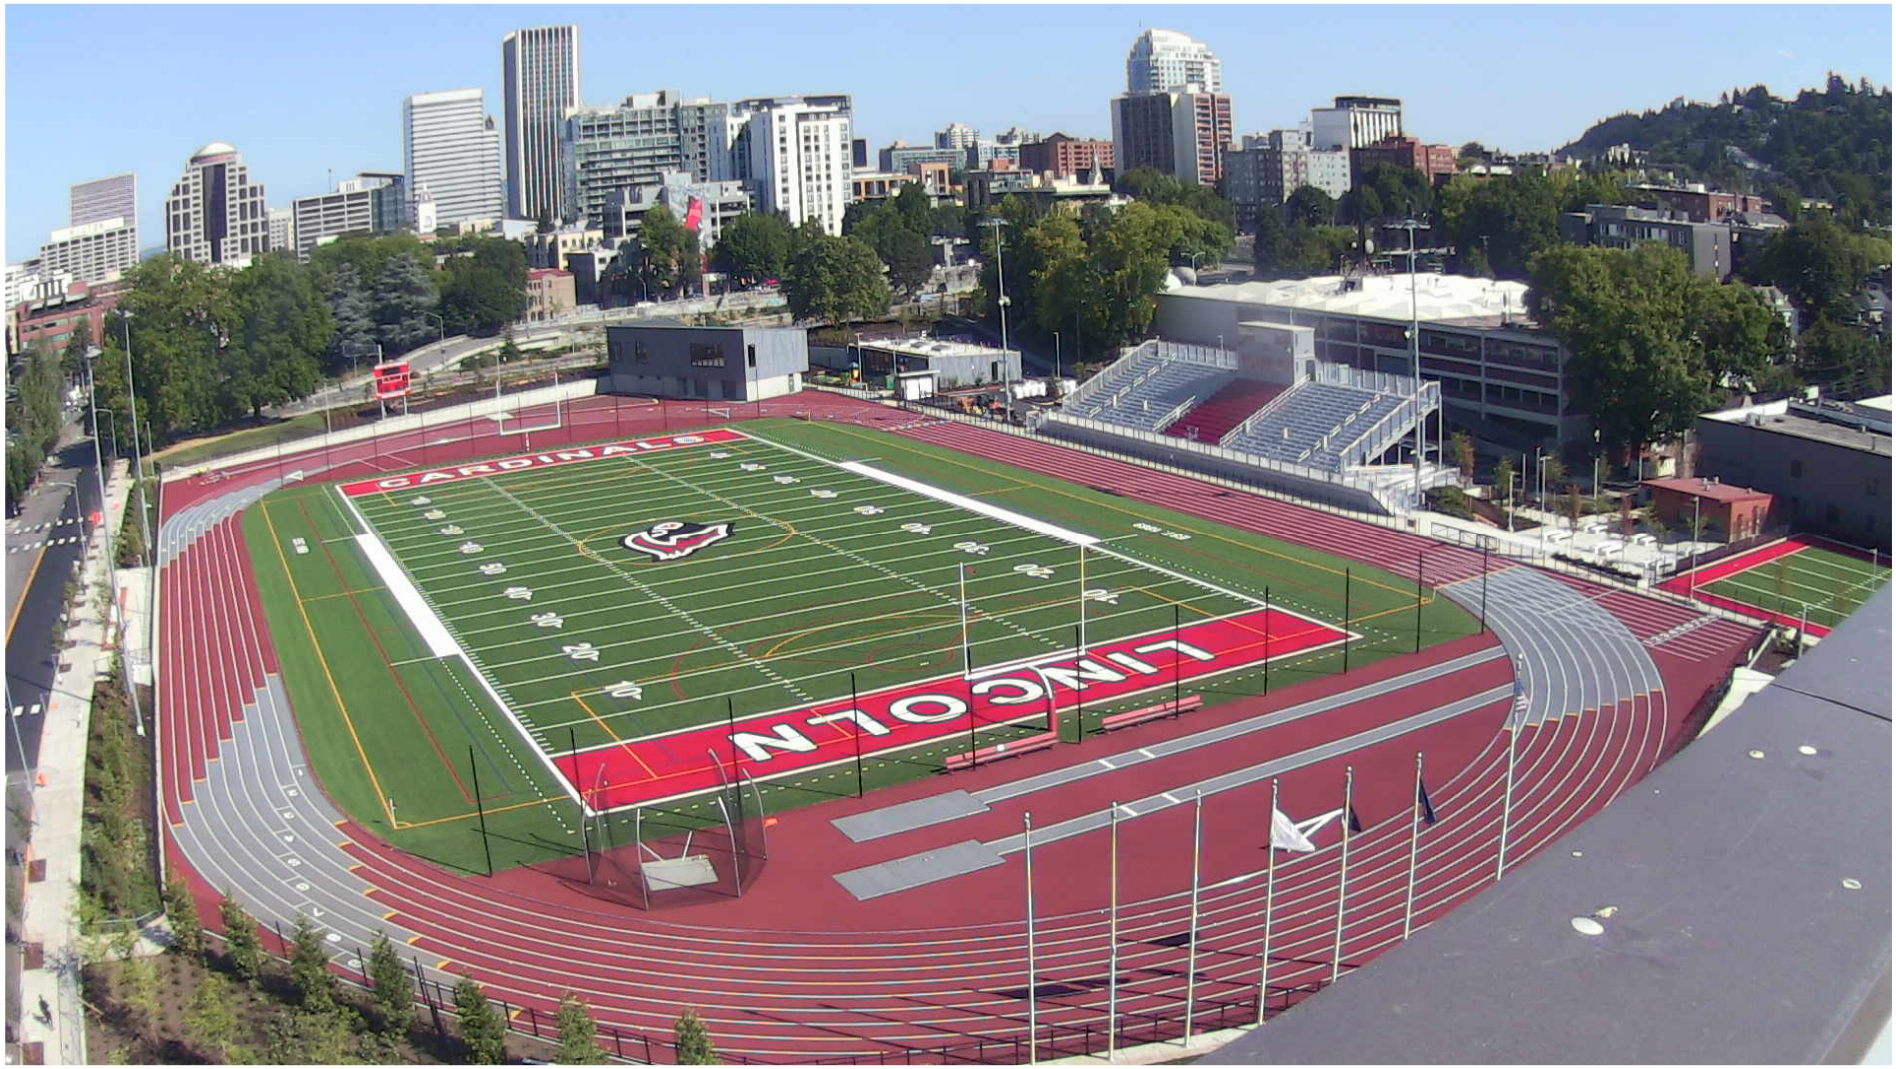

View from main building August 2023

Lincoln HS Modernization

Field Service Building

Lincoln HS Modernization

Lincoln HS Modernization

Teen Parent Center Play Area

Lincoln HS Modernization

Play Area and Field Service Building

Lincoln HS Modernization

Teen Parent Center

Lincoln HS Modernization

Concessions Plaza

Lincoln HS Modernization

Practice Field

SCHOOL BUILDING IMPROVEMENT BOND

Benson HS Modernization and Multiple Pathways to Graduation (MPG)

Benson HS / Benson Swing Sites / MPG
August 2023

PPS Team Lead: Armand Milazzo
Design Bassetti Architects
Construction Andersen Construction Co.

STATUS AT A GLANCE

Legend:

- As planned: no concerns
- Caution: requires attention
- Impacts: impacts occurring

	As Planned	Caution	Impacts
Budget		X	
Equity		X	
Schedule	X		
Overall		X	

BUDGET

	BUDGET		FUNDING		PROGRESS		FORECAST		CONTINGENCY	
	Original Budget	**Current Budget**	Bond Funds	Other Funds	Actuals To Date	Additional Encumbered	**Estimate At Completion**	*Over/Under*	Work Compl	Cont Remain
Benson HS	202,000,000	**320,388,075**	306,453,971	13,934,104	196,556,115	114,131,823	**321,704,885**	1,316,810	74%	1%
Swing Sites	-	**13,550,089**	13,544,288	5,801	12,205,396	27,883	**12,233,279**	(1,316,810)	100%	0%
MPG Building	-	**80,476,726**	80,447,075	29,651	34,296,468	42,237,109	**80,476,726**	-	50%	3%
Benson Totals	***202,000,000***	***414,414,890***	***400,445,334***	***13,969,556***	***243,057,979***	***156,396,815***	***414,414,890***	-		

EQUITY

Percent of payments made to Certified owned businesses, percent of labor hours of apprenticeable trades; cumulative

	MBE	WBE	SDVBE	ESB	N-C	**TOTAL**	*goal*	MIN	*goal*	FEM	*goal*	**APPR**	*req*
Consultants	4.99%	7.95%	0.00%	1.36%	0.00%	**14.31%**	*18%*						
Contractors	4.98%	7.24%	0.00%	2.81%	0.79%	**15.81%**	*18%*						
Overall	4.98%	7.34%	0.00%	2.60%	0.68%	**15.60%**	*18%*						
Workforce								36%	*25%*	8%	*14%*	**23%**	*20%*

SCHEDULE

NEXT MILESTONE: Substantial Completion On Track? Yes



BPHS & MPG Modernizations

BENSON & MPG SITES

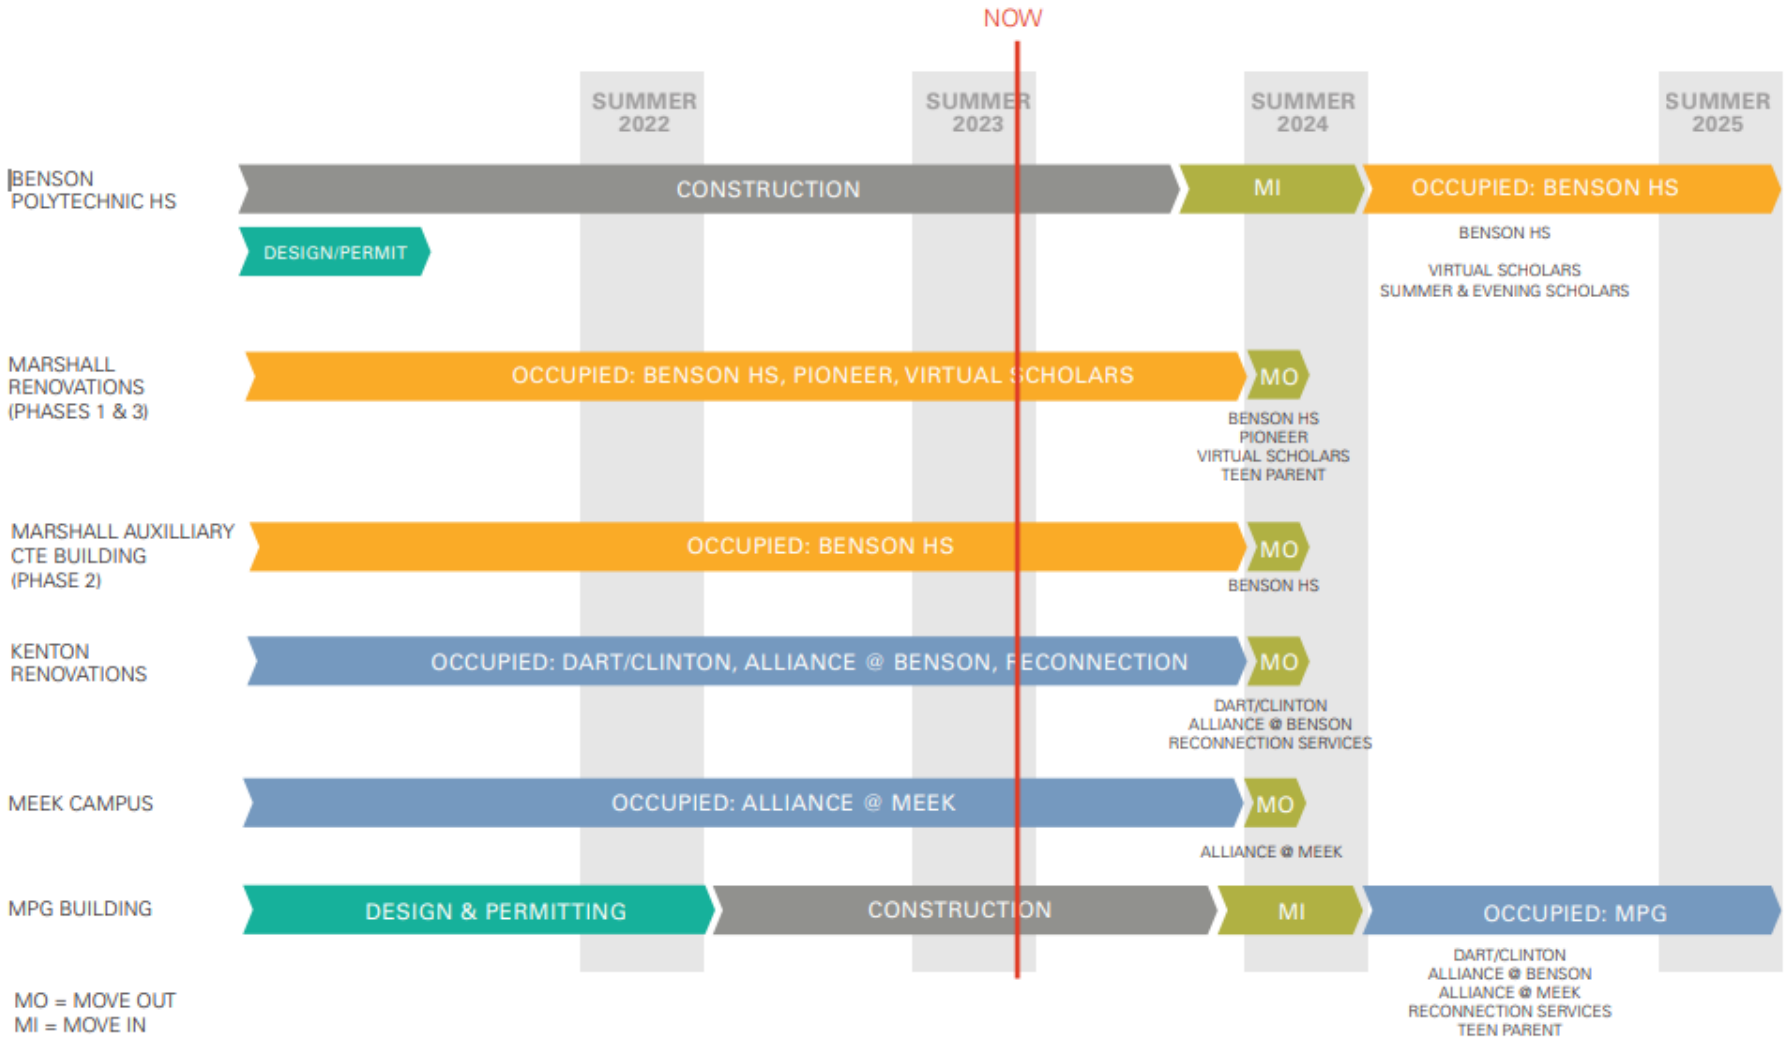

Benson Tech HS Modernization

Benson Polytechnic – All buildings are in construction

Benson Tech HS Modernization

Benson Tech incoming 9th grader site visit & grading for Universal Design Accessible main entrance

Benson Tech HS Modernization

Building B: New elevator shaft opening at Building E & A

Benson Tech HS Modernization

Historic building structural retrofit continues in historic foundry & gym buildings

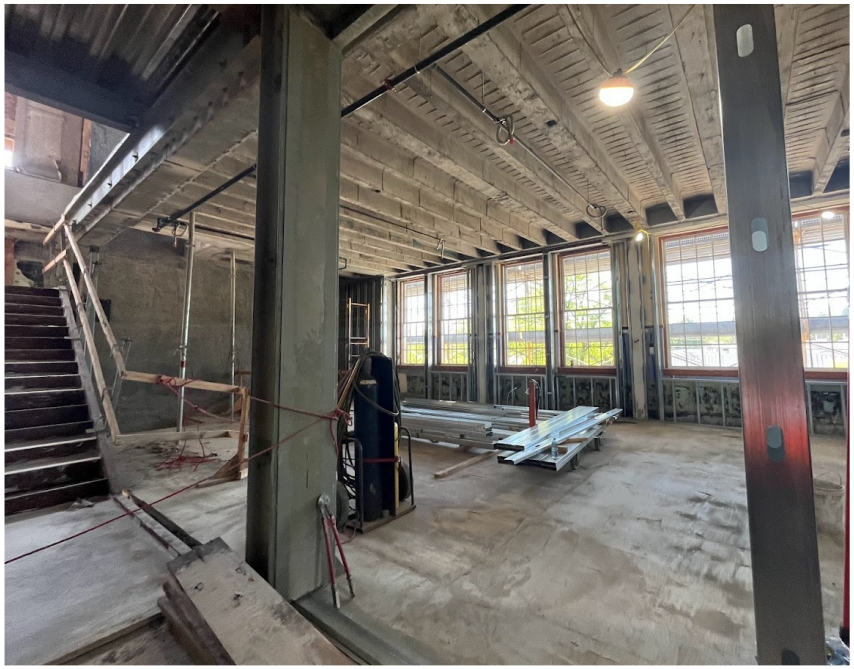

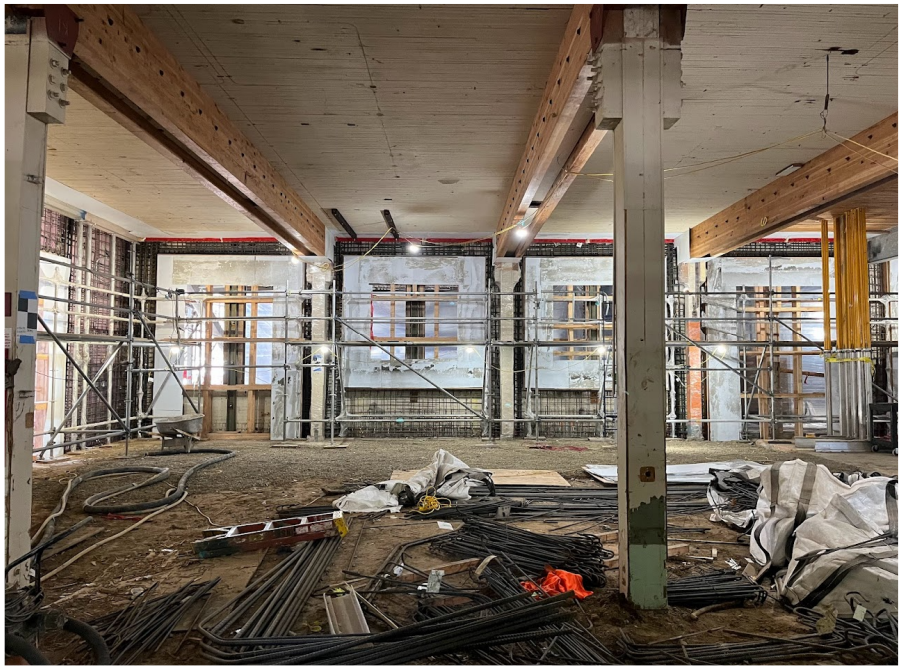

Benson Tech HS Modernization

Historic Gym window testing & truss / ceiling painting

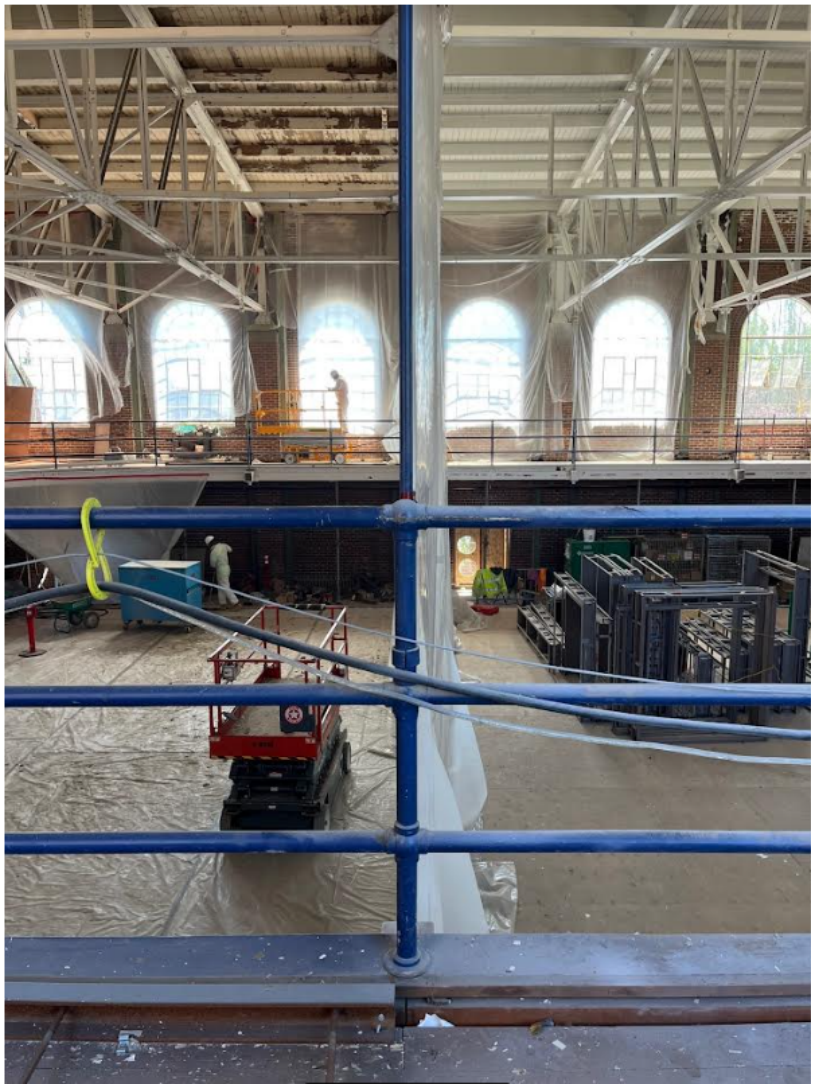

Benson Tech HS Modernization

South courtyard view above entry between Building H & the Main Gym

New Commons with Learning Stair & Kitchen/Cafeteria Servery in Building F

August 2023

Benson Tech HS Modernization

Exterior: New CTE shop wings / Building C & H

Benson Tech HS Modernization

Interior: Building C, New CTE shop wing

Benson Tech HS Modernization

Interior Finishes

Benson Tech HS Modernization

Interior Finishes

Benson Tech HS Modernization

Buckman Field Connection: new concrete stair & ramp footings

August 2023

Multiple Pathways to Graduation Building

From the top/ counter-clockwise: view of Multiple Pathways to graduation from Buckman Field, north entry elevation and parking garage interior.
