Multiple Pathways to Graduation Building

Exterior pre-fab wall panels arriving from Vancouver, WA and being installed.

Multiple Pathways to Graduation Building

Views of the interior showing mass timber construction, clockwise: west stairwell, Student Services and CTE Automotive shop.

SCHOOL BUILDING IMPROVEMENT BOND

Jefferson HS Modernization

Jefferson HS Modernization

August 2023

PPS Team Leads: Steve Effros, Kiesha Locklear, Ayana Horn
Design: BORA Architects, Lever Architecture
Construction: Andersen Construction, with Crossover Construction, Faison Construction, Northwest Infrastructure, Professional Lath & Plaster, Professional Minority Group

STATUS AT A GLANCE

Legend:

- As planned: no concerns
- Caution: requires attention
- Impacts: impacts occurring

	As Planned	Caution	Impacts
Budget	X		
Equity*		X	
Schedule	X		
Overall	X		

BUDGET

BUDGET		FUNDING		PROGRESS		FORECAST		CONTINGENCY IN CONTEXT	
Original Budget	**Current Budget**	Bond Funds	Other Funds	Actuals to Date	Additional Encumbered	**Estimate At Completion**	*Over/Under*	Work Complete / %	Contingency Remain / %
311,000,000	**366,007,500**	366,000,000	7,500	5,888,991	22,749,069	**366,007,500**	-	0%	15.00%

EQUITY

Percent of payments made to Certified owned businesses, percent of labor hours of apprenticeable trades; cumulative

	MBE	WBE	SDVBE	ESB	N-C	**TOTAL**	*goal*	MIN	*goal*	FEM	*goal*	**APPR**	*req*
Consultants	4.19%	2.84%	0.00%	0.00%	2.25%	**9.28%**	*18%*						
Contractors*	0.00%	0.00%	0.00%	0.00%	0.00%	**0.00%**	*18%*						
Overall	4.19%	2.84%	0.00%	0.00%	2.25%	**9.28%**	*18%*						
Workforce*								0%	*25%*	0%	*14%*	**0%**	*20%*

** Construction payments have not yet been made.*

SCHEDULE

NEXT MILESTONE: 100% SD

On Track? Yes



Baseline | Planning | Design | Construction | School Opening

Project Design & Budget Update Topics

1. **Schematic Design Process to date** Overview of cost estimates and main factors affecting cost differences
2. **Value Engineering Workshop** Process
3. **Value Engineering Workshop** Studies
4. **Value Engineering Workshop** Findings & Project Updates

Design Process Overview

●Schematic Design
Starting in January 2023, the Design team started developing the design with feedback from PPS stakeholders, JHS leadership, DAG, neighbors, alumni, current & future students, staff, City and land use officials

●SD Pricing Set (issued 4/28/23)
a set of concept drawings and narratives to describe the project at this early stage of design

●Design Team estimate (mid-May)
shows 19% overage for the project. This is within typical range at this phase.
(Estimate used national cost data, similar regional projects.)

●Andersen Construction joins Project Team (early May)
Andersen begins working with the design team to provide input on construction logistics and durations.

●Andersen provides second cost estimate (mid-June)
based on 4/28 SD Pricing Set using expertise in construction logistics and durations; shows significant overage.

●Value Engineering Workshop (7/10-14)
A week-long 9am-5pm workshop with members of the entire design & construction team to review, validate, and critique the design goals, re-assess previous assumptions and decisions, and look for opportunities to get the project cost back in line with the budget.

Jefferson HS Modernization

Integrated Collaborative Team

Project Values +
Goals

DAG/Neighbors/
Alumni/Current &
Future Students /Staff

Building Site
Project Scope +
Objectives
Project Schedule
Budget

Owner Team
PPS OSM

Construction Logistics
Construction Durations
Site Constraints
Market Conditions

(Contractor: Andersen
Construction)

Building features, systems, equipment, and material selections of a building design.

Design Team: Bora, Lever + Colloqate + Consultants

Jefferson HS Modernization

Jefferson Budget & Schedule Progresion

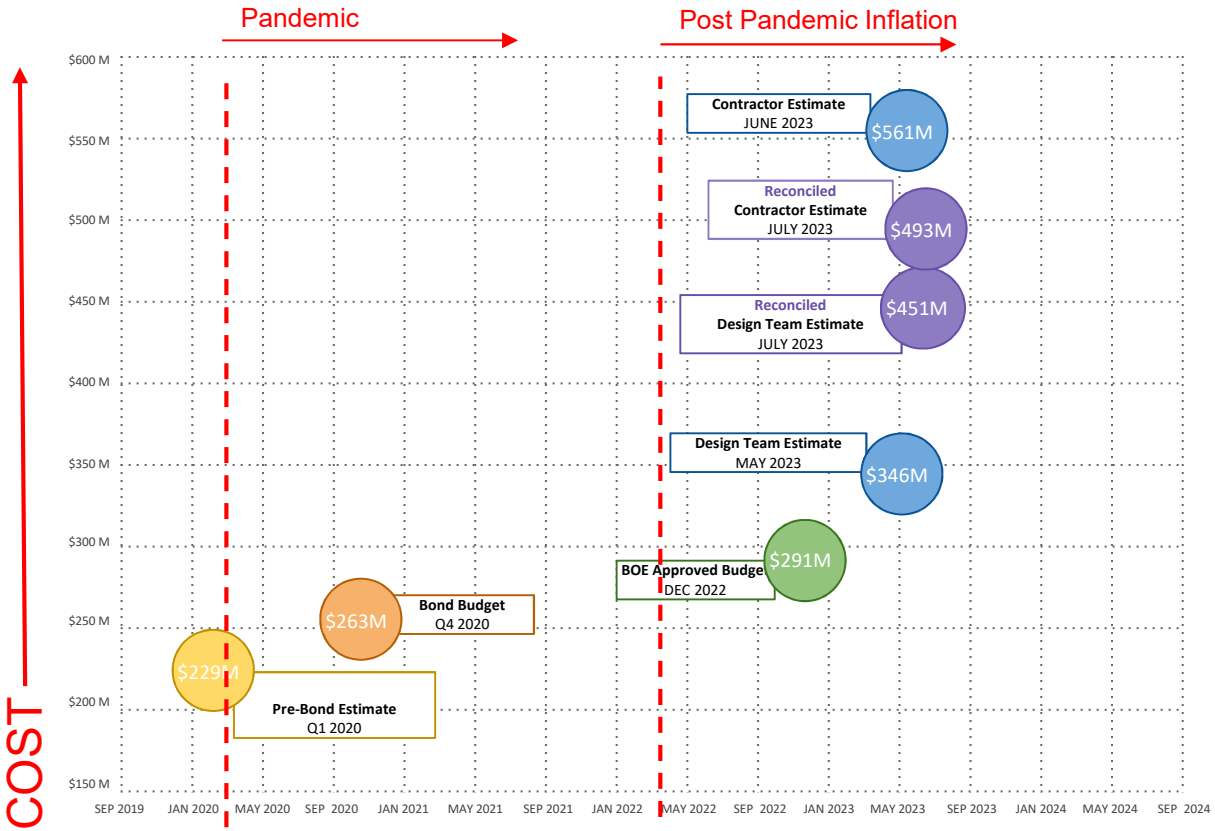

CMPC & 2020 BOND | COMPREHENSIVE PLANNING | DESIGN + PERMITTING | CONSTRUCTION to FALL 2027

Jefferson HS Modernization

Jefferson Budget & Schedule Progresion

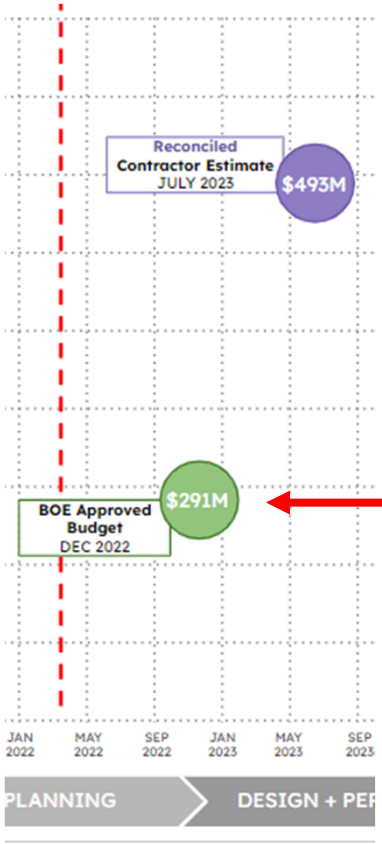

COST: $493M

BUDGET: $291M

$202 MILLION OVER BUDGET

Jefferson HS Modernization

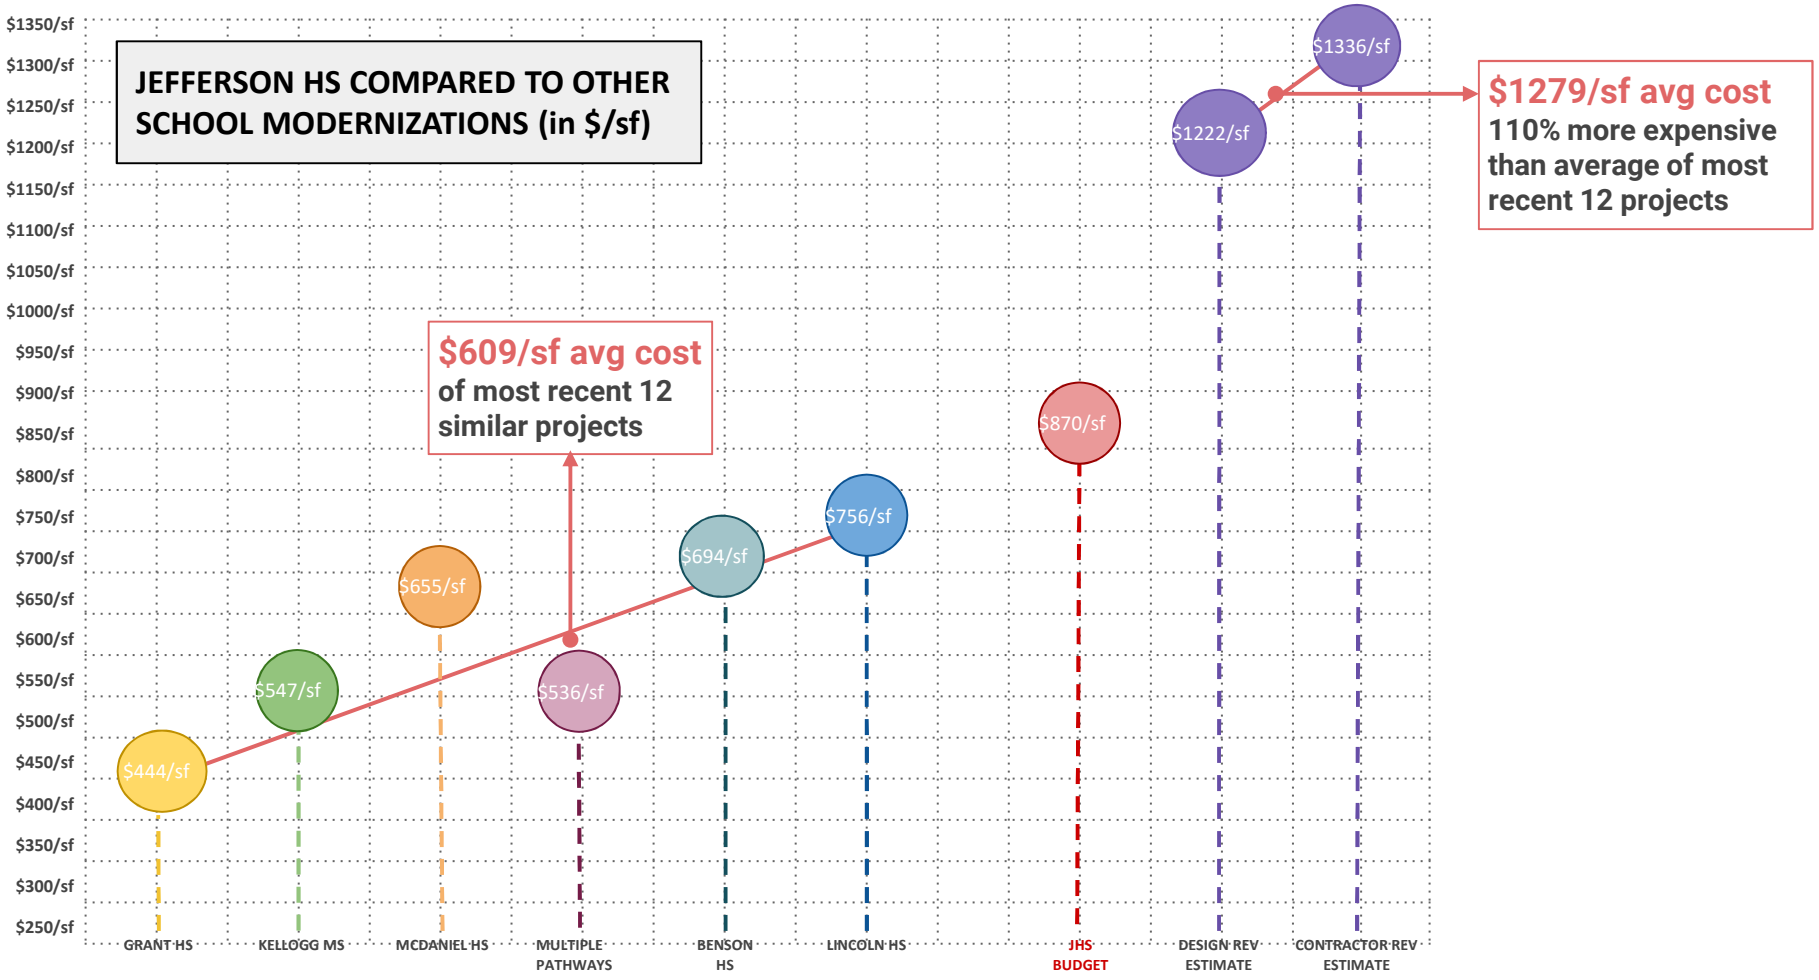

Jefferson HS Modernization

Multiple Factors Affecting Cost Difference vs. Budget

Keeping Students On Campus

Building Inefficiencies Due to Phasing + Accommodating Interim School Needs (~15,000-20,000sf) +

Complexity of phased partial demolition +

Complexity Of Phased Construction Increasing Construction Time +

Escalation (for 4 yrs) +

Increased Program (~18,000sf) +

Logistics On Constrained Site +

Constrained Building Area + Height Requires Basement +

Keeping 1909 4-Story Unreinforced Masonry Building (URM) +

Whole Project Designed To Seismic Category 4 +

Market + Labor Volatility (HVAC + Electrical Systems)

Jefferson HS Modernization

Immediate Actions & Studies

EVERYTHING ON THE TABLE

Reconsider demolishing the existing **1909 internal structure**

Saves $$$

Reconsider **temporary school** program (more efficient 1909 & less new construction)

Saves $$

Reconsider the **size of the school**

Not viable solution

Reconsider keeping the 1909 building - **students stay** on campus but **build a new school**.

Longer schedule- may not save $, broken commitment

Reconsider keeping and renovating the **1964 Gym**

Seismic upgrades- may not save $

Reconsider keeping and renovating the **existing theater**

Seismic & equipment upgrades- may not save $

Reconsider the **impact of phasing** construction - $$$$

Can we further condense the building **keeping** phasing?

OR

What would we do differently if we were NOT phasing? **(Condensed Option)**

Saves $$$$$

Broken commitment

Jefferson HS Modernization

Opportunities for more Study

Eliminate Phasing / Swing Off-Site

- Allows more efficient building organization
- Requires reconsideration of program distribution
- Avoids inefficiencies and expense of on-site interim school
- Note: changes move-in date no earlier than Fall 2027

Optimize Approach For **1909** Building

Explore:

- All new interior structure versus careful retention and upgrading
- Consider replacing 1909 building with a new similar structure

Reduce Building Size

- Find efficiencies
- Review all program especially added program since Board approval
- Reduce Basement
- Reconsider courtyards

Why is the 1909 Building so costly to retain?

- It's a 4-story unreinforced masonry building (URM)
- It's significantly more complex than the 2-story structures at Grant HS and Benson HS
- Complexity is exponential, causing logistics challenges and safety concerns
- And, complexity is compounded by PPS requirement to meet Risk Category IV

Schedule Implications of the Studies

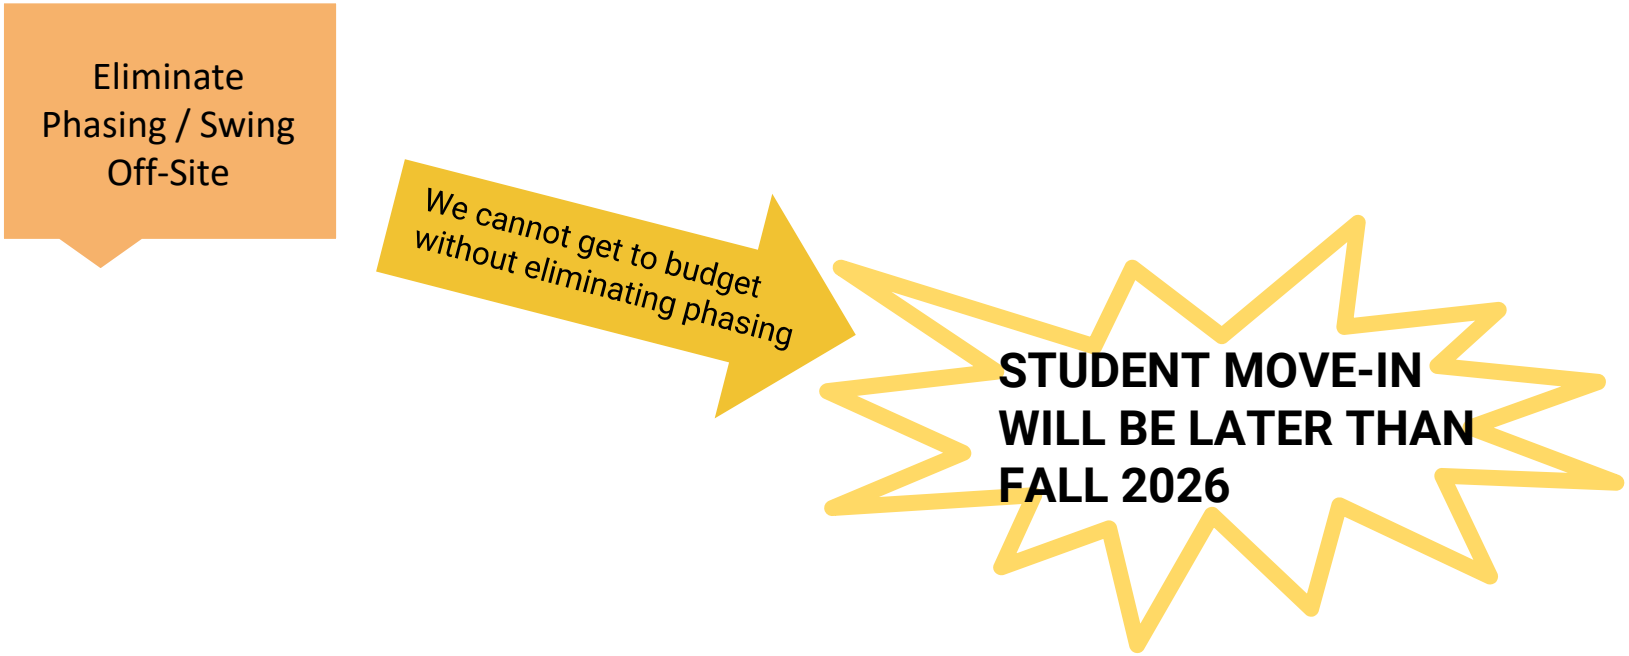

Jefferson HS Modernization

"Value engineering" is **standard part of the process**, and happens at each design phase. It is a formal process for reviewing design & cost.

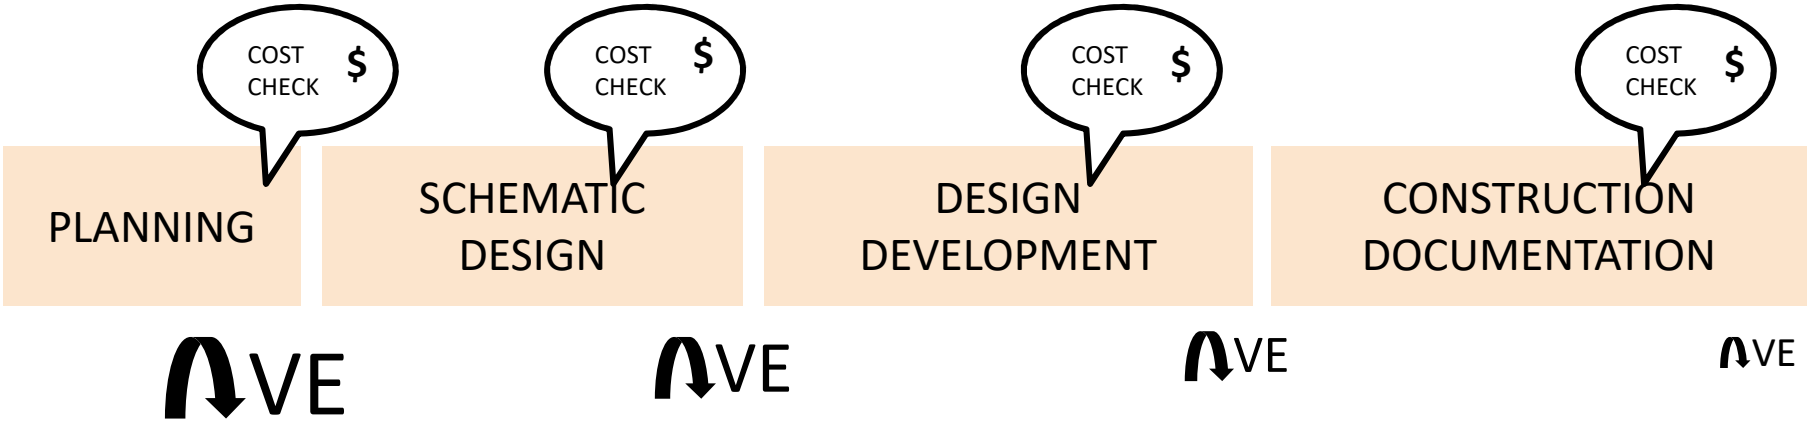

The difference between cost estimates and the project budget usually decreases as we progress through the design phases.

Jefferson HS Modernization

VE Workshop

July 10-14, 2023
Facilitated by an outside consultant

Roster of Attendees

- PPS leadership + stakeholders
- Design Team
  - Architectural
  - Structural engineers
  - MEP engineers
  - Landscape Architect
  - Other Design Consultants
  - Cost Estimator
- Construction Team
  - Project Manager
  - Cost Estimators
  - Consortium Partners
- Community Engagement team (Colloqate + CDOs)
- Members of the DAG

VE Workshop: Value Methodology

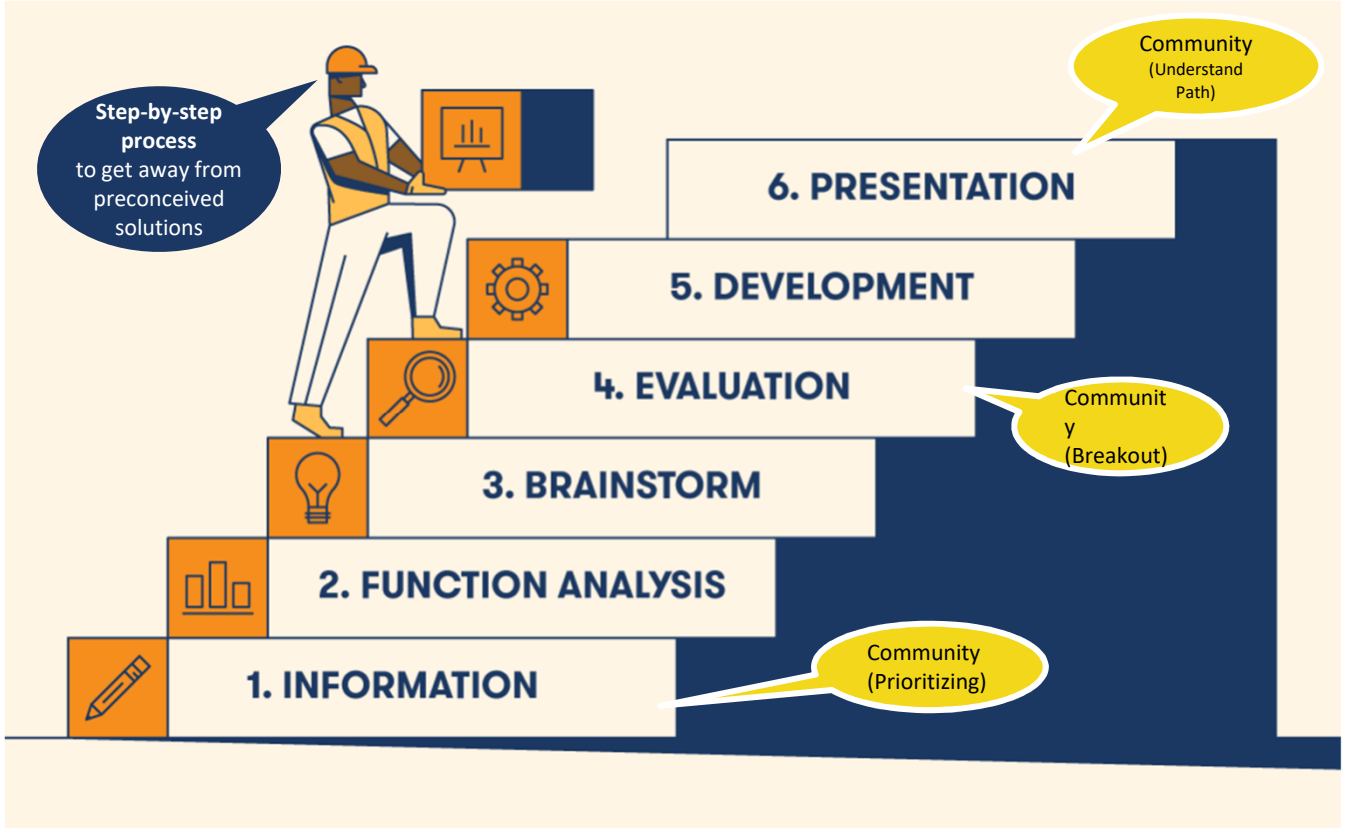

VE Workshop Objectives

- Align with Board-approved $291M budget
- Identify essential values and functions
- Bring:
  active participation
  creative ideas
  open minds

Jefferson HS Modernization

VE Workshop Performance Criteria

(filters to evaluate and score ideas)

- Trust & Racial Equity
- Flexibility & Change
- Access
- Identity, Culture & Belonging
- Resources
- Embrace the Outdoors
- Safety & Security
- Delight

- Durability & Resilience
- Schedule
- Maintain Academic Program during Construction
- Maintainability
- Sustainability

Community Narrative Themes

Creative Ideas Generated During Workshop

Jefferson HS Modernization

Review Schemes

Reconsider:

- "Condensed"
  Current design, condensed to single phase
- "Rebuild 1909"
  Build replica of 1909, all new in single phase
- "New NewSouth"
  Full replacement on south, aka Lincoln approach
- "New NewNorth"
  Full replacement on north, aka Lincoln approach

Threw away assumptions reconsider big ideas

against …

- Swing Required
- Land Use & Permitting
- Seismic Upgrades
- Area Reductions
- Program Alignment
- Design Schedule
- Construction Schedule
- Potential for Cost Alignment

… for more detail

- "Condensed"
- "Rebuild 1909"
- "New NewSouth"
- "New NewNorth"

These two offered more than the others

Jefferson HS Modernization

Original Design

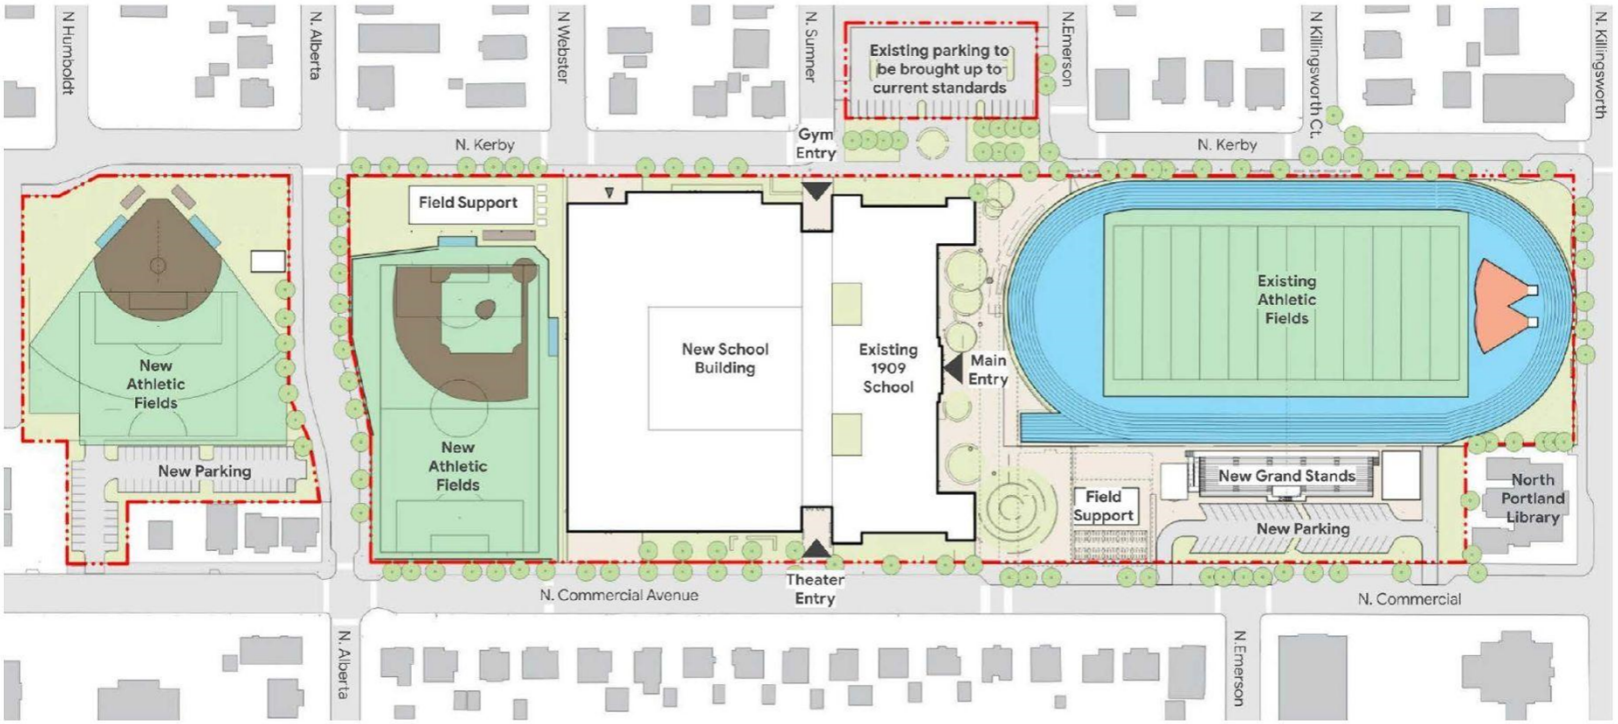

Jefferson HS Modernization

"Condensed" Scheme

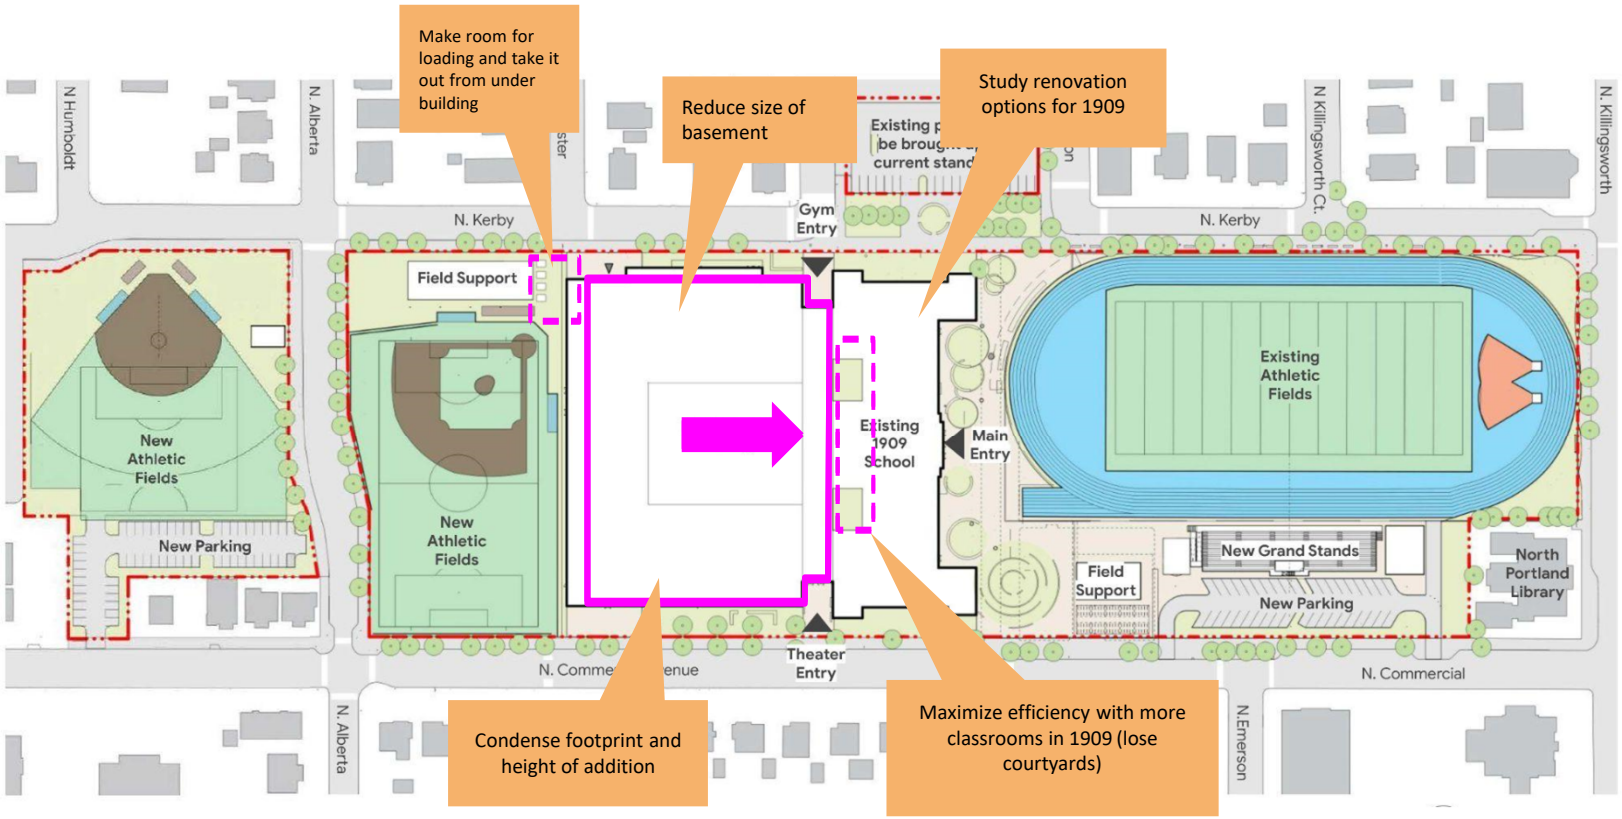

Jefferson HS Modernization

"Condensed" Scheme

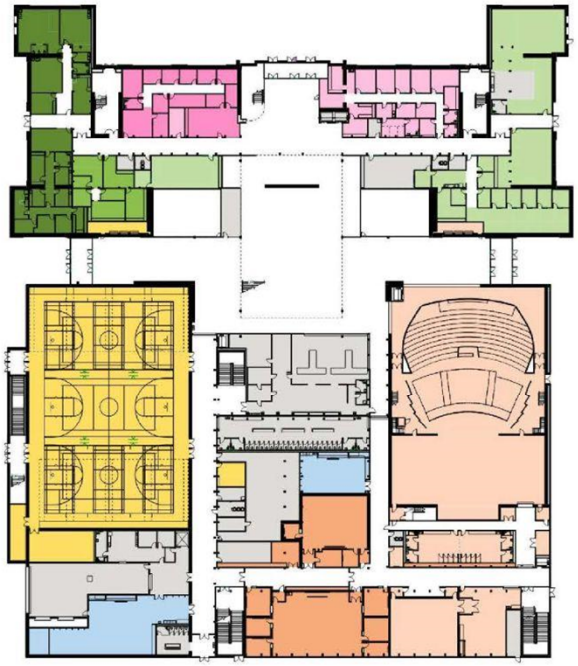

Previous 'Phased' Schem

Condensed 1-phase Scheme

- Keeps all approved program
- Keeps 1909 building
- Maximize 1909 building
- Reduce new construction to 2-stories
- No courtyards
- Students swing off campus

Jefferson HS Modernization

“New” New South Scheme

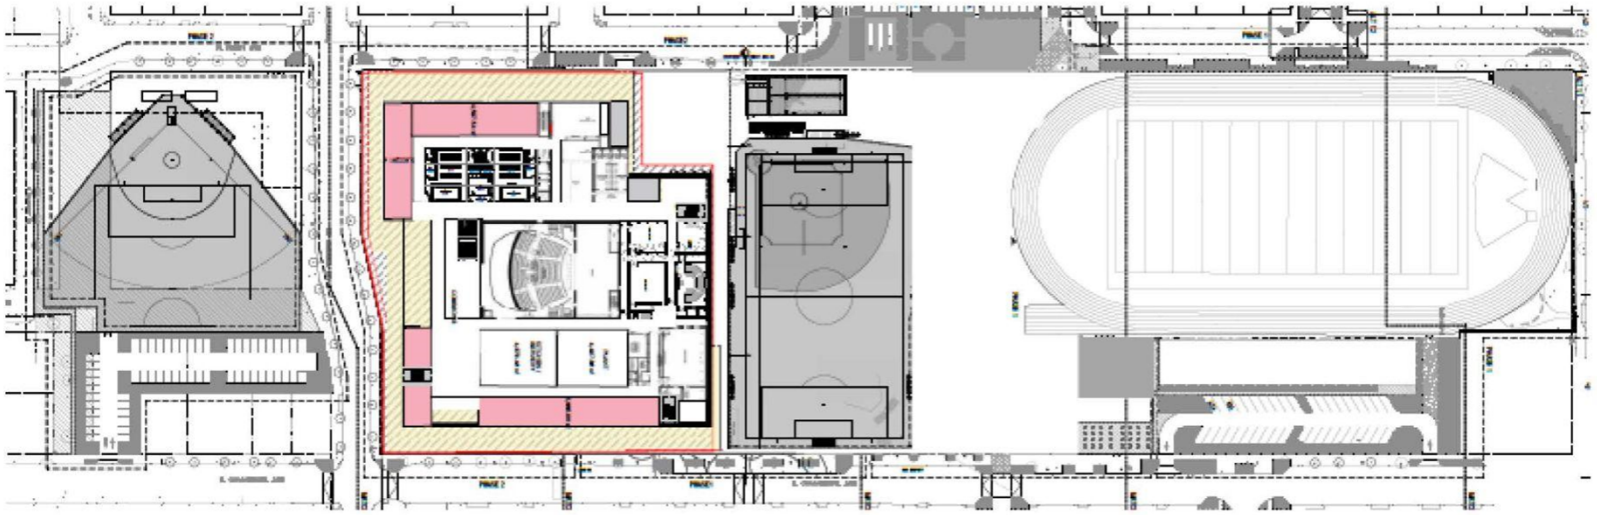

Jefferson HS Modernization

"New" New South Scheme

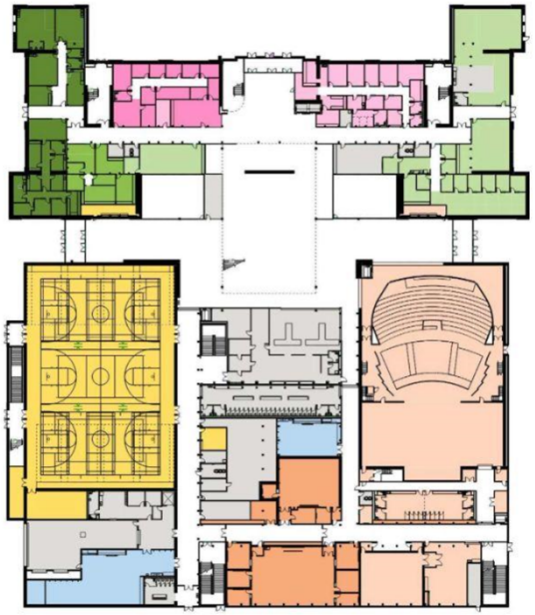

Previous 'Phased' Schem

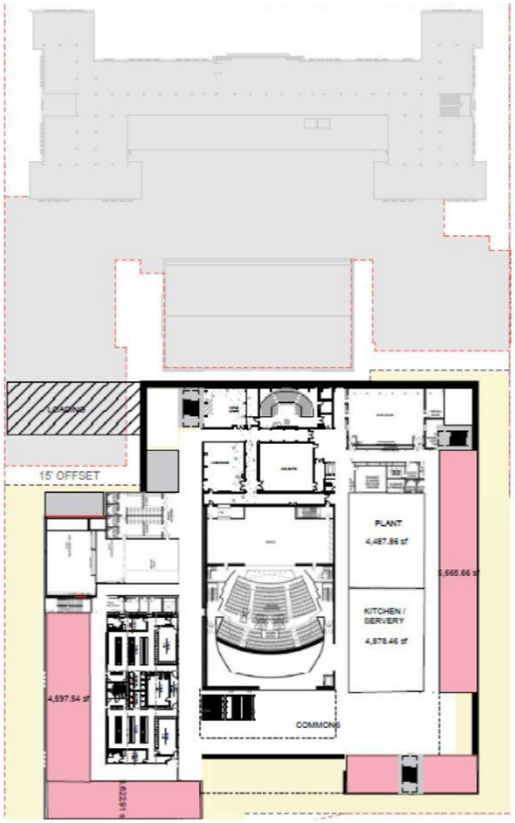

New "New South" Scheme

- Keeps all approved program
- Demolishes 1909 building
- Students stay on campus
- Highly compact new construction
- No opening until 2028 or 2029

Jefferson HS Modernization

"Condensed" Scheme Schedule

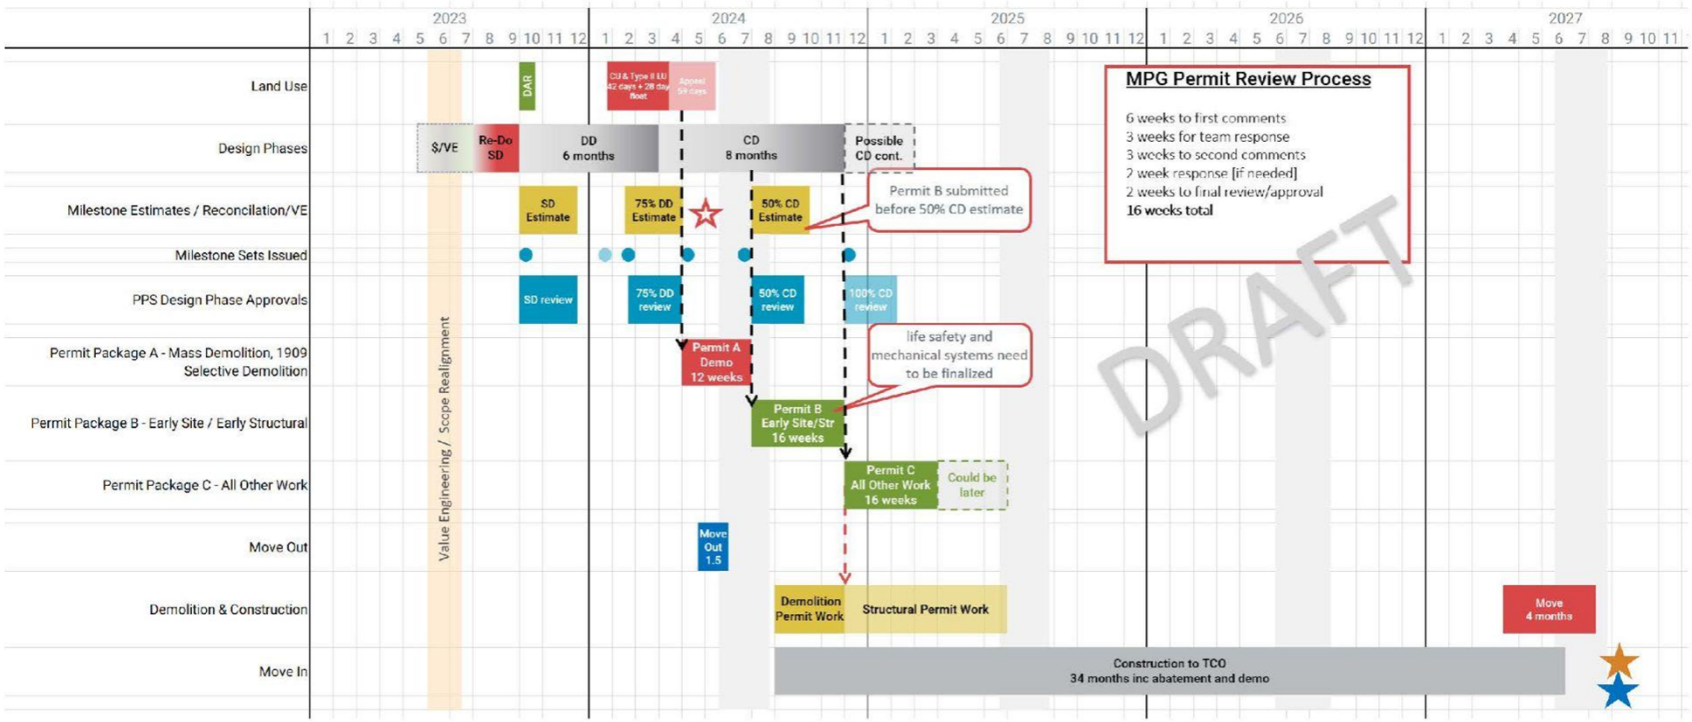

Jefferson HS Modernization

"New" New South Schedule

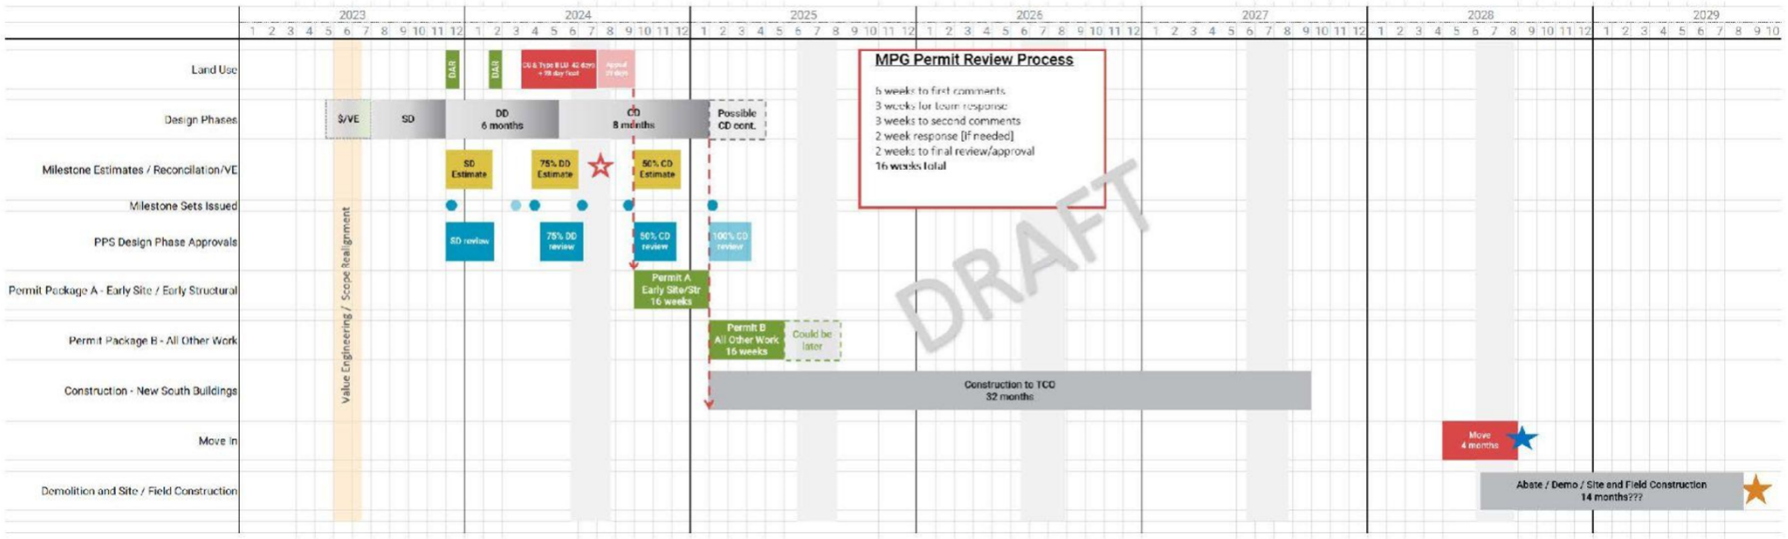

Jefferson HS Modernization

Budget with a SINGLE PHASE

Original "Phased" Scheme estimate: $493M		
Cost Item	Condensed Scheme	"New" New South Scheme
PPS Board-approved Budget	$291M	$291M
After changing to single phase	**$374M**	**$378M**

Jefferson HS Modernization

Target Value Design

Establishes target costs for each building system to guide design

BUILDING SYSTEMS

$ in system buckets can't add up to more than what was in the budget bucket

Jefferson HS Modernization

Target Value Design Results

Original "Phased" Scheme estimate: $493M		
Cost Item	Condensed Scheme	"New" New South Scheme
PPS Board-approved Budget	$291M	$291M
After changing to single phase	$374M	$378M
TVD Savings	($70M)	($77M)
After TVD exercise	**$304M**	**$301M**
Add'l savings needed from design process	($15M)	($10M)

Jefferson HS Modernization

Option Comparison

Variables	Condensed Scheme	"New" New South Scheme
Target Value Estimate	$304M	$301M
Swing	Off-site	On-site
Keep 1909?	Yes	No
Land Use Process	Easy	Hard
Schedule	Fall 2027	Fall 2028 (2029?)
Performance Criteria	???	???

Jefferson HS Modernization

Option Comparison

IMPACT TO PERFORMANCE: SCHEME ANALYSIS					
		CONDENSED SCHEME		"NEW" NEW SOUTH SCHEME	
Performance Criteria	Weight	Impact	Score	Impact	Score
Trust & Racial Equity	9.71%	9	0.9	-8	-0.8
Identity, Culture & Belonging	9.14%	10	0.9	-10	-0.9
Safety	13.71%	8	1.1	-5	-0.7
Access	1.14%	10	0.1	-5	-0.1
Flexibility & Change	6.86%	6	0.4	6	0.4
Resources	8.00%	8	0.6	6	0.5
Delight	6.86%	9	0.6	-5	-0.3
Embracing the Outdoor	6.86%	8	0.5	4	0.3
Durability & Resiliency	12.57%	7	0.9	10	1.3
Maintain Academic Program during Construction	0.57%	5	0.0	9	0.1
Schedule	2.29%	-5	-0.1	-10	-0.2
Maintainability	14.29%	9	1.3	7	1.0
Sustainability	8.00%	10	0.8	5	0.4
		TOTAL IMPACT TO PERFORMANCE SCORE	8.1		0.9

Value Engineering Workshop: Key Outcomes

Implications and process towards value alignment with $291M Board-approved budget:

1

Move forward with Target Value Design Process

Retain + update 1909 existing main structure

Continuous estimating feedback as design elements, systems, equipment and materials are further defined

2

Condensed building footprint with renovation of 1909 and addition

Review + finetune space program to board approved area of 334,410 gsf

Revisit site design to meet outdoor space needs + desires

Refine building organizational layout to find more design efficiencies

3

Eliminate multiple phases to single phase project complete in 2027

Swing school evaluations + implications

Jefferson HS Modernization

JHS Swing Site Evaluation

Variables	Marshall	Kenton	PCC
Meets Educational Program			
Meets Gen Ed classroom count	Yes	Yes	Yes
Meets Science classroom count	Yes	No	No
Meets Visual Arts classroom count	Yes	No	No
Meets Performing Arts count	Yes	No	No
Accommodates Athletics + PE	Yes	Impacted	Impacted
Accommodates CTE programs	Yes	No	No
Maintain access to PCC	Likely	Likely	Yes
Meets Common Spaces Needs			
Cafeteria	Yes	Yes	Impacted
Library	Yes	Yes	Impacted

Jefferson HS Modernization

JHS Swing Site Evaluation

Variables	Marshall	Kenton	PCC
Meets Administrative & Student Support Needs			
Accommodates offices	Yes	Yes	Yes
Access to childcare	Yes	No	No
Room for Community Partners	Yes	No	No
Accommodates Health Clinic	Yes	No	No
Other Considerations			
Opportunity for growth in student population	Yes	No	No
Land use/ zoning	Yes	Impacted	No
Travel Distance from Jefferson	11 miles	2 miles	0
Travel Distance from Swing Site to PCC	1.5 miles	1.7 miles	0
Cost to project	~ $1.5MM	~ $3MM	~ $10MM

JHS Next Steps

- PCC Middle College Partnership – development and communication of details on how this will be accessed from Marshall Campus
- Transportation – continued work with PPS Transportation on details of busing, development of maps/flyers/web, communication to Jefferson families
- Design Development phase starts in two weeks

Adjourn

Next meeting:
November 29, 2023, 5:30-8:00pm
location TBD (in person)
