School Improvement Bond Update

Bond Accountability Committee Meeting

July 24, 2024

Agenda

• Welcome & Introduction	5:30 – 5:40 pm
• Public Comment	5:40 – 5:45 pm
• Program Administration Updates	5:45 – 6:00 pm
• 2020 Technology Project Updates	6:00 – 6:15 pm
• Modernization Project Updates	6:15 – 7:15 pm
• Audit Implementation Review	7:15 – 7:30 pm
• Adjourn	7:30 pm

Public Comment

(public comments received via email prior to the meeting will be read aloud)

Business Equity Utilization Data Constraints

Business equity utilization data from the B2GNow software system represents a point in time and may not fully represent actual payments received by Certified Businesses. The accuracy of the utilization data is contingent on several factors:

- PPS's payment data from PeopleSoft is uploaded into B2GNow monthly and reflects all payments from PPS to prime contractors during the prior month.
- Accurate data on payments to subcontractors is contingent on prime contractors or upper tier subs entering their subcontractors in B2GNow and subsequently self-reporting their monthly payments to each subcontractor in a timely and accurate manner.
- If prime contractors (or first tier subs) enter payments to first tier or subsequent tier subs in a timely manner, the total equity utilization calculation can be expected to accurately reflect contract expenditures as of approximately one to two months prior to the report date.
- If prime contractors (or first tier subs) do not enter payments to first tier or subsequent tier subs in a timely manner, accurate equity utilization data will be delayed, at times significantly. Even closed contracts may be updated later if PPS learns of new subcontractor payments that were made months or even years prior.

Program Administration Updates

Bond Program Administration

Office of School Modernization - Program

July 2024

STATUS AT A GLANCE

Legend:

	As planned: no concerns
	Caution: requires attention
	Impacts: impacts occurring

	As Planned	Caution	Impacts
Budget	X		
Equity		X	
Overall	X		

EQUITY

		BUSINESS EQUITY							WORKFORCE EQUITY					
		MBE	WBE	SDVBE	ESB	N-C	**TOTAL**	*goal*	MIN	*goal*	FEM	*goal*	**APPR**	*req*
Cumulative	Current	4.96%	8.33%	0.05%	2.03%	1.14%	**16.51%**	*18%*	**31%**	*25%*	**5%**	*14%*	**23%**	*20%*
	Prior Report	4.91%	8.44%	0.05%	2.27%	1.15%	16.82%		**31%**		5%		**23%**	
12 Month	Current	7.17%	8.29%	0.00%	0.73%	1.94%	**18.13%**	*18%*						
	Prior Report	6.89%	8.35%	0.00%	0.76%	1.99%	17.99%							

Percent of payments made to Certified owned businesses, cumulative and 12-month rolling; Percent of labor hours of apprenticeable trades, cumulative

BUDGET

	BUDGET		FUNDING		PROGRESS		FORECAST	
2012 PROGRAM	Original Budget	**Current Budget**	Bond Funds	Other Funds	Actuals To Date	Additional Encumbered	**Estimate At Completion**	*Over/Under*
Franklin HS Mod	81,585,655	**112,932,069**	110,950,414	1,981,656	112,932,069	-	**112,932,069**	-
Grant HS Mod	88,336,829	**158,531,760**	155,310,987	3,220,774	158,531,760	-	**158,531,760**	-
Roosevelt HS Mod	68,418,695	**101,631,108**	97,127,989	4,503,119	101,631,108	-	**101,631,108**	-
Faubion Replace	27,035,537	**50,028,171**	34,328,327	15,699,845	50,028,171	-	**50,028,171**	-
Grant Upper Field	-	**3,170,988**	3,170,988	-	3,170,988	-	**3,170,988**	-
RHS Phase IV	-	**6,157,969**	6,153,741	4,228	6,157,969	-	**6,157,969**	-
Other Projects	123,441,923	**118,273,603**	113,012,885	5,260,717	118,273,603	-	**118,273,603**	-
							2012 Project Subtotals	-
Administration	68,117,563	**28,074,794**	27,324,871	749,923	28,074,794	-	**28,074,794**	-
Contingency	25,063,798	**452,047**	452,047	-	-	-	-	(452,047)
							2012 Program Subtotals	*(452,047)*
Totals	*482,000,000*	***579,252,509***	*547,832,248*	*31,420,261*	*578,800,463*	-	***578,800,463***	*(452,047)*

2012 Budget Notes

99.9% Spent

- Staff are working through closing out all non-active 2012 commitments and projects, and returning unspent funds to the Program.
- Any remaining 2012 funding will go towards prior add-on project requests at 2012 modernizations.
- Remaining program contingency is being shown for transparency but, as noted above, will go to prior add-on project requests once all other funding sources and expenditures have been reconciled.

Bond Program Administration

Office of School Modernization - Program

July 2024

2017 PROGRAM	BUDGET		FUNDING		PROGRESS		FORECAST	
	Original Budget	**Current Budget**	Bond Funds	Other Funds	Actuals To Date	Additional Encumbered	**Estimate At Completion**	*Over/Under*
Benson HS Mod	202,000,000	**156,828,877**	142,894,773	13,934,104	138,539,291	44,925,671	**157,402,082**	573,204
Benson Swings	-	**12,205,396**	12,199,595	5,801	12,205,396	-	**12,205,396**	-
Lincoln HS Repl	187,000,000	**242,619,558**	242,500,000	119,558	223,857,113	6,772,135	**224,416,443**	(18,203,115)
Kellogg MS Replace	45,000,000	**57,941,414**	57,697,500	243,914	57,892,035	582	**57,892,617**	(48,797)
McDaniel Mod	146,000,000	**200,717,847**	197,000,000	3,717,847	200,370,769	171,496	**200,533,888**	(183,959)
Health & Safety	-	**155,707,888**	124,526,616	31,181,272	143,929,782	2,474,025	**155,707,888**	-
Athletics	-	**5,013,412**	4,895,489	117,923	1,798,724	994,969	**5,013,412**	-
	-	-	-	-	-	*2017 Project Subtotals*		*(17,862,666)*
Administration	40,000,000	**61,807,686**	61,661,660	146,026	52,510,369	4,790,815	**57,505,530**	(4,302,156)
Contingency	20,000,000	**18,777,898**	18,777,898	-	-	-	**14,400,000**	(4,377,898)
Unallocated H&S	150,000,000	**25,562,238**	25,562,238	-	-	-	**25,562,238**	-
Unalloc Athletics	-	**104,511**	104,511	-	-	-	**104,511**	-
	-	-	-	-	-	*2017 Program Subtotals*		*(8,680,054)*
Totals	*790,000,000*	***937,286,725***	*887,820,281*	*49,466,444*	*831,103,480*	*60,129,694*	***910,744,005***	*(26,542,720)*

2017 Budget Notes

88% Spent

- Benson HS Modernization funding is split between 2017 and 2020. The 2017 Benson HS Modernization information shown above reflects 2017 funding and budget only, with actuals and additional encumbered specific to the 2017 funding as well.
- The Lincoln Modernization project is forecasting roughly $18.2M under budget after Substantial Completion of Phase 2. These funds will ultimately be returned to 2017 Program contingency.
- There is ongoing discussion with the Board of Education (BOE) regarding use of remaining 2017 Program contingency funds. $10M in bond funds were committed as a match to Portland Clean Energy Fund (PCEF) funds as part of Portland Association of Teachers (PAT) contract negotiations.
- As the 2017 Health & Safety projects wind down, OSM is also reviewing to ensure that any Health & Safety funds not needed to complete certain categories of H&S scope get reallocated to other H&S categories, to ensure that the full $150M dedicated to Health & Safety projects by the 2017 Bond measure is utilized as such. Current pressing needs include ongoing roof replacements, as well as replacement of fire alarm panels.

Bond Program Administration

Office of School Modernization - Program

July 2024

2020 PROGRAM	BUDGET		FUNDING		PROGRESS		FORECAST	
	Original Budget	**Current Budget**	Bond Funds	Other Funds	Actuals To Date	Additional Encumbered	**Estimate At Completion**	*Over/Under*
Benson 2020 funds	-	**164,903,890**	164,903,890	-	134,214,300	30,689,590	**164,903,890**	-
Jefferson HS Mod	311,000,000	**366,007,500**	366,000,000	7,500	13,425,940	25,946,752	**490,752,796**	124,745,296
CBSE	60,000,000	**60,000,000**	60,000,000	-	-	-	**60,000,000**	-
Cleveland HS Design	20,000,000	**20,000,000**	20,000,000	-	1,913,744	9,593,842	**20,000,000**	-
Wells HS Design	20,000,000	**20,000,000**	20,000,000	-	1,230,467	269,730	**20,000,000**	-
Roosevelt PhV Desigr	2,000,000	**2,000,000**	2,000,000	-	97,625	80,861	**2,000,000**	-
MPG Building	64,000,000	**80,476,726**	80,447,075	29,651	67,603,919	10,188,355	**80,536,704**	59,978
Curriculum	53,444,000	**53,444,000**	53,444,000	-	44,032,485	8,662,492	**53,444,000**	-
Technology	128,200,000	**143,503,600**	128,200,000	15,303,600	86,099,107	26,821,329	**142,630,791**	(872,809)
Infra Projects	-	**247,170,421**	242,112,555	5,057,866	150,655,743	67,806,657	**247,170,421**	-
						2020 Project Subtotals		*123,932,465*
Administration	63,098,640	**63,124,758**	63,098,640	26,118	16,951,772	3,504,231	**63,124,758**	-
2017 Bond Balance	152,000,000	-	-	-	-	-	-	-
Contingency - OSM	93,257,360	**52,962,689**	52,962,689	-	-	-	**52,962,689**	-
Unalloc Proj Funds	241,000,000	**36,261,005**	36,261,005	-	-	-	**36,261,005**	-
	-	-	-	-	-	*2020 Project Subtotals*		-
Totals	*1,208,000,000*	***1,309,854,589***	*1,289,429,855*	*20,424,735*	*516,225,101*	*183,563,840*	***1,433,787,054***	*123,932,465*

2020 Budget Notes

35% spent

- The Benson HS modernization team has worked diligently to remain in budget, despite early unanticipated costs (detailed in previous reports), however OSM is negotiating change orders with contractor Andersen Construction for overtime labor to mitigate schedule delays. This is a potential significant financial risk and OSM is reviewing this issue with the contractor.
- OSM anticipates utilizing another $31M of 2020 Bond Program contingency to ensure planned district-wide scopes in mechanical improvements (controls upgrades) are completed equitably across the District.
- Estimate at Completion for Jefferson HS Modernization has been updated to the cost estimate for the revised conceptual plan that was presented to the Board in early April. The needed additional funds are currently included in planning for a 2024 Bond measure.
- Encumbrances shown for Cleveland HS are for design fees through the Design Development phase.
- Encumbrances shown for Wells HS are for design fees through the end of Comprehensive Planning. Design fees through the end of Design Development are in negotiation with the Architect. CM/GC Pre-Construction fees will be negotiated and encumbered within the next 12 weeks.
- As the District's CBSE team continues to review potential options for CBSE-related construction, no CBSE funds have been spent. Bond funds may only be spent on capitalizable assets; once such assets have been further defined, funds will be able to be used for planning, design and construction.
- Curriculum reporting in the Bond Programs Report shows Bond funds only. Non-bond funds related to planned bond scope were tracked in eBuilder for a short period of time only. For a full report of non-Bond funds used for planned bond scope, please see the Curriculum Project Status reports.

Bond Program Administration

Office of School Modernization - Program

July 2024

OVERALL BOND PROGRAM	BUDGET		FUNDING		PROGRESS		FORECAST	
	Original Budget	**Current Budget**	Bond Funds	Other Funds	Actuals To Date	Additional Encumbered	**Estimate At Completion**	*Over/Under*
Totals	*2,480,000,000*	***2,826,393,824***	*2,725,082,384*	*101,311,440*	*1,926,129,043*	*243,693,534*	***2,923,331,522***	*96,937,698*

PROGRAM NOTES

Approved Usage of Bond Funds

- OSM continues to work closely with PPS Finance to ensure individual bond expenditures meet bond compensability requirements. A Bond Compensability Committee meets regularly to review compensability questions.
- All bond-funded projects are reported to the Bond Accountability Committee. Criteria for selection of projects to be funded by the 2017 Health & Safety allocation have been previously presented to the Board and are available on OSM's webpages. Criteria for long-term selection of projects to be funded by 2020 Infrastructure allocations were shared with the Facilities & Operations Committee in October 2022.

Bond Budget

- Please see budget notes above for more detailed information by bond measure.

Bond Scope

- No active projects remain in the 2012 Bond. Remaining funds and expenditures need to be fully reconciled to know final remaining funds in program and whether additional projects can be completed. The lengthy process of reconciliation is in progress.
- In the 2017 Bond, staff are working through returning unused funds from prior Health & Safety projects to the unallocated funding buckets for Health & Safety, to determine next steps for funding additional projects. Substantial unneeded funds being returned from the water quality and lead paint programs will likely be allocated to roof replacement projects, due to the great need for ongoing roof replacements. Additional needs include replacements of fire alarm panels at multiple sites; this work was overlooked in previous scopes because these panels were at sites that did not need additional fire alarm upgrades.
- In the 2020 Bond, please see notes above under 2020 Budget Notes regarding additional budget needs for Infrastructure projects in the mechanical, ADA, and SPED categories, in order for those projects to complete anticipated scope.

Bond Schedule

- MPG, while addressing tight timing due to unforeseen conditions in construction, is on schedule. Benson project team is reviewing schedule delays with the general contractor.
- Schematic Design for Jefferson HS, Cleveland HS, and Ida B Wells HS modernizations are proceeding with minor delays from the originally anticipated schedule for planning and design. Construction schedules will depend on design phase schedules and future funding.
- 2020 Infrastructure and Capacity projects continue to move forward as quickly as possible. The extent of work that OSM is placing as part of the 2020 Bond puts significant pressure on both the local contracting market and the use of schools. Staff work carefully to balance market constraints, District needs, and bond spending requirements when determining project schedules.

2020 Technology Project Updates

2020 Technology Project Updates

Technology

2020 Bond - Technology

July 2024

PPS Team Leads: Don Wolff, Derrick Brown

STATUS AT A GLANCE

Legend:

- As planned: no concerns
- Caution: requires attention
- Impacts: impacts occurring

	As Planned	Caution	Impacts
Scope		X	
Budget		X	
Schedule			X
Overall		X	

BUDGET

	BUDGET		FUNDING		PROGRESS		FORECAST	
	Original Budget	**Current Budget**	Bond Funds	Other Funds	Actuals to Date	Additional Encumbered	**Estimate At Completion**	*Over/(Under)*
Tech Program Admin - 5519	23,264,652	**16,487,162**	13,037,257	3,449,904	3,453,065	9,202,563	**9,784,906**	(6,702,256)
Classroom Modernization	24,780,325	**25,846,375**	25,796,375	50,000	14,940,960	3,383,535	37,799,828	11,953,453
Infrastructure & Security	38,041,500	**39,515,112**	39,069,839	445,273	23,156,450	1,543,312	39,460,303	(54,809)
Device Replacement - 5515	31,006,443	**48,022,761**	38,683,834	9,338,927	37,278,451	1,867,200	**44,023,775**	(3,998,986)
ERP Replacement Planning - 5518	11,107,080	**15,714,034**	10,756,427	4,957,606	3,696,305	973,830	**13,034,568**	(2,679,466)
Harrison Park MS Conv - 5706	-	**856,267**	856,267	-	607,479	248,788	**856,267**	-
Totals	*128,200,000*	***146,441,711***	*128,200,000*	*18,241,711*	*83,132,710*	*17,219,228*	***144,959,647***	*(1,482,064)*

SCHEDULE

January 1st = Q1

	2024				2025				2026				2027			
	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4
Tech Program Admin - 5519			★													
Classroom Modernization																
Analysis/Planning			★													
Procurement			★													
Placement			★													
Device Replacement - 5515			★													
ERP Replacement Planning - 5518			★													
Infrastructure & Security																
Analysis/Planning			★													
Procurement			★													
Placement			★													

Baseline | Analysis/Planning | Procurement | Distribution | Placement

Technology

https://www.pps.net/2020Bond-Tech

The Teaching Station Project

The Teaching Station Project team has completed 74 schools so far and includes the installation of a new Chromebox desktop and 22” monitor) in each classroom. The project team are currently finishing up School Group 15. The classroom teaching station project is forecasted to be completed with all classroom teaching station refresh by late October 2024.

Group 15

Project Description	Actual Start	Actual Finish	% Complete	Estimated Start	Estimated Completion	T	W	C	F	% Underserved	Total Student Impact	CSI	TSI	Title 1	Year Built
Ockley Green Middle School: Teacher Station U	05/09/24	05/15/24	100%	05/09/24	05/19/24					69%	487	☐	☑	☐	1925
Kelly Elementary School: Teacher Station Upgra	05/20/24	05/31/24	100%	Summer 2024						84%	419	☑	☐	☑	1952
James John Elementary School: Teacher Statior	06/18/24	06/26/24	100%	06/18/24	06/28/24					69%	316	☑	☐	☑	1929
Woodlawn Elementary School: Teacher Station	06/25/24		80%	06/27/24	07/07/24					75%	315	☐	☐	☑	1926
Woodmere Elementary School: Teacher Station	06/26/24		56%	Summer 2024						75%	315	☐	☐	☑	1926

Classroom Improvement and Wifi Improvement Projects

- Wifi Improvement Project has been completed in two schools: Jefferson and Cleveland since these two schools are earmarked for future locations they are not currently getting the Wall mounted: Lightspeed, Airtame, Projectors.

- Classroom Improvement and Wifi Improvement Projects are currently in the implementation phase for 20 schools in School Group 1-4 and bids will be going out soon for contractors for School Group 5.

Pilot Group: Currently In Implementation Phase

Task Name	Actual Start	Actual Finish	% Complete	Estimated Start	Estimated Completion	T	W	C	F	% Underserved	Total Student Impact	CSI	TSI	Title 1	Year Built
George Middle School: Design	04/20/21	12/15/21	100%	04/20/21	12/14/21		✓	✓	✓	89%	432		✓	✓	1950
Boise-Eliot Elementary/Humboldt School: Design	11/23/20	12/15/21	100%	12/18/20	12/16/21		✓	✓	✓	85%	334	✓		✓	1926
Lane Middle School: Design	05/03/21	12/15/21	100%	03/23/21	12/16/21		✓	✓	✓	74%	416		✓	✓	1927
Cesar Chavez K8: Design	12/01/20	12/15/21	100%	12/18/20	12/21/21		✓	✓	✓	86%	544	✓		✓	1928
Cesar Chavez Kindergarten - 8th Grade: Teacher Station Upgrade	04/13/22	04/26/22	100%	04/11/22	04/21/22	✓				86%	544	✓		✓	1928
Boise-Eliot Elementary/Humboldt School: Teacher Station Upgrade	04/26/22	05/03/22	100%	04/25/22	05/05/22	✓				85%	334	✓		✓	1926
George Middle School: Teacher Station Upgrade	05/06/22	05/17/22	100%	05/04/22	05/14/22	✓				89%	432		✓	✓	1950
Lane Middle School: Teacher Station Upgrade	05/16/22	05/24/22	100%	05/16/22	05/26/22	✓				74%	416		✓	✓	1927
George Middle School: Implementation	05/02/22		100%	02/15/22	07/31/24		✓	✓	✓	89%	432		✓	✓	1950
Cesar Chavez K8: Implementation	02/21/22		74%	02/15/22	08/06/24		✓	✓	✓	86%	544	✓		✓	1928
Lane Middle School: Implementation	08/22/22	08/23/23	100%	02/15/22	08/22/24		✓	✓	✓	74%	416		✓	✓	1927
Boise-Eliot Elementary/Humboldt School: Implementation	02/21/22		100%	04/05/22	09/05/24		✓	✓	✓	85%	334	✓		✓	1926

Classroom Improvement and Wifi Improvement Projects

- Classroom technology improvements will include:
  - A wall phone for the teachers by the classroom door for security and standardization,
  - A laser projector mounted to the wall,
  - A Lightspeed teacher and student engagement audio amplification system and microphones so everyone can hear the teacher in the room.
  - A new gym intercom call box will be installed in each school's gym which will be included in the school's emergency communications plan and will enable the gym to call the front office or 911.
    - In addition it enables any office in the school to call the gym intercom call box directly.
  - Wi-Fi will be installed in each classroom and fiber network improvements will increase Wi-Fi speeds for faster online connectivity throughout the school.
  - Gyms will be receiving a table-top style laser projector to replace the existing projectors that can be rolled into the gym on a tech cart and will be used for daily health and gym classes.

Classroom Improvement and Wifi Improvement Projects

Group 2: Currently In Implementation Phase

Task Name	Actual Start	Actual Finish	% Complete	Estimated Start	Estimated Completion	T	W	C	F	% Underserved	Total Student Impact	CSI	TSI	Title 1	Year Built
Roseway Heights School: Teacher Station Upgrade	05/25/22	06/02/22	100%	05/23/22	06/02/22	✓				65%	617			✓	1923
Terwilliger School: Teacher Station Upgrade	06/06/22	06/14/22	100%	06/01/22	06/11/22	✓									
Alliance at Meek: Teacher Station Upgrade	06/16/22	06/21/22	100%	06/08/22	06/18/22	✓				75%	213	✓			1925
Jefferson High School: Teacher Station Upgrade	06/23/22	07/06/22	100%	06/21/22	07/01/22	✓				76%	620		✓		1909
Cleveland High School: Teacher Station Upgrade	07/08/22	07/26/22	100%	07/07/22	07/17/22	✓				32%	1581				1929
Ida B Wells High School: Teacher Station Upgrade	07/22/22	08/11/22	100%	07/18/22	07/28/22	✓				30%	1540				1956
Jefferson High School: Implementation	01/10/23	05/04/23	100%	01/31/23	07/27/23		✓			76%	620		✓		1909
Alliance at Meek: Implementation	10/02/23		88%	09/18/23	07/31/24		✓	✓	✓	75%	213	✓			1925
Ida B Wells High School: Implementation	08/30/23		51%	09/05/23	07/30/24		✓	✓		30%	1540				1956
Cleveland High School: Implementation	02/01/23		100%	01/30/23	11/16/23		✓	✓		32%	1581				1929
Roseway Heights Middle School: Implementation	05/22/24		1%	Spring 2024			✓	✓	✓	65%	617			✓	1923

Group 3: Currently In Implementation Phase

Project Description	Actual Start	Actual Finish	% Complete	Estimated Start	Estimated Completion	T	W	C	F	% Underserved	Total Student Impact	CSI	TSI	Title 1	Year Built
Pioneer Program at Youngson 5th to 9th Grade: Teacher Station U	08/09/22	08/23/22	100%	08/05/22	08/15/22	✓				99%	108				1970
Community Transition Program - Green Thumb: Teacher Station U	08/09/22	08/09/22	100%	08/09/22	08/19/22	✓				99%	77				1974
Community Transition Program - King Annex: Teacher Station Upg	08/10/22	08/16/22	100%	08/16/22	08/26/22	✓				72%	324			✓	1925
Dr. Martin Luther King Jr Elementary School: Teacher Station Upgr	08/10/22	08/16/22	100%	08/16/22	08/26/22	✓				65%	617			✓	1923
Chapman Elementary School: Teacher Station Upgrade	08/16/22	08/18/22	100%	08/18/22	08/28/22	✓				52%	375		✓		1923
Community Transition Project - Green Thumb: Implementation	06/24/24		1%	Fall 2024			✓	✓	✓	99%	77				1974
Community Transition Project - King Annex: Implementation	10/16/23		56%	10/05/23	07/15/25		✓	✓		72%	324				1925
Dr. Martin Luther King Jr Elementary School: Implementation	10/16/23		45%	10/05/23	07/15/25			✓	✓	72%	324				1925
Chapman Elementary School: Implementation			1%	Spring 2024			✓	✓	✓	52%	375		✓		1923
Pioneer Program at Youngson 5th to 9th Grade: Implementation	11/28/23		26%	10/19/23	07/16/26		✓	✓	✓	99%	108				1970

Classroom Improvement and Wifi Improvement Projects

- Markham and Gray were closed in the spring of 2024 due to storm damage and so the Bond 2020 Tech team started the implementation phase after the initial repairs were completed.

Group 4: Currently In Implementation Phase

Project Description	Actual Start	Actual Finish	% Complete	Estimated Start	Estimated Completion	T	W	C	F	% Underserved	Total Student Impact	CSI	TSI	Title 1	Year Built
Jackson Middle School: Teacher Station Upgrade	09/20/22	10/07/22	100%	09/20/22	09/30/22					40%	803				1966
Chief Joseph Elementary School: Teacher Station U	10/10/22	10/13/22	100%	10/10/22	10/20/22					43%	305				1949
Sabin Elementary School: Teacher Station Upgrad	10/17/22	10/20/22	100%	10/13/22	10/23/22					42%	360				1928
Creston Elementary School: Teacher Station Upgra	10/24/22	11/04/22	100%	10/25/22	11/04/22					55%	385				1948
Chief Joseph Elementary School: Implementation			0%	Spring 2024						43%	305				1949
Creston Elementary School: Implementation	06/18/24		5%	Spring 2024						55%	385				1948
Jackson Middle School: Implementation	05/22/24		16%	05/29/24	08/08/24					40%	803				1966
Sabin Elementary School: Implementation			0%	Spring 2024						42%	360				1928

Group 4.5: Currently In Implementation Phase

Project Description	Actual Start	Actual Finish	% Complete	Estimated Start	Estimated Completion	T	W	C	F	% Underserved	Total Student Impact	CSI	TSI	Title 1	Year Built
Markham Elementary School: Teacher Station Upgrade	11/08/22	11/15/22	100%	11/07/22	11/17/22					56%	416				1951
Gray Middle School: Teacher Station Upgrade	05/17/23	05/24/23	100%	05/15/23	05/25/23					32%	509				1952
Markham Elementary School: Implementation			1%	Spring 2024						56%	416				1951
Gray Middle School: Implementation	06/17/24		1%	Fall 2024						32%	509				1952

Artome All In One AV Cart

Pronounced: "Art-Oh-May"

Short video overview of Artome AV Carts: https://artome.fi/en/

Modernization Project Updates

Definitions

STATUS DEFINITIONS

	As Planned	Caution	Impacts
Budget	Pre-50% const: > 10% Project Contingency	Pre-50% const: 0% - 10% Project Contingency	Pre-50% const: < 0% Project Contingency
	Post-50% const: > 5% Project Contingency	Post-50% const: 0% - 5% Project Contingency	Post-50% const: < 0% Project Contingency
Equity	certified business participation > 18% ***and*** workforce equity > 20%	certified business participation 10% - 18% ***or*** workforce equity 10% - 20%	certified business participation < 10% or workforce equity < 10%
Schedule	0 or less weeks delay to SC	0+ up to 4 weeks delay to SC	greater than 4 weeks delay to SC
Overall	budget, equity and schedule are all green	at least one category is yellow	at least one category is red

EQUITY CATEGORIES

MBE = Minority-owned Business Enterprise

WBE = Woman-owned Business Enterprise

SDVBE = Service Disabled Veteran-owned Business Enterprise

ESB = Emerging Small Business

N-C = Non-Certified, counted for credit from a Certified Business that "graduated" out or did not reapply for certification

Benson HS Modernization and Multiple Pathways to Graduation (MPG)

Benson HS / Benson Swing Sites / MPG
July 2024

PPS Team Lead: Armand Milazzo
Design Bassetti Architects
Construction Andersen Construction Co.

STATUS AT A GLANCE

Legend:

- As planned: no concerns
- Caution: requires attention
- Impacts: impacts occurring

	As Planned	Caution	Impacts
Budget			X
Equity		X	
Schedule			X
Overall			X

BUDGET

	BUDGET		FUNDING		PROGRESS		FORECAST		CONTINGENCY	
	Original Budget	**Current Budget**	Bond Funds	Other Funds	Actuals To Date	Additional Encumbered	**Estimate At Completion**	*Over/Under*	Work Compl	Cont Remain
Benson HS	202,000,000	321,732,767	307,798,663	13,934,104	272,753,591	75,615,261	**322,305,972**	573,204	95%	0.2%
Swing Sites	-	**12,205,396**	12,199,595	5,801	12,205,396	-	**12,205,396**	-	100%	0.0%
MPG Building	-	**80,476,726**	80,447,075	29,651	67,603,919	10,188,355	**80,536,704**	59,978	95%	2.1%
Benson Totals	***202,000,000***	***414,414,890***	***400,445,334***	***13,969,556***	***352,562,907***	***85,803,616***	***415,048,072***	***633,182***		

EQUITY

Percent of payments made to Certified owned businesses, percent of labor hours of apprenticeable trades; cumulative

	MBE	WBE	SDVBE	ESB	N-C	**TOTAL**	*goal*	MIN	*goal*	FEM	*goal*	**APPR**	*req*
Consultants	4.54%	15.67%	0.00%	2.72%	2.32%	**25.24%**	*18%*						
Contractors	7.41%	5.79%	0.00%	1.89%	1.66%	**16.76%**	*18%*						
Overall	7.14%	6.73%	0.00%	1.97%	1.72%	**17.56%**	*18%*						
Workforce								36%	*25%*	9%	*14%*	**23%**	*20%*

SCHEDULE

NEXT MILESTONE: Substantial Completion On Track? No



BPHS & MPG Modernizations

BENSON & MPG SITES

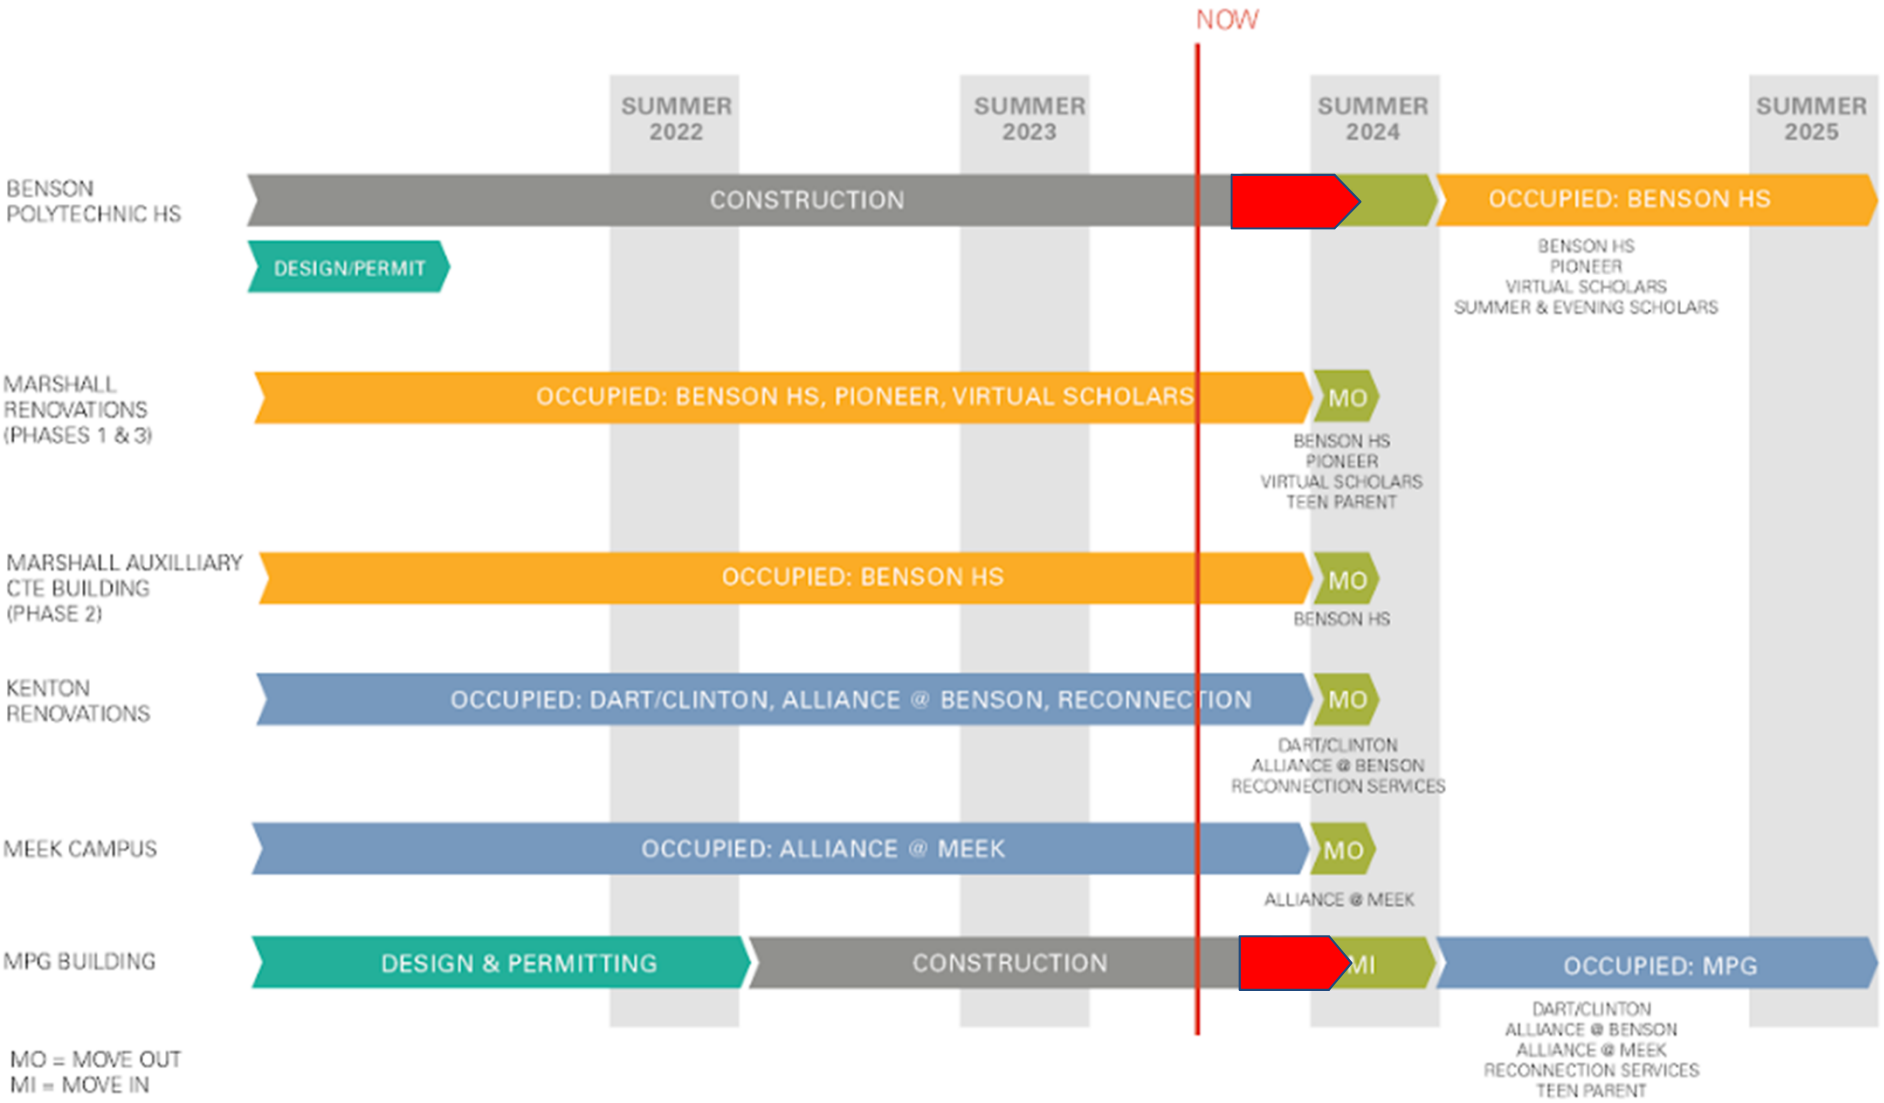

Benson Tech HS Modernization

Benson Polytechnic – All buildings are nearing completion

Photos from June 24th & 25th, 2025

Benson Tech HS Modernization

New Commons, Cafeteria, and the adjacent Social Courtyard

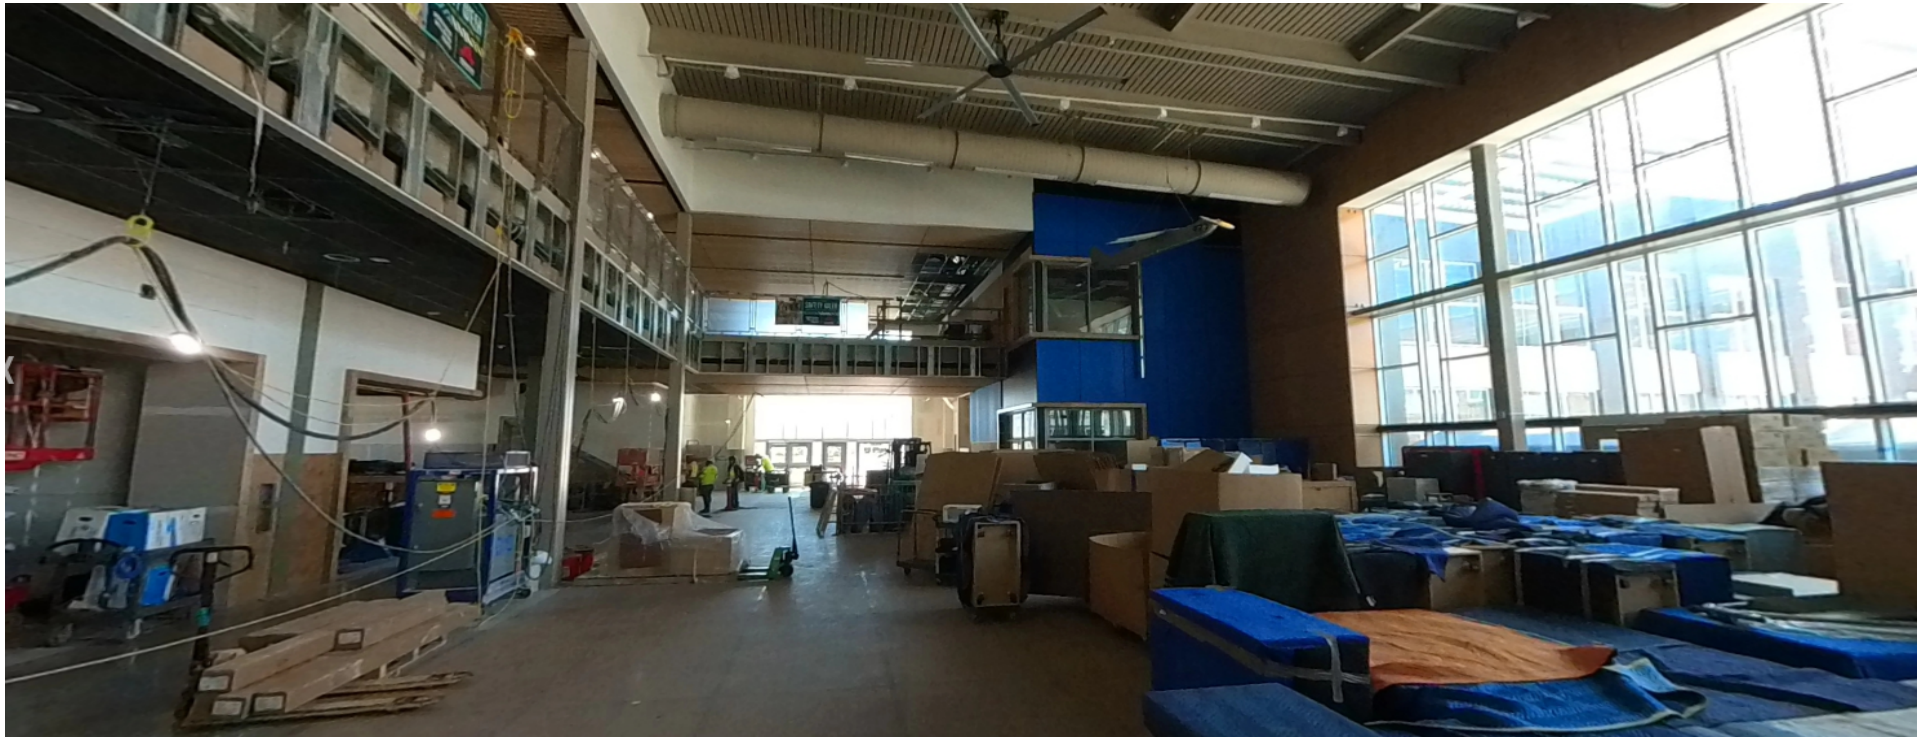

July 2024

New Media Center & Theatre

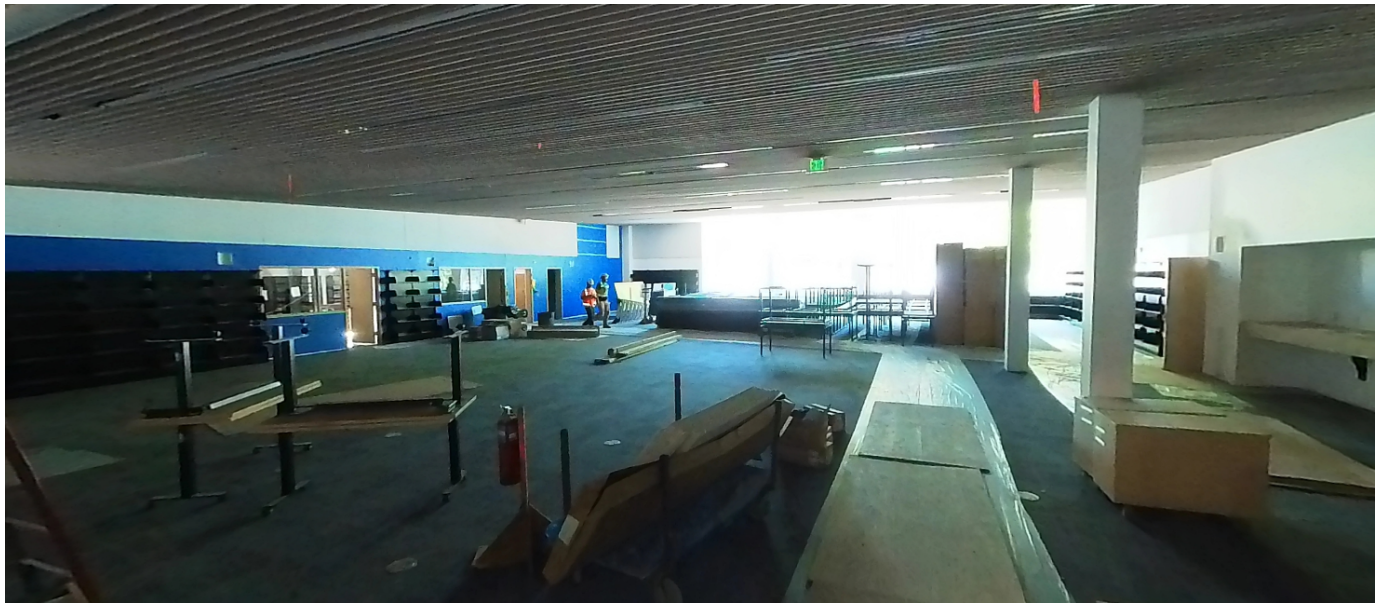

Benson Tech HS Modernization

Building E: Final finish Installation in the Historic Administration building

Benson Tech HS Modernization

Construction Progress: Auto Courtyard, Restrooms, Central Plant

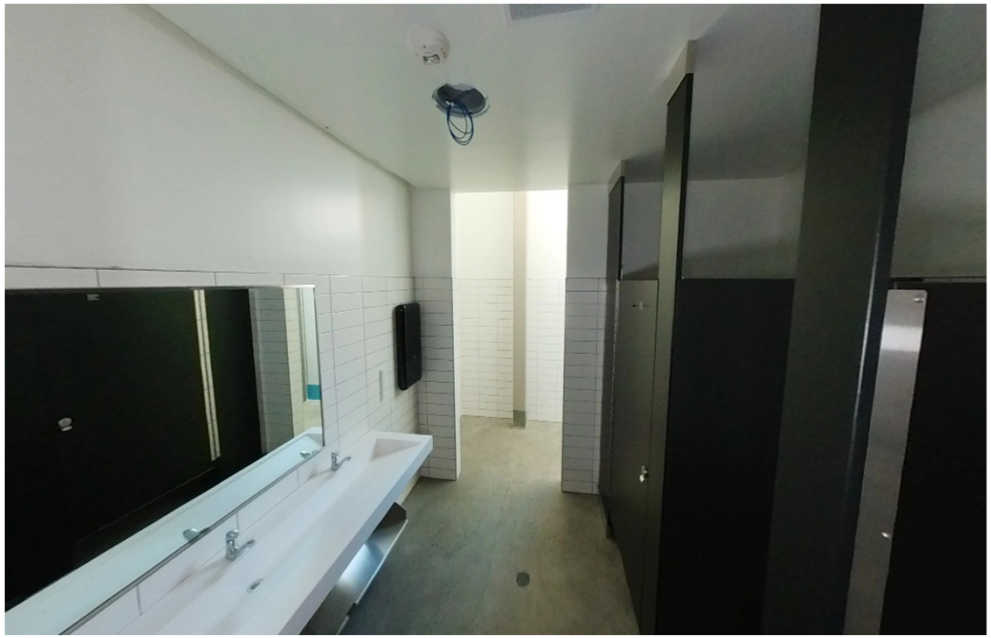

Benson Tech HS Modernization

Interior: Historic G1 Gym & Running Track Mechanical Duct & G2 Sound Panel preparation

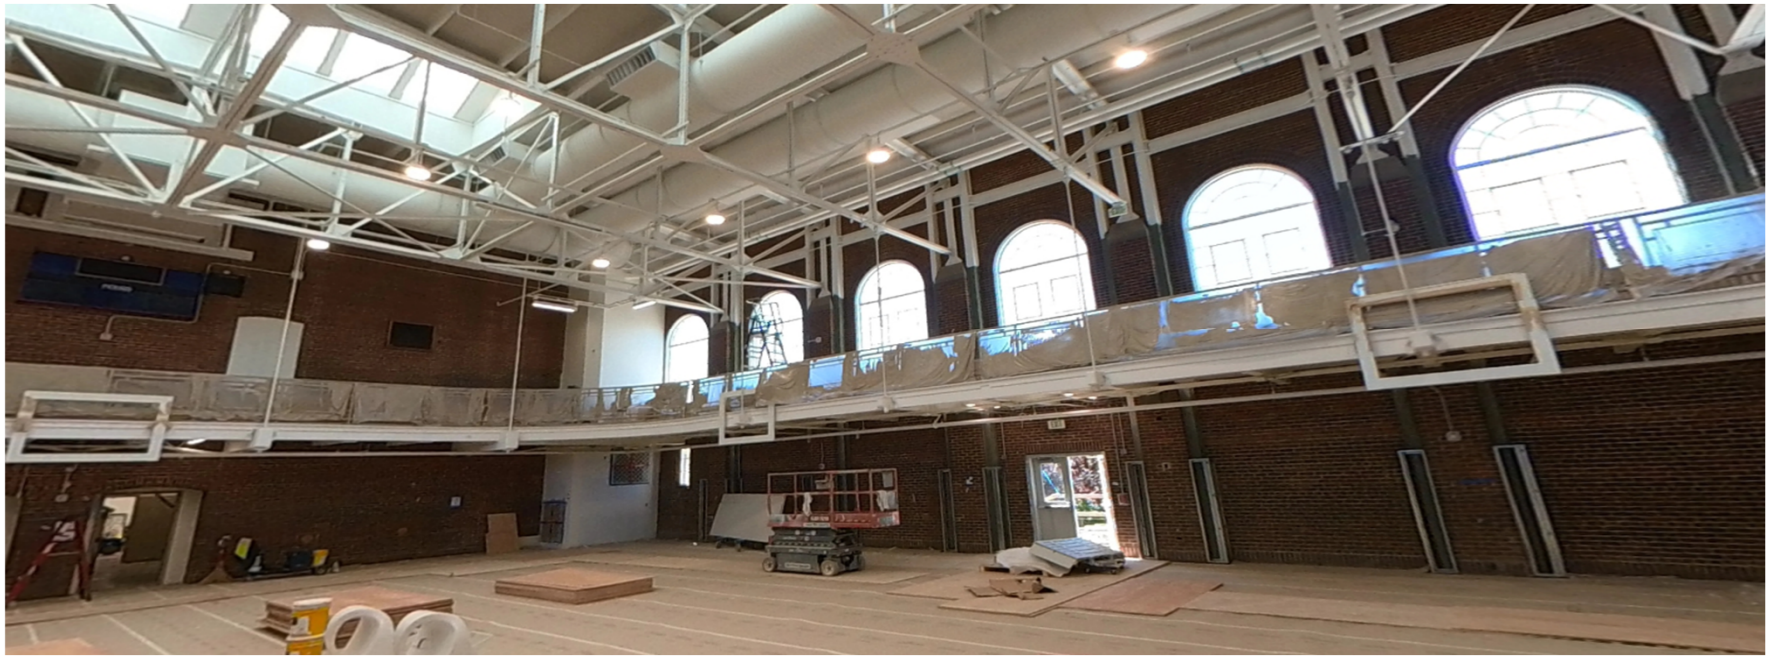

Benson Tech HS Modernization

Exterior: Solar Panel Installation & Green Roof

Benson Tech HS Modernization

Exterior: Radio Tower & Dust Collector

Benson Tech HS Modernization

Interior: Building H Auto Shop

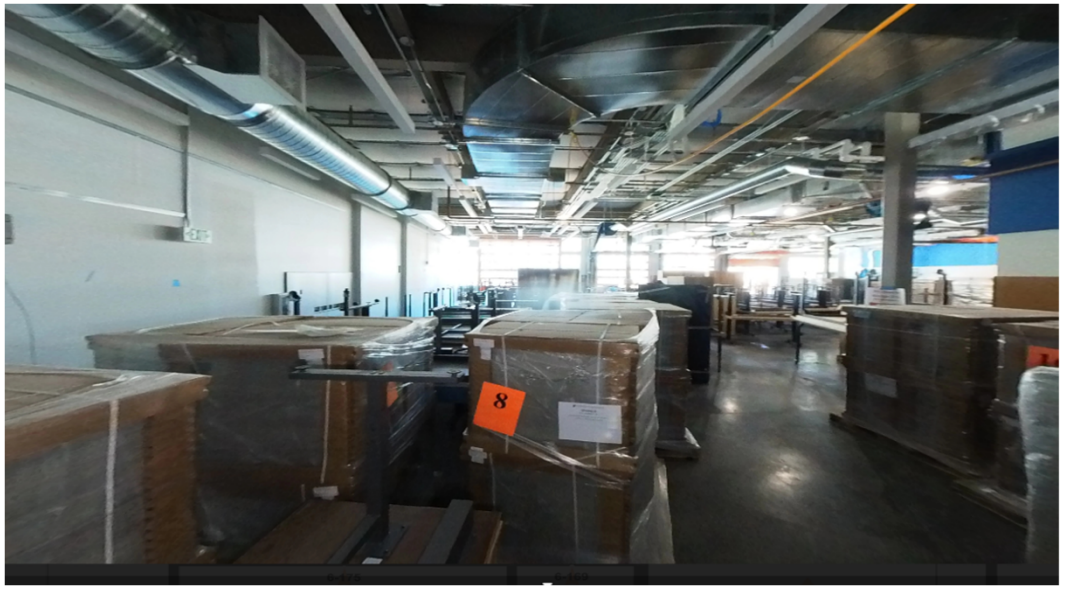

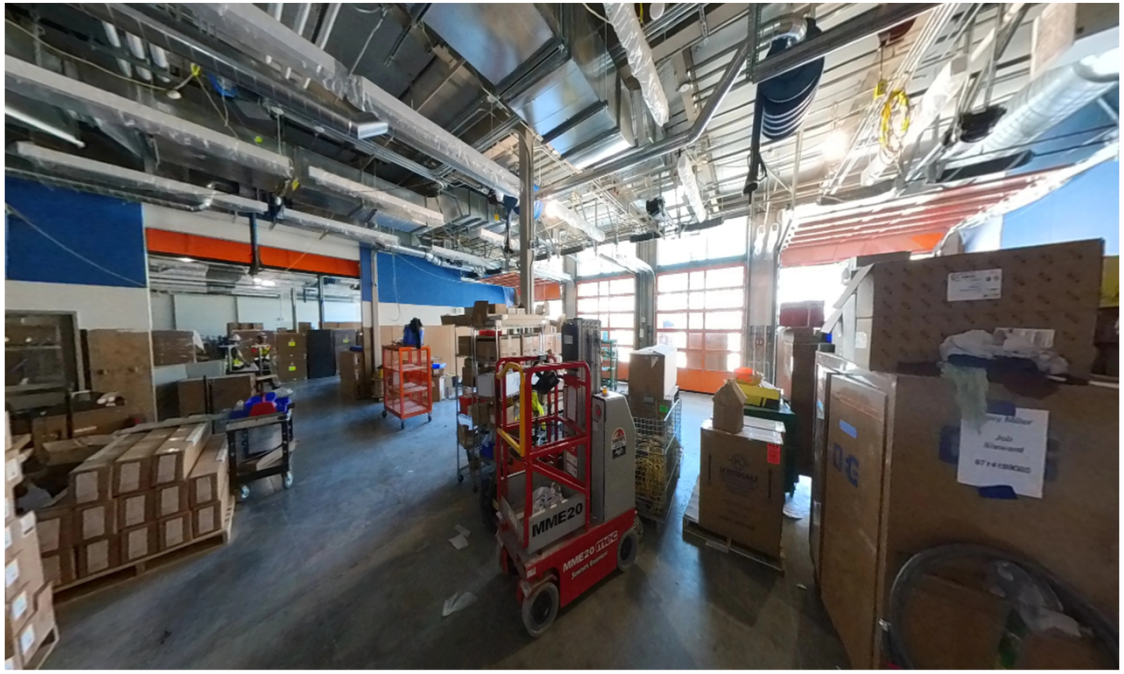

Benson Tech HS Modernization

Interior Finishes: Mockup Classroom, Science Lab, CTE Hallway

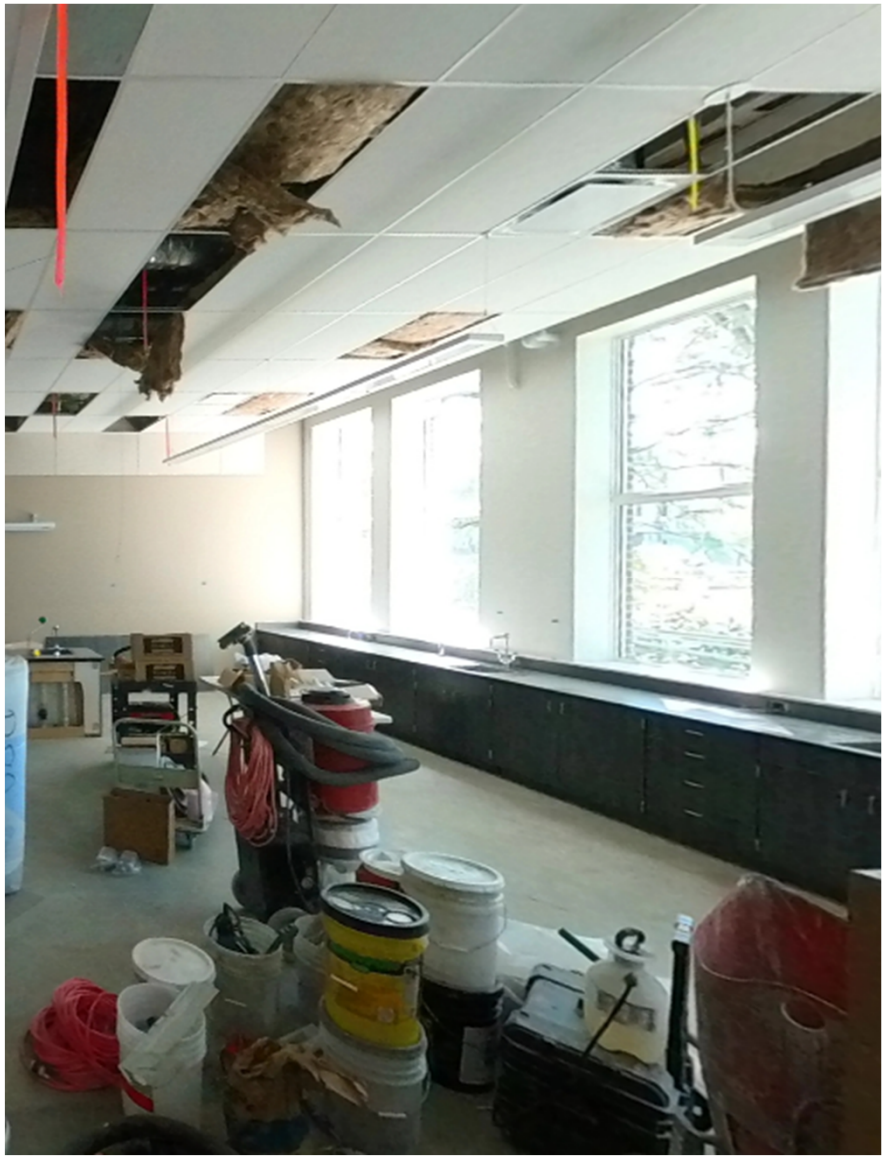

Benson Tech HS Modernization

Interior Finishes: Historic Auditorium

Benson Tech HS Modernization

Buckman Field Connection: new concrete stair & ramp nearing completion

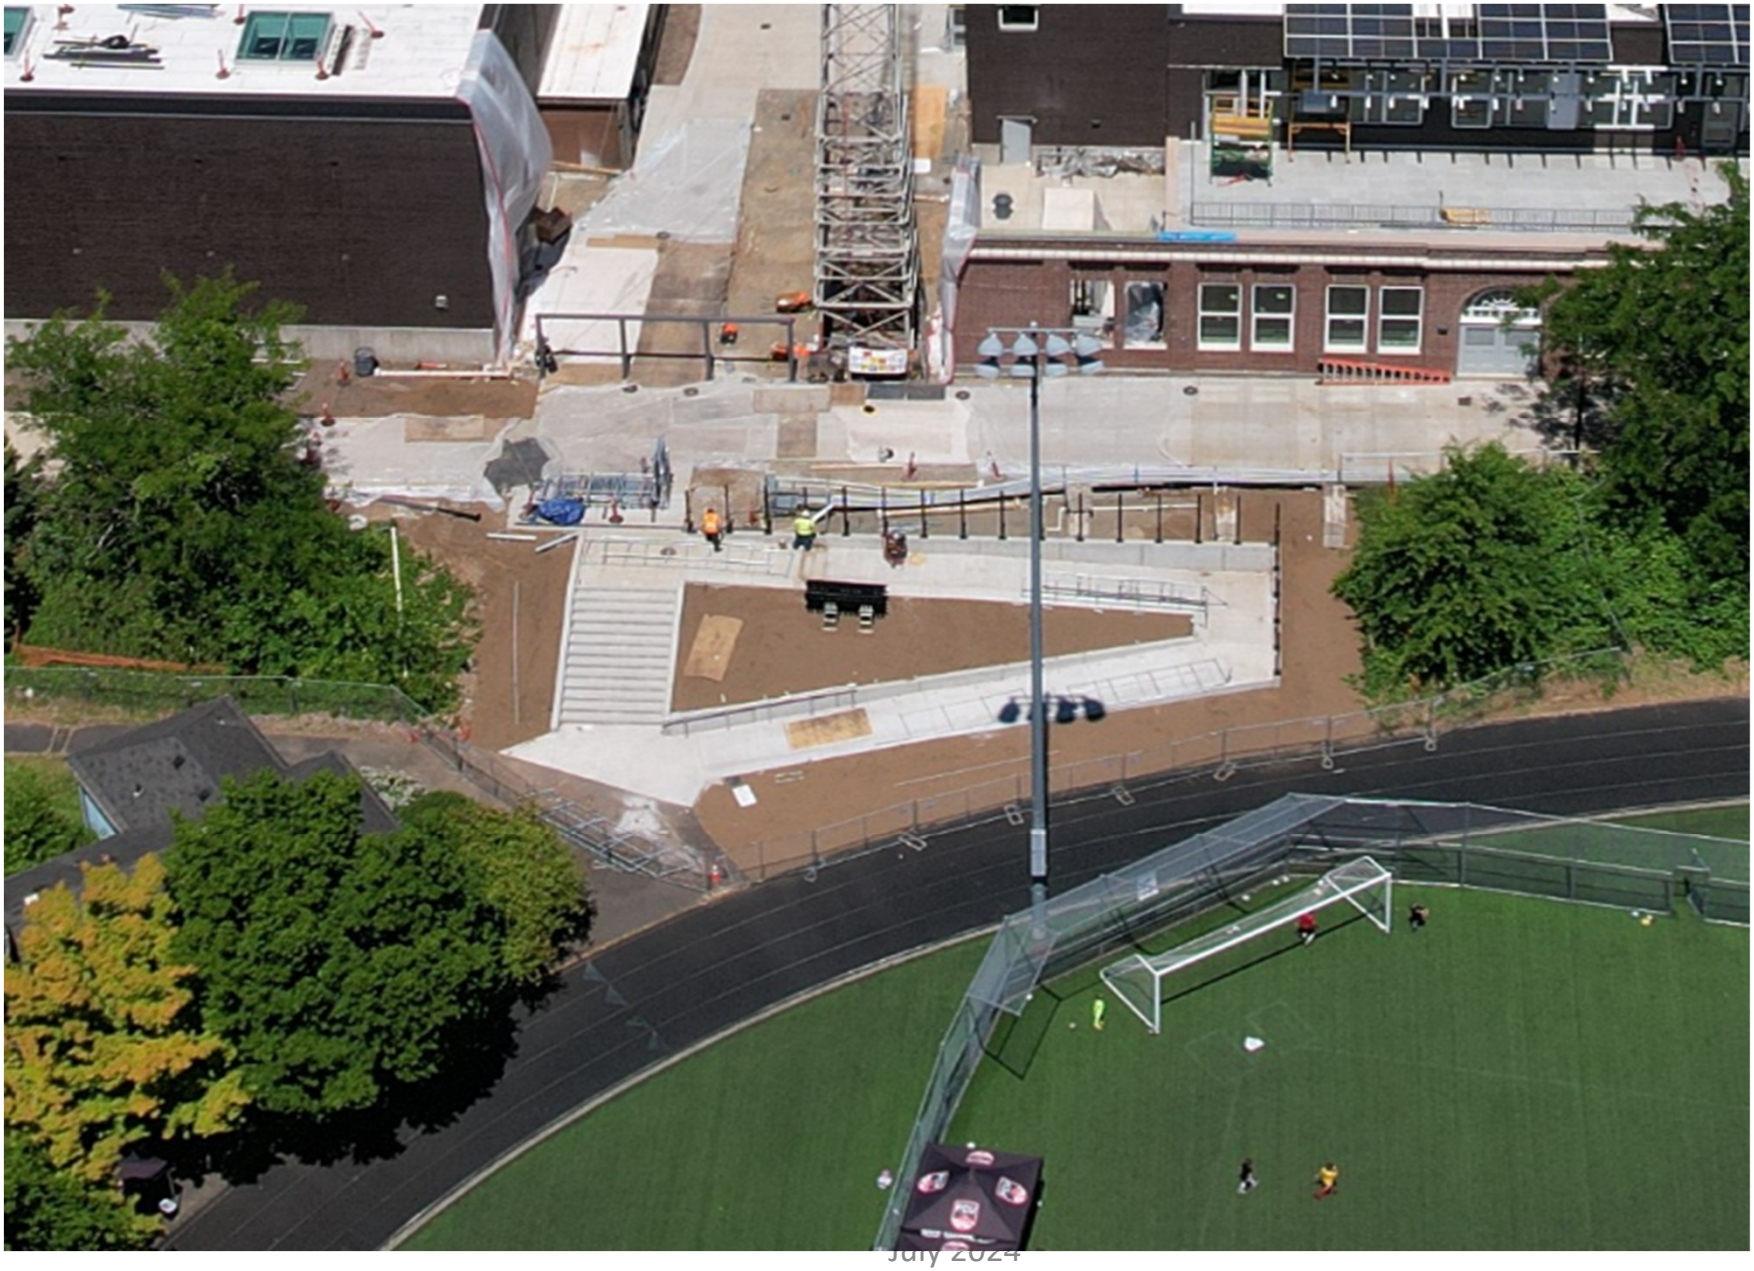

Multiple Pathways to Graduation Building

Exterior Progress: West Elevation

Photos from June 24th & 25th, 2025
