Multiple Pathways to Graduation Building

Multiple Pathways to Graduation Building

Work Progress: Gym, Cafeteria, Stair, Hallway

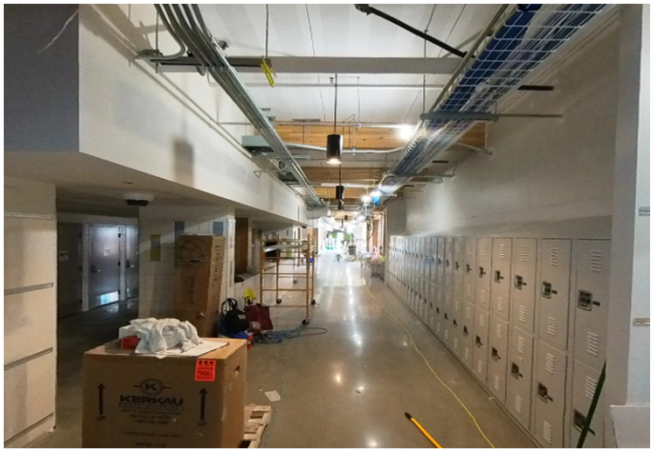

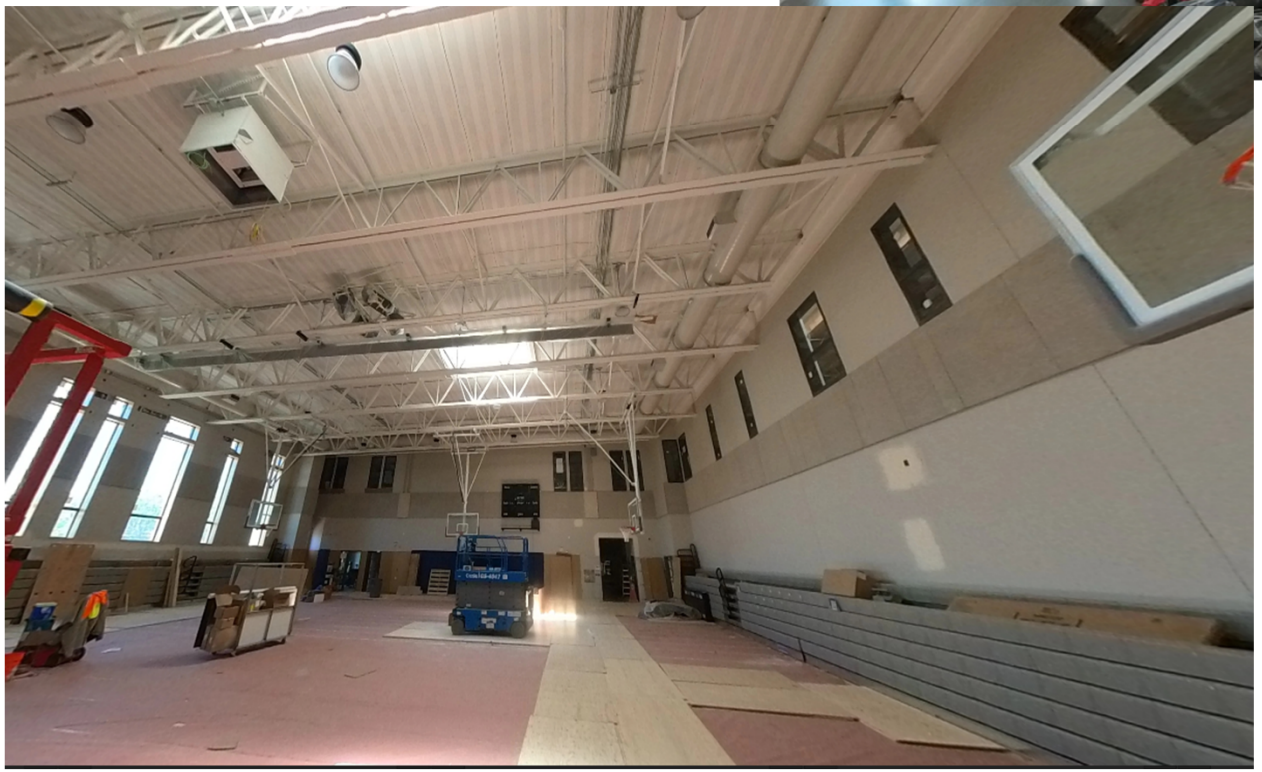

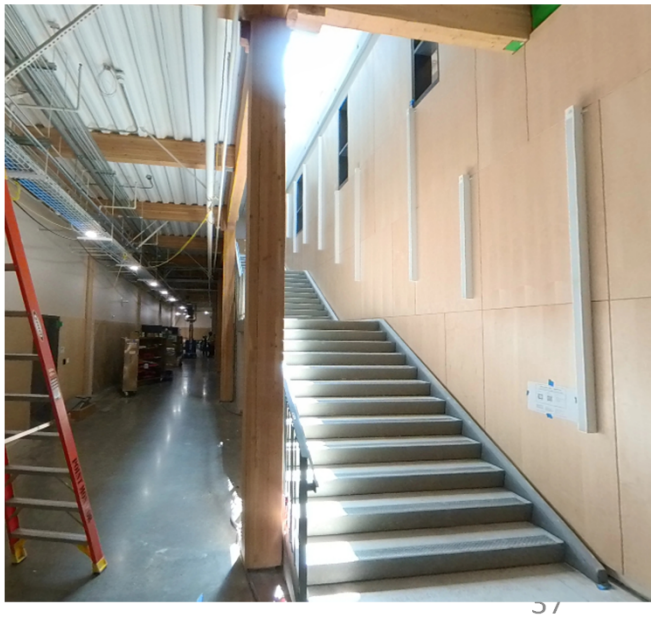

Multiple Pathways to Graduation Building

Work Progress: Stairwell, gym, medicine wheel, media center, cafeteria

Jefferson HS Modernization

Jefferson HS Modernization
July 2024

PPS Team Leads: Steve Effros, Kiesha Locklear, Ayana Horn
Design: BORA Architects, Lever Architecture
Construction: Andersen Construction, with Crossover Construction, Faison Construction, Northwest Infrastructure, Professional Lath & Plaster, Professional Minority Group

STATUS AT A GLANCE

Legend:

- As planned: no concerns
- Caution: requires attention
- Impacts: impacts occurring

	As Planned	Caution	Impacts
Budget	X		
Equity*		X	
Schedule	X		
Overall	X		

BUDGET

BUDGET		FUNDING		PROGRESS		FORECAST		CONTINGENCY IN CONTEXT	
Original Budget	**Current Budget**	Bond Funds	Other Funds	Actuals to Date	Additional Encumbered	**Estimate At Completion**	*Over/Under*	Work Complete / %	Contingency Remain / %
366,007,500	**366,007,500**	366,000,000	7,500	13,425,940	25,946,752	**491,000,000**	124,992,500	5%	10%

EQUITY

Percent of payments made to Certified owned businesses, percent of labor hours of apprenticeable trades; cumulative

	MBE	WBE	SDVBE	ESB	N-C	**TOTAL**	*goal*	MIN	*goal*	FEM	*goal*	**APPR**	*req*
Consultants	4.46%	5.69%	0.00%	0.00%	1.71%	**11.86%**	*18%*						
Contractors*	0.00%	0.00%	0.00%	0.00%	0.00%	**0.00%**	*18%*						
Overall	4.08%	5.21%	0.00%	0.00%	1.57%	**10.86%**	*18%*						
Workforce*								0%	*25%*	0%	*14%*	**0%**	*20%*

** Construction trade payments have not yet been made.*

SCHEDULE

NEXT MILESTONE: 100% SD ▼ On Track? No ▼

PROJECT PHASE	2024							2025							2026							2027						
Planning			★																									
Design			★																									
Construction			★																									
School Opening(s)			★																									

Baseline — Planning — Design — Construction — School Opening

Jefferson HS Modernization

DECEMBER 2023

On Tuesday, December 12, 2023, the PPS Board of Education passed RESOLUTION No. 6806 that directed the Superintendent and the Office of School Modernization to reassess the current Jefferson High School site plan, building design and related land-use efforts so that Jefferson High School students and staff would not relocate to another temporary site during construction of the modernized school.

This meant Jefferson students would remain at Jeff for the 2024-25 school year and beyond until the new building is completed. In addition, the Jefferson Modernization design team was directed to return to the Board of Education in 120 days with an updated plan to modernize Jefferson High School.

Per the resolution, the plan will:

- Keep students & staff largely on the Jefferson campus during construction.
- Include a targeted student enrollment of 1,700.
- Demolish the 1909 building and build a new building.
- Seek to conform to PPS's current high school education specifications area program.

The plan will also strive to deliver the project within the currently available bond (and other available) funding and will identify anticipated budget overage.

The plan will not include colocation of the Center for Black Student Excellence, Harriet Tubman Middle School, or other unaffiliated to Jefferson High School programs.

These decisions were made by the Board of Education in response to feedback from the community. Community members strongly preferred keeping students on site during construction and building a new Jefferson instead of retaining the 1909 building.

Jefferson HS Modernization

APRIL – JUNE 2024

Board Direction

Following Board direction in April, project team moved forward with the start of Schematic Design phase on new Jefferson modernization plan that will keep students & staff largely on the Jefferson campus during construction, design the school for a targeted student enrollment of 1,700, demolish the 1909 building, and seek to conform to PPS's current high school education specifications area program.

Coordination with City

Project team working directly with City staff to coordinate the land use approach, as well as participating in the Major Projects Group (MPG) in preparation for the permitting process.

Community Engagement

OSM team moving forward with a new community engagement & communications plan that centers student voice as well as internal and community stakeholder input, including the first in a series of Community Design Workshops earlier this month that included a project update, a discussion of Cultural Placemaking, and opportunities to provide input on design elements for the new school.

Jefferson HS Modernization

APRIL – JUNE 2024 (cont'd)

Project Team Work

- Owner/Architect/Contractor group meeting on a regular basis in functional teams with members of the technical design/engineering & contractor/trade partner groups to address early procurement, target value and interdisciplinary coordination of building & site systems, among other topics.
- Project team kicked off internal stakeholder engagement as part of program refinement and layout process, including broader discussions & summits among the Jefferson, IB Wells and Cleveland project teams covering site/building resilience, theater design, and CTE/maker space systems, among other topics.

Next Steps

- 100% Schematic Design Package – September, 2024
- Community Design Workshops – August and throughout Fall 2024

Jefferson HS Modernization

VIEW FROM NORTHWEST

VIEW FROM SOUTHWEST

Ida B Wells HS Modernization Planning & Design

Ida B Wells HS Modernization Planning & Design

July 2024

PPS Team Lead: Donna Bezio
Design: Bora Architecture
Construction: n/a

STATUS AT A GLANCE

Legend:

- As planned: no concerns
- Caution: requires attention
- Impacts: impacts occurring

	As Planned	Caution	Impacts
Budget	X		
Equity*			
Schedule	X		
Overall	X		

BUDGET

BUDGET		FUNDING		PROGRESS		FORECAST		CONTINGENCY IN CONTEXT	
Original Budget	**Current Budget**	Bond Funds	Other Funds	Actuals to Date	Additional Encumbered	**Estimate At Completion**	*Over/Under*	Work Complete / %	Contingency Remain / %
20,000,000	**20,000,000**	20,000,000	-	1,230,467	269,730	**20,000,000**	-	14%	5%

EQUITY

Percent of payments made to Certified owned businesses, percent of labor hours of apprenticeable trades; cumulative

	MBE	WBE	SDVBE	ESB	N-C	**TOTAL**	*goal*	MIN	*goal*	FEM	*goal*	**APPR**	*req*
Consultants	12.47%	6.69%	0.00%	6.21%	0.00%	**25.36%**	*18%*						
Contractors*	0.00%	0.00%	0.00%	0.00%	0.00%	**0.00%**	*18%*						
Overall	12.47%	6.69%	0.00%	6.21%	0.00%	**25.36%**	*18%*						
Workforce*								0%	*25%*	0%	*14%*	**0%**	*20%*

** No construction in this design/planning project.*

SCHEDULE

NEXT MILESTONE: 100% SD On Track? Yes

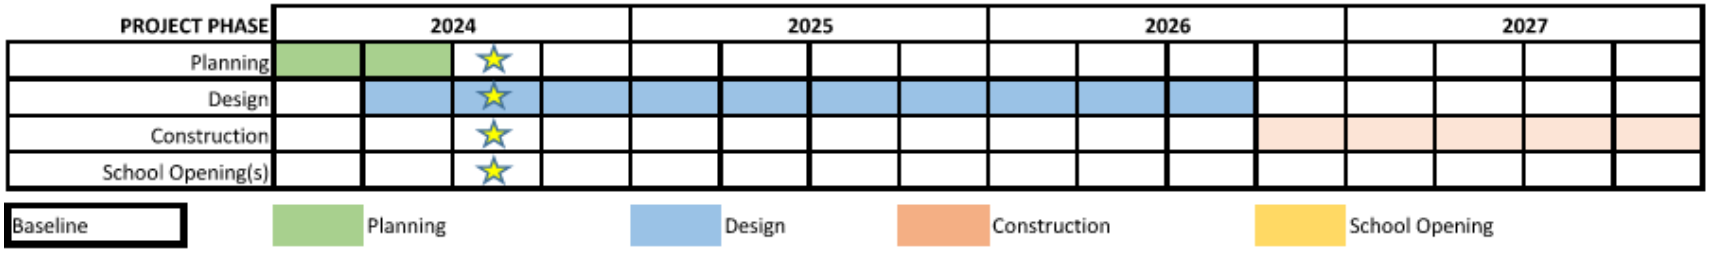

Design and Construction Schedule

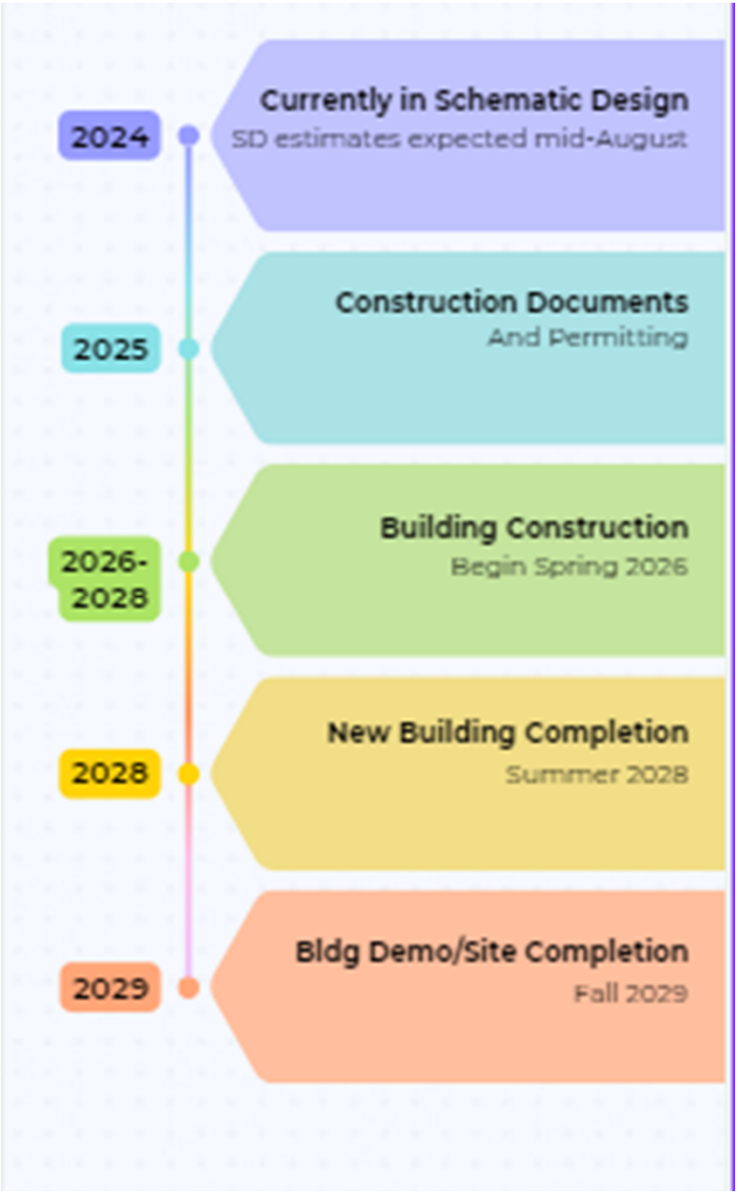

2024

- 50% SD Set completed for cost estimates
- Cost estimates expected mid August 2024
- CM/GC has been selected, expected to join end of August
- 100% SD estimate - by December 2024

2025

- 100% DD estimate - Summer 2025
- CD set - by December 2025
- Permitting (Major Projects Group) - approx. 16 weeks
- *Construction funding contingent upon passing future Bond Measure*

2026-2028

- New building construction - 25 months (with students/staff in existing building)
  - Earliest building completion - Summer 2028

2028-2029

- Demo of existing bldg & replacement of fields - 12 months
  - Earliest completion of fields - Fall 2029

Community Engagement Summary

Various community outreach events have continued to provide valuable input to help develop the schematic design.

Design Advisory Group (DAG)

- 2 DAG meetings so far, Next Meeting August 14

Teachers and Staff:

- Presentation at IBW Staff Meeting
- Programming meetings with all departments

General Community & Affinity Groups:

- Public Open House was well attended in May
- Public Design Workshops begin again in the fall
- Interviews and Engagement Sessions with various groups including student leaders, community based organizations, special education staff, Muslim and Arab students, immigrant and refugee community members, and additional affinity groups

Ida B Wells HS Modernization
Planning & Design

DESIGN DRIVERS:

TOPOGRAPHY
ENHANCE THE ECOLOGY OF THE SITE
CONNECTIVITY



Proposed Site Design

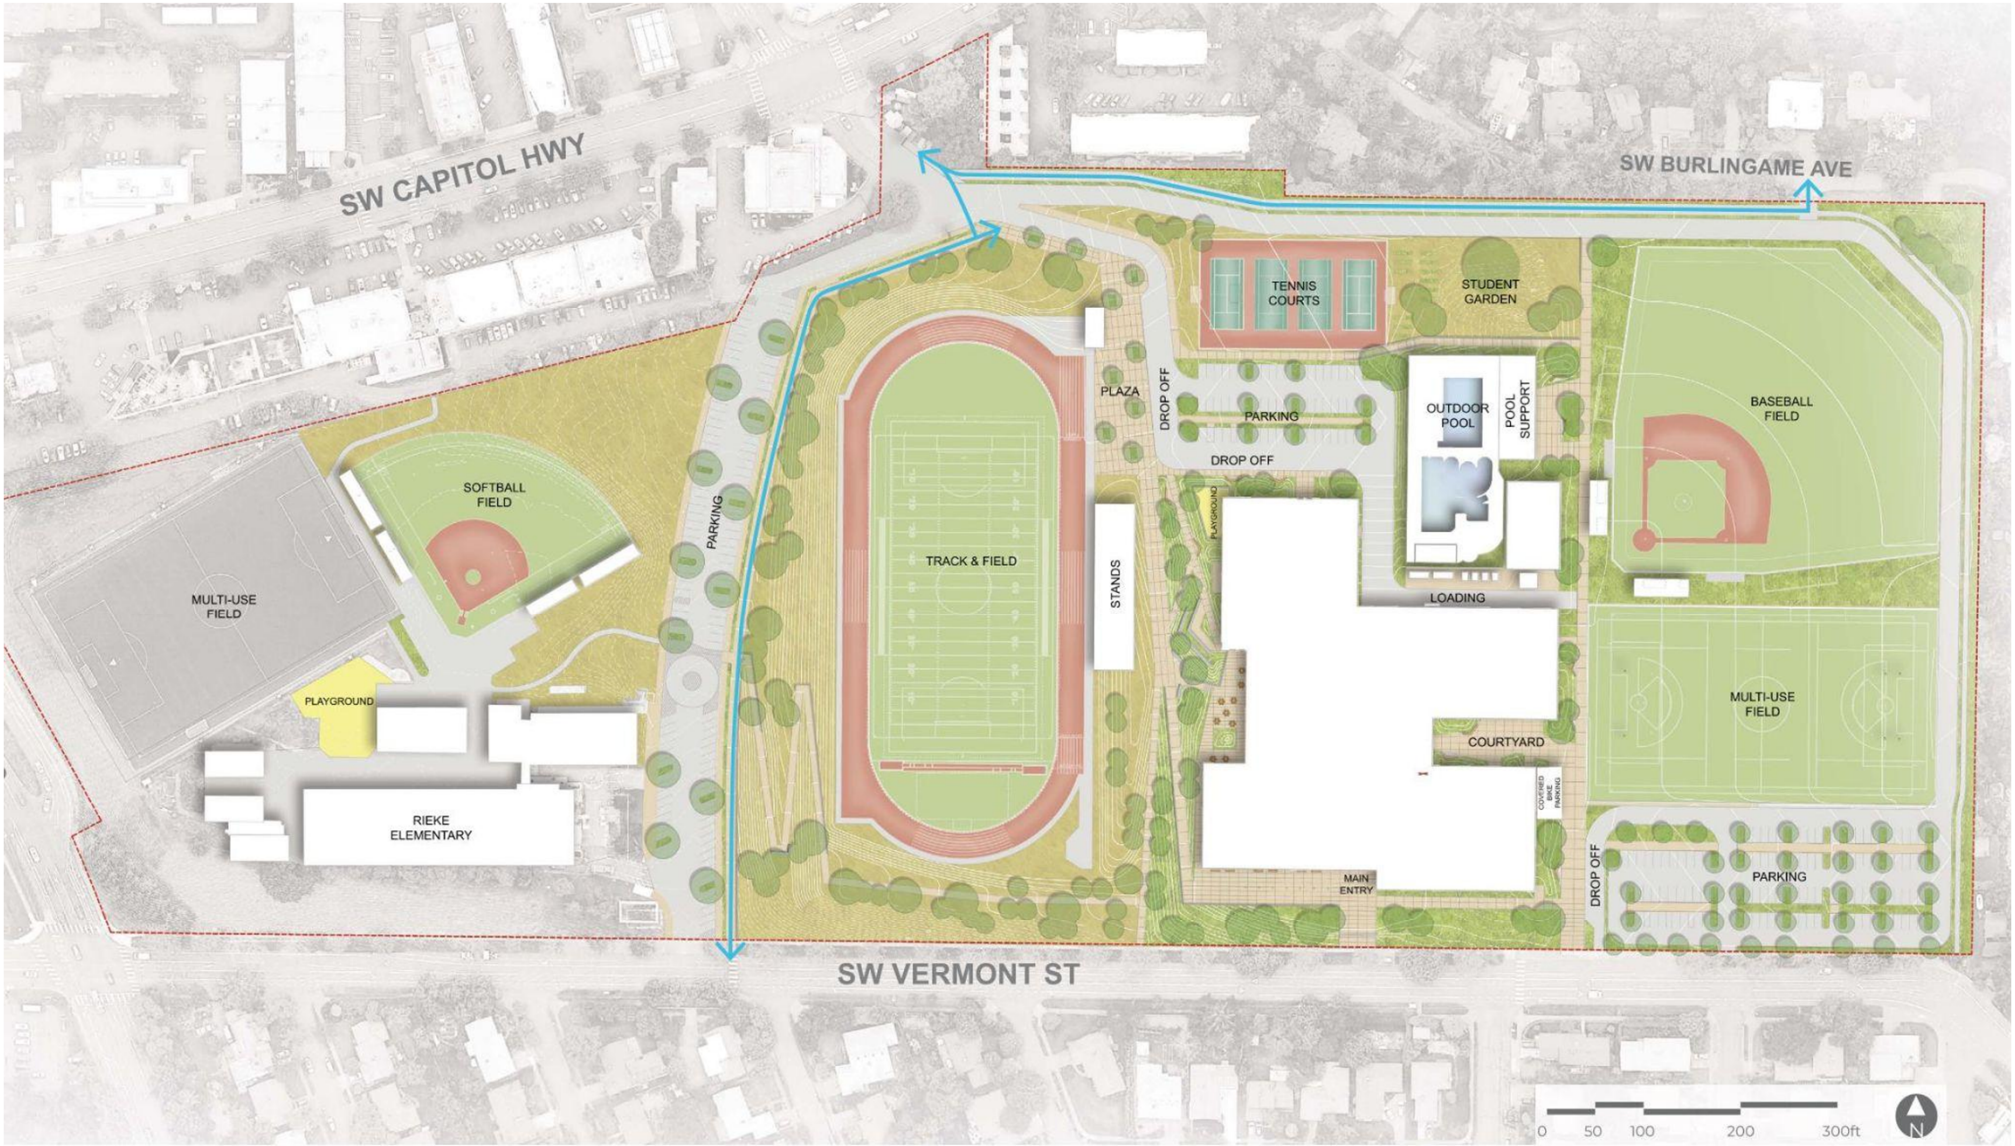

Building Massing

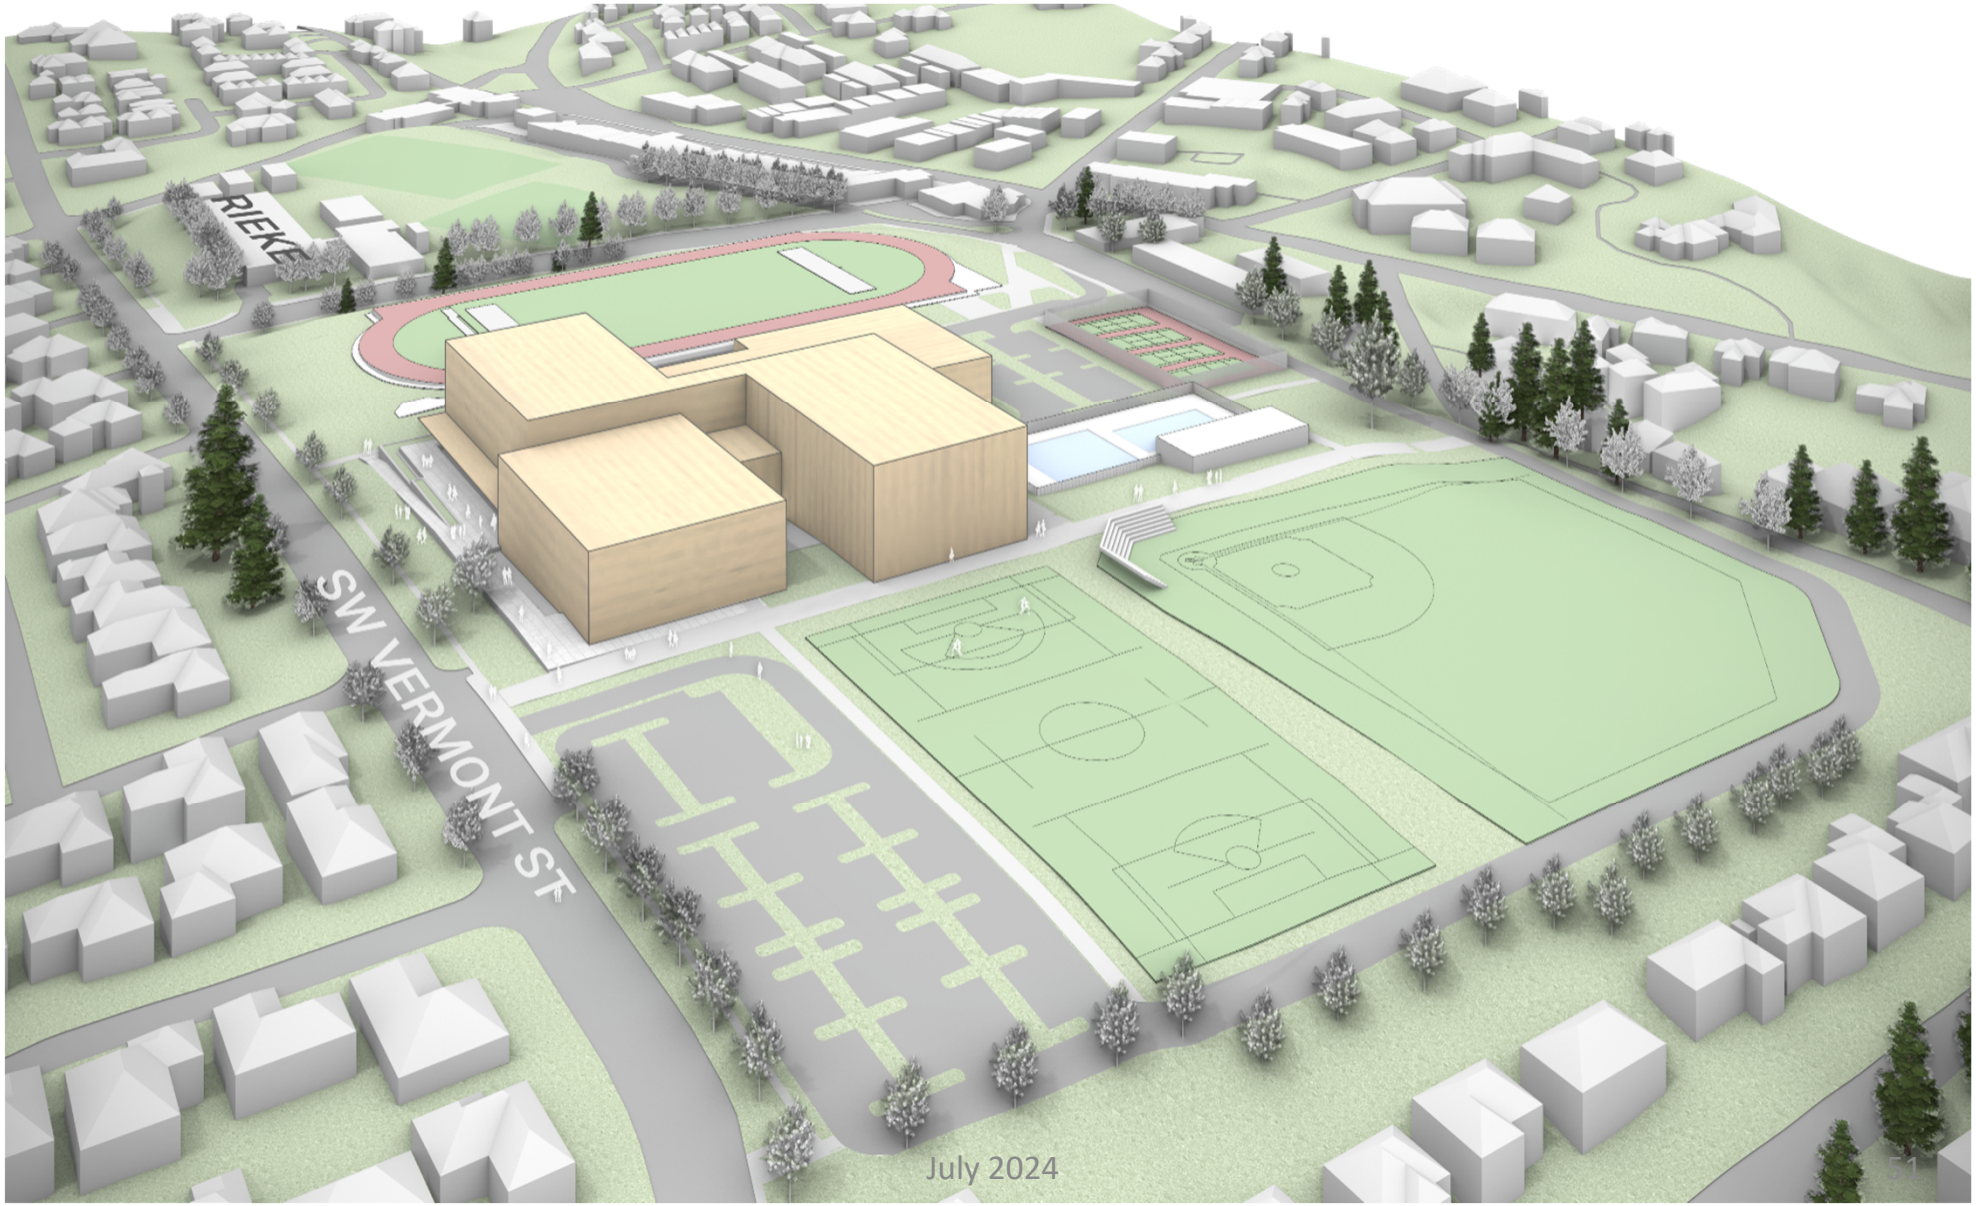

FLOOR PLAN - LEVEL 1

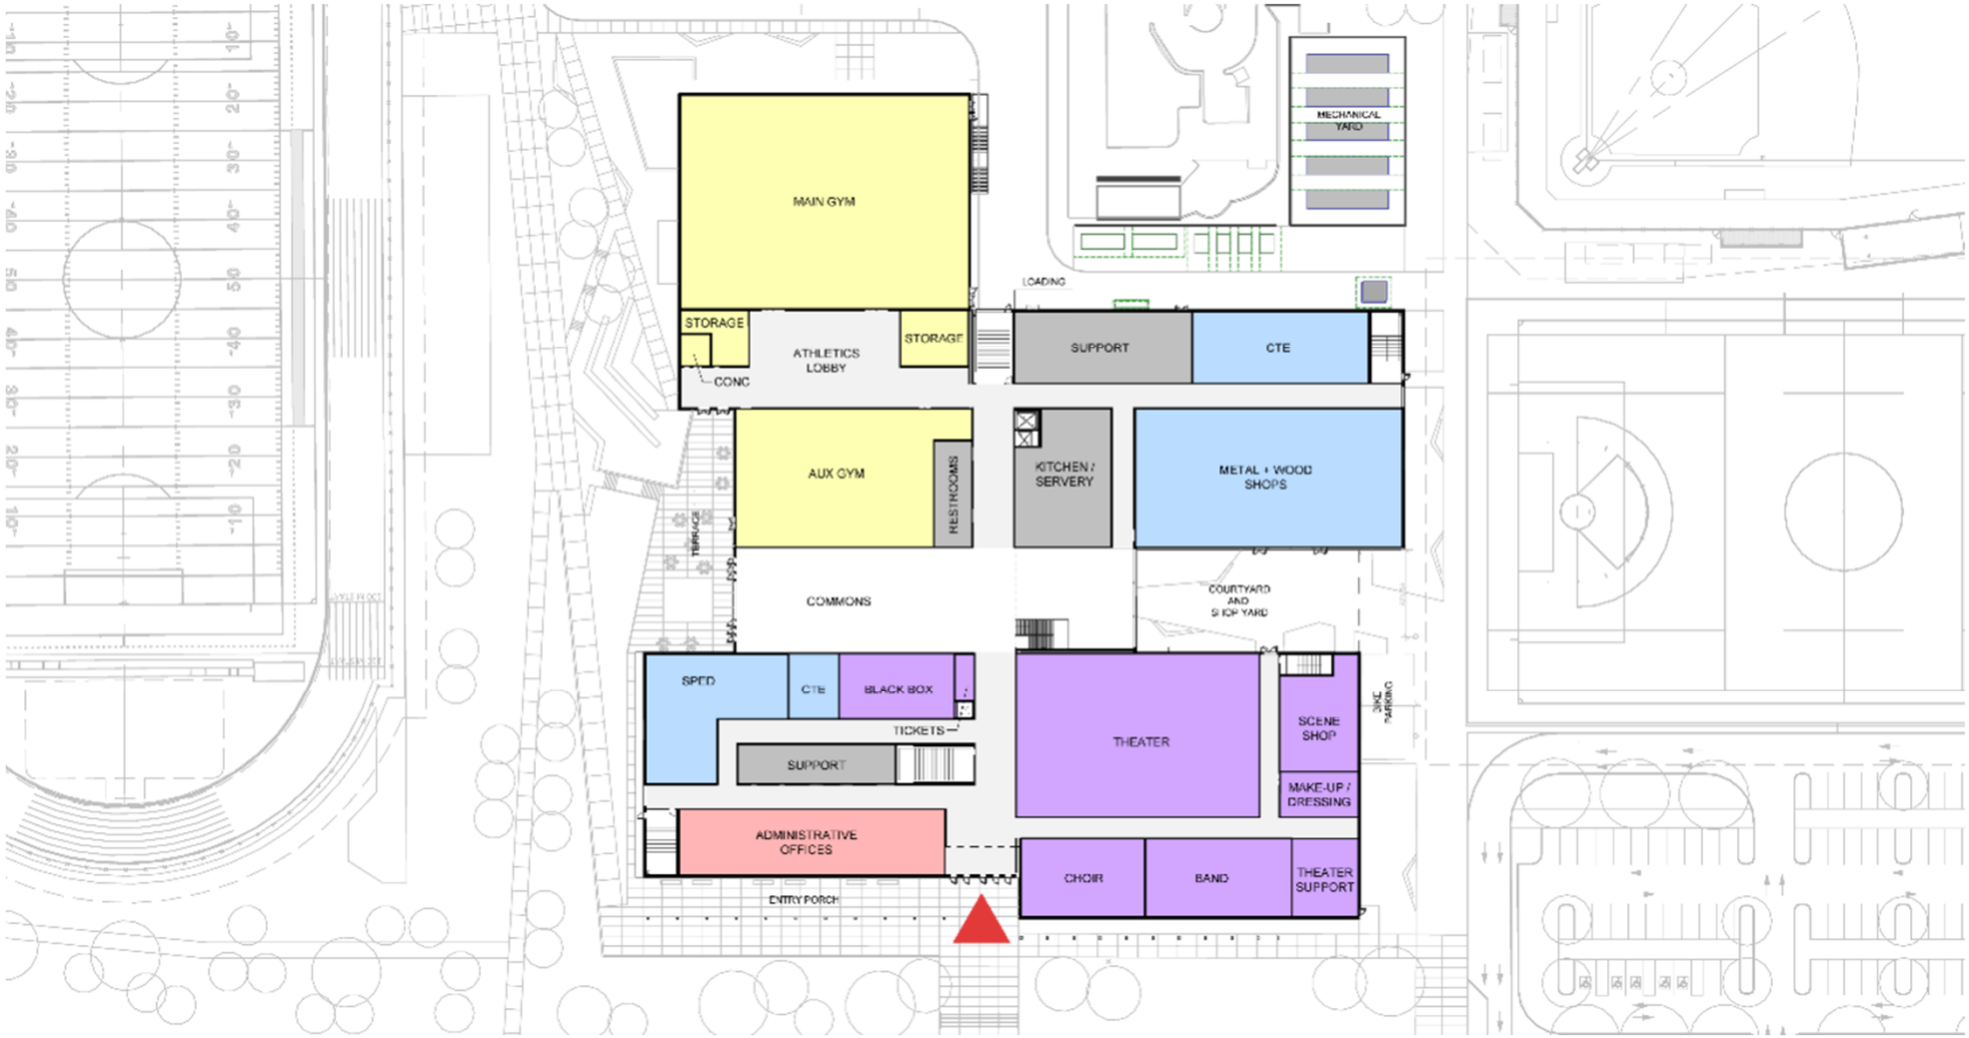

FLOOR PLAN - LEVEL 0 (LOWER LEVEL)

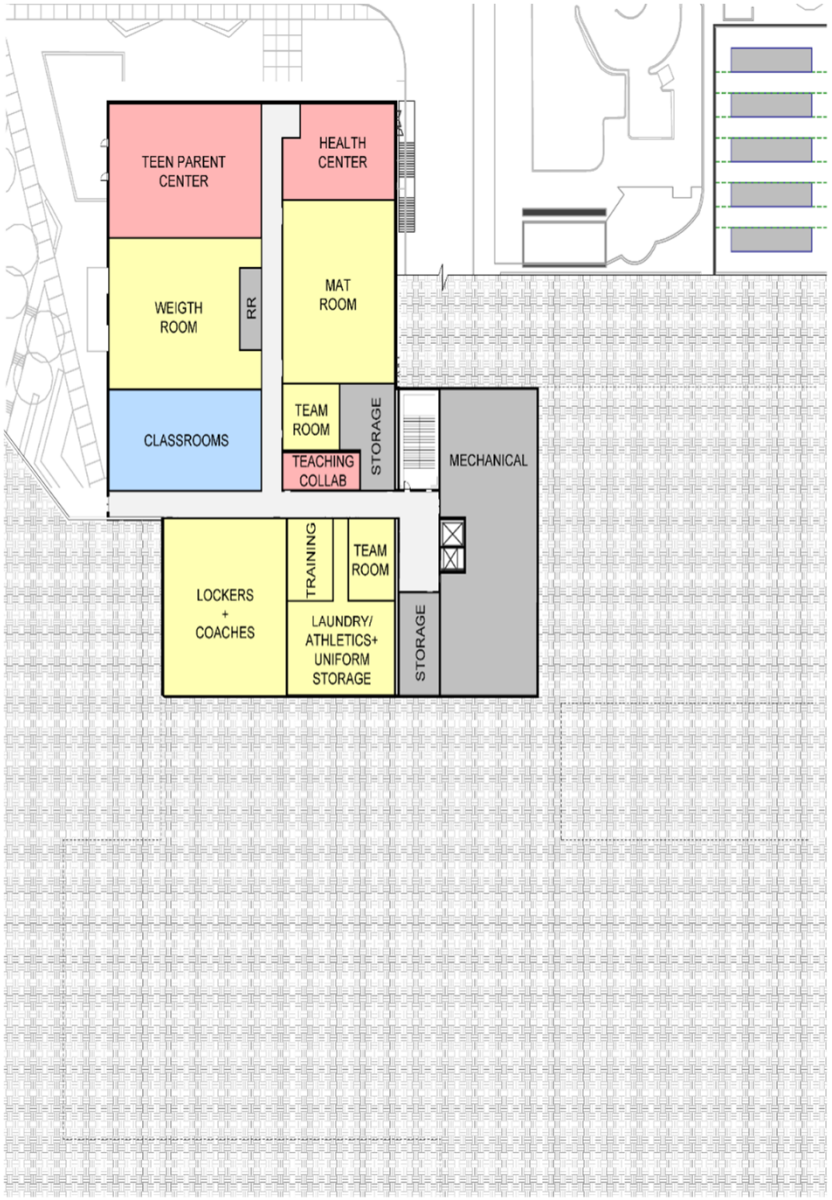

FLOOR PLAN - LEVEL 2

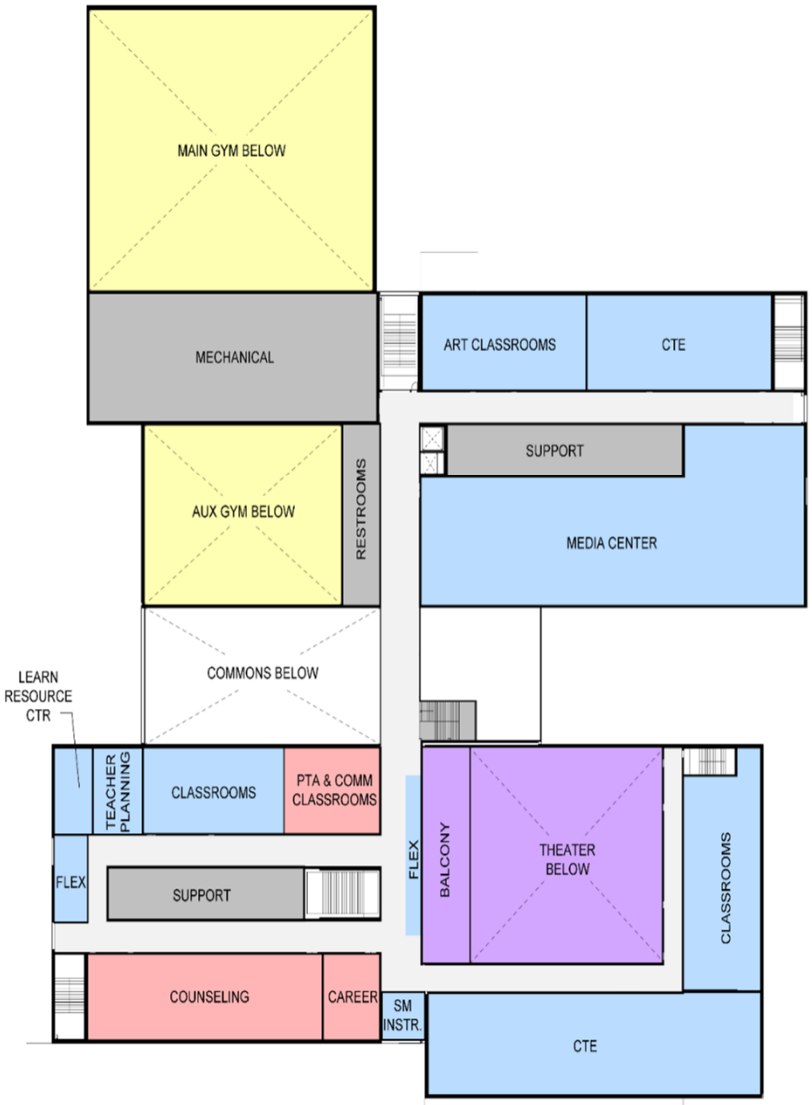

FLOOR PLAN - LEVEL 3

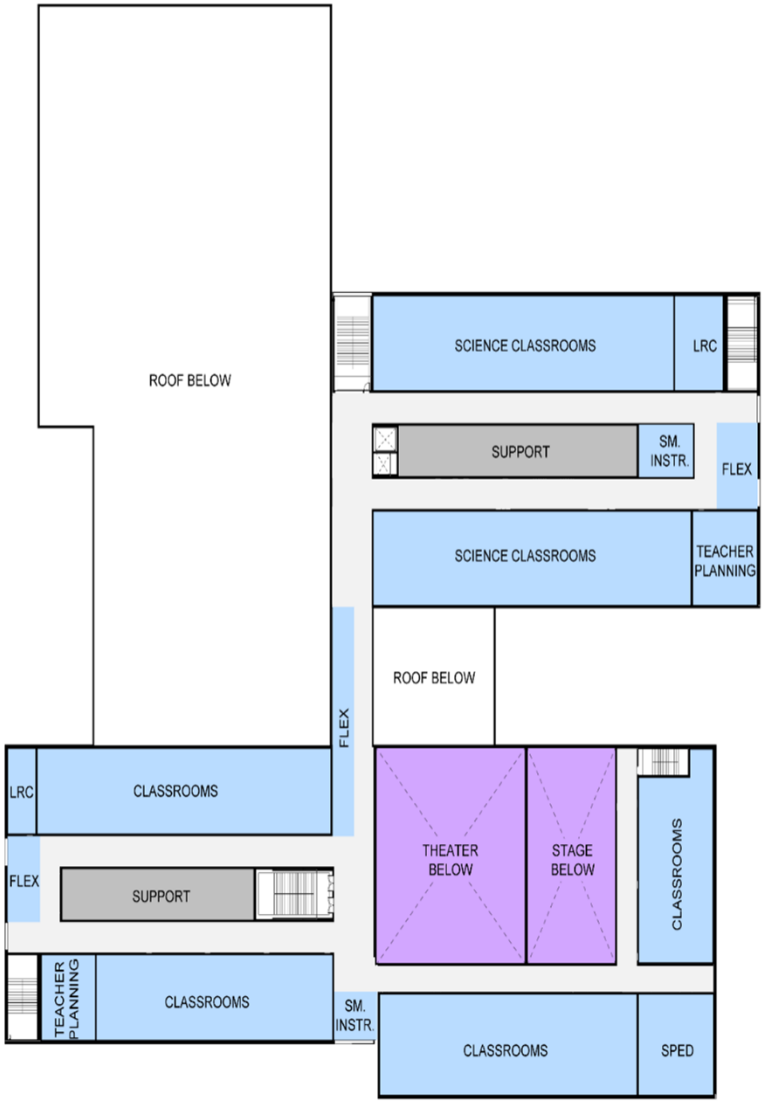

FLOOR PLAN - LEVEL 4

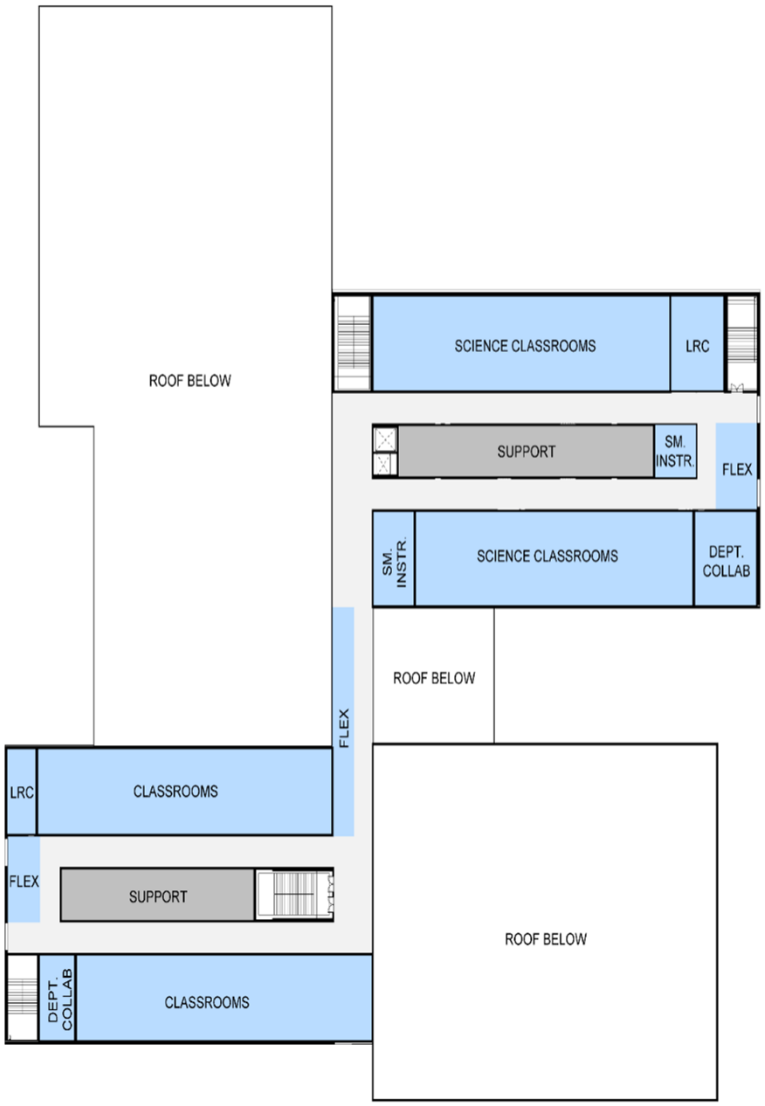

Next Steps

CM/GC onboarding at end of August

Continuing Schematic Design

DAG Meeting #3 August 14th

DAG Meeting #4 September 18th

Community Design Workshop September 22nd

Cleveland HS Modernization Planning & Design

Cleveland HS Modernization Planning & Design

July 2024

PPS Team Lead: Erik Gerding
Design: Mahlum Architects
Construction: n/a

STATUS AT A GLANCE

Legend:

- As planned: no concerns
- Caution: requires attention
- Impacts: impacts occurring

	As Planned	Caution	Impacts
Budget	X		
Equity*			
Schedule	X		
Overall	X		

BUDGET

BUDGET		FUNDING		PROGRESS		FORECAST		CONTINGENCY IN CONTEXT	
Original Budget	**Current Budget**	Bond Funds	Other Funds	Actuals to Date	Additional Encumbered	**Estimate At Completion**	*Over/Under*	Work Complete / %	Contingency Remain / %
20,000,000	**20,000,000**	20,000,000	-	1,913,744	9,593,842	**20,000,000**	-	12%	4.3%

EQUITY

Percent of payments made to Certified owned businesses, percent of labor hours of apprenticeable trades; cumulative

	MBE	WBE	SDVBE	ESB	N-C	**TOTAL**	*goal*	MIN	*goal*	FEM	*goal*	**APPR**	*req*
Consultants	0.00%	0.00%	0.00%	0.00%	0.00%	**0.00%**	*18%*						
Contractors*	0.00%	0.00%	0.00%	0.00%	0.00%	**0.00%**	*18%*						
Overall	0.00%	0.00%	0.00%	0.00%	0.00%	**0.00%**	*18%*						
Workforce*								0%	*25%*	0%	*14%*	**0%**	*20%*

** No construction in this design/planning project.*

SCHEDULE

NEXT MILESTONE: 100% SD

On Track? Yes

PROJECT PHASE	2024				2025				2026				2027			
Planning			★													
Design			★													
Construction			★													
School Opening(s)			★													

Baseline — Planning — Design — Construction — School Opening

Schematic Design Phase

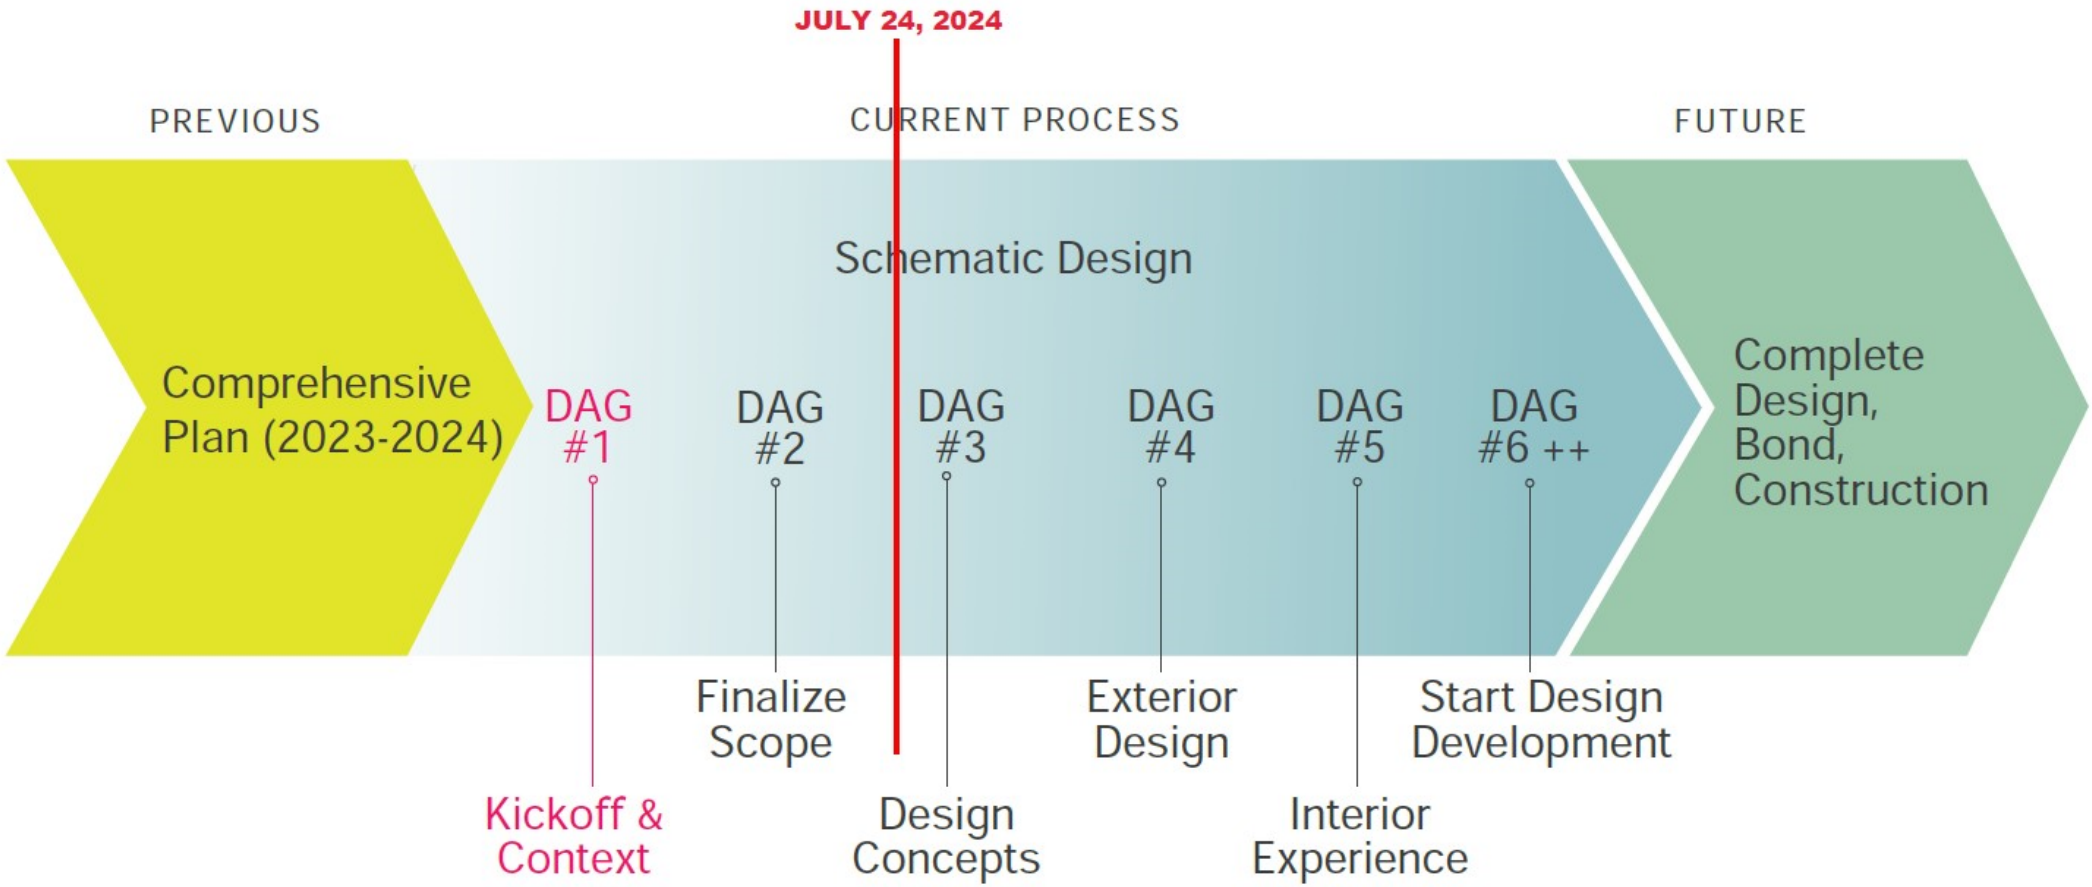

Community Engagement Summary – Schematic Design

Design Advisory Group (DAG)

- 2 DAG meetings so far. Next meeting scheduled for August 1st.

CHS Teachers and Staff:

- Staff meeting presentation and feedback exercise for Schematic Design.

General Community & Affinity Groups:

- Design Workshop on June 1st
- Engagement Sessions with Affinity Groups and Community Based Organizations

Cleveland HS Modernization

Recommended Approach

- PPS Ed Spec: taller, more compact structures
- Allows large open space for student use
- Lowest-cost approach
- Least-risky approach
- Preserves space for CHS staff to park

Cleveland HS Modernization

Recommended Approach

- 315,000-323,000 square feet
- Mass Timber Construction
- All-electric systems, highly efficient
- Upgraded staff parking

Cleveland HS Modernization

Massing option with central courtyard

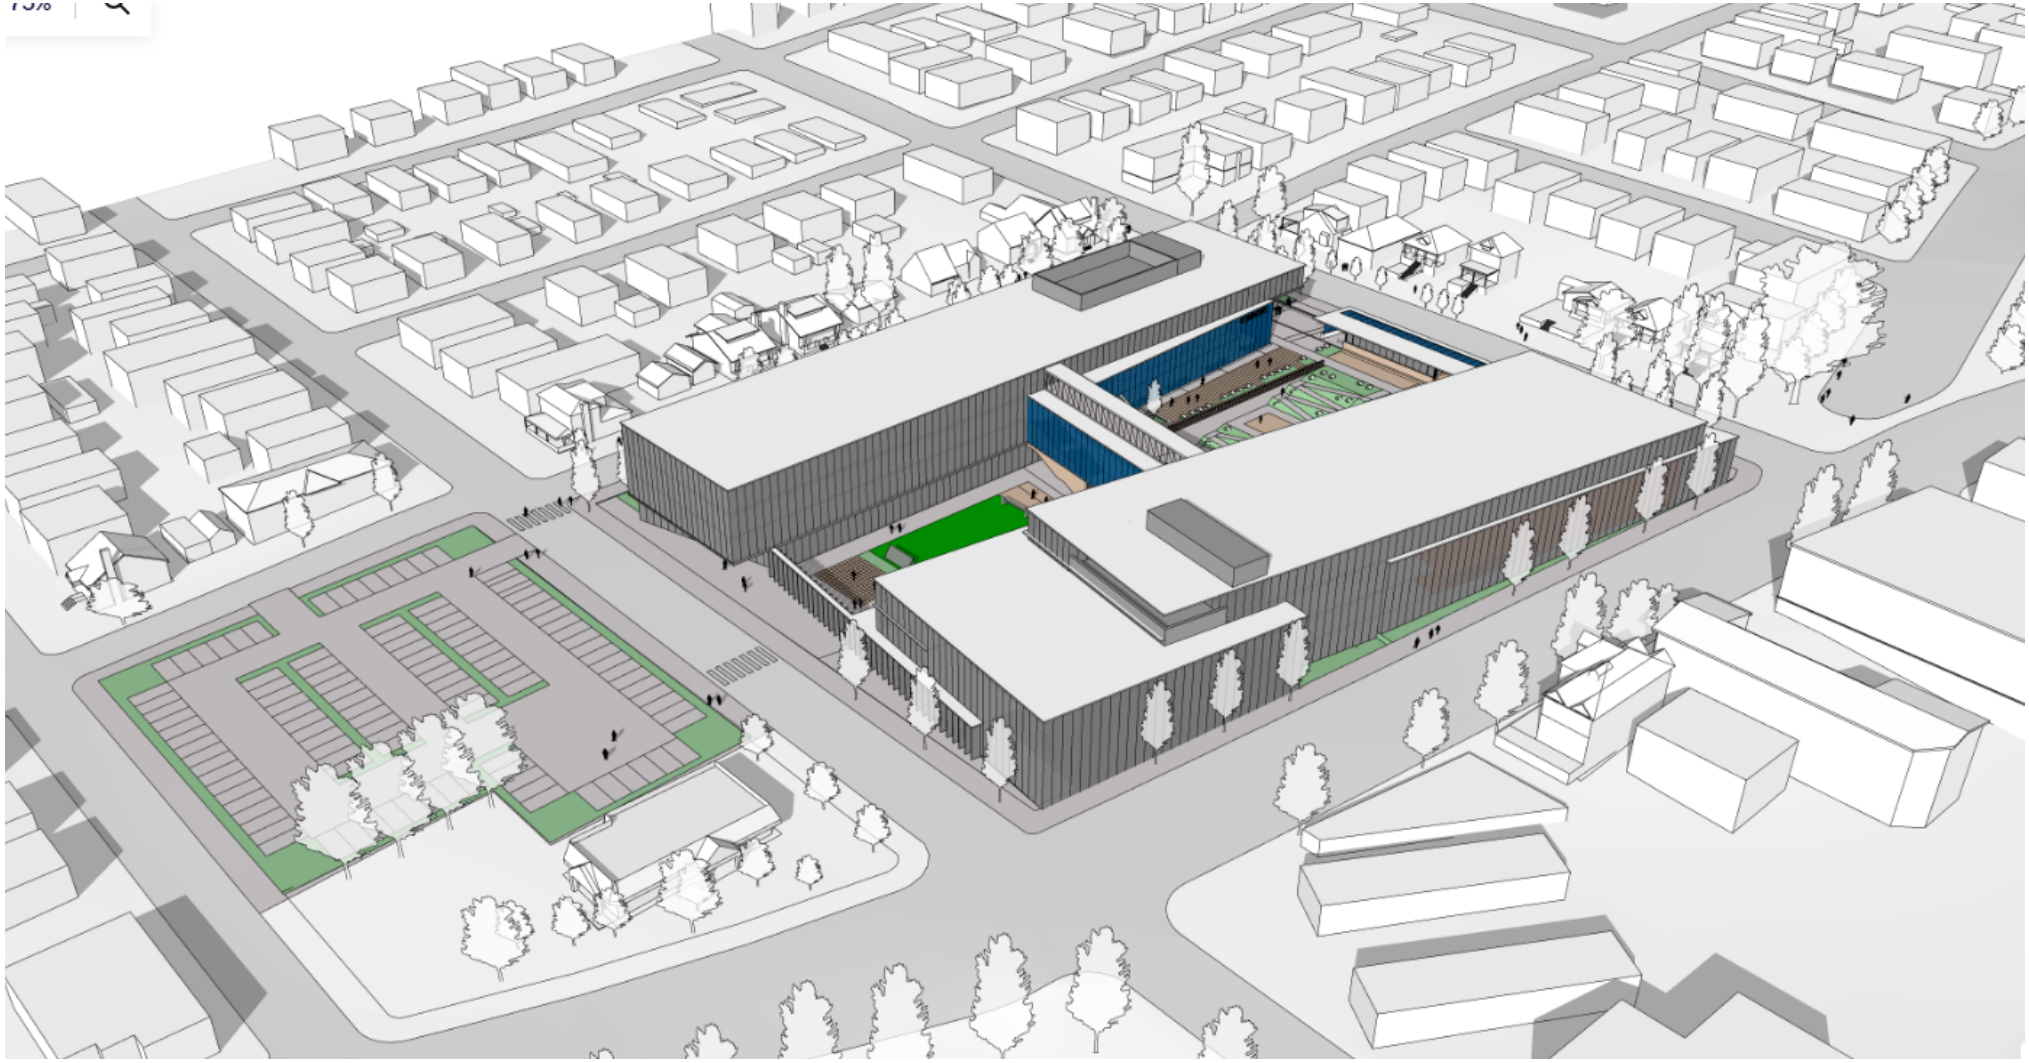

View from the SW over Powell Park.

Cleveland HS Modernization

Massing option with central courtyard

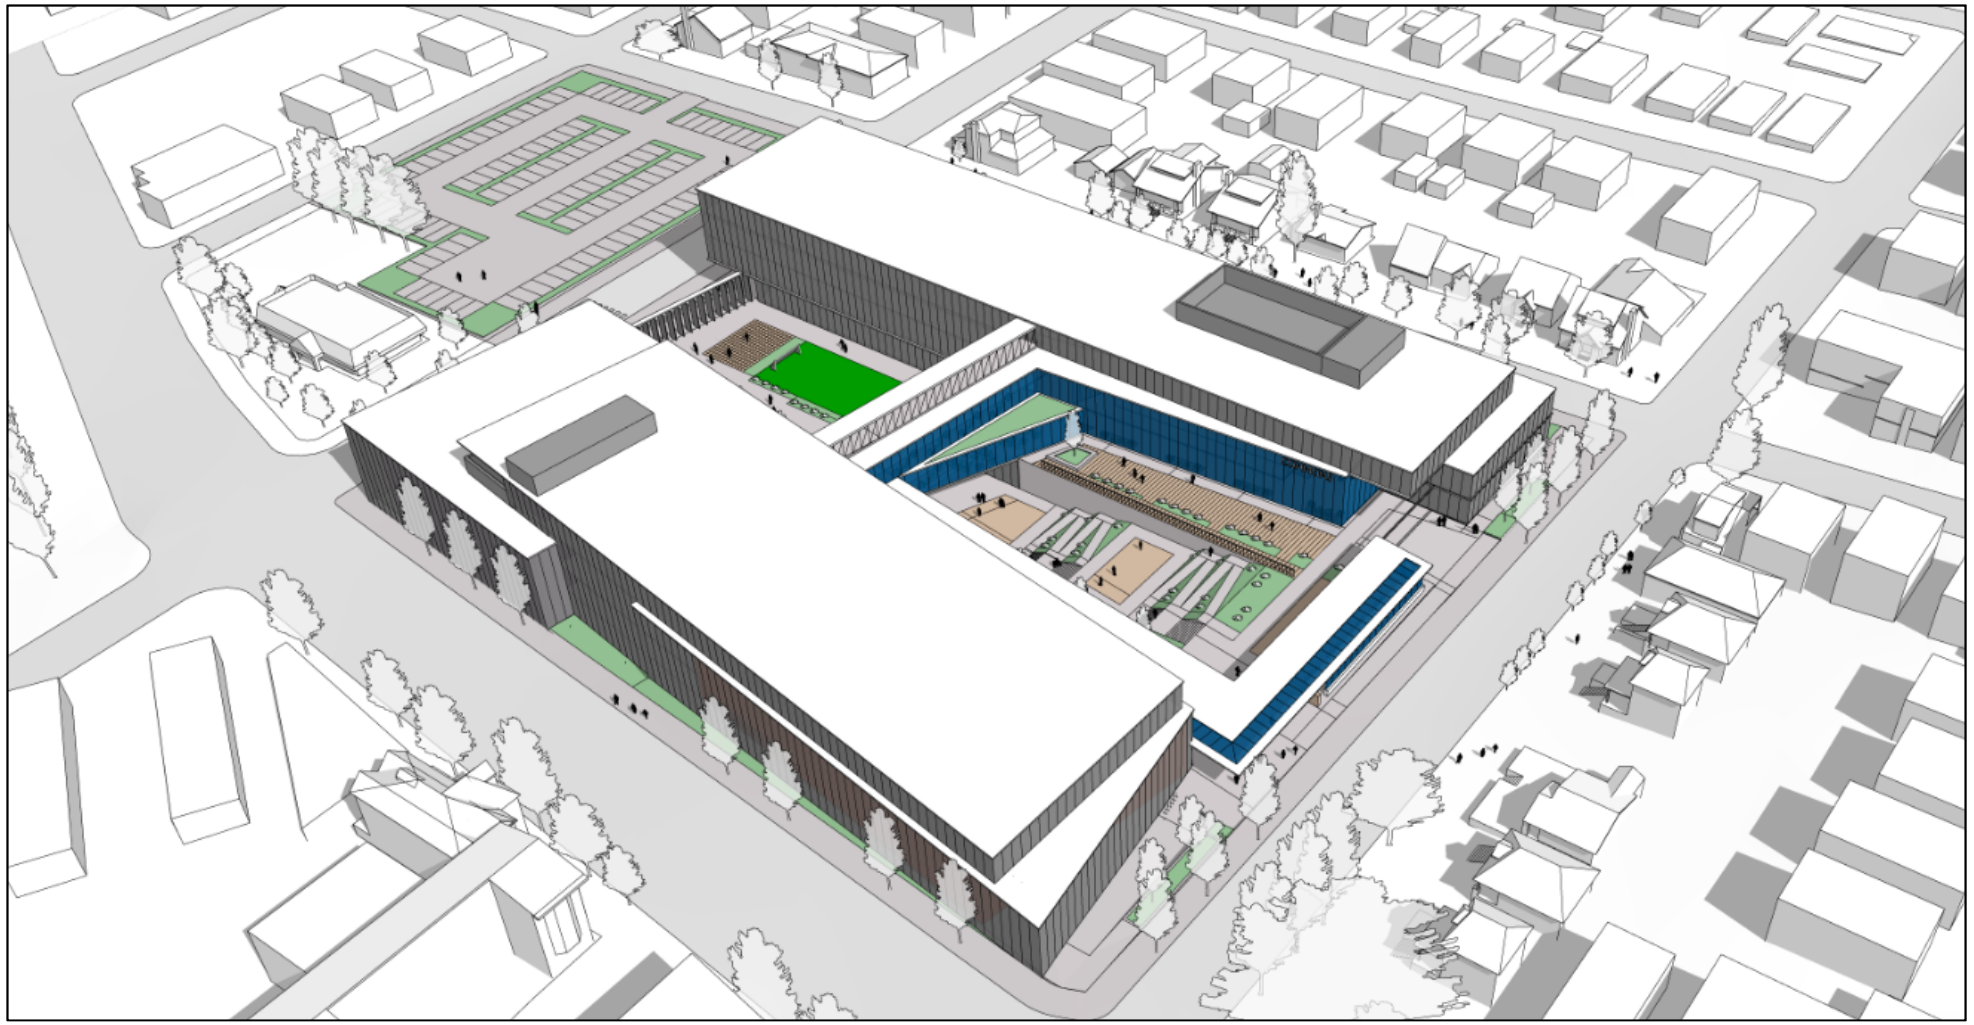

Cleveland HS Modernization

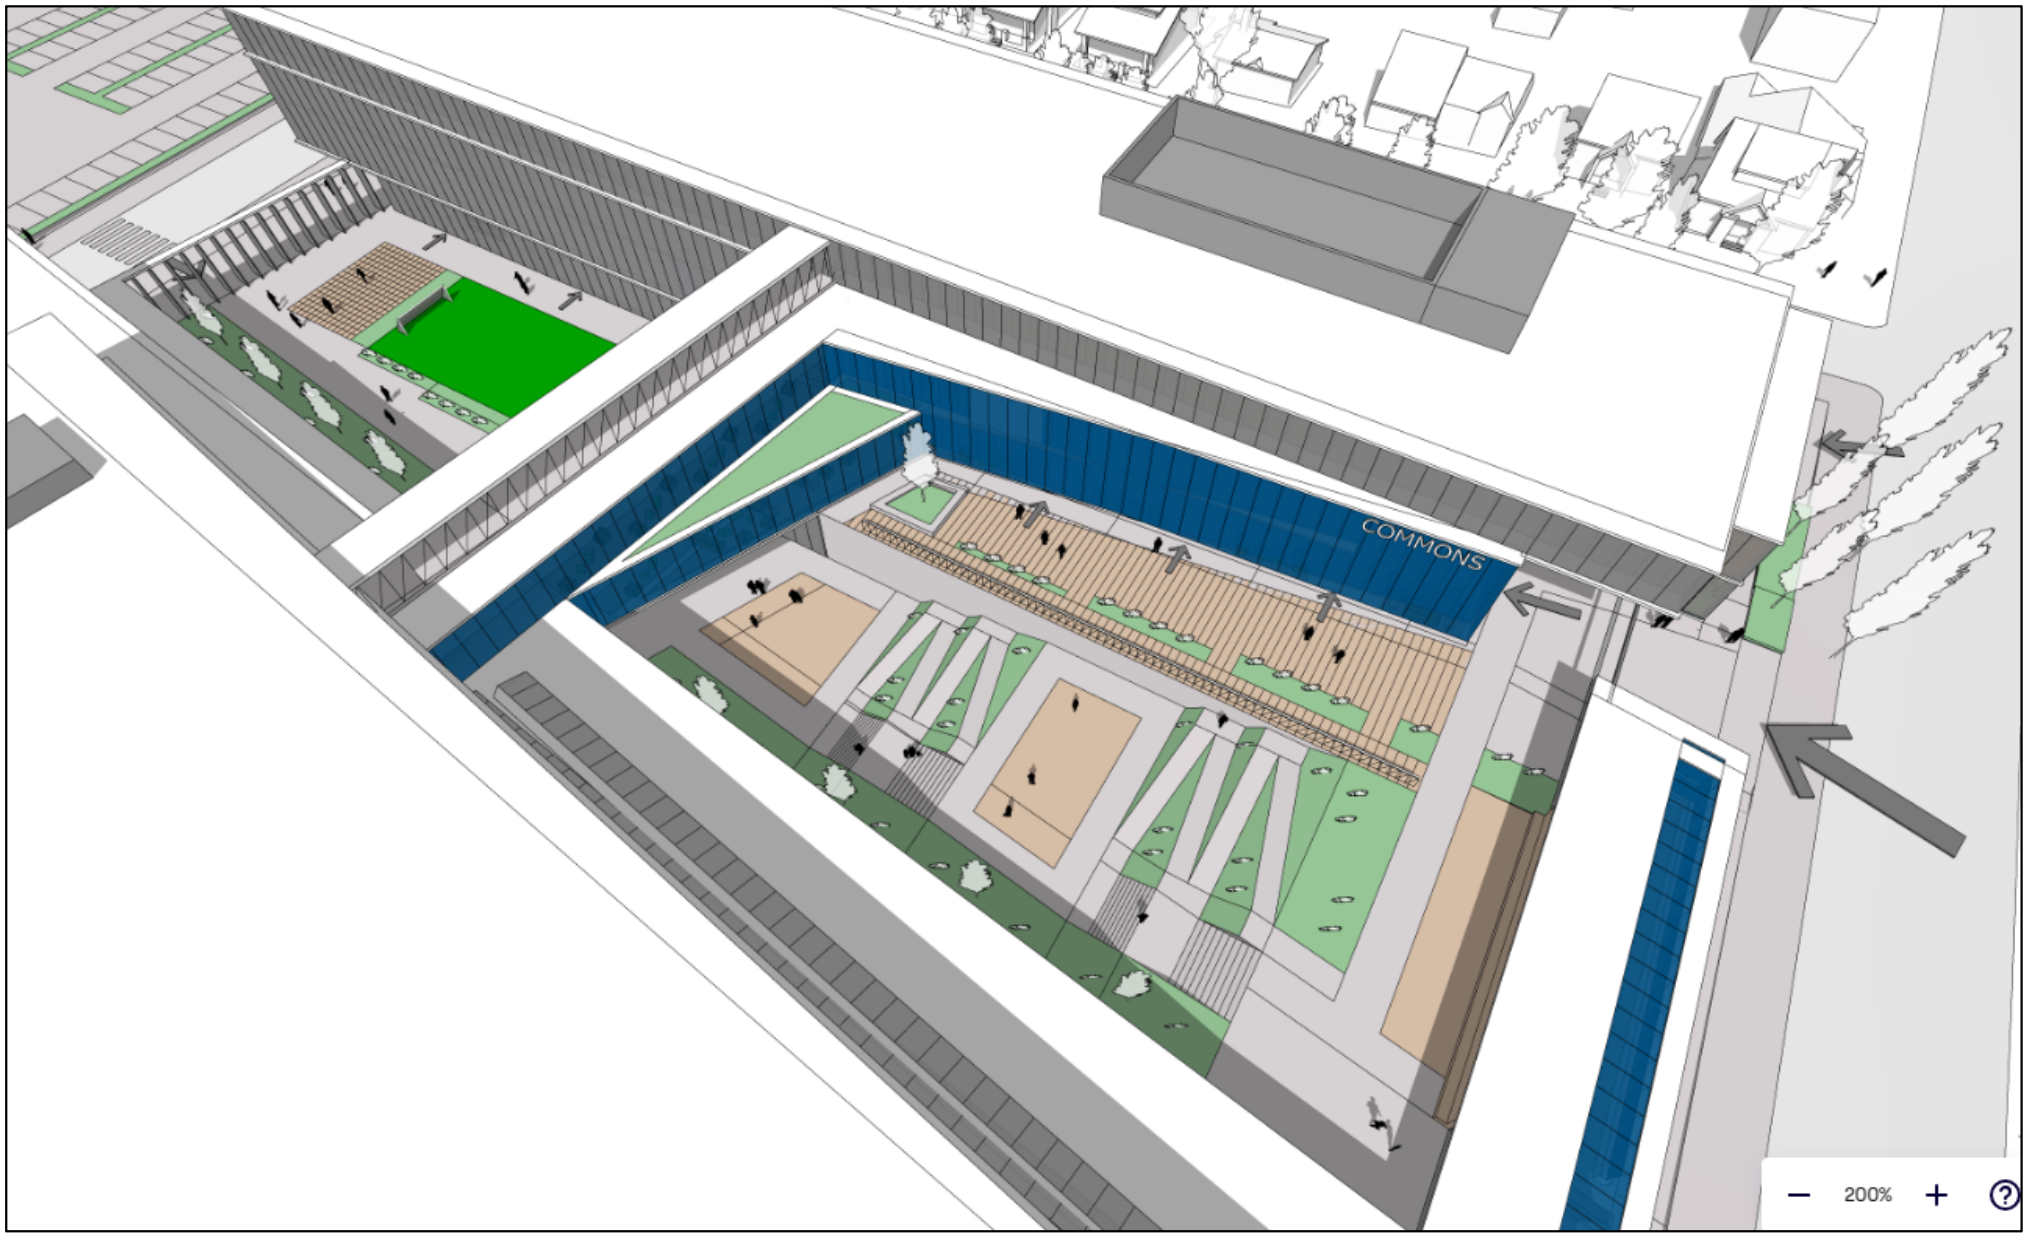

Cleveland HS Modernization

Entry Massing

Next Steps

Major Projects Group review process with City of Portland

CMGC RFP and Selection

Ongoing Schematic Design and Community Engagement

Audit Implementation Status Updates

Adjourn

Next meeting:
October 23, 2024
(In-Person Meeting – Location TBD)
