SEPTEMBER 16, 2025

Cleveland High School

Comprehensive Plan Update

PORTLAND PUBLIC SCHOOLS

Topics for Review

> Site opportunities and constraints
> Proposed building design
> Building area reductions
> Cost reduction strategies
> Updated floor plans
> Interior renderings
> Updated athletic fields
> Project schedule
> Updated project budget



Site Opportunities and Constraints



Site Opportunities and Constraints

CURRENT CHS BUILDING
254,000sf



- 4 acre main site; smallest in District
- On Powell Boulevard (state highway)
- 2-3 story configuration fills entire site
- No secure outdoor space for students
- No extra space for construction logistics;
- Opportunity to create secure open space in new design
- Opportunity to reduce construction logistics costs with smaller building footprint

Proposed Design

CURRENT CHS BUILDING
254,000sf



PROPOSED BUILDING
Approx. 297,000sf





Views from NE corner (SE Franklin and 28th Ave)




Building Area Reductions

Square feet reduced from 317,000 to 297,000. Areas shown in yellow were removed from the building.

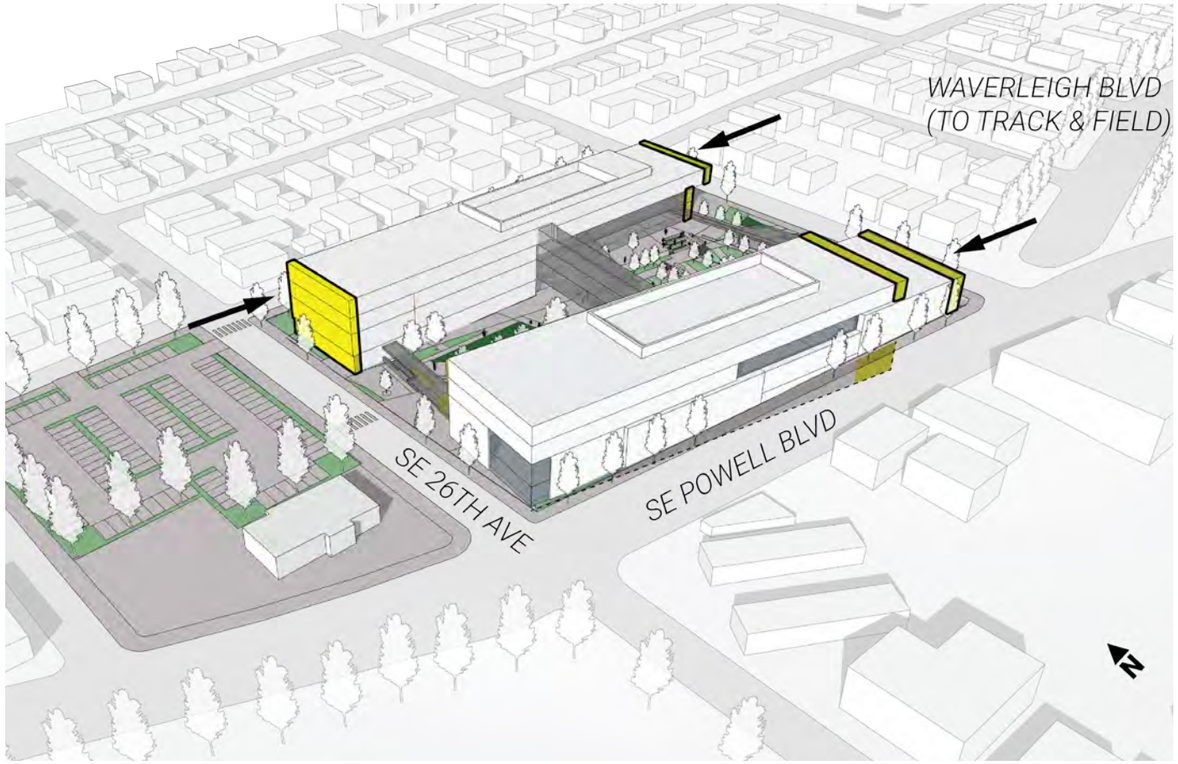

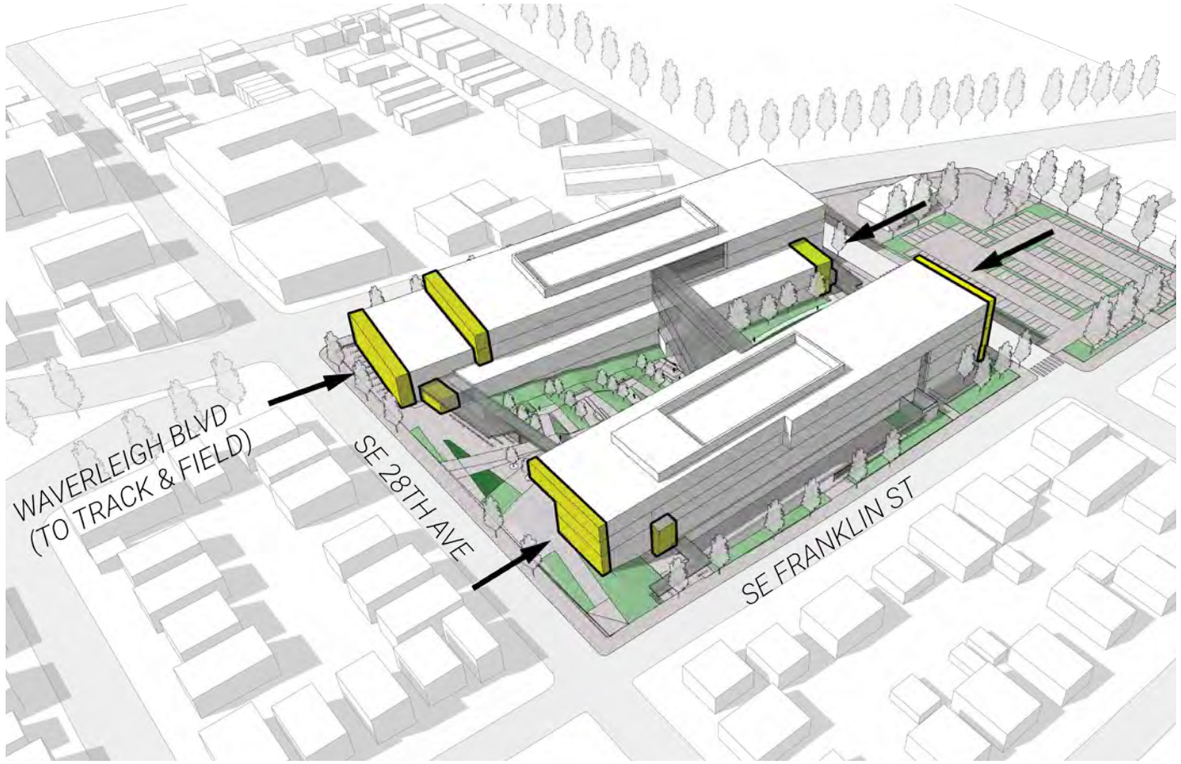

Area Program Comparison

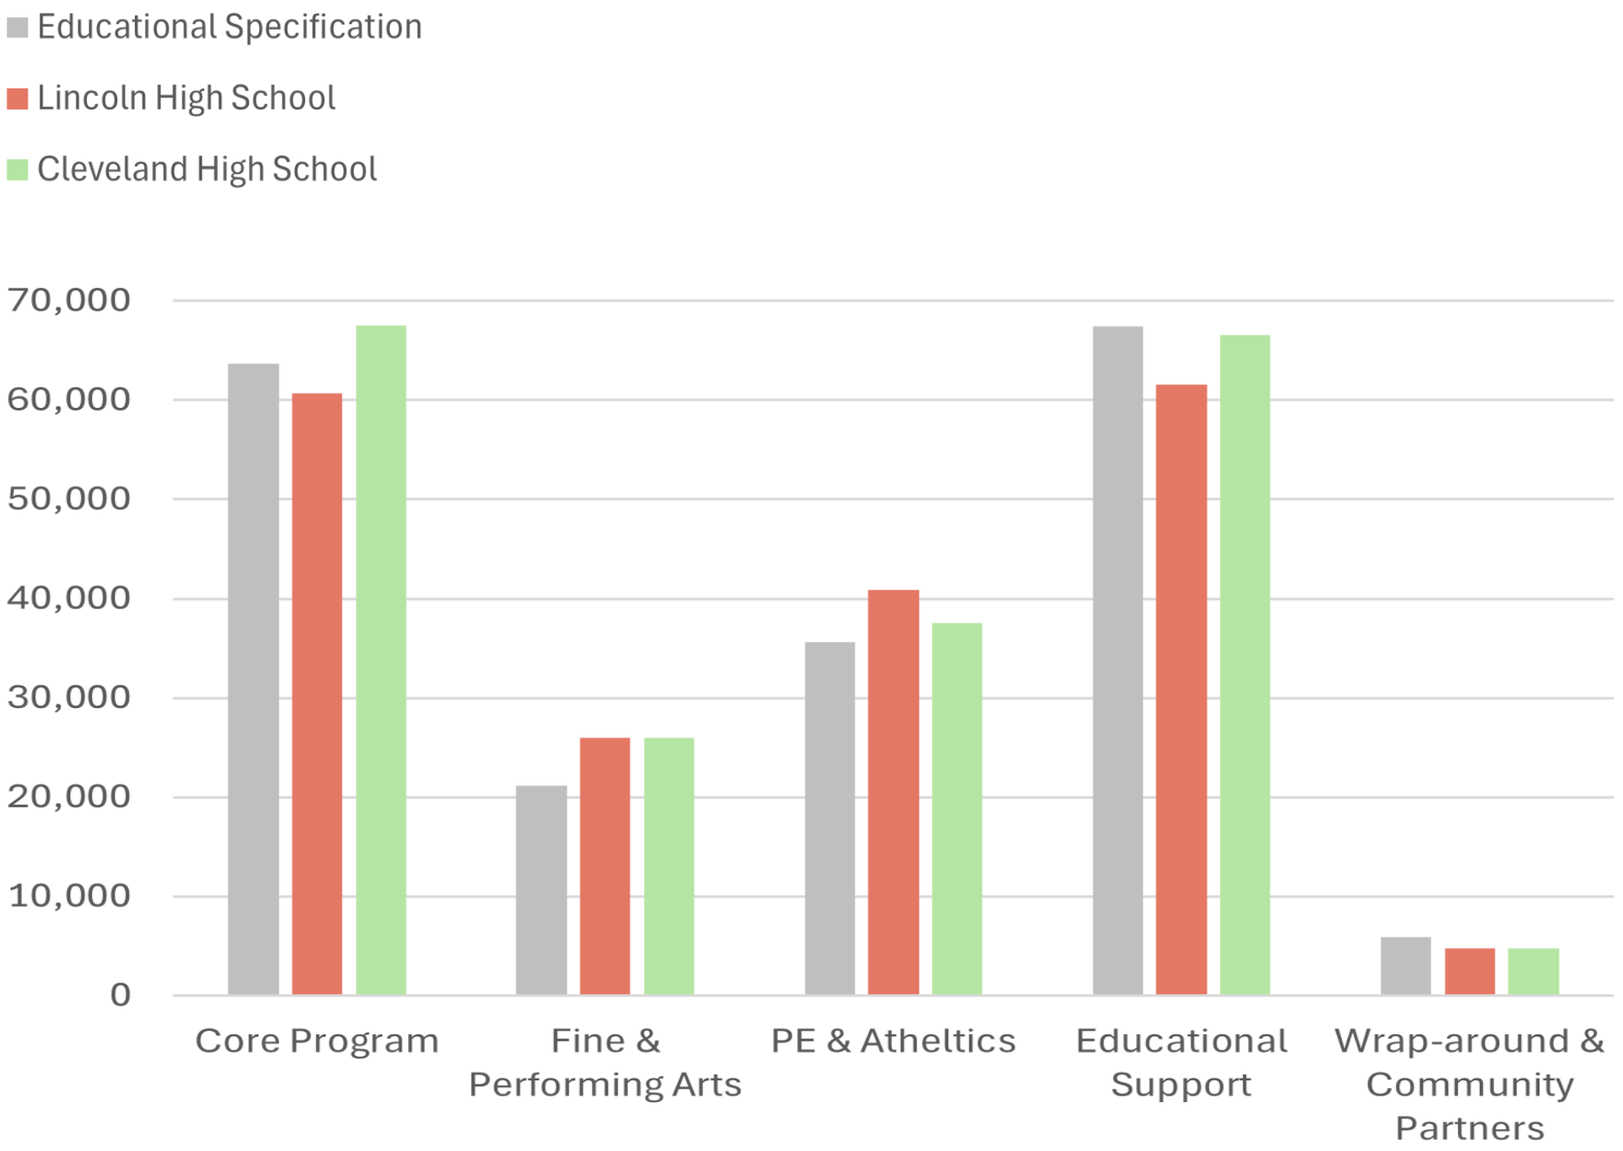

Building Design: Floor Plan Updates

L01

- FLEX LEARNING
- SPED + LRC
- CTE
- VISUAL + PERFORMING ARTS
- WRAPAROUND SERVICES
- GYM + ATHLETICS
- MISCELLANEOUS
- CUSTODIAL



Building Design: Floor Plan Updates

L02

- ADMIN / STUDENT SPACE
- COUNSELING / CAREER
- FLEX LEARNING
- SPED + LRC
- GENERAL CLASSROOMS
- VISUAL + PERFORMING ARTS
- STUDENT COMMONS
- GYM + ATHLETICS
- MISCELLANEOUS
- CUSTODIAL



Building Design: Floor Plan Updates

L03

- ADMIN / STUDENT SPACE
- LIBRARY / MEDIA CENTER
- FLEX LEARNING
- SPED + LRC
- GENERAL CLASSROOMS
- CTE
- VISUAL + PERFORMING ARTS
- MISCELLANEOUS
- CUSTODIAL



Building Design: Floor Plan Updates

L04


- ADMIN / STUDENT SPACE
- FLEX LEARNING
- SPED + LRC
- GENERAL CLASSROOMS
- CTE
- MISCELLANEOUS
- CUSTODIAL



Updated Athletic Fields

Athletics Cleveland Stadium Site

- > Reduced size of Field House
- > Number of team rooms from 3 to 2
- > Storage building is now an Add Alternate
- > Batting facility/multi- purpose space
- > New practice field
- > Updated field lighting
- > Replacement of main field turf

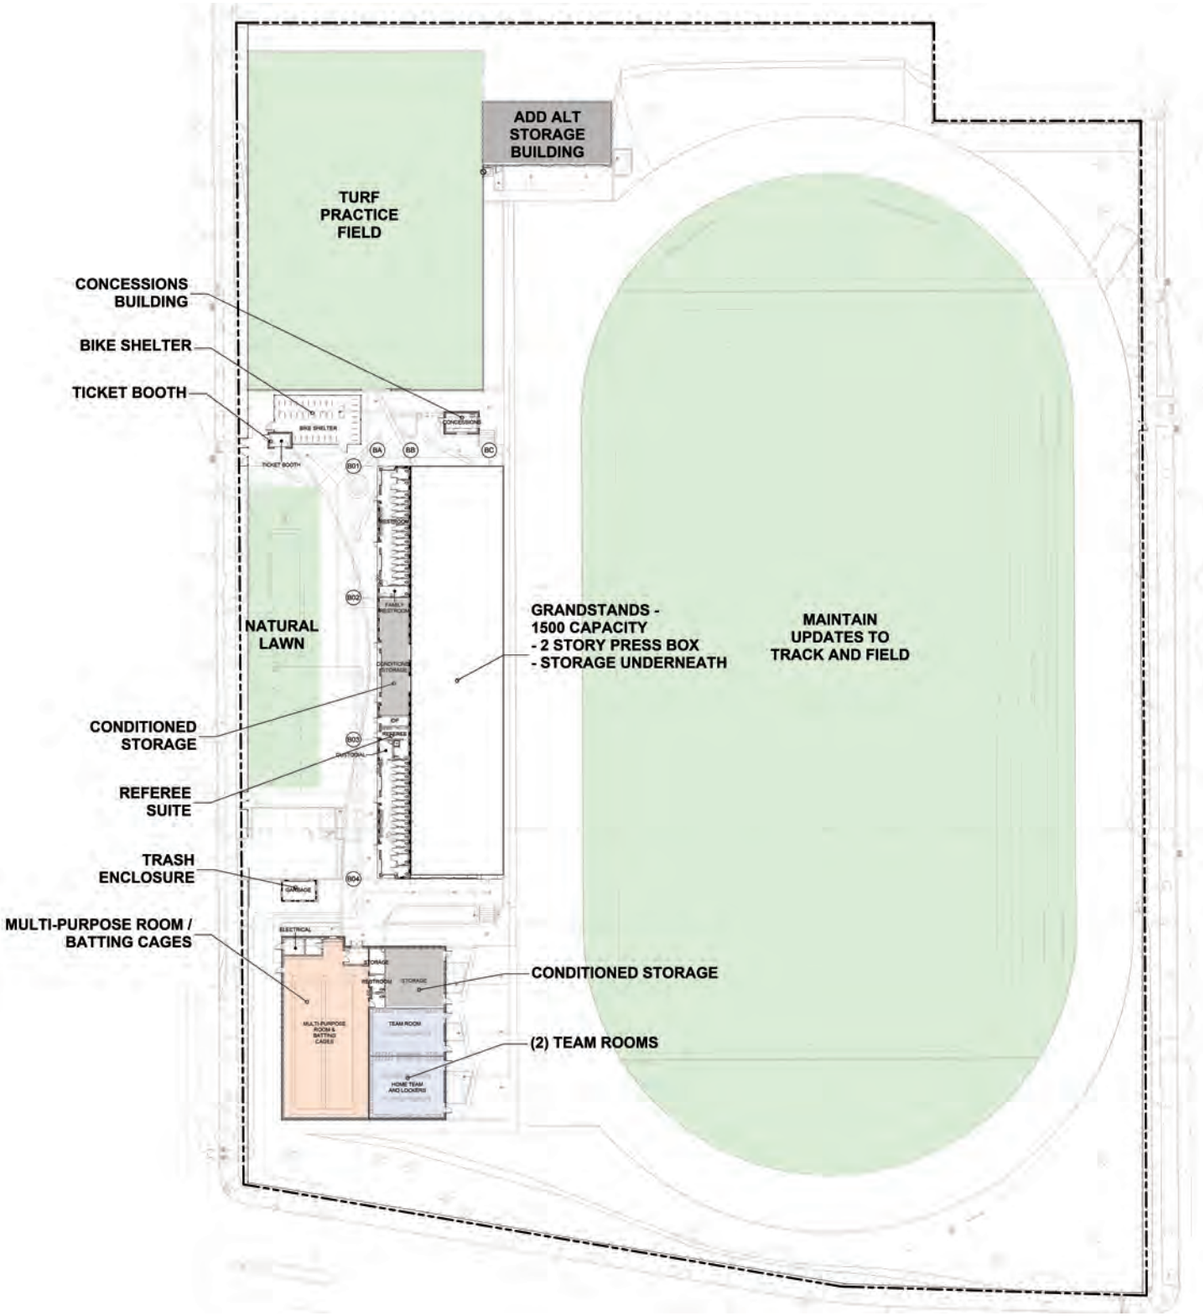

Interior Views



Interior Views



Connector Looking North


Interior Views



Interior Views



Interior Views

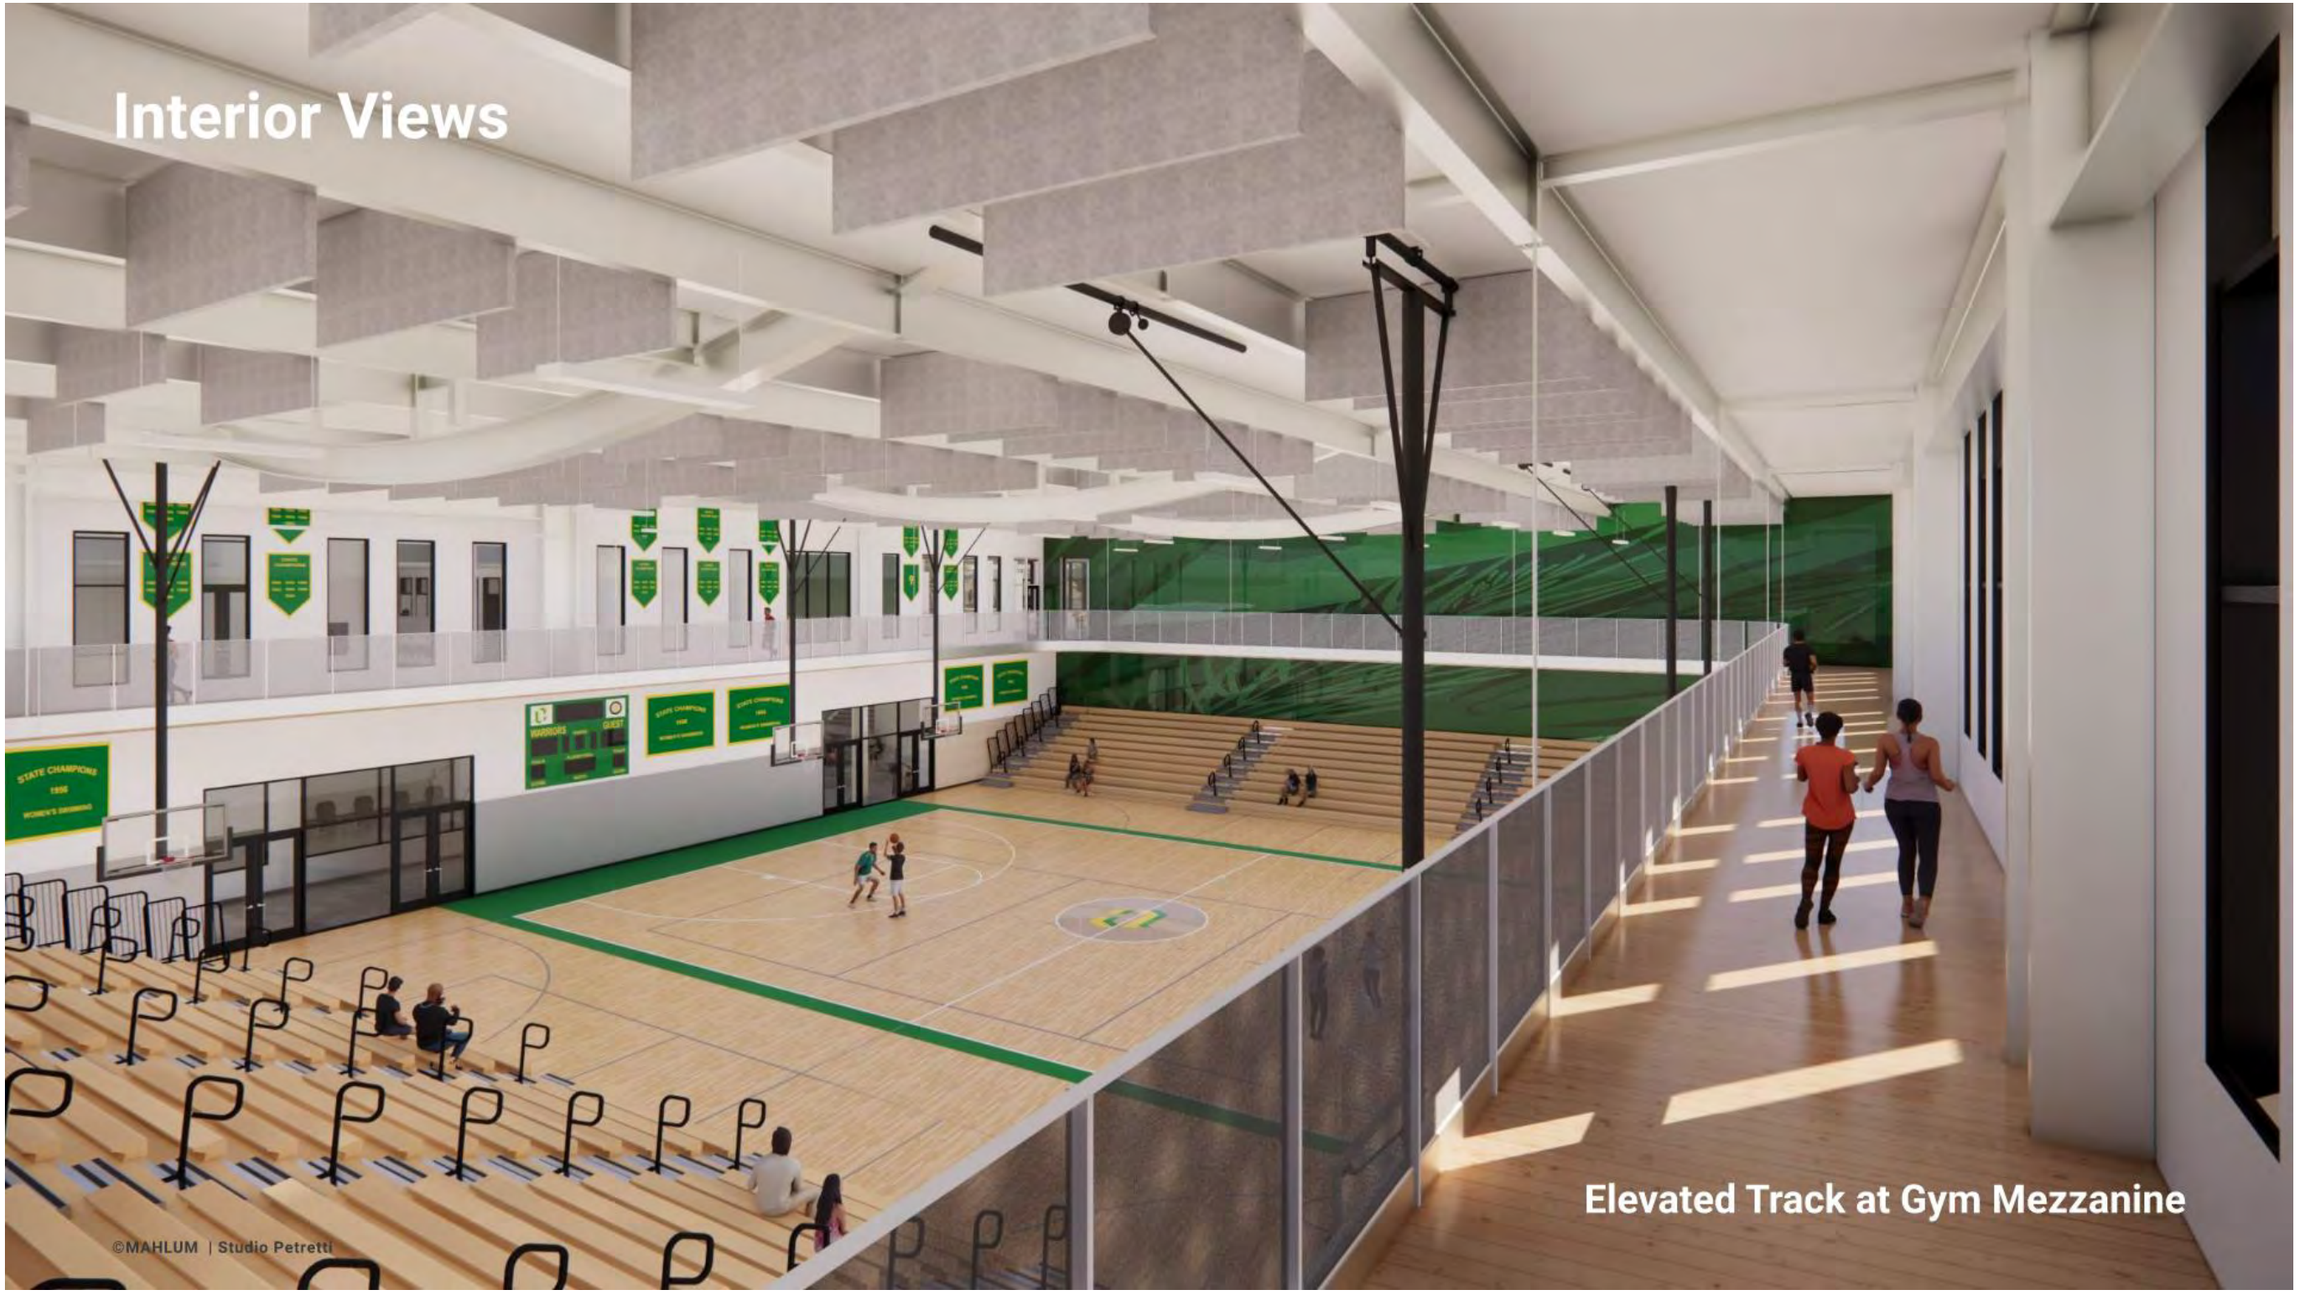

Elevated Track at Gym Mezzanine


Updated Athletic Fields

Potential Powell Park Improvements

- Baseball field & multi-purpose field for soccer and lacrosse
- Separate softball field



CHS Overall Project Schedule

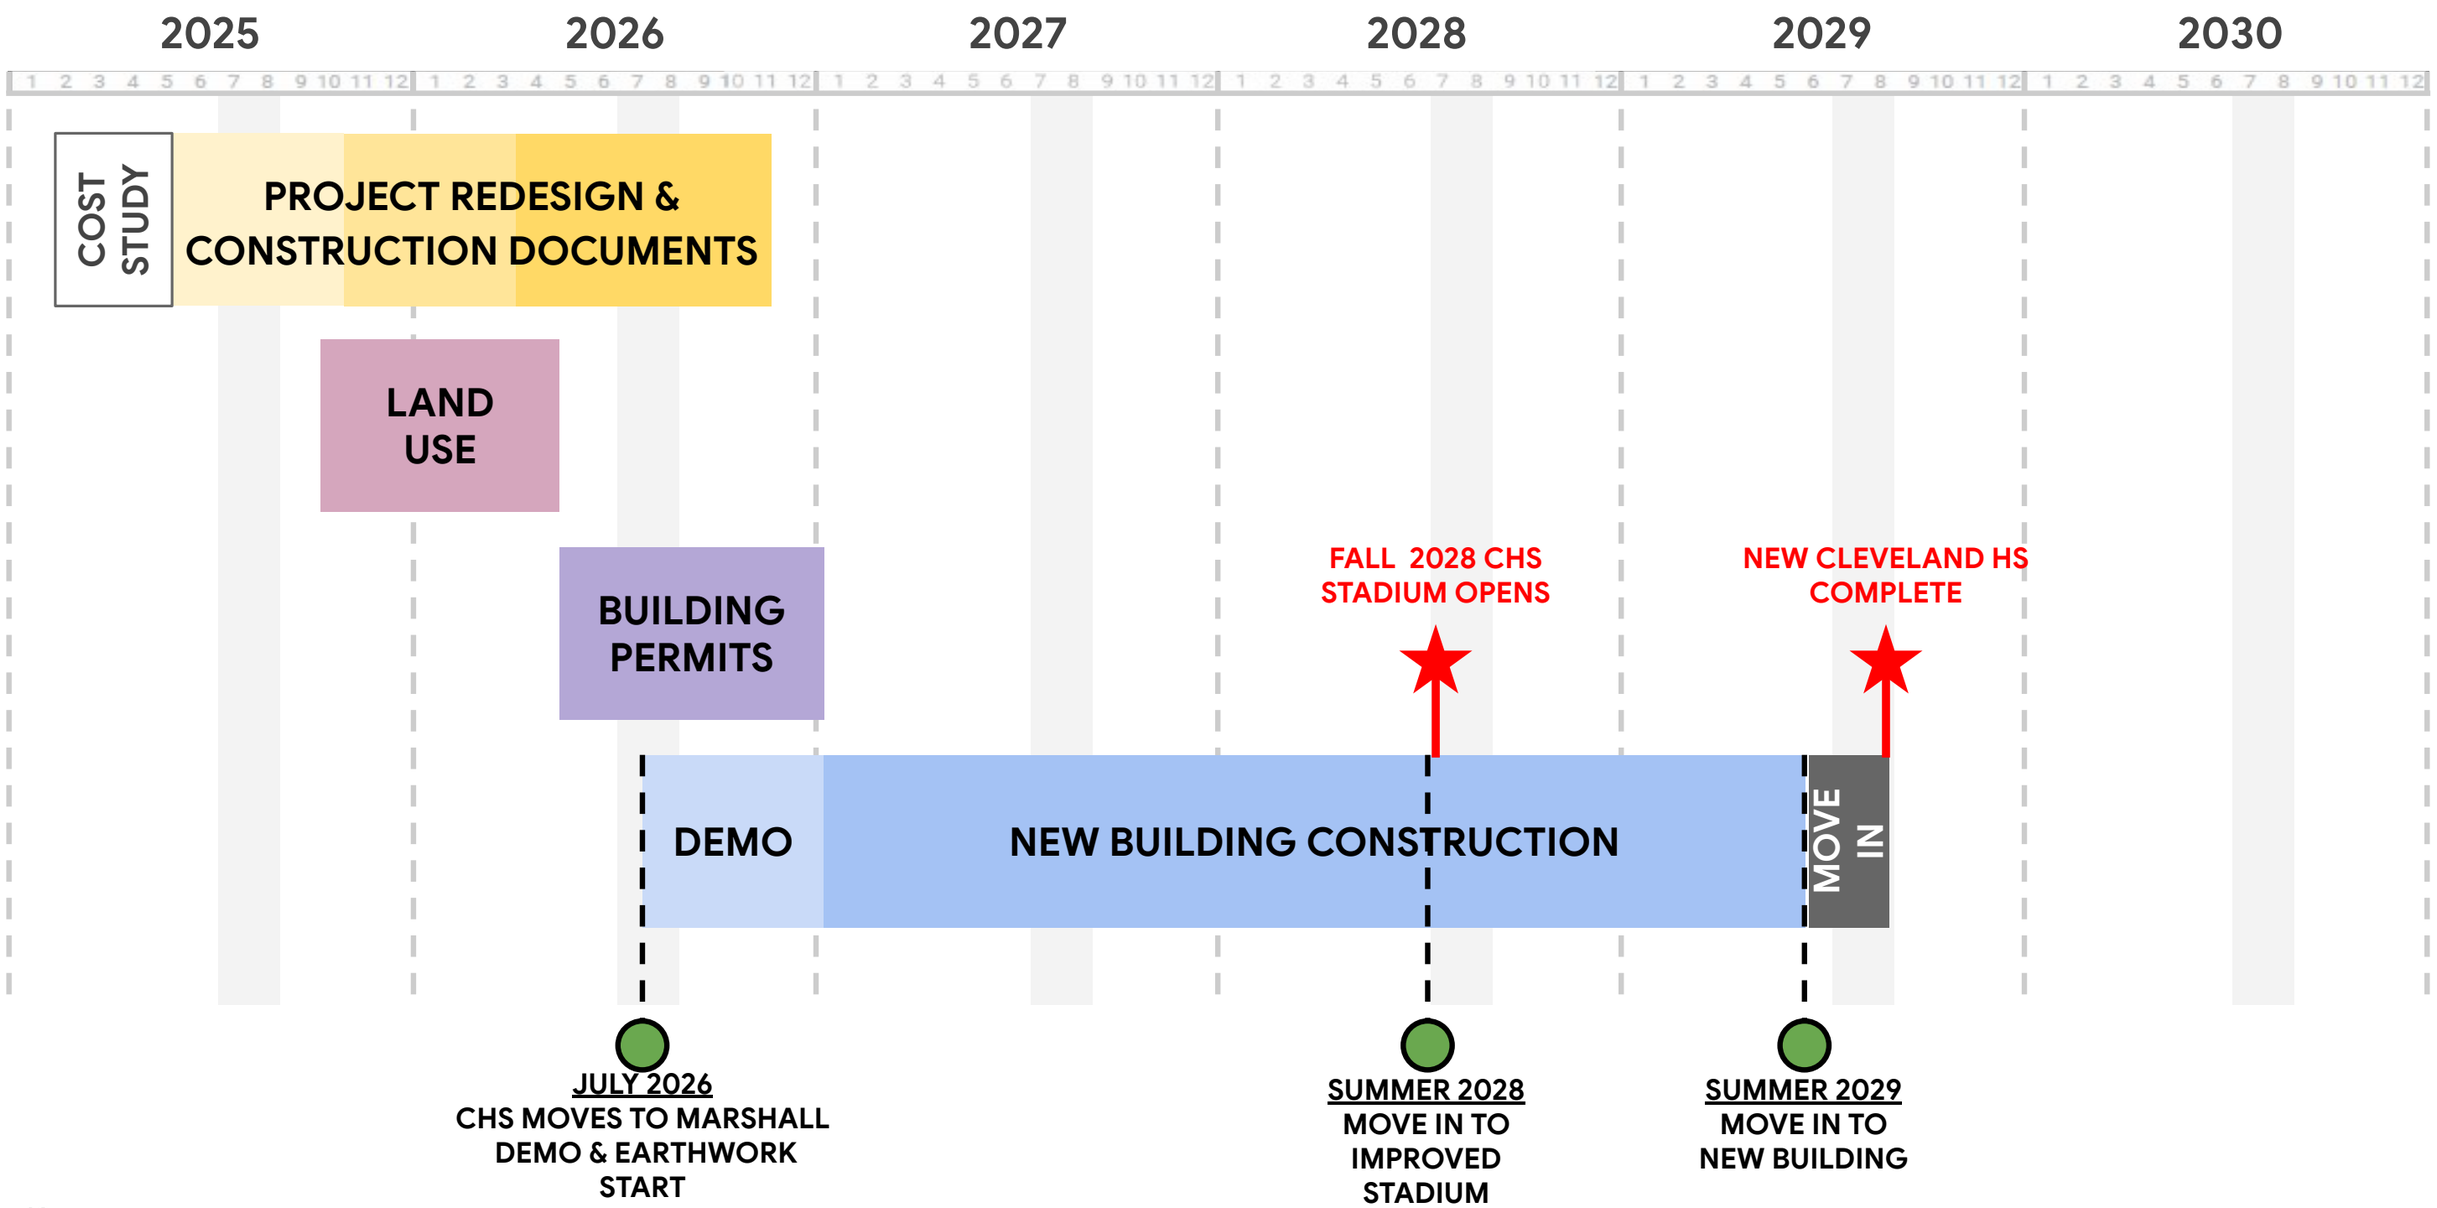

CHS MODERNIZATION BUDGET SUMMARY

COMPONENT	COMMENTS	2024 BOE APPROVED COMPREHENSIVE PLAN	2025 REVISED COMPREHENSIVE PLAN
Hard Cost	Building & Site Work 2025: Includes actuals paid-to-date to CM/GC	$ 377,654,178	$ 364,284,431
1.5% Green Energy Tech		$ 5,664,813	$5,529,547
Subtotal		**$ 383,318,991**	**$ 369,813,978**
Owner Direct Hard Costs	Off site improvements, utility costs not included above	**$ 1,650,000**	**$ 1,200,000**
TOTAL HARD COSTS		**$ 291,057,660**	**$ 371,013,978**
Soft Costs	Approx. 9.5% of Hard Costs	$ 33,155,000	$ 34,580,000
Fixtures, Furniture & Equipment, including technology	Approx. $34/SF	$ 8,700,000	$ 10,000,000
Moves / Swing Space / Temp Facilities		$500,000	$1,500,000
Contingency	10% of Total Costs (additional 5% CM/GC contingency included in Hard Cost Estimate)	$ 41,320,859	$ 40,449,622
Escalation	Included in Hard & Soft Costs		
MAIN BUILDING BUDGET		**$ 468,644,850**	**$ 457,553,760**
SAVINGS FROM 2024 DESIGN			**$(11,091,090)**
OFF SITE ATHLETIC FIELDS	Work may include fields at Powell park and Hosford MS		**$15,000,000**
TOTAL PROJECT BUDGET			**$472,553,760**

CHS Project Next Steps

- Design Development Phase
  - Ongoing design review with PPS stakeholders
  - 75% DD milestone documents to be issued October 24th
  - New cost estimates to follow 75% documents

- Preconstruction Services - CMGC
  - Skanska to issue trade partner preconstruction service contracts with MEP and Framing subcontractors

- Community Engagement
  - Design Advisory Group (DAG) - September 18th, 2025
  - Community Design Workshop - October 4th, 2025
  - Sellwood MS - October 16th, 2025
