Jefferson High School Modernization

PPS Facilities Improvement & Oversight Committee

September 16, 2025


BORA PLACE LEVER

AGENDA

- Current Plan Overview
- Current Design Work
- Current Project Schedule
- Updated Budget Summary
- Next Steps


Current Plan Overview

Overall Site Plan

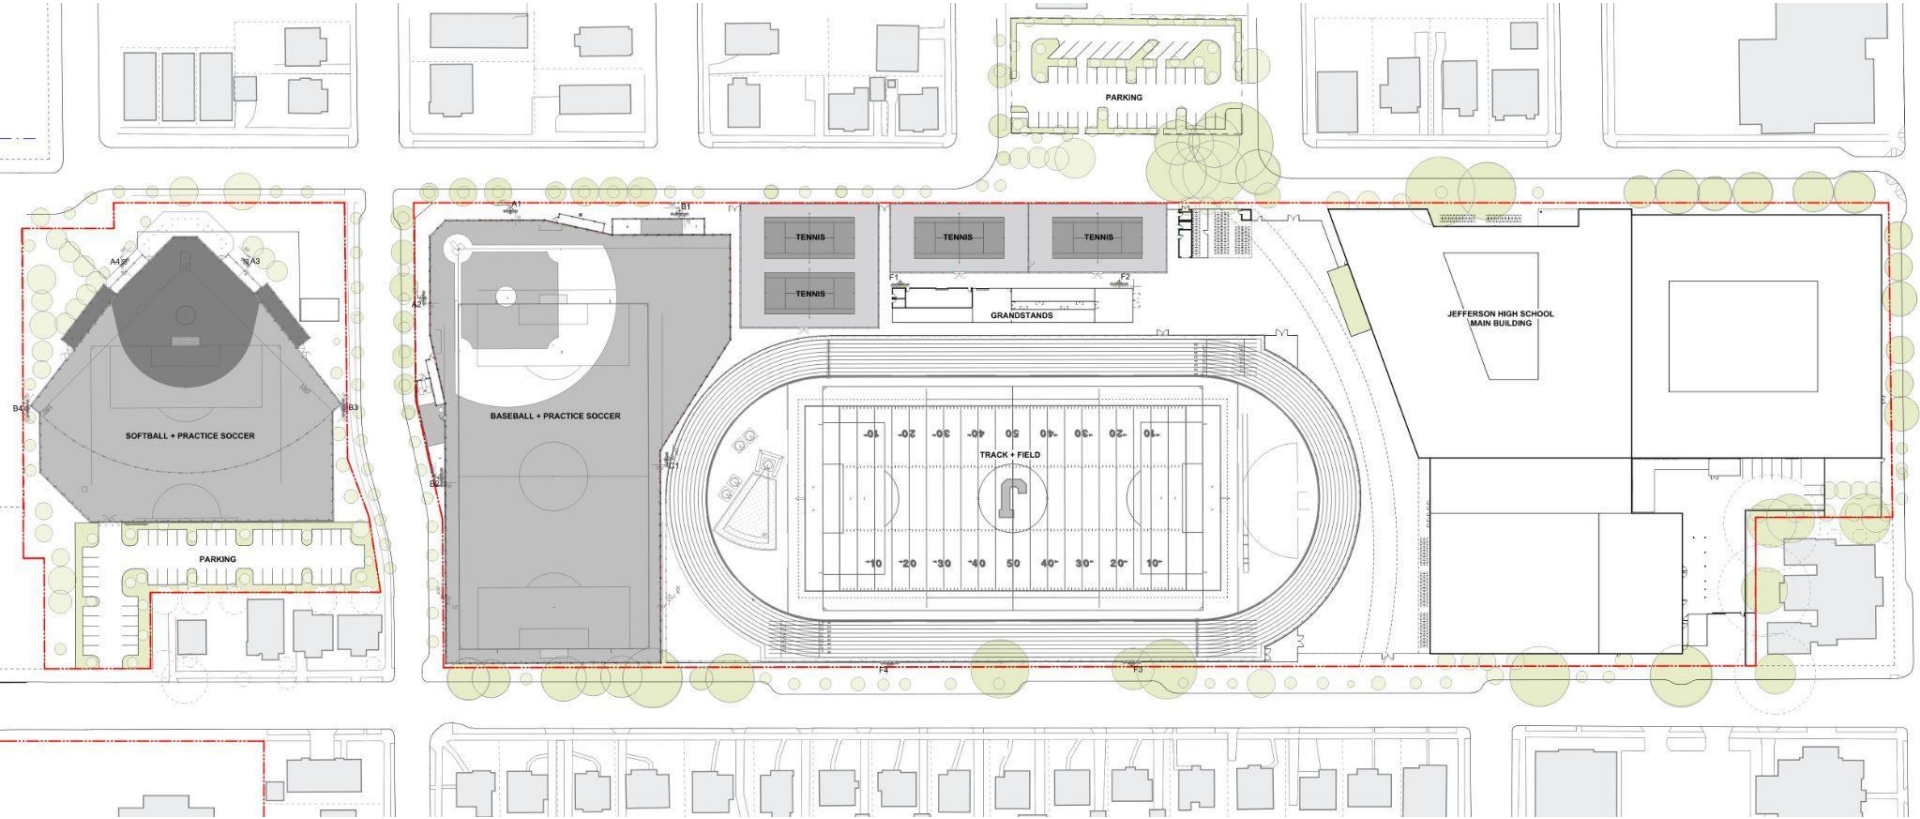


Cost Reduction Study Review

Previous Design

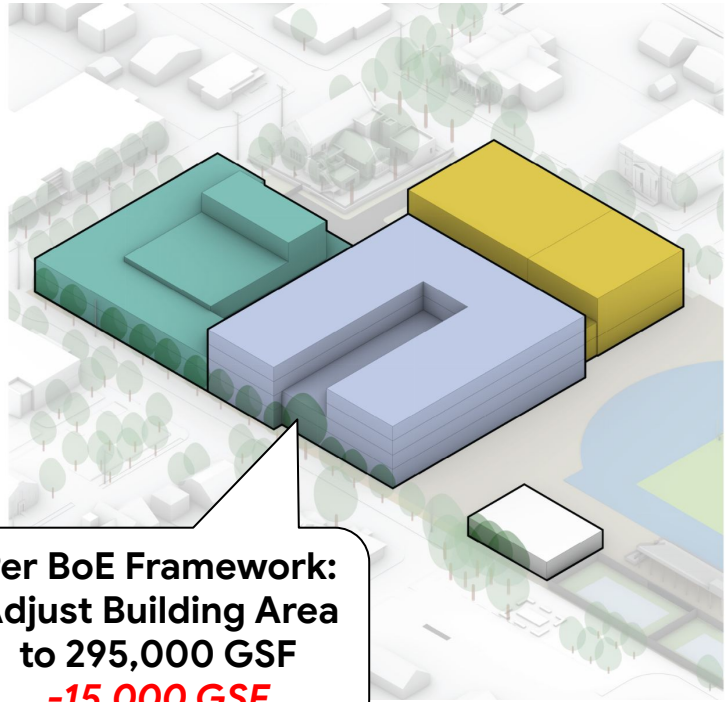


Per BoE Framework: Adjust Building Area to 295,000 GSF
-15,000 GSF

Updated Design

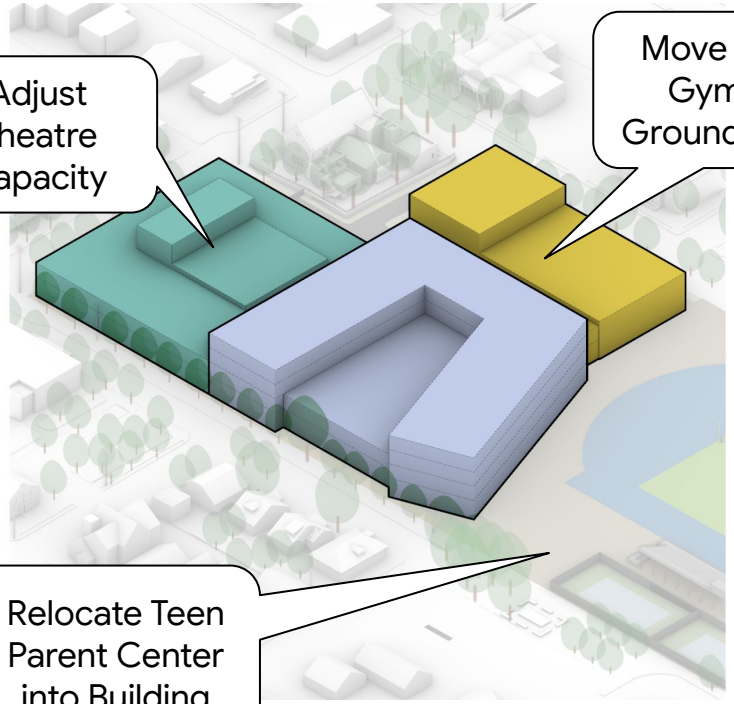


ACADEMICS PERFORMING ARTS ATHLETICS


Floor Plan Overview - Level 1

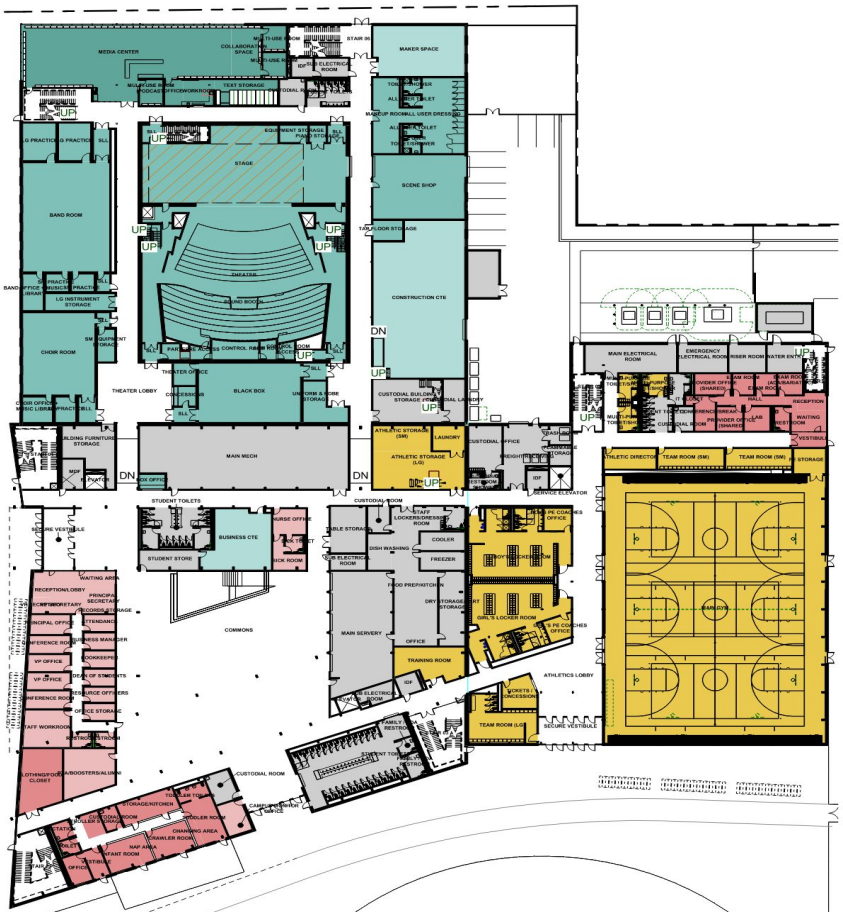


- ADMIN, COUNSELING & CAREER
- COMMUNITY & PARTNERS
- GENERAL CLASSROOMS & SCIENCE
- SPED
- FINE / GRAPHIC ARTS & CTE
- PERFORMING ARTS
- MEDIA CENTER
- ATHLETICS
- BUILDING SUPPORT

Floor Plan Overview - Levels 2 thru 4

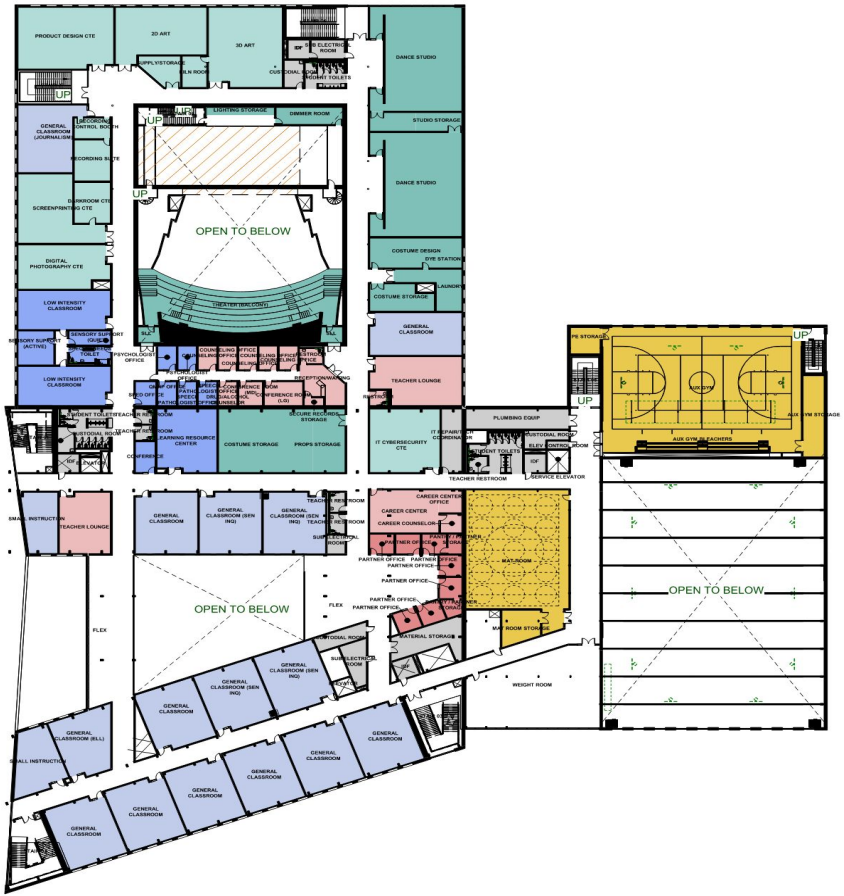

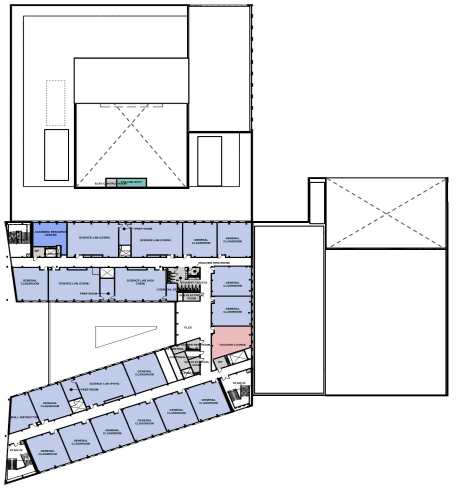

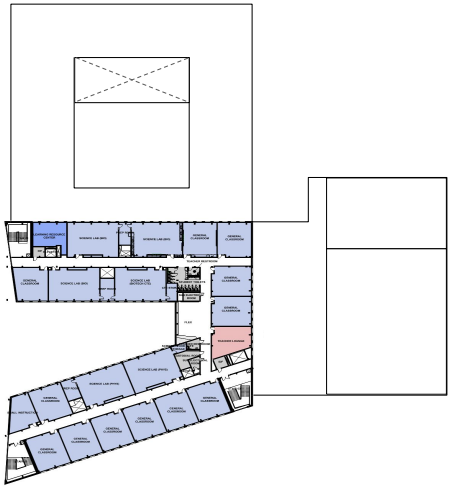

PPS Comprehensive Education Specifications

Ed Spec Minimum

Building Area
284,190 GSF

Previous Design - 50%DD

(EdSpec+)

Building Area
311,139 GSF


2025 Comprehensive Plan

Building Area
299,044 GSF

Reduction of 12,095sf from 50% DD

5,233 GSF of additional Mech/Elec for All Electric

293,811 GSF

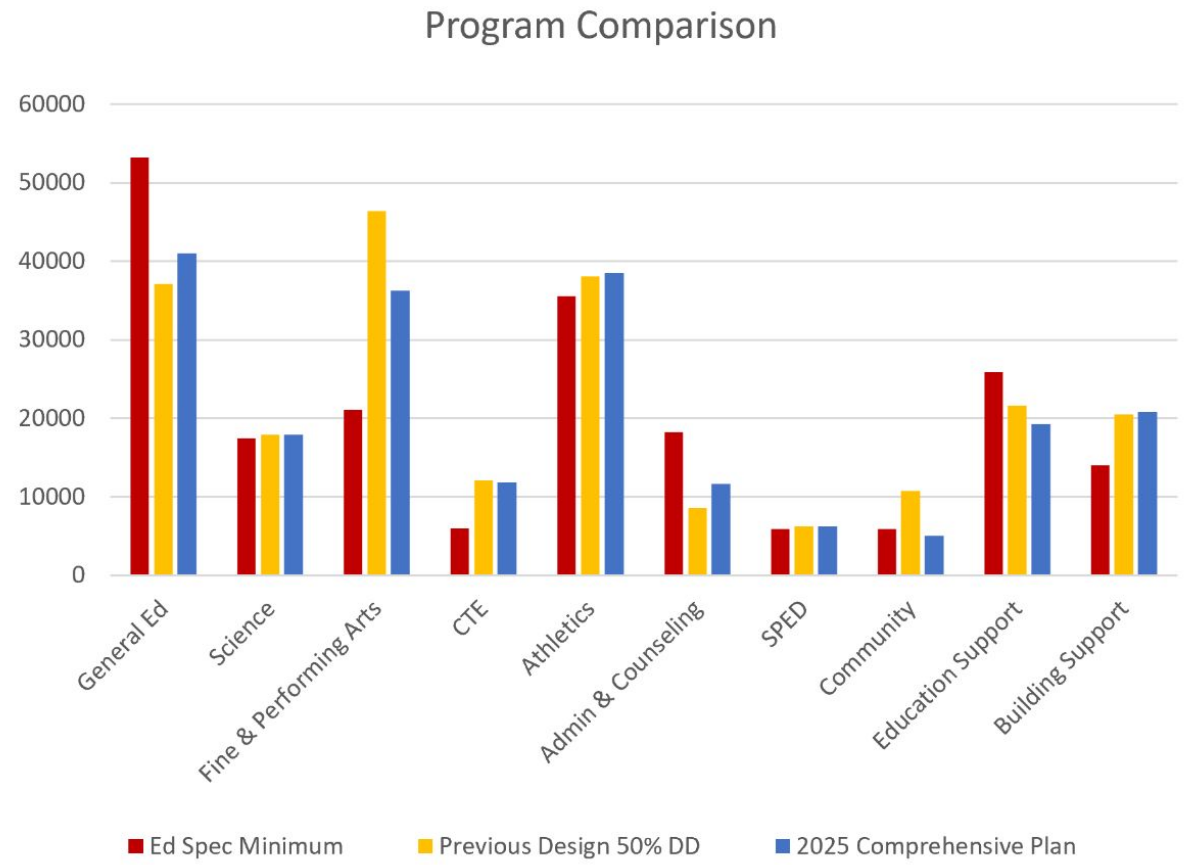

Current Design Work

Kerby Main Entry



View from Killingsworth



Athletics Entry, Crossblock, & Track



Main Gym



Commons




Bird’s Eye View



Current Project Schedule

Jefferson HS Overall Project Schedule

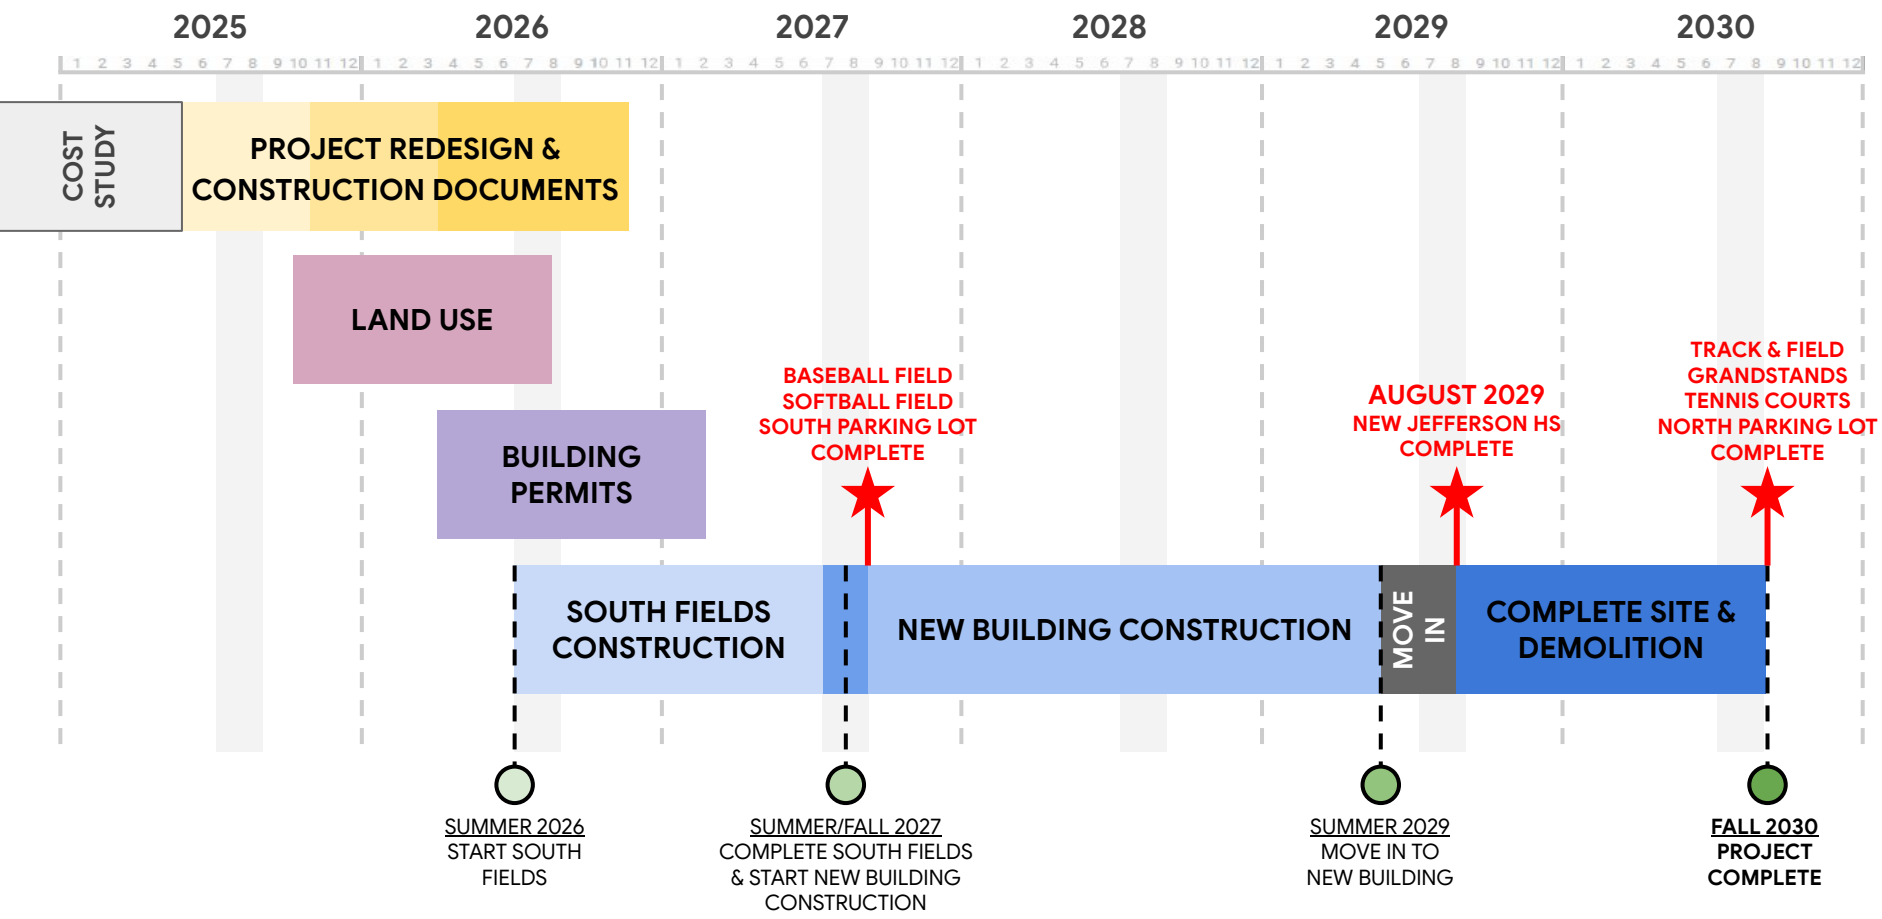

Updated Budget Summary

JHS MODERNIZATION BUDGET SUMMARY

COMPONENT	COMMENTS	2022 BOE APPROVED COMPREHENSIVE PLAN	2023 BOE APPROVED PROJECT PIVOT	2025 CURRENT REVISED COMPREHENSIVE PLAN
Hard Cost	Building & Site Work 2025: Includes actuals paid-to-date to CM/GC	$ 284,185,237	$ 407,397,113	$ 357,601,866
1.5% Green Energy Tech		$ 3,450,423	Included in Hard Cost Estimate	
Subtotal		**$ 287,635,660**	**$ 407,397,113**	**$ 357,601,866**
Owner Direct Hard Costs	Potential additional public improvements, hazardous materials abatement not included in Hard Cost 2025: Added allowance for potential additional off-site improvements	**$ 3,422,000**	**$ 1,900,000**	**$ 3,900,000**
TOTAL HARD COSTS		**$ 291,057,660**	**$ 409,297,113**	**$ 361,501,866**
Soft Costs	Approx. 12% of Hard Costs (includes design, engineering, consultant services, permitting, moving, insurance) 2025: Includes Added Redesign Costs	$ 33,338,529	$ 42,007,914	$ 50,513,864
Fixtures, Furniture & Equipment, including technology	Approx. $34 per SF	$ 8,360,250	$ 9,988,000	$ 10,500,000
Moves / Swing Space / Temp Facilities		n/a	n/a	$ 800,000
Contingency	2022: 10% of Total Costs (additional 5% CM/GC contingency included in Hard Cost Estimate) 2023: 10% minus $16,669,553 CM/GC contingency included in Hard Cost Estimate 2025: 10% of Total Costs (additional 5% CM/GC contingency included in Hard Cost Estimate)	$ 33,243,561	$ 29,459,770	$ 42,691,769
Escalation	Included in Hard & Soft Costs	Included in Hard & Soft Costs Above		
TOTAL PROJECT BUDGET		**$ 366,000,000**	**$ 490,752,797**	**$ 466,007,500**
SAVINGS FROM 2023 DESIGN				**$ (24,745,297)**

Next Steps

Next Steps

- Schematic Design (SD) Phase Approval: REVIEW PHASE
  - Document review by internal OSM staff
  - Page turn reviews by district stakeholders
  - Estimating by RLB (Design Team Estimating Consultant)
- New CM/GC Contractor - COLAS/HOFFMAN
  - Contractor Estimating based on 8/29/25 SD drawings
  - Construction Logistics/Phasing/Schedule Workshops/OACs
- Community Engagement
  - Community Information Session: October 15th
