PORTLAND
Public Schools

Facility Improvement & Oversight Committee



10/8/25

Agenda

- Center for Black Student Excellence
- Athletics update
- Ida B Well High School Budget update
- Work orders and Maintenance impact
- Seismic update



Center for Black Student Excellence

DUE DILIGENCE

ALTA Survey: **COMPLETE - NO MATERIAL ISSUES**

Phase I Environmental Study: **COMPLETE- NO MATERIAL ISSUES**

Building Assessment Report: **IN REVIEW**

Title report **- COMPLETE- NO MATERIAL ISSUE**

Eco Commons LLC review **- COMPLETE- NO MATERIAL ISSUE**

OPERATING COSTS

Building: Historical Building Operation Costs: **In Process**



Center for Black Student Excellence

Next Steps:

FIO meeting: November 3

Follow up with full analysis of:

- Building assessment report
- Building operating costs

Feasibility & Building Programming Study

- Program/Space Design
- Parking/transportation Strategy
- Operating Plan/Budget
- Property management strategy

Board Vote: December 2

Vote to determine if PPS moves forward with purchase of building



Athletics Update

- 2025 bond work aligns with high priority improvements in the PPS Long Range Facility Plan (LRFP):
  a. Athletic hubs at Marshall and Jackson include multipurpose fields and field lighting.
  b. High school improvements at GHS, RHS, and FHS include seating and grandstand work, baseball and softball fields, and field lighting.
- High priority middle school improvements include multipurpose fields, tracks, and gym spaces.



Ida B Wells Update

Update on Budget

Recent Value Engineering at the end of Schematic Design resulted in an attainable Path to Budget.

Savings are $5.6M




IBW MODERNIZATION BUDGET SUMMARY

COMPONENT	COMMENTS	2024 BOE APPROVED COMPREHENSIVE PLAN	2025 CURRENT REVISED COMPREHENSIVE PLAN
Hard Cost	Building & Site Work 2025: Includes actuals paid-to-date to CM/GC	$359,310,855	$345,000,000
1.5% Green Energy Tech		$ 5,989,663	Included above
Subtotal		$365,300,518	$345,000,000
Owner Direct Hard Costs	2025: Utilities, additional right-of-way/ public improvements	$2,200,000	$4,750,000
TOTAL HARD COSTS		**$367,500,518**	**$349,750,000**
Soft Costs	(Includes design, engineering, consultant services, permitting, insurance, etc) 2025: Includes Added Redesign Costs	$36,300,000	$45,500,000
Fixtures, Furniture & Equipment, including technology	Approx. $36 per SF	$10,000,000	$10,750,000
Moves/Swing Space/Temp Facilities		Included in soft costs	$2,500,000
Contingency	10% of Total Costs (add'l 5% CM/GC contingency included in Hard Cost Estimate)	$41,200,000	$40,850,000
Escalation	Included in Hard & Soft Costs	-	-
TOTAL PROJECT BUDGET		**$**455,000,518	**$**449,350,000
SAVINGS FROM 2024 DESIGN*	*Recent Value Engineering at end of SD phase resulted in an attainable Path to Budget within 1.5% over the hard cost of $345M, within industry standards and PPS SOPs. Full Land Use Jurisdictional Requirements unknown at this time.		$ (5,650,518)

PPS Work Orders

- Maintenance Operations
- Work Order Prioritization
- Work Order Numbers
- Way Forward

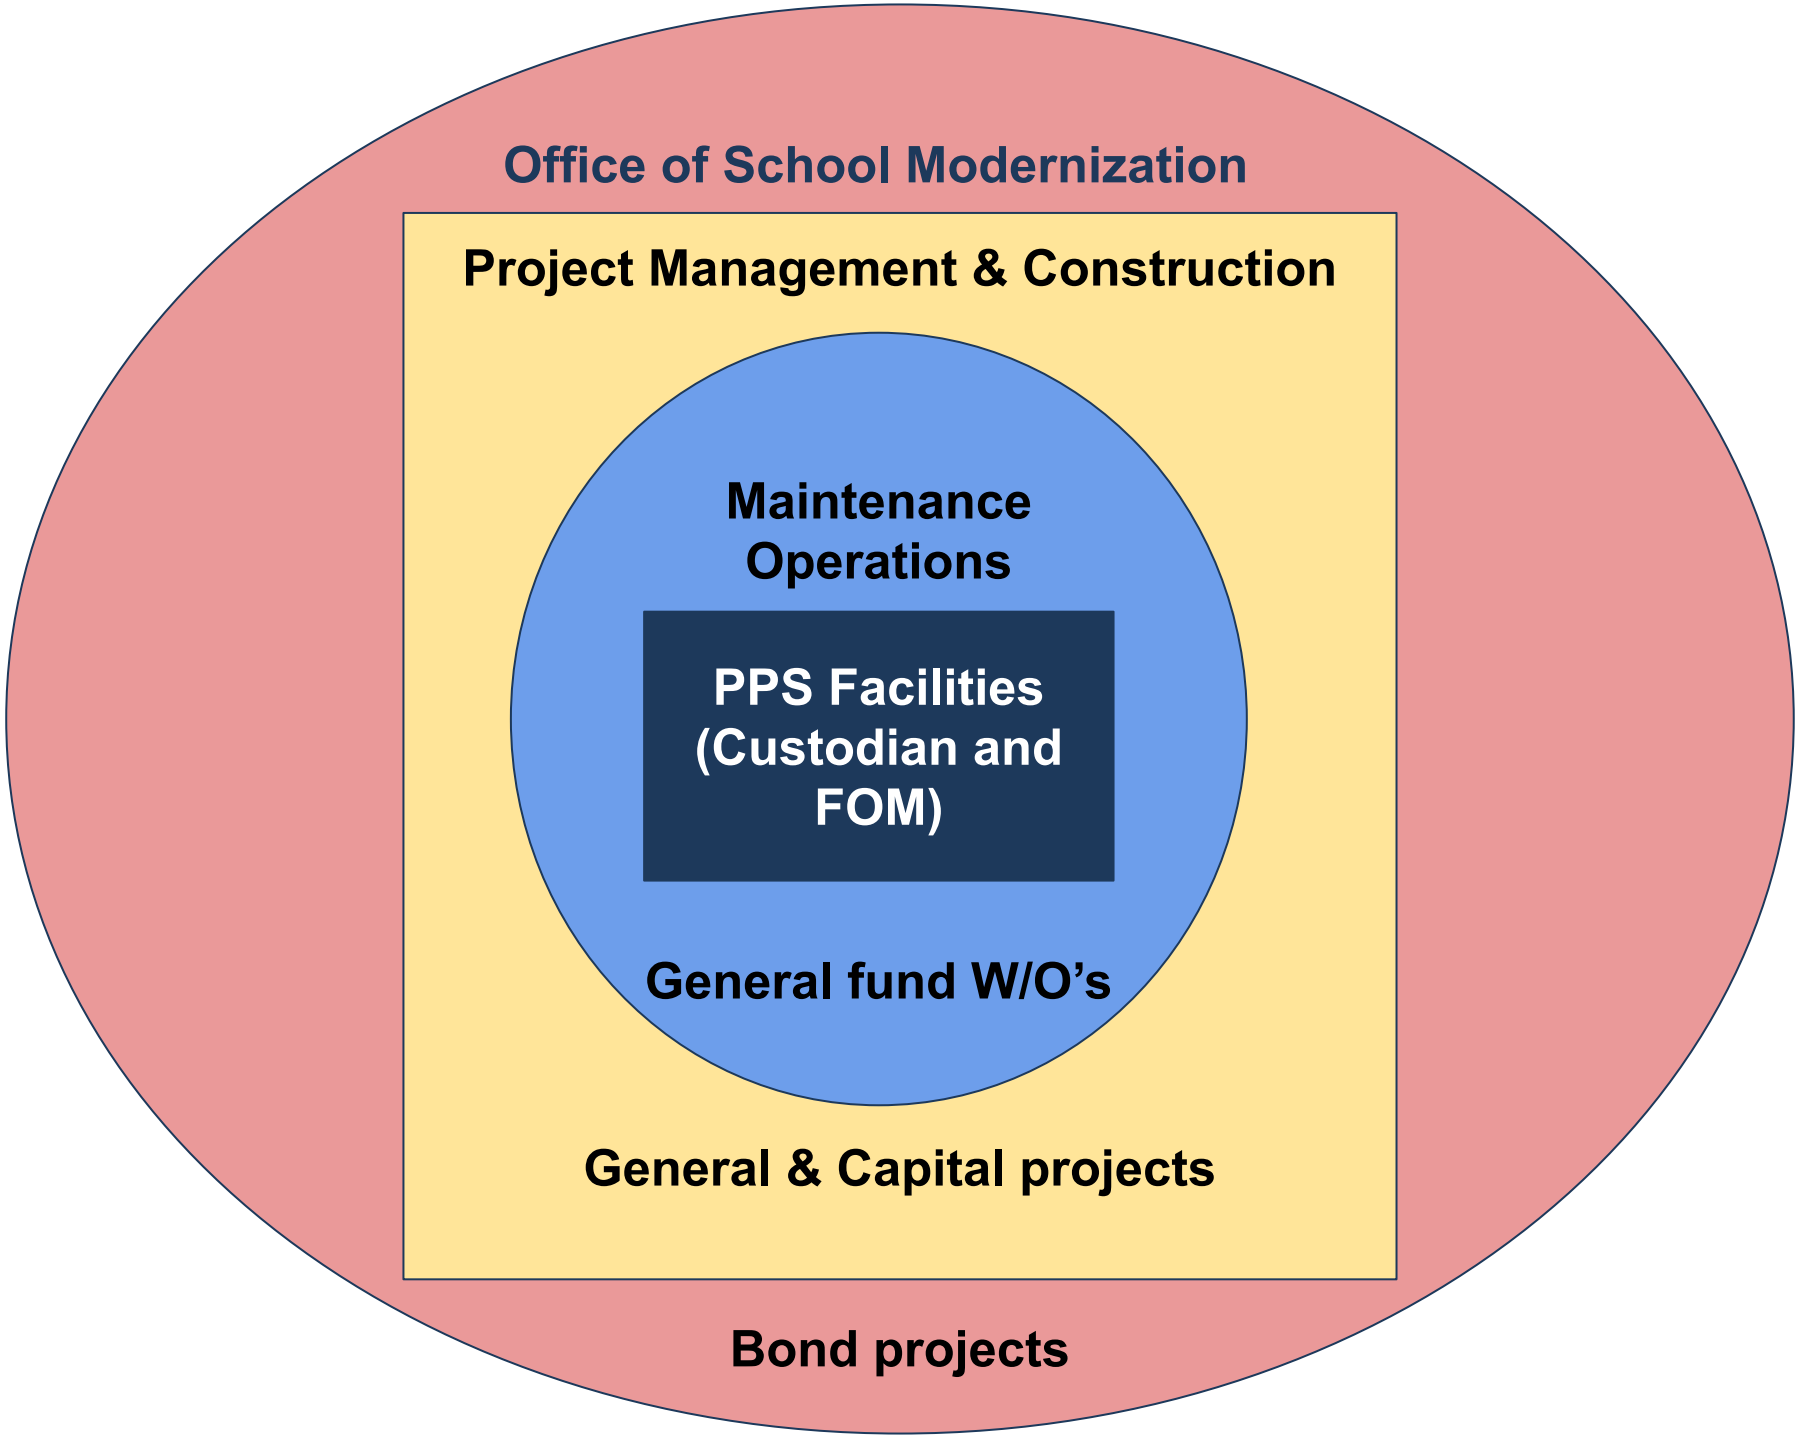


Office of School Modernization
Project Management & Construction
Maintenance Operations
PPS Facilities (Custodian and FOM)
General fund W/O's
General & Capital projects
Bond projects

Maintenance Operations Staffing


- **Technicians:** 77 technicians from multiple trades; Plumbing, HVAC, Electrical, Carpentry, Painting, Glazing, Flooring, Machinist, Sheet Metal

- **Management:** 2 technician managers and one project manager


Maintenance Impact

- 2000 Sq Ft = 5000 homes
- NOT a family of four; one adult and 25 under 18 year olds

  Eg: Four service plumbers

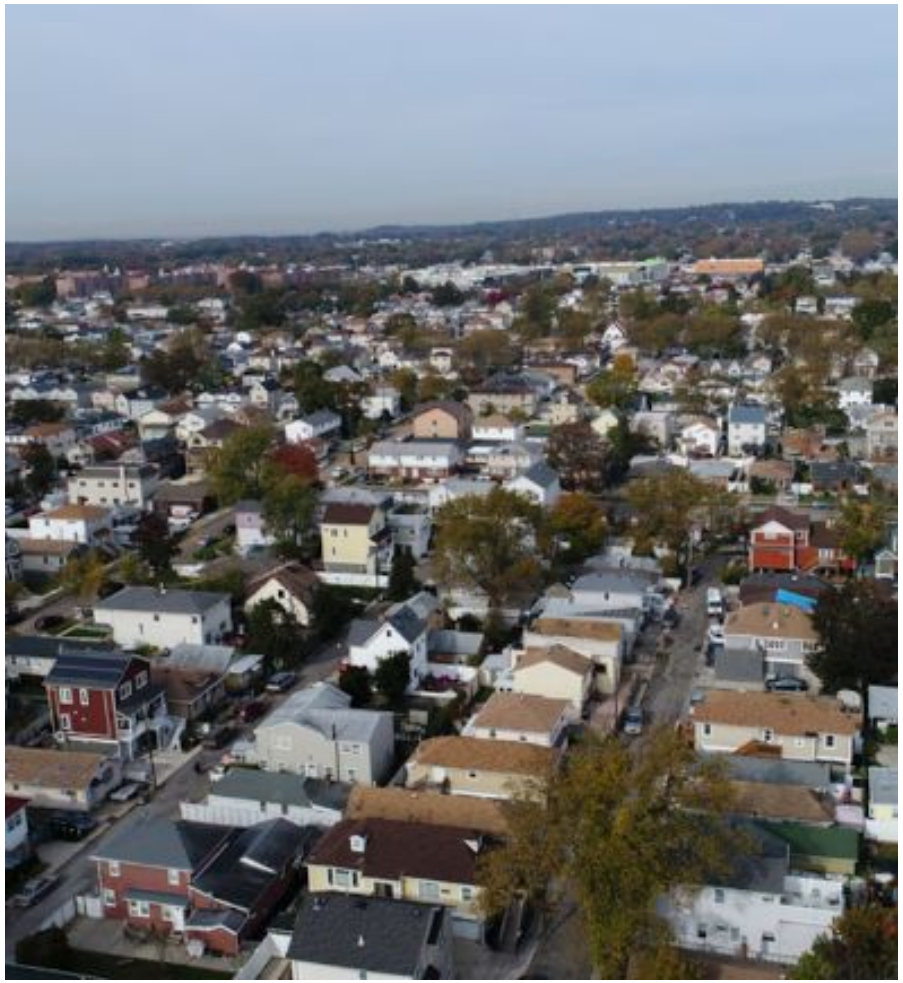

9.5 million square feet of service area

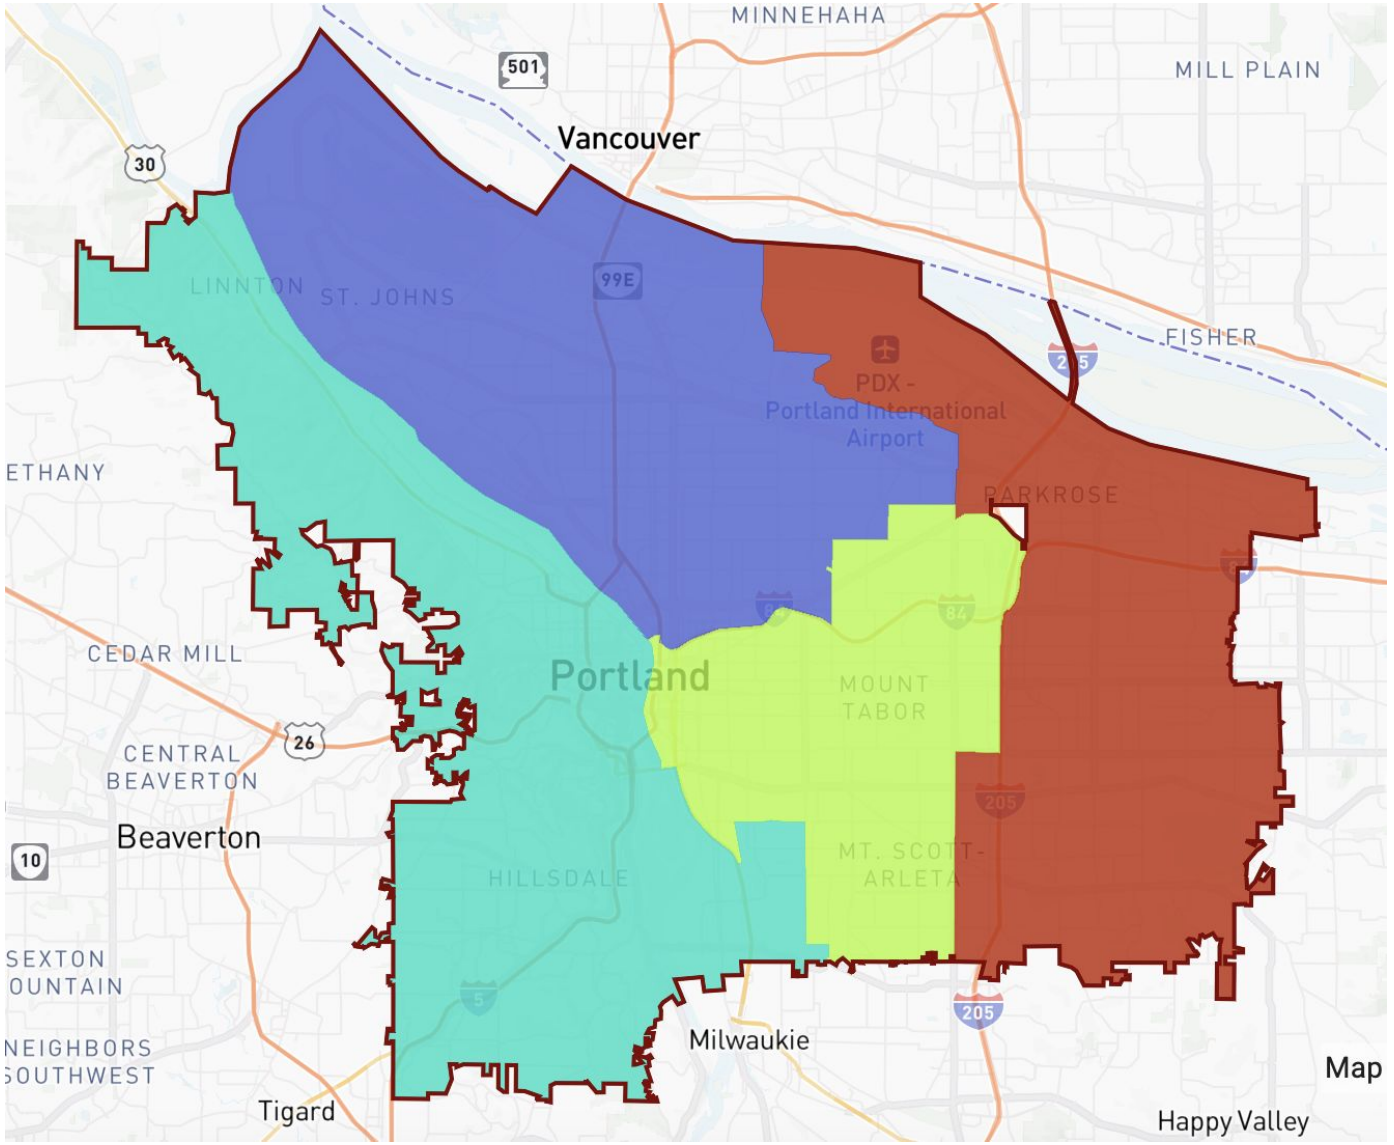

Maintenance Impact

- **Personnel:** approximately 40% below like-size school district standard operations
  - No new FTE allocations projected

- **Work Order Numbers:** Approximately 3900 active work orders
  - Includes corrective and scheduled maintenance



Maintenance Work Orders

- Mechanical & Plumbing: **1,600**
- General Repair: **1,400**
- Landscape: **520**
- Electrical: **370**



⚡ *Mechanical and General Repair together account for nearly 70% of all open requests.*

Maintenance Priority Matrix

- **Emergency** – Immediate threat to safety, health, or building operations same day after immediate triage (e.g., boiler failure in winter, major water leak).
- **High –** Impacts safety, instructional delivery, or critical services if not addressed soon and preventative maintenance.
- **Medium** – Important, but does not immediately threaten safety or instruction.
- **Low –** Cosmetic or discretionary requests; lowest impact on students/staff.

Maintenance Priority Matrix

Category		Priority	Sub Category	Assignment	Assessment	Completion	Total
				Days (Calendar)			
1	Emergency	1	Life Safety Emergencies	1	1	30	32
		2	Situational Emergencies	1	1	30	32
2	High						
		3	Safety Issues (No immediate Danger to students/personnel)	3	3	30	36
		4	Craft Support	5	5	60	70
		5	Senior Leadership Tasks	5	5	60	70
3	Medium						
		6	CSI/TSI/Title 1 Sites	60	30	90	180
		7	Specialty Tasks	60	30	90	180
		8	Craft Support	60	30	90	180
		9	All Other Tasks	60	30	90	180
4	Low			Indefinite	Indefinite	Indefinite	Indefinite

Performance Way Forward

- Optimizing employee shift schedules
  - Minimizing interruption to student learning time
- Remote Operations Center
  - Active facility monitoring and response



Seismic Updates

- Framework for Prioritization
- Seismic Scenarios revisited
- Deliverables Status



Seismic - October Actions

Establish reporting & communication framework (dashboards, community)

Finalize prioritization **formula** - Seismic, FCI (Facility Condition Index), Enrollment, TSI/CSI, Grade Level

Begin dashboard prototype & engagement sessions

*September foundation is complete. October focuses on **grants and communication**, November on **procurement and prioritization formula**. School list will not advance until leadership approval.*

Seismic - November Actions

Establish school priority based on approved formula


Secure outside grant support and prepare draft application

Launch procurement for design services

Begin dashboard prototype and community engagement sessions (FIO, Incident IQ)

Our commitment: a clear, transparent, equity-centered process that positions PPS to make informed, sustainable seismic investments.

Seismic Priority Formula Sample

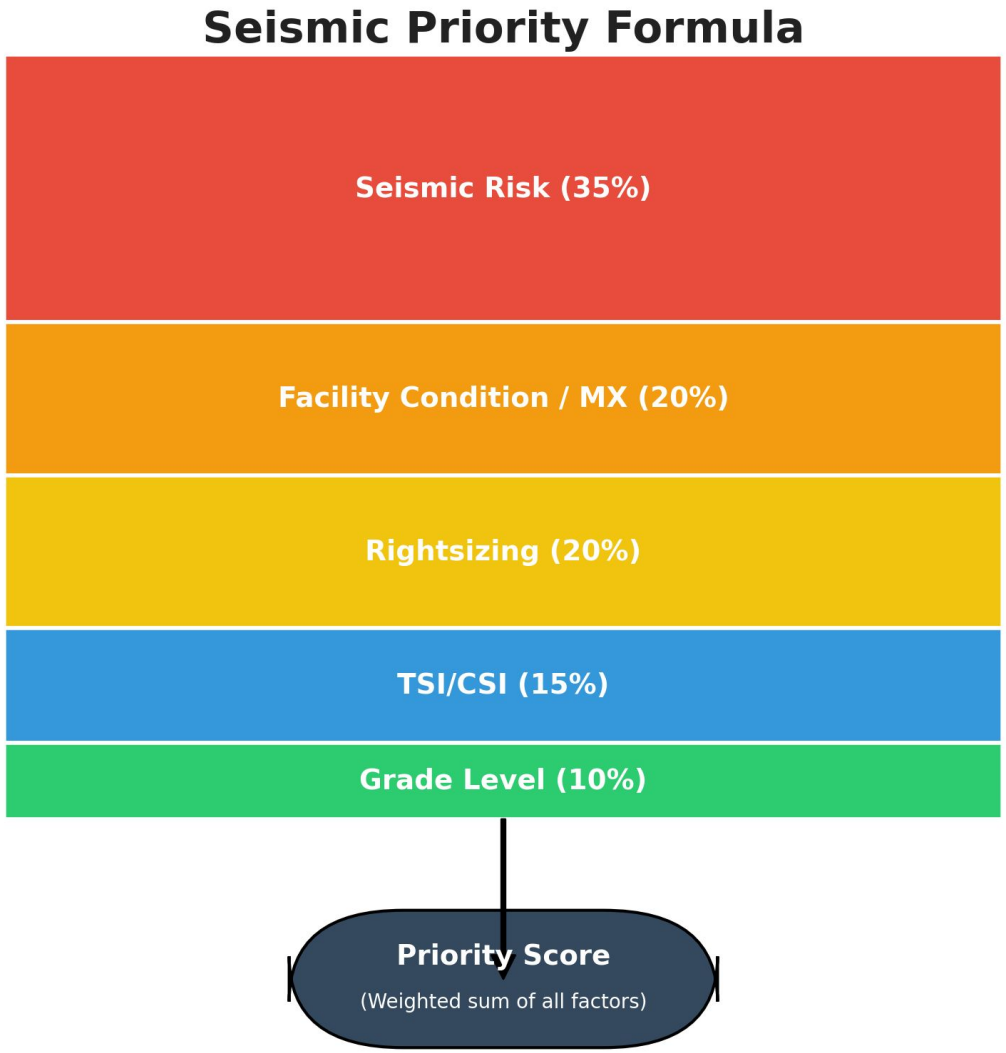

Seismic Approach

Hybrid

Some full retrofit and targeted upgrades to critical structural elements to lessen catastrophic collapse (e.g., roofs, walls, key connections).

Seismic Deliverable Status

- **Framework Complete** – A/B/C approaches defined, equity and risk filters applied.
- **Prioritization in Progress** – Schools ranked; recommendations aligned to $100M budget.
- **Technical Report Delivered** – Holmes assessments and scoring methodology complete.
- **Integration Underway** – Seismic planning linked with rightsizing, maintenance, and modernization.
- **Next Step:** Approval of prioritization list and scope for first round of projects.

* Positioned to launch first seismic retrofits by Summer 2026.

Verbal Updates

- Rightsizing
- RFP
- Wells Farmer’s Market & Fence



Questions?

