RESOLUTION No. 7187

Resolution Authorizing Amending the Jefferson High School Modernization Comprehensive Plan

RECITALS

A. The Board of Education adopted resolutions 6627 authorizing a Comprehensive Plan for the modernization of Jefferson High School.

B. The District has proposed revisions to the Jefferson High School Comprehensive Plan to, among other things, revise the size of the modernized school to approximately 300,000 square feet and to begin construction of the new building at the start of 2027, concluding in the spring of 2029. Those revisions were presented to the Facilities Improvement & Operations Committee on September 16th 2025.

RESOLUTION

1. The Board of Education authorizes a revised Jefferson High School Comprehensive Plan as detailed on Exhibit A.

Exhibit A

BORA

Jefferson High School Modernization
Revised Comprehensive Plan Executive Summary DRAFT
August 15, 2025

EXECUTIVE SUMMARY

Process & Timeline:
In December 2022, the PPS Board of Education approved the Jefferson High School Comprehensive Plan, as follows:

- Total hard costs: $291,057,660 [including construction costs, 1.5% GET, hazardous material abatement, and public ROW improvements]
- Total project cost: $366,000,000 [including soft costs, FF&E, contingencies and escalation]
- School capacity: 1,700 students +/-
- Includes spaces to support JHS unique programs, such as 1000-seat theater, dance studios, and construction CTE program
- Includes right-sizing of spaces to reflect lessons learned from other PPS modernized high schools
- Incorporates PPS' current Facility Standards
- Reflects PPS' Climate Crisis Response Policy and Resiliency Goals
- Schedule: Phase 1 building and new Track & Field complete June 2026, Renovation of the 1909 building complete Fall 2028.

In June 2023, Andersen Construction's first estimate of the project showed that a phased renovation, keeping students on site during construction, was adding over $150M to the project. Following a 3rd party VE workshop in July 2023, OSM directed the design team to design the project in a single phase in which students would swing off-site during construction.

In December 2023, the PPS Board of Education approved a change to the approach, where students would remain on campus during construction in the existing building, while a new building is constructed on the North end of the site. On April 2, 2023, the Board approved the following:

- Total hard costs: $409,297,113 [including construction costs, 1.5% GET, hazardous material abatement, and public ROW improvements]
- Total project cost: $490,752,796 [including soft costs, FF&E, contingencies and additional escalation]; the delta from the 2020 bond of $124,745,297 would be included in a new bond.
- School capacity: 1,700 students +/-
- Includes spaces to support JHS unique programs, such as 1000-seat theater, dance studios, and construction CTE program
- Includes right-sizing of spaces to reflect lessons learned from other PPS modernized high schools
- Incorporates PPS' current Facility Standards
- Reflects PPS' Climate Crisis Response Policy and Resiliency Goals
- Schedule: New building complete June 2028, Demolition of existing building and new fields complete Fall 2029.

Based on this direction, Bora delivered a Schematic Design for JHS on September 9th, 2024. This project has been estimated by Andersen Construction and RLB [a third-party estimator], and after a Value Engineering effort the project was tracking on budget and schedule as follows:

- Total hard costs: at or below the budget of$409M [including construction costs, 1.5% GET]
- School capacity: 1,700 students +/- with space to support JHS unique programs
- Schedule: building complete June 2028, and site complete June 2029

In December 2024, the JHS design team was directed to develop a series of cost reduction strategies for the JHS modernization, reducing project scope and costs associated with the 100% Schematic Design. A series of memos and meetings have informed this work:

1. "Cost Reduction Study Proposal and Deliverables Memo" issued December 9, 2024, and Appendix A, issued December 3, 2024, further clarified in the "High School Modernization Cost Reduction Study – Option Clarifications" issued on December 12, 2024;
2. Additional direction was provided in OSM in two ways: marked up comments in draft materials for CHS, JHS and IBW HS studies shared on 12/20/24, and a 10 AM phone conversation with OSM on 12/21/24 [recorded by OSM].

Bora delivered a Cost Reduction Study Phase 1 Package on December 24, 2024. The study provide (3) options framed within the parameters set by these memos and conversations, specifically that at least one option reaches a target construction budget of $270M. The information for these studies was developed as a collaboration between PPS OSM, Design Team led by Bora and PPS' CMGC, Andersen Construction. Andersen has provided schedule input and ROM pricing. Bora's third-party estimator, RLB, was provided the draft submissions on December 17, 2024, and is compared overall costs with benchmarks from projects in other school districts in the area.

In February 2025, JHS design team was directed to develop a Cost Reduction Study Phase 2 that meets the framework provided in the Board Resolution No. 7051 to Adopt a Framework to Build High-Quality High Schools in a Cost-Efficient Manner. The design team has worked collaboratively with OSM to determine the revised scope and appropriate cost reductions. As part of the Cost Reduction Study Phase 2, the third-party estimator, RLB, delivered a cost model and draft project schedule based on the Cost Reduction Study Phase 2 package reviewed by OSM and the design team. OSM presented the JHS Modernization Budget and Scope based on the Cost Reduction Study Phase 2 at the 7/22 Bond Accountability Committee [BAC] as follows:

- Total hard cost range: $356M-361M
- Total project budget range: $464M-469M
- School capacity: 1,700 students +/- with space to support JHS unique programs, including the following modifications from December 2024:
    - 295,290 GSF
    - 500-seat Theatre
    - No site buildings except a ticket booth.
    - Schedule: early baseball field complete Fall 2026, building complete June 2029, and site complete June 2030

In Spring 2025, the design was directed to re-start the Phase 2 scope of services from the beginning with a new Schematic Design [SD] Phase based on the Cost Reduction Study Phase 2 package. During SD discussions with PPS and the OSM team, the design team was directed to revise the following major scope and schedule items from the Cost Reduction Study Phase 2:

- Increase the theatre size to 720 seats by adding a 220-seat balcony to the 500-seat theatre footprint.
- Add a 360gsf field support building to include concessions and single-user restrooms
- Include the softball field as part of the early field work.

BORA

Per discussions in late July 2025, the OSM team directed the design team to further revise the Comprehensive Plan to include modifications from the 2025 SD phase. The Cost Reduction Study Phase 2 budget and schedule were modified as follows:

- Total hard cost: $357.6M
- Total project cost: $465.6M
- Schedule: early baseball & softball field complete Fall 2026, building complete June 2029, and site complete June 2030

BORA

Previous Design: The Jefferson High School modernization paused work at the completion of the 50% Design Development progress set on December 6, 2024. The basis of the Cost Reduction Study is the last reconciled cost estimate by Andersen and RLB, the 100%SD Revision 2 Estimate with a Construction Cost of $415,593,991 for a building size of 322,451 gross square feet.

Site Constraints: The JHS site is extremely constrained. At only 14.2 acres, the site is roughly 5 blocks long by 1.5 block wide. This narrow configuration means it barely has enough area to fit a track & field and a combination baseball / multipurpose field. Consequently, some cost-reduction measures are not feasible:

- *Not enough room to fully utilize tilt-up concrete construction. It will be evaluated where achievable.*
- *To meet the full 1700-student program, the structure must be 4 stories tall.*

The following matrix summarizes the revisions to the Comprehensive Plan from the 2024 100% SD design:

Revised Comprehensive Plan Comparison

	Previous Design 2024 100% SD	Revised Comprehensive Plan
Building Size (GSF)	322,451	299,044
Student Capacity	1700	1700
Teaching Stations	73	73
Deviate from Standards	No	No
Site Program		
Track & Field	New	New
Baseball	New	New
Softball	New	New
Tennis	New	New
Swing	No	No
School Opening Date	Building: Fall 2028 Track: Fall 2029	Building: Fall 2029 Track: Fall 2030
ROM cost	$409M	$357.6M

There will be no change to the following project criteria:

1. Students will remain on-site for the duration of construction. This will require at least two-phases of work.
2. Capacity will remain at 1700 students at 85% classroom utilization
3. Building on the North end of the site to maximize the new athletic fields provided.

BORA

REVISIONS TO THE COMPREHENSIVE PLAN

Revisions to the Comprehensive Plan Summary:

- The revised Comprehensive Plan proposes a compact, four-story, 299,044 GSF building on the North side of the site, accommodating 1,700 students at 85% utilization.
- Key area changes are outlined below; the most significant changes from 2024 100% SD scope are the reduction of the 1000 Seat Theater and removal of dedicated Community Partner Spaces: Indian Education and SEI Coordinator Office. Classrooms have increased in size from 920sf to 950sf.
- Softball will be added to the early fields construction scope. All other construction phasing will remain unchanged.
- There has been no change to the following:
    - Commitment to PPS Climate Policy. Maintains all-electric infrastructure.
    - Inclusion of PPS's Facility Standards.
    - Inclusion of 1.5% of the construction budget will be allocated for Green Energy Technology in accordance with Oregon State law.
    - Overall Construction Phasing: In the first phase, students will remain on site in the existing school buildings during the construction of the new school. Upon completion of the new school, students will occupy the new facility and the old school buildings will be demolished. Following demolition of the old school, a second phase of construction will complete the site work for the modernization project. To avoid the complete loss of athletic fields during construction, early fields will be permitted and constructed during the first construction phase. This work will be scheduled for completion before demolition of the existing track and field begins.
- Site Changes from the 2024 100% SD Scope
    - Remove the Teen Parent Center and majority of the all-user restrooms from the site support program. The Teen Parent Center and site accessed all-use restrooms will be located in the building.
    - The site support program has been reduced to:
        - (1) building with (2) single-user restrooms and site concessions.
        - (1) independent ticket booth at the entrance to the crossblock.
    - Site storage will be located below the grandstands only.
    - Remove improvements at the Kerby Grove.
    - Reduce site improvements at cross block connection by 15%.
- Building from the 2024 100% SD Scope
    - Reduce the GSF to 299,044, see program summary
    - Locate the Main Gym to the first floor
        - Reduces area and stairs for egress
        - Reduces structural requirements below Main Gym
    - Reduce the size of the Theatre from 1000 seats to 720 seats including a balcony.
    - Net to Gross multiplier decreased from 46% to 42% from the 100%SD Design
    - Optimize the building layout and structure for the base classroom mechanical option, see Mechanical Narrative
    - Reduce number of main entrances with event lobbies from three to two minimum
    - Avoid stacking program which requires vibration mitigation over other learning spaces, i.e. Dance Studios, Auxiliary Gym, etc.
    - Optimize solar orientation to reduce mechanical loads from a West classroom orientation

Site Program Summary:

- Demolition and abatement of the existing school.

- The 14.02-acre site includes: a new grandstand with weatherproof storage below, track and football field, combined baseball field and practice soccer field, softball field and (4) tennis courts
- The site will include a City of Portland required public cross block connection south of the new building, PBOT required ROW and sidewalk improvements, and fencing around the main Jefferson HS site and the parcel south of Alberta.
- The parking scope will include:
    - Updates to the existing Kerby parking lot to conform to existing zoning. No other upgrades are assumed in this area.
    - New parking lot within the parcel south of Alberta.
- Reduce site improvements at cross block connection by 15%.
- The site support program has been reduced to:
    - (1) building with (2) single-user restrooms and site concessions.
    - (1) independent ticket booth at the entrance to the crossblock. No site improvements at the Kerby Grove

Building Program Summary:

- Accommodates 1,700 students at 85% Utilization [requires some sharing of classrooms, shared teacher planning spaces are provided]
- Program adjusted from the 2024 100% SD scope including:
    - Theatre reduced to a 720-seat with balcony from a 1000-seat with balcony
        - Theatre maintains features such as the sound and light locks, orchestra pit, fly-tower and grid iron
    - Highlighted program removed:
        - Dedicated Community Partner Spaces: SEI Coordinator Offices and Indian Education
        - (2) Team Rooms
        - Student Mediation
        - Student Government Office
        - Library Classroom
        - School Archive Room
    - Reduced Gym Size
    - Reduced locker count from 1700 to 1000
    - Reduced Dance Studios by 700sf each
    - Reduced Choir Room by 200sf
    - Modifies the following, with agreement from OSM:
        - Target Net to Gross multiplier of 42%
        - Standard classroom size reduced from 980 SF to 950 SF
        - Updates single user restrooms to 64 SF to meet current code requirements

BORA

Area Program Summary [compare with page 49 of 2017 Education Specification [Page 55 of PDF]
https://www.pps.net/cms/lib/OR01913224/Centricity/Domain/58/PPS%20Comp%20HS%20Ed%20Specs%20September%2017.pdf

2025 SD Jefferson High School Program - 1700 Students at 85% Utilization

SUMMARY					
Recommended / Preferred / Optional	Recommended		Pref / Opp		950
AREA	Quant.	SF Room	Quant.	SF Room	Total
COMPREHENSIVE HIGH SCHOOL PROGRAM - TEACHING STATIONS					
General Education (Gen-Ed) Classrooms	39				41,050
Science Labs	11				17,880
Fine & Performing Arts (Drama, Theater)	7				36,230
Career Preparation/CTE [3]	6				11,750
Athletics (incudes area for P.E. instruction)	4				38,510
Education Support [4]					57,960
SPED	5				
ELL	1				
Sub-Total Recommended Teaching Stations	***73***				***203,380***
Community Partners [5]					660
Wrap-Around Service Providers [5]	0				4,353
Sub-Total					***5,013***
SUB-TOTAL COMPREHENSIVE HIGH SCHOOL REQUIRED AREA					***208,393***
Net to Gross Ratio of 43.5% [6]					***90,651***
TOTAL COMPREHENSIVE HIGH SCHOOL REQUIRED					***299,044***

BORA

Schedule Summary:

The design schedule for the revised Comprehensive Plan assumes the following:

- 6-month Schematic Design Phase with a 1-month GC Coordination phase, 5-month Design Development Phase, 8-month Construction Documents Phase.
- Students remain in the existing building during construction of the new building, resulting in a "phased" construction process.
- Early baseball and softball field delivery is provided to support on-site athletics during construction. This results in three rounds of permit review.
- Most of the complexities stemming from a phased project, site utility scope, and a compact building will remain the same as the current project scope. The scope of site improvements will also remain nearly the same.
- The schedule assumes the following:
    - CMGC pricing at 100% Schematic Design
    - 26-month Construction duration for the new building to allow for move in Fall 2029

Attachments:

Exhibit 1: REVISED DESIGN AND CONSTRUCTION SCHEDULE
Exhibit 2: 2025 SD SPACE PROGRAM
Exhibit 3: 2025 SD REVISED SITE PLAN
Exhibit 4: 2025 SD PROGRAM FLOOR PLANS
Exhibit 5: REVISED UPDATED BUILDING MASSING
Exhibit 6: COST REDUCTION STRUCTURAL NARRATIVE
Exhibit 7: COST REDUCTION MECHANICAL NARRATIVE
Exhibit 8: COST REDUCTION STUDY LAND USE NARRATIVE
Exhibit 9: REVISED COMPREHENSIVE PLAN COST MODEL
Exhibit 10: DRAFT CONSTRUCTION SCHEDULE FROM RLB


PRELIMINARY DESIGN SCHEDULE

JHS

Updated 3/21/25

Exhibit A

EXHIBIT 1

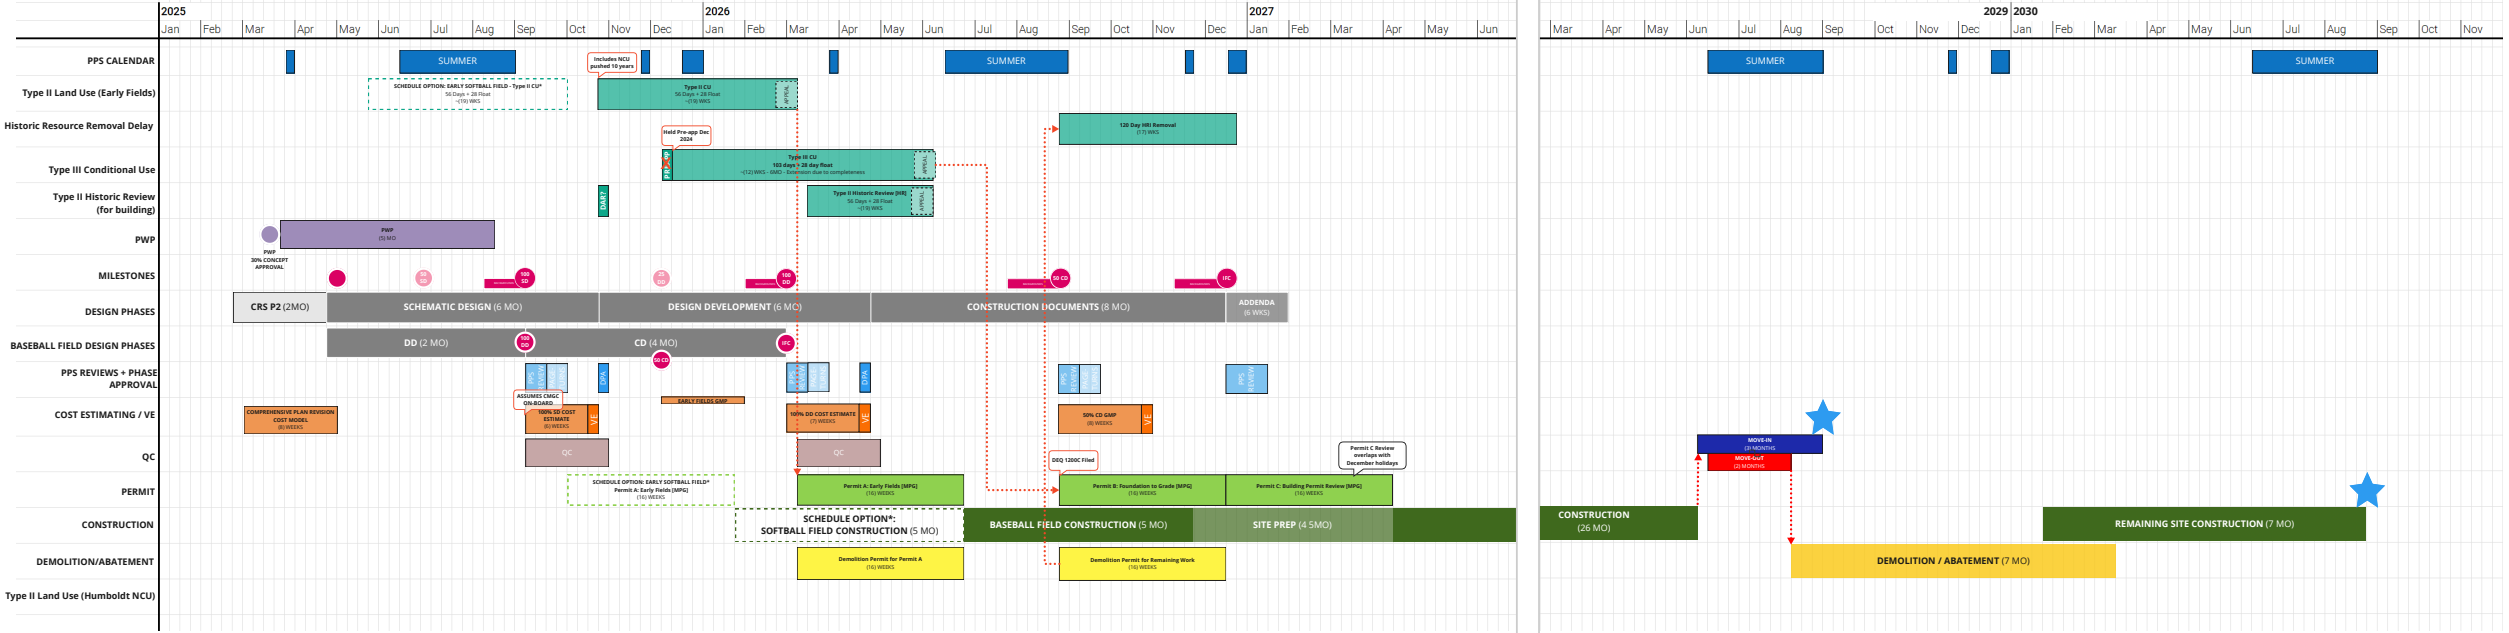

*Early Softball Field phase is being reviewed with OSM. This is not included in project scope at this time

Exhibit A

EXHIBIT 2
COST REDUCTION STUDY SPACE PROGRAM

2025 SD Jefferson High School Program - 1700 Students at 85% Utilization

SUMMARY

Recommended / Preferred / Optional	Recommended		Pref / Opp		950
AREA	Quant.	SF Room	Quant.	SF Room	Total
COMPREHENSIVE HIGH SCHOOL PROGRAM - TEACHING STATIONS					
General Education (Gen-Ed) Classrooms	39				41,050
Science Labs	11				17,880
Fine & Performing Arts (Drama, Theater)	7				36,230
Career Preparation/CTE [3]	6				11,750
Athletics (incudes area for P.E. instruction)	4				38,510
Education Support [4]					57,960
SPED	5				
ELL	1				
Sub-Total Recommended Teaching Stations	***73***				***203,380***
Community Partners [5]					660
Wrap-Around Service Providers [5]	0				4,353
Sub-Total					***5,013***
SUB-TOTAL COMPREHENSIVE HIGH SCHOOL REQUIRED AREA					***208,393***
Net to Gross Ratio of 43.5% [6]					***90,651***
TOTAL COMPREHENSIVE HIGH SCHOOL REQUIRED					***299,044***

Notes:

[1] *Area program for 1,700 student enrollment. Required program refers to the education program needed to meet graduation requirements. The area program*
[1] *Based on 980 SF/General education classroom*
[2] *Areas identified in Area Program are more readily achieved in new construction; it is expected the area of rooms and spaces in existing buildings will vary*
[3] *Each Comprehensive High School will contain a minimum of 6,000 SF for career preparation/CTE/Maker Space*
[4] *Includes Optional Teacher planning/collaboration areas*
[5] *Assumptions based upon current average area of partners/providers in high schools*
[5] *Gross areas includes walls, corridor, circulation*
[6] *Bold & Italics text in the quantity column identifies teaching stations*
[6] *Gross area includes walls, corridors and circulation areas; 36% net to gross for new construction; ratio for modernization projects will vary depending on*

PPS Comprehensive High School(s) Area Program

Recommended / Preferred / Optional	Recommended		Pref / Opp		
AREA	Quant.	SF Room	Quant.	SF Room	Total
CORE PROGRAM [7]					
Career Preparation | CTE [8]					
Classrooms	TBD per site				0
CTE Specialized Classrooms					
Art Room (Screenprinting CTE)	***1***	1,200			1,200
Darkroom (Screenprinting CTE)	1	400			400
Digital Media (Digital Photography CTE) (Computer Lab)	***1***	1,100			1,100
Product Design (CTE)	***1***	1,500			1,500
IT Cybersecurity (CTE) (Computer Lab)	***1***	1,100			1,100
Business & Marketing (CTE)	***1***	950			950
Recording Suite	1	600			600
Shop (Construction CTE)	***1***	3,700			3,700

Exhibit A

Culinary Arts				
Robotics				
Maker Space	1	1,200		1,200
Sub-Total Career Prep | CTE	***6***			***11,750***
General Education Classrooms - Core Program Recommendations [9,10,11,12]				
English	***11***	950		10,450
Math	***8***	950		7,600
Social Studies	***8***	950		7,600
Health	***2***	950		1,900
World Language	***6***	950		5,700
Electives [13]	***4***	950		3,800
Sub-Total Gen Ed Classrooms	***39***			***37,050***
Specialized Classrooms - Core Program Recommendations				
Science Lab	***10***	1,500		15,000
Health Sciences / Biotech Lab (CTE)	***1***	1,500		1,500
Chemical Storage	1	180		180
Prep Rooms	6	200		1,200
Electives	0	950		0
Sub-Total Specialized Classrooms	***11***			***17,880***
Smaller Instructional Spaces [14]			4	500
Flexible Learning Areas [14]			4	500
Sub-Total Preferred				
Sub-Total Optional				
Sub-Total Optional				4,000
Sub-Total Recommended Classrooms				***66,680***
SUB-TOTAL RECOMMENDED: CORE PROGRAM WITHOUT FLEXIBLE LEARNING + SMALLER INSTRUCTIONAL				***70,680***

Notes:

[7] *Bold italics text in quantity column indicates teaching station*

[8] *See "Career Preparation Spaces" and "STE(A)M" for a list of Career Preparation | CTE | STE(A)M spaces. Space devoted to classrooms and/or labs for*

[9] *See Education support for computer labs, SPED Learning Resource Centers, and ELL classrooms. Programmatic needs for ELL and SPED Resource*

[10] *Classrooms greater than 1,000 SF require two exits*

[11] *Advanced classes held in regular classrooms*

[12] *Assumes general education classrooms could be used all periods. See classroom utilization in Program Development above.*

[13] *"Electives" include core and non-core program subjects; some electives may require specialized classroom space which will make them unavailable for*

[14] *Smaller Instructional Spaces and Flexible Learning Areas as defined in room information sheet are optional. HOWEVER, the general requirements,*

PPS Comprehensive High School(s) Area Program

Recommended / Preferred / Optional	Recommended		Pref / Opp		
AREA	Quant.	SF Room	Quant.	SF Room	Total
FINE & PERFORMING ARTS					
Fine & Visual Arts					

Exhibit A

	Art Room (2D)	***1***	1,200	1	1,700	1,200
	Art Room (3D)	***1***	1,500	1	1,700	1,500
	Kiln Room	1	200			200
	Supply /Storage	1	280			280
	Art Office(s)	0	120			0
	Sub-Total Fine & Visual Arts					***3,180***
Band/Orchestra [24, 27]						
	Band Room	***1***	2,200	1	2,400	2,400
	Large Instrument Storage Room	1	250			250
	Uniform & Robe Storage [shared]	1	300			300
	Music Library [shared]	1	100			100
	Small Equipment Storage	1	200			200
	Large Practice Rooms/Music Lab	1	300	2	300	600
	Small Practice Rooms	2	100	3	100	300
	Band Office [26]	1	120			120
	Sub-Total Band/Orchestra					***4,270***
Choir [24,27]						
	Choir Room	*1*		1	1,500	1,500
	Choir Office [26]			1	120	120
	Equipment & Robe Storage			0	200	0
	Sub-Total Choir					***1,620***
	Sub-Total Preferred				6,700	
	Sub-Total Optional				1,700	
	SUB-TOTAL RECOMMENDED FINE & PERFORMING ARTS Fine & Visual Arts					***9,070***

Notes:

#REF! *Separate band and orchestra spaces are preferred. If installed as a single space, it should be able to accommodate band, orchestra, and choir functions (if*

#REF! *Single music library to serve any combination of band/orchestra/choir room(s)*

#REF! *Single office space to serve any combination of band/orchestra/choir rooms*

#REF! *If separate choir room is not built, space for choir will be shared with band/orchestra*

PPS Comprehensive High School(s) Area Program

Recommended / Preferred / Optional	Recommended		Pref / Opp		
AREA	Quant.	SF Room	Quant.	SF Room	Total
FINE & PERFORMING ARTS					
Theater/Dance [28]					
Theater (500 seat)	1	5,000	1	6,000	6,000
Theater Balcony (~220 seats)	1	2,200			2,200
Orchestra Pit	1	500			500
Stage	1	3,500			3,500
Drama Classroom/Black Box	***1***	1,600	1	2,600	1,600
Dance Studio	***2***	2,000			4,000
Dance Studio Storage	2	200			400
Dance Costume Storage	1	*1,500*			1,500
Dance Prop Storage	1	*500*			500
Dance Sewing & Costume Design	1	*500*			500
Dance Dye Station	1	*100*			100
Dance Tap Floor Storage	1	*150*			150
Dance Office / Conference	1	*120*			120
Arts Event Lobby (Multi-Purpose Production Area) [29]	NA		1	1,500	1,500
Laundry	1	250			250
Control Room	1	200			200
Sound Booth	1	100			100
Office	1	120			120
Box Office/Tickets [29]	1	100			100
Concession Stand [30]	1	100	1	200	100
Scene Shop	1	1,500			1,500

Exhibit A

Equipment Storage	1	120			120
Lighting Storage	1	100			100
Theater Costume Storage	1	400			400
Make-up Room	1	500			500
All User Dressing	1	900			900
All User Toilet	2	40			80
All User Toilet / Shower	2	60			120
Green Room			1	400	
Sub-Total Preferred				8,800	
Sub-Total Optional				1,900	
SUB-TOTAL RECOMMENDED FINE & PERFORMING ARTS Theater/Dance					***27,160***
Notes:					***36,230***

#REF! *Dance accommodated in Mat/Wrestling/Dance room. See Physical Education/Athletics.*

#REF! *If built, Multi-Purpose Production Area to include or be adjacent to shop, provide storage for equipment, lighting, costumes, make-up room, boy's and girl's*

#REF! *Box office and concession stand to be located with other public venues when possible.*

PPS Comprehensive High School(s) Area Program

Recommended / Preferred / Optional	Recommended		Pref / Opp		
AREA	Quant.	SF Room	Quant.	SF Room	Total
PHYSICAL EDUCATION/ATHLETICS					
Athletics Events Lobby	1	1,400			1,400
Gym (large; two teaching stations) [31]	***1***	15,080	1	14,676	15,080
Mat/Wrestling/Dance [32]	***1***	3,000	1	3,500	3,000
Mat/Wrestling/Dance Storage	1	300			300
Weight Room/Aerobics	***1***	2,500	1	3,000	2,500
Boy's PE Coaches Office	1	150			150
Girl's PE Coaches Office	1	150			150
Boy's Locker Room/Shower [33]	1	1,600			1,600
Girl's Locker Room/Shower [33]	1	1,600			1,600
Multi-purpose Toilet/Shower	3	150			450
PE Storage	2	200			400
Training Room	1	580			580
School Team Room (Large)	1	600	1	800	600
School Team Room (Small)	2	300	1	800	600
Athletic Storage - Large	1	1,000			1,000
Athletic Storage - Small	1	500			500
Ticketing / Concessions [34]	1	100	1	200	200
Laundry Room	1	200			200
Uniform/Equipment Storage	1	1,000			1,000
Gym (auxiliary - practice)	***1***	5,700	1	7,500	5,700
Auxiliary gym bleachers	1	1,000			1,000
Auxiliary gym storage	1	500			500

Exhibit A

Field Equipment Storage [35]	0	1,000			0
Sub-Total Preferred				**28,876**	
Sub-Total Optional				**800**	
SUB-TOTAL REQUIRED PHYSICAL EDUCATION/ATHLETICS					***38,510***

Notes:

#REF! *Elevated running track is optional*

#REF! *Optional size should be used with two mats; storage for dance included in area*

#REF! *Locker rooms to use stacked baskets not individual lockers*

#REF! *Concession area to be combined with and in proximity to other public venues*

#REF! *Field Equipment Storage to be located outside of building. See "Site Requirements" for requirements related to outdoor athletic/recreational facilities*

[24] Auxiliary gym is optional at size noted. Preferred size is 7,500 SF

PPS Comprehensive High School(s) Area Program

Recommended / Preferred / Optional	Recommended		Pref / Opp		
AREA	Quant.	SF Room	Quant.	SF Room	Total
EDUCATION SUPPORT					
Administration					
Reception/Lobby	1	400			400
Waiting Areas	1	100			100
Principal's Office	1	200			200
Principal's Secretary	1	80			80
Vice Principal's Office	2	150			300
Vice Principal's Secretary	2	80			160
Dean of Students	1	120			120
Teacher Planning/Collaboration Area			5	950	0
Attendance	1	120			120
Bookkeeper	1	120			120
Campus Monitor Office	1	200			200
Resource Officers [37]	1	100			100
Camera Monitors [37]	0	100			0
Restrooms	2	64			128
Records Storage	1	50			50
Office Storage	1	125			125
Business Manager	1	120			120
Health Office	1	220			220
Sick Room	1	150	2	150	150
Sick Toilet	1	100			100
Student Support/Mediation Office	0	700			0
Student Support/Mediation Support	0	300			0
Staff Workroom/Mail/Delivery Process Center	1	300			300
Staff Break Room	0	400			0
Conference Rooms	2	150			300
Parent Volunteers/Family Resource/PTA/Boosters/Alumni Room	1	500			500
Sub-Total Optional				5,050	
Sub-Total Administration					***3,893***
Sub-Total ADMINISTRATION without Teacher Planning/Collaboration Areas [36]					***8,643***
Counseling/Career					
Counseling Offices	5	120			600
Counseling Secretary/Waiting	1	400			400
Drug/Alcohol Counselor Office	1	125			125
Conference Room (large)	1	240			240
Conference Room (medium)	1	150			150
Career Center	1	700	1	980	700
Career Center Office	1	120			120
Career Counselor	1	100			100
Secure Records Storage	1	80			80

Exhibit A

	Restroom	2	64		128
	Sub-Total Counseling/Career				***2,643***

Notes:

#REF! *Teacher planning/collaboration areas as defined in room information sheet are optional. HOWEVER, the general requirements, functions, location, and*

[37] *Resource officer and campus monitor to be in separate rooms; camera monitors to be located in main office*

PPS Comprehensive High School(s) Area Program

Recommended / Preferred / Optional	Recommended		Pref / Opp		
AREA	Quant.	SF Room	Quant.	SF Room	Total
EDUCATION SUPPORT					
Student Activities					
Athletic Director & Staff	1	270			270
AD Support Staff	0	120			0
Sub-Total Student Activities					***270***
Technology Access [38]					
Computer Lab (dedicated)	***0***	1,100			0
Computer Lab (non-specialized)	***0***	1,100			0
Computer Cart Storage	0	250			0
Sub-Total Student Testing					**0**
Special Education (SPED)					
Sensory Support Room (active)	1	350			350
Sensory Support Room (quiet)	1	150			150
Learning Resource Center	***3***	950			2,850
Intensive Skills Classes [39]					
Low Intensity Classroom (includes kitchen)	***2***	950			1,900
Storage	1	100			100
Reception	0	100			0
Conference	0	120			0
Office [SPED & QMHP]	2	100			200
Special Needs Toilet	1	200			200
Itinerants					
Speech Pathologist offices	2	120			240
Psychologist Offices	2	120			240
Sub-Total SPED					***6,230***
Emerging Language Learning (ELL)					
Emergent Bi-Lingual Classroom [40]	***1***	950			950
Sub-Total ELL					
Student Center					
Student Center/Commons: One lunch @ 600 students	1	7,800			7,800
Main Servery	1	1,400	1	1,800	1,400
Demo Kitchen	1	500			500
Food Prep/Kitchen	1	1,500			1,500
Dish Washing	1	200			200
Dry Storage/Cart Storage	1	500			500
Cooler	1	200			200
Freezer	1	200			200
Office	1	120			120
Staff Lockers/Dressing Rooms	1	150			150
Table Storage	1	400			400
Student Store	1	300			300
Sub-Total Student Center				1,800	***13,270***

Notes:

Exhibit A

[38] *Dedicated computer labs support specific programs/ curriculum within each school. Non-specialized computer labs provide school wide technology access*

[39] *Number of Life Skills classrooms dependent on number of students in each school needing life skills and/or medical support*

[40] *Assumes more ELL instruction in classrooms (push-in pedagogy)*

PPS Comprehensive High School(s) Area Program

Recommended / Preferred / Optional	Recommended		Pref / Opp		
AREA	Quant.	SF Room	Quant.	SF Room	Total
EDUCATION SUPPORT					
Media Center/Library [41]					
Library	1	3,200	1	4,500	3,200
Office	1	120			120
Workroom	1	200			200
Text Storage	1	400			400
Collaboration Space	1	400			400
Multi-use Rooms	3	150			450
IT Repair/Tech Coordinator	1	300			300
Library Classroom	0	0	1	950	0
Sub-Total Media Center				950	***5,070***
Student Space					
Student Government Room/Office [42]	0	200			0
Sub-Total Student Space					***0***
Custodial					
Custodial Office	1	350			350
Custodial Restroom / Shower	1	150			150
Freight / Receiving	1	550			550
Custodial Laundry	1	150			150
Custodial Rooms	10	150			1,500
Building Storage	1	1,000			1,000
Building Furniture Storage	1	500			500
Material Storage	1	500			500
Flammable Storage	1	100			100
Sub-Total Custodial					***4,800***

Notes:

[41] *Size of media center presumes renovation of existing larger space (auditorium in older structures). Optional space size is for new construction. Preference is*

[42] *Student government areas should be located near Counseling/Career Center*

PPS Comprehensive High School(s) Area Program

Recommended / Preferred / Optional	Recommended		Pref / Opp		
AREA	Quant.	SF Room	Quant.	SF Room	Total
EDUCATION SUPPORT					
Miscellaneous					
Lobby	1	1,500			1,500
Student Lockers [43]	500	1			500
Student Toilets	10	480			4,800
Gender Neutral Toilet [44]	1	60	1	64	64
Gender Neutral Shower	1	100			100
Boiler Room [Main Mech Room]	1	4,000			4,000
MDF	1	180			180
IDF	11	100			1,100
Main Electrical Room	1	1,000			1,000
Emergency Electrical Room	1	300			300
Sub Electrical Room	10	100			1,000
Restroom (teacher planning/collaboration areas)	10	70			700

Exhibit A

Riser Room	1	250			250
Water Entry	1	250			250
Satellite Water	1	100			100
Elevator Room	3	80			240
Mechanical Fan Rooms [45]			1	2,000	0
Corridors [46]	Variable				
Sub-Total Miscellaneous					***16,084***
Sub-Total Preferred Educational Support				**1,864**	
Sub-Total Optional Educational Support				**3,450**	
SUB-TOTAL RECOMMENDED EDUCATIONAL SUPPORT					***57,960***

Notes:

[43] *Half size, double-stacked lockers are at the discretion of each school administration*

[44] *Provide at least one gender neutral restroom on each floor and near gym facilities. Also ensure at least one gender neutral and one accessible restroom are*

[45] *Preference is to locate mechanical fan rooms within building; otherwise mechanical fans should be located on roof*

[46] *See Corridor Characteristics*


PPS Comprehensive High School(s) Area Program

Recommended / Preferred / Optional	Recommended		Pref / Opp		
AREA	Quant.	SF Room	Quant.	SF Room	Total
PARTNER & COMMUNITY USES [47]					
Partner Program Office	0		1	150	
Pantry / Partner Storage	2	80	1	200	160
Clothing/Food Closet	1	500	1	2,000	500
After School Instruction [48]			4	500	
Sub-Total Preferred				**2,000**	
Sub-Total Optional Educational Support				**850**	
SUB-TOTAL COMMUNITY & PARTNER USES					**660**
WRAP AROUND SERVICE PROVIDERS [48]					
Health Clinic					
Reception	1	125			125
Waiting	1	350			350
Office					0
Office, Service Provider [shared]	2	160			320
Conference/Break	1	180			180
Lab	1	160			160
Restroom	1	80			80
Exam Room	2	110			220
Exam Room, accessbile/bariatric	1	130			130
Hall	1	180			180
Sub-Total Health Clinic					**1,745**
Teen Parent Services					
Infant Room [49]	1	250	1	50	250
Breastfeeding Room			1	64	64
Toddler Room	1	300			300
Crawler Room	1	300			300
Toilet	1	64			64
Toddler toilet room	1	90			90
Changing Area	1	50			50
Nap Area	1	100			100
Storage/Kitchen	1	300			300
Stroller Storage	1	100			100
Office	1	150			150
Sub-Total Teen Parent Services					**1,768**
Office Space Social Service Providers (Includes SUN, STEP UP and ESL)	7	120	5	200	840
Classroom(s)	***0***	950			0
SUB-TOTAL WRAP AROUND SERVICE PROVIDERS					***4,353***

Exhibit A

EXHIBIT 3

Final Condition Site Plan

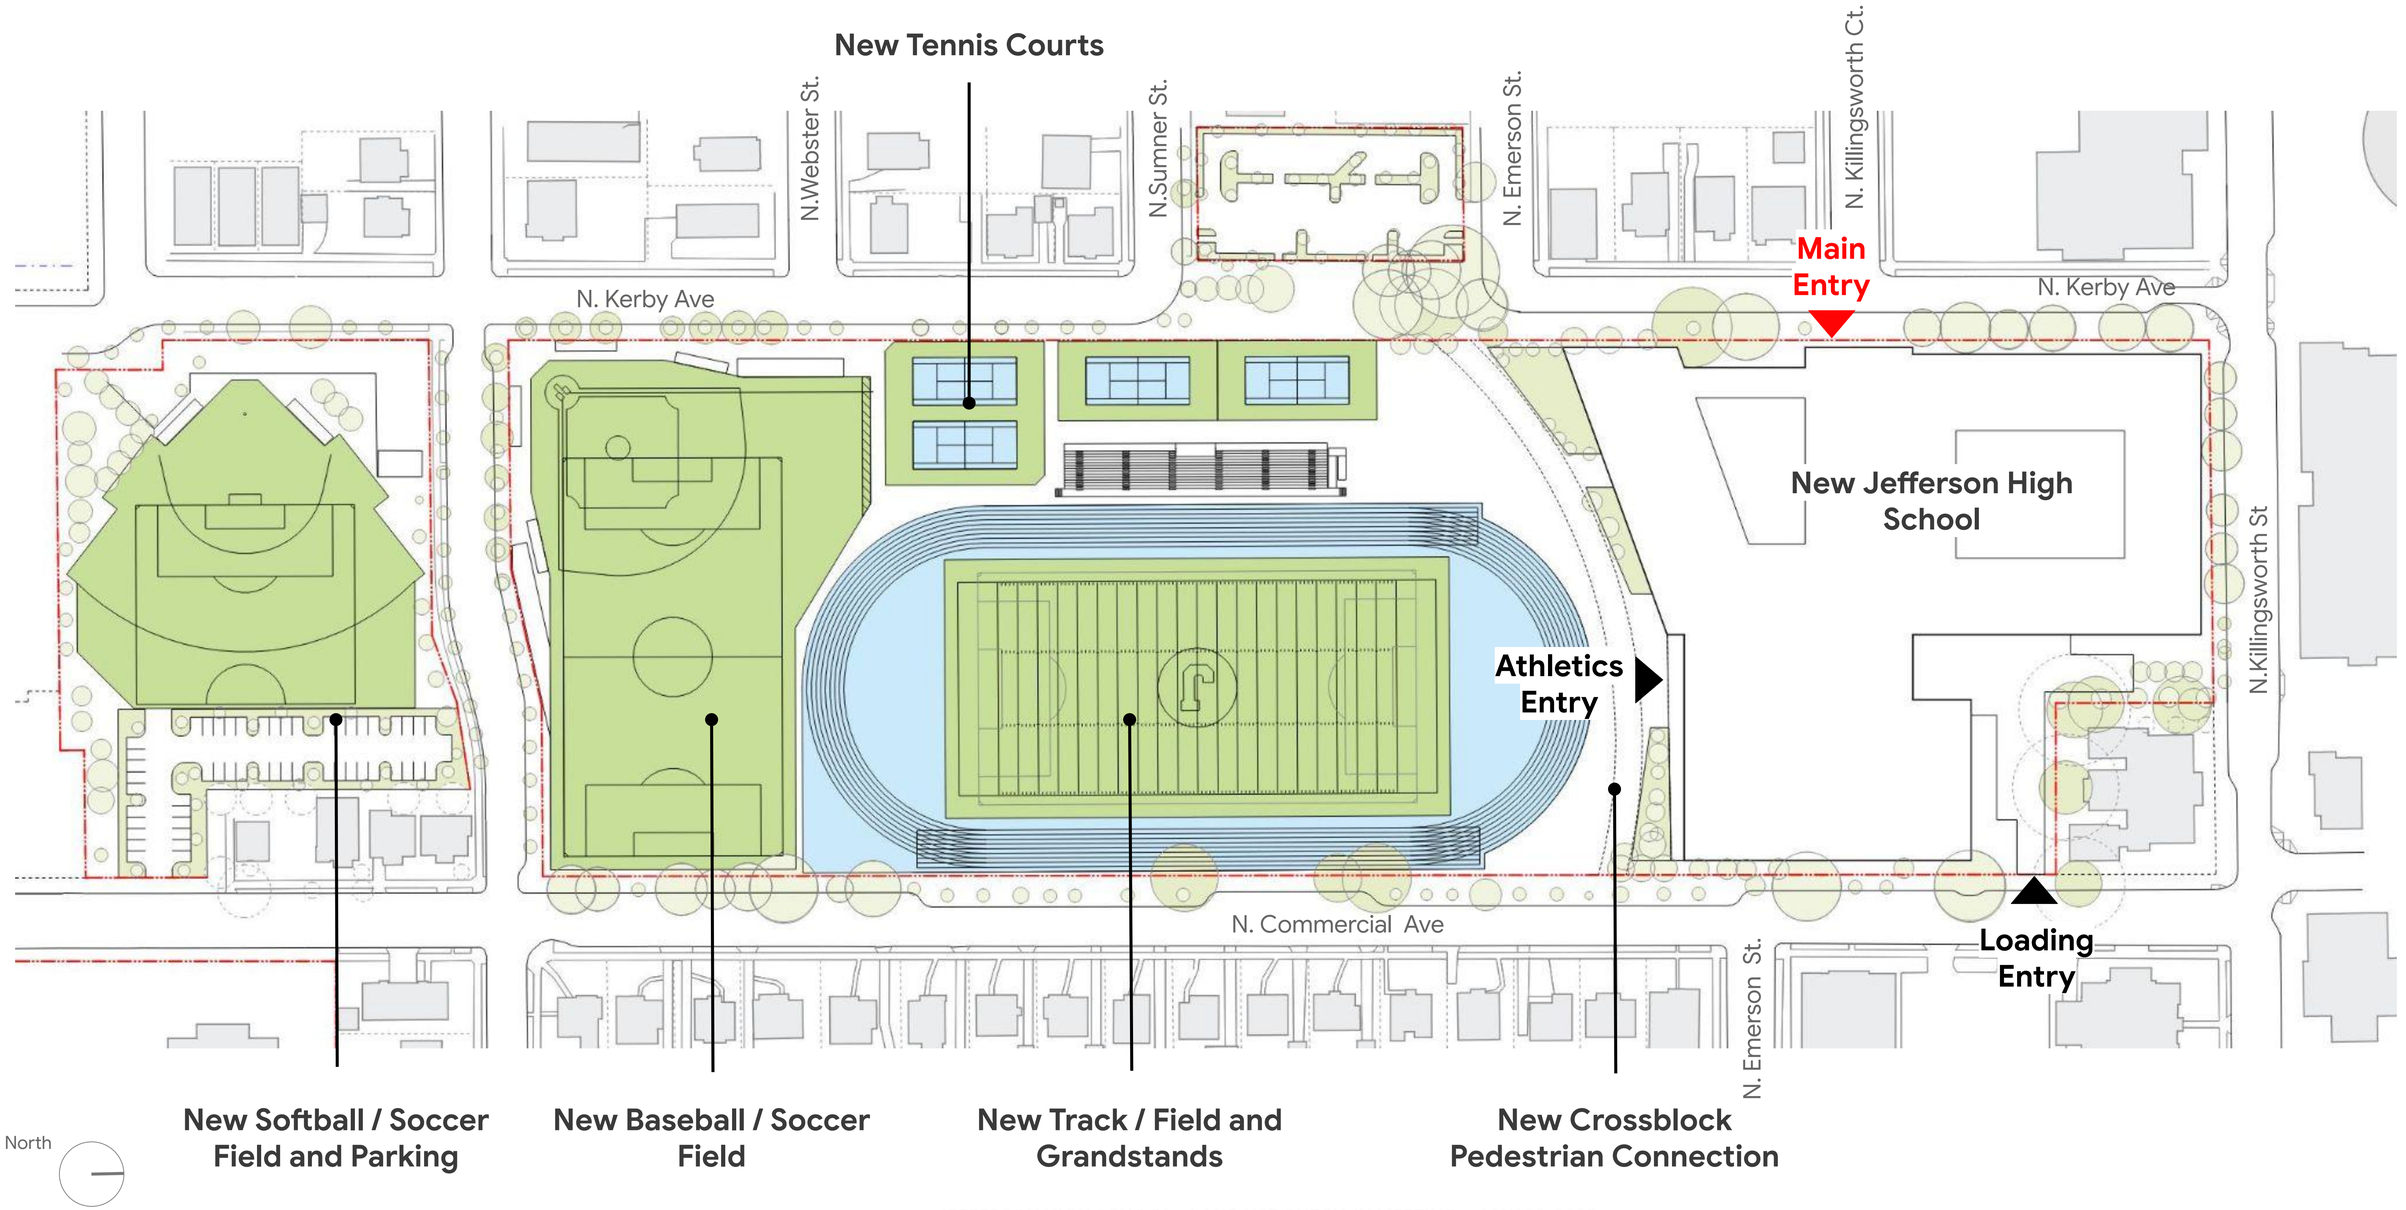

Floor Plan - Level 1

- ADMIN, COUNSELING & CAREER
- COMMUNITY & PARTNERS
- GENERAL CLASSROOMS & SCIENCE
- SPED
- FINE / GRAPHIC ARTS & CTE
- PERFORMING ARTS
- MEDIA CENTER
- ATHLETICS
- BUILDING SUPPORT

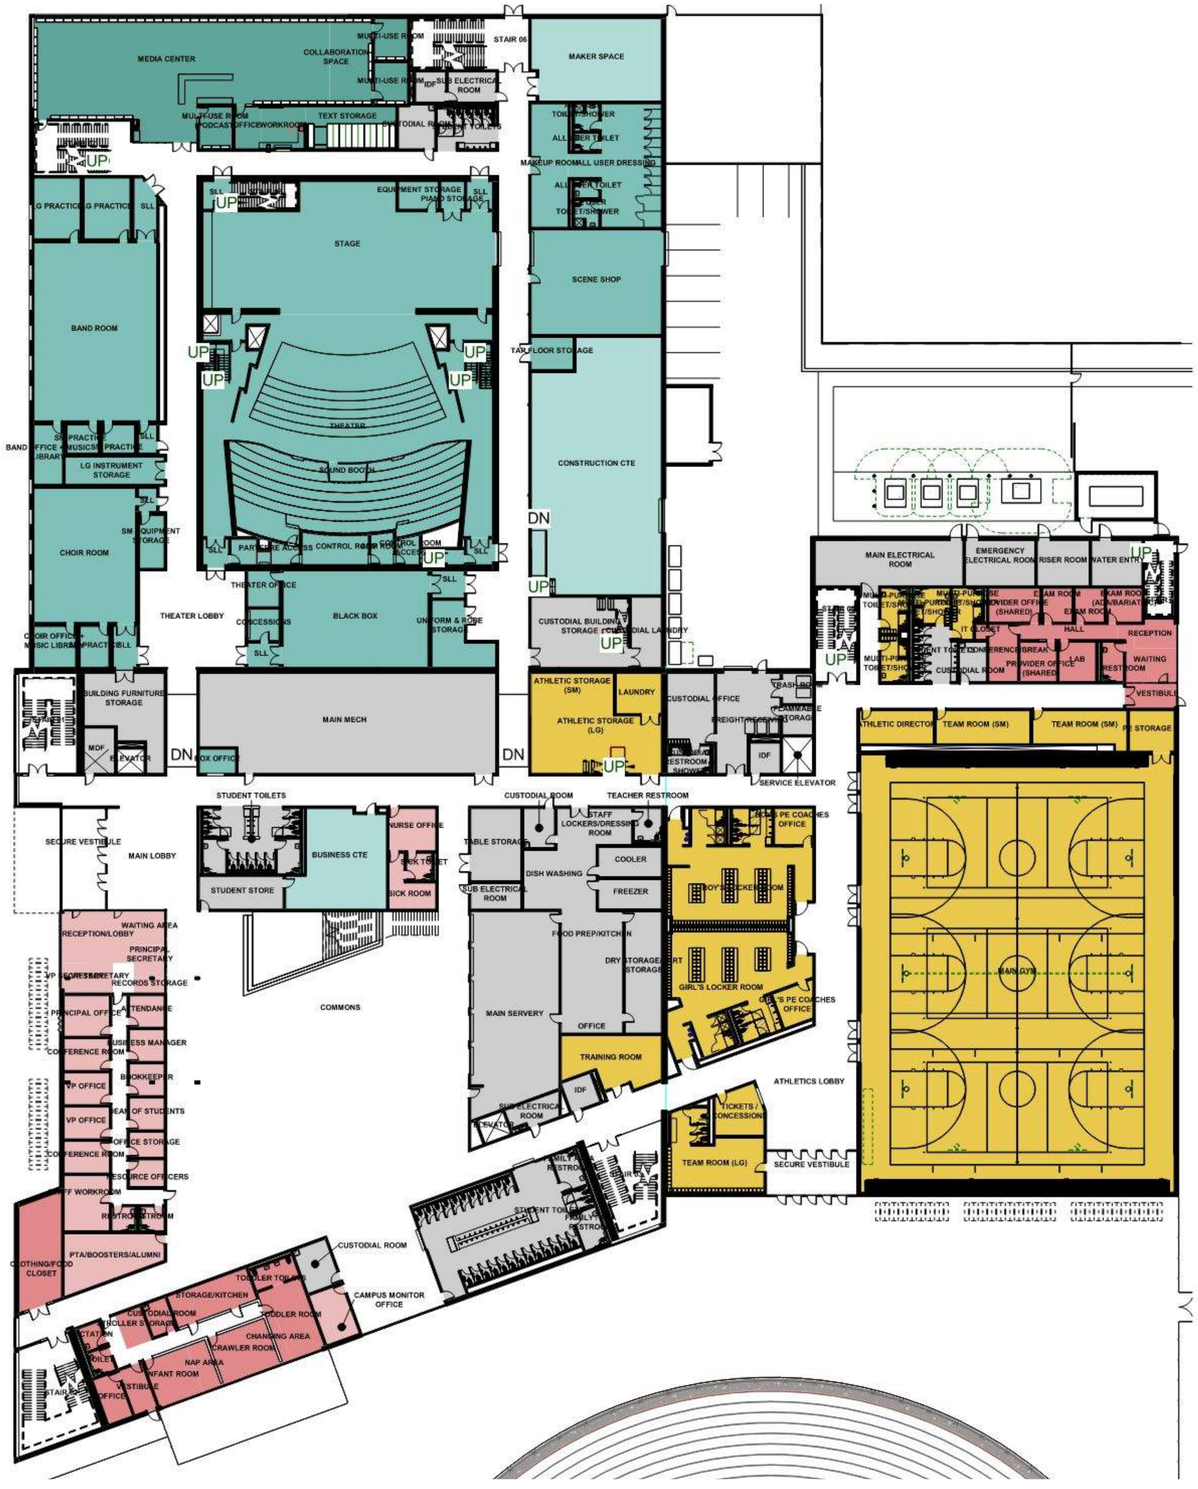


Exhibit A

Floor Plan - Level 2

- ADMIN, COUNSELING & CAREER
- COMMUNITY & PARTNERS
- GENERAL CLASSROOMS & SCIENCE
- SPED
- FINE / GRAPHIC ARTS & CTE
- PERFORMING ARTS
- MEDIA CENTER
- ATHLETICS
- BUILDING SUPPORT



Floor Plan - Level 3

ADMIN, COUNSELING & CAREER

COMMUNITY & PARTNERS

GENERAL CLASSROOMS & SCIENCE

SPED


FINE / GRAPHIC ARTS & CTE

PERFORMING ARTS

MEDIA CENTER

ATHLETICS

BUILDING SUPPORT

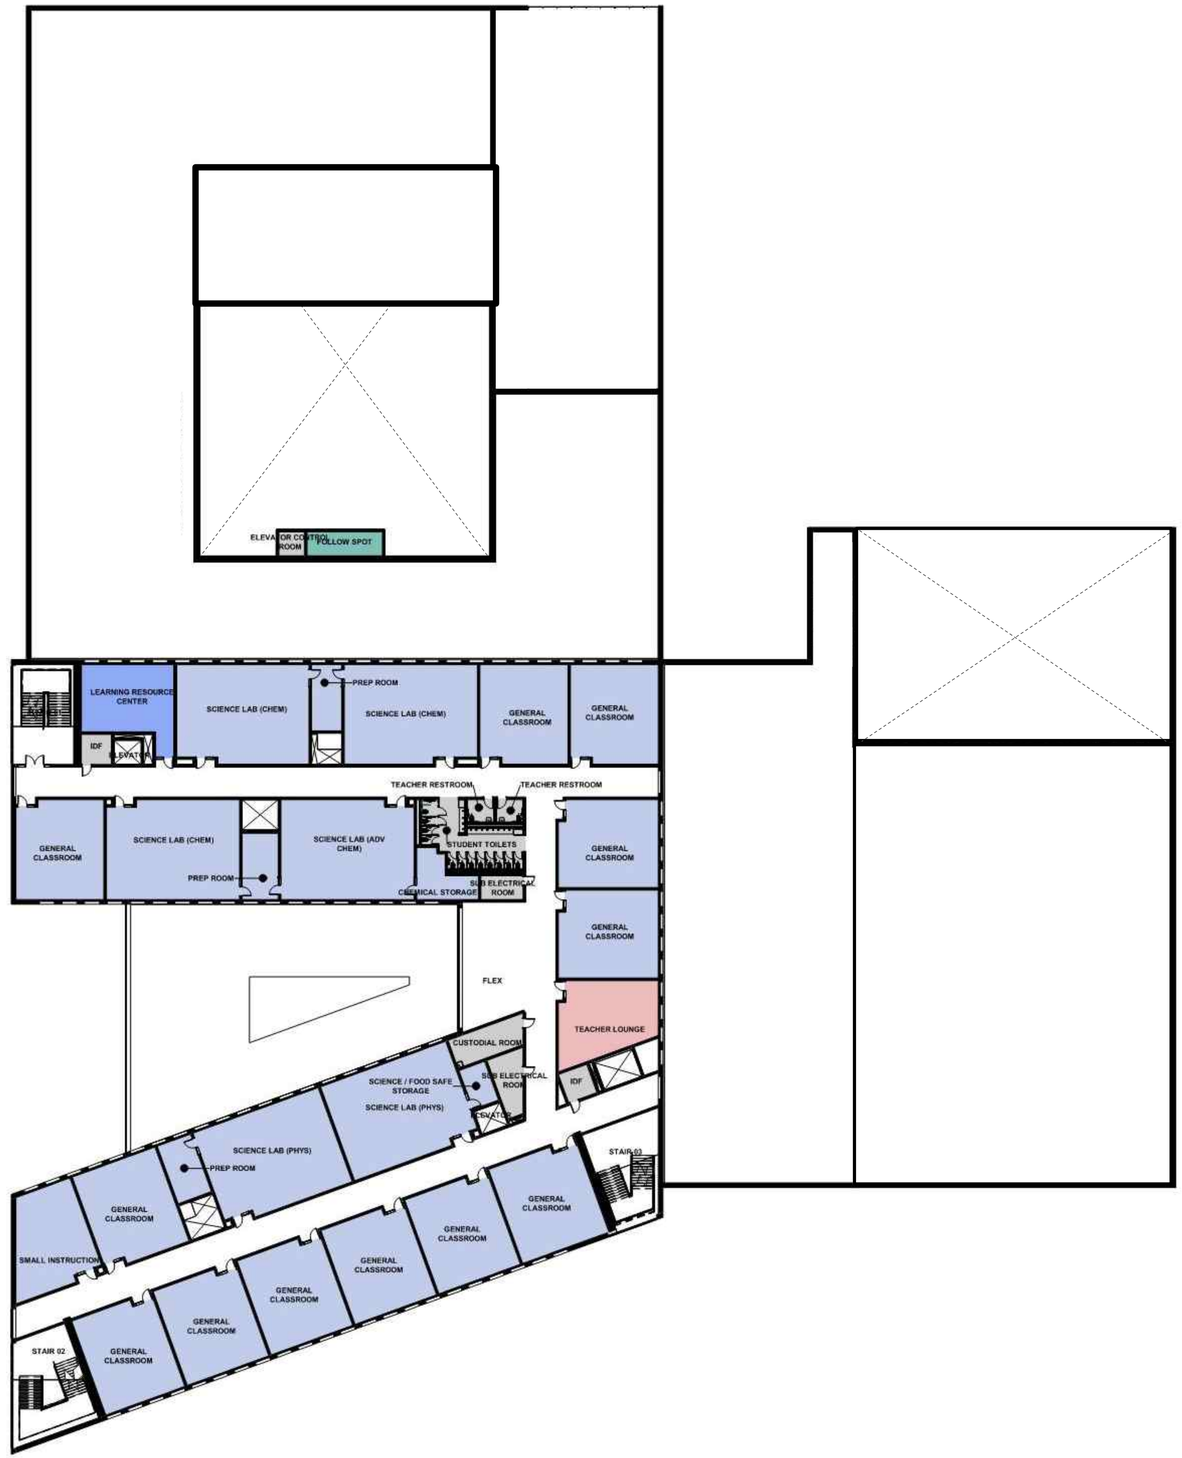

Floor Plan - Level 4

- ADMIN, COUNSELING & CAREER
- COMMUNITY & PARTNERS
- GENERAL CLASSROOMS & SCIENCE
- SPED
- FINE / GRAPHIC ARTS & CTE
- PERFORMING ARTS
- MEDIA CENTER
- ATHLETICS
- BUILDING SUPPORT

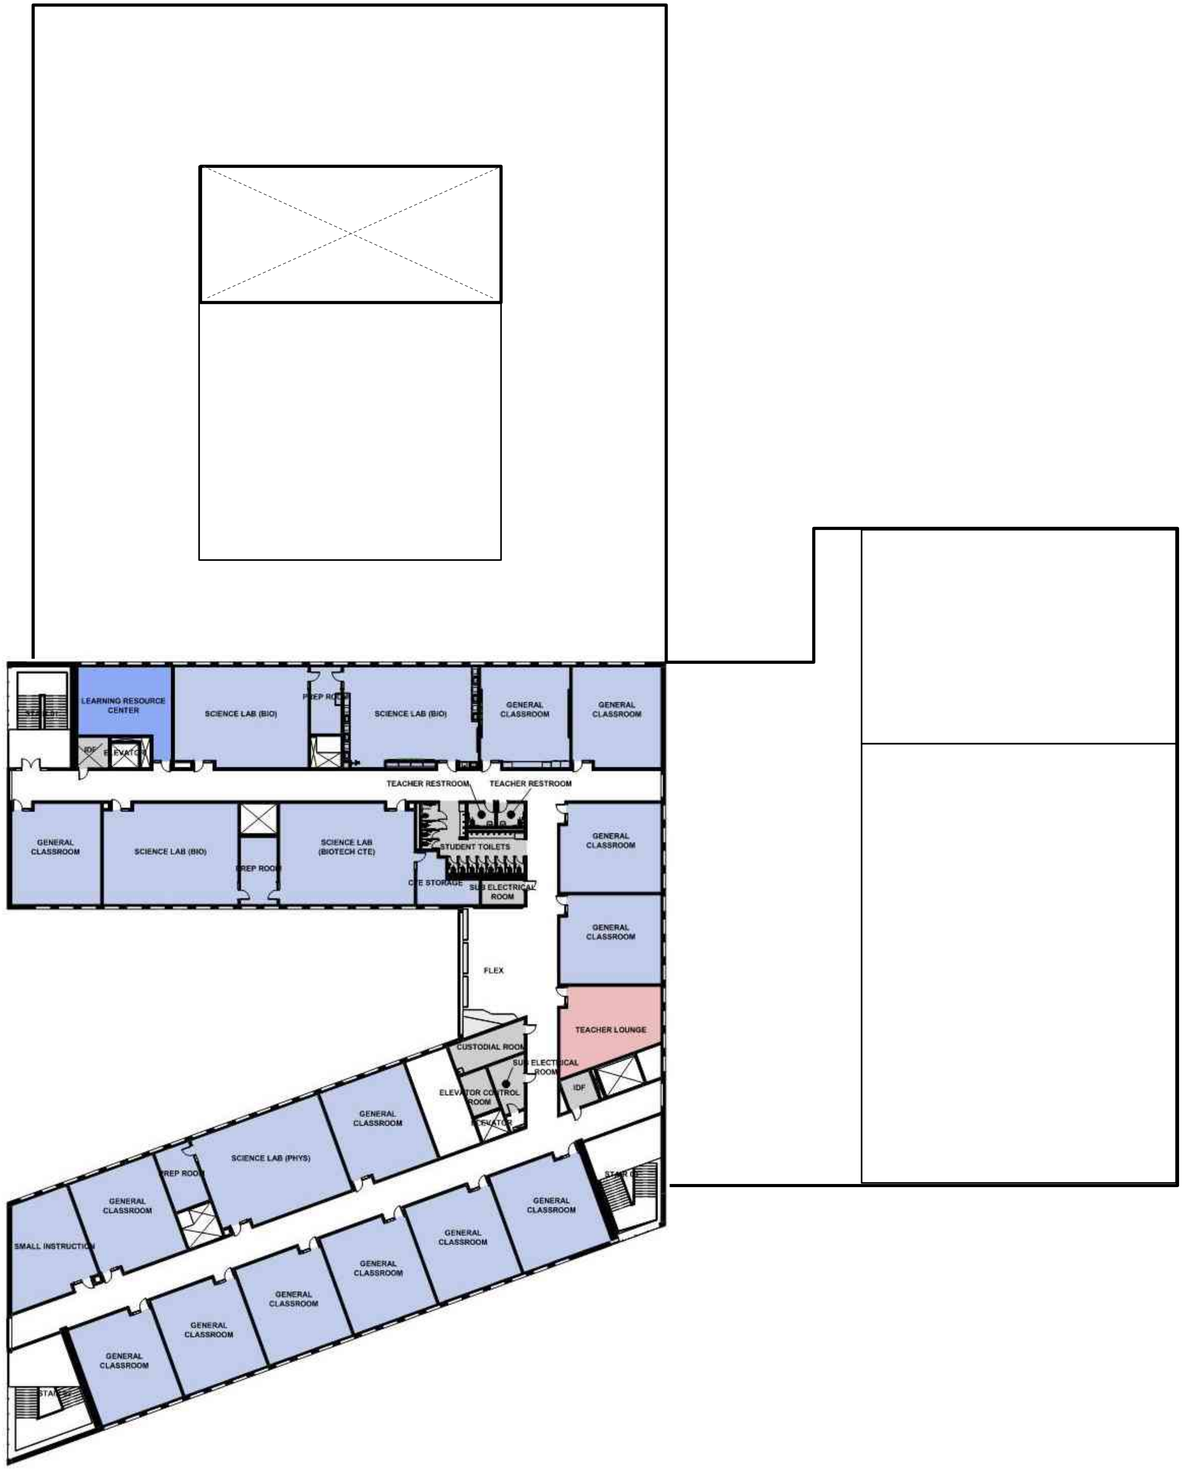


EXHIBIT 5
REVISED BUILDING MASSING

Academics / Entry



Academics / Entry



Academics / Entry



Academics / Entry



Academics / Entry



JEFFERSON HIGH SCHOOL
PORTLAND PUBLIC SCHOOLS
COST REDUCTION STRUCTURAL NARRATIVE
APRIL 18, 2025

INTRODUCTION

Jefferson High School is located at Killingsworth Ave and North Kerby Ave in North Portland. The existing high school will be replaced with a new building that includes a four-story classroom sector with a commons space and servery, a two-story arts sector with dance studios and an auditorium, and an athletics sector with main gym, auxiliary gym, locker rooms, and CTE spaces. This narrative focuses on cost reduction studies for the building structure and is based on concept drawings from BORA.

Over the last two years, the design team has studied several structural system options for the new building. Based on these studies and KPFF's experience on numerous high school projects, this narrative presents structural systems that we believe will be the most cost-efficient. This narrative aims to provide concept-level pricing information for the high school to assist the cost estimator.

The current concept design has three seismically separated buildings: theater, gym, and classroom. Reference the figures 1 through 4 below for the floor plan of each level. The classroom is a 4-story story building in the southeast. It features a central courtyard space surrounded by learning spaces. The south wing of the classrooms is angled towards the athletic fields to the south. The gym building is to the east and is a 2-story building with high-volume spaces at the gym and auxiliary gym. It also houses the locker/team rooms, storage, and support spaces. The performing arts is to the north and houses the media center and support spaces; it is a 2-story building. The theater will be 500 seats with a full fly loft but no balcony. Choir, band, and media spaces are on the ground level, the second floor supports Dance, arts, and other support spaces.

Exhibit A

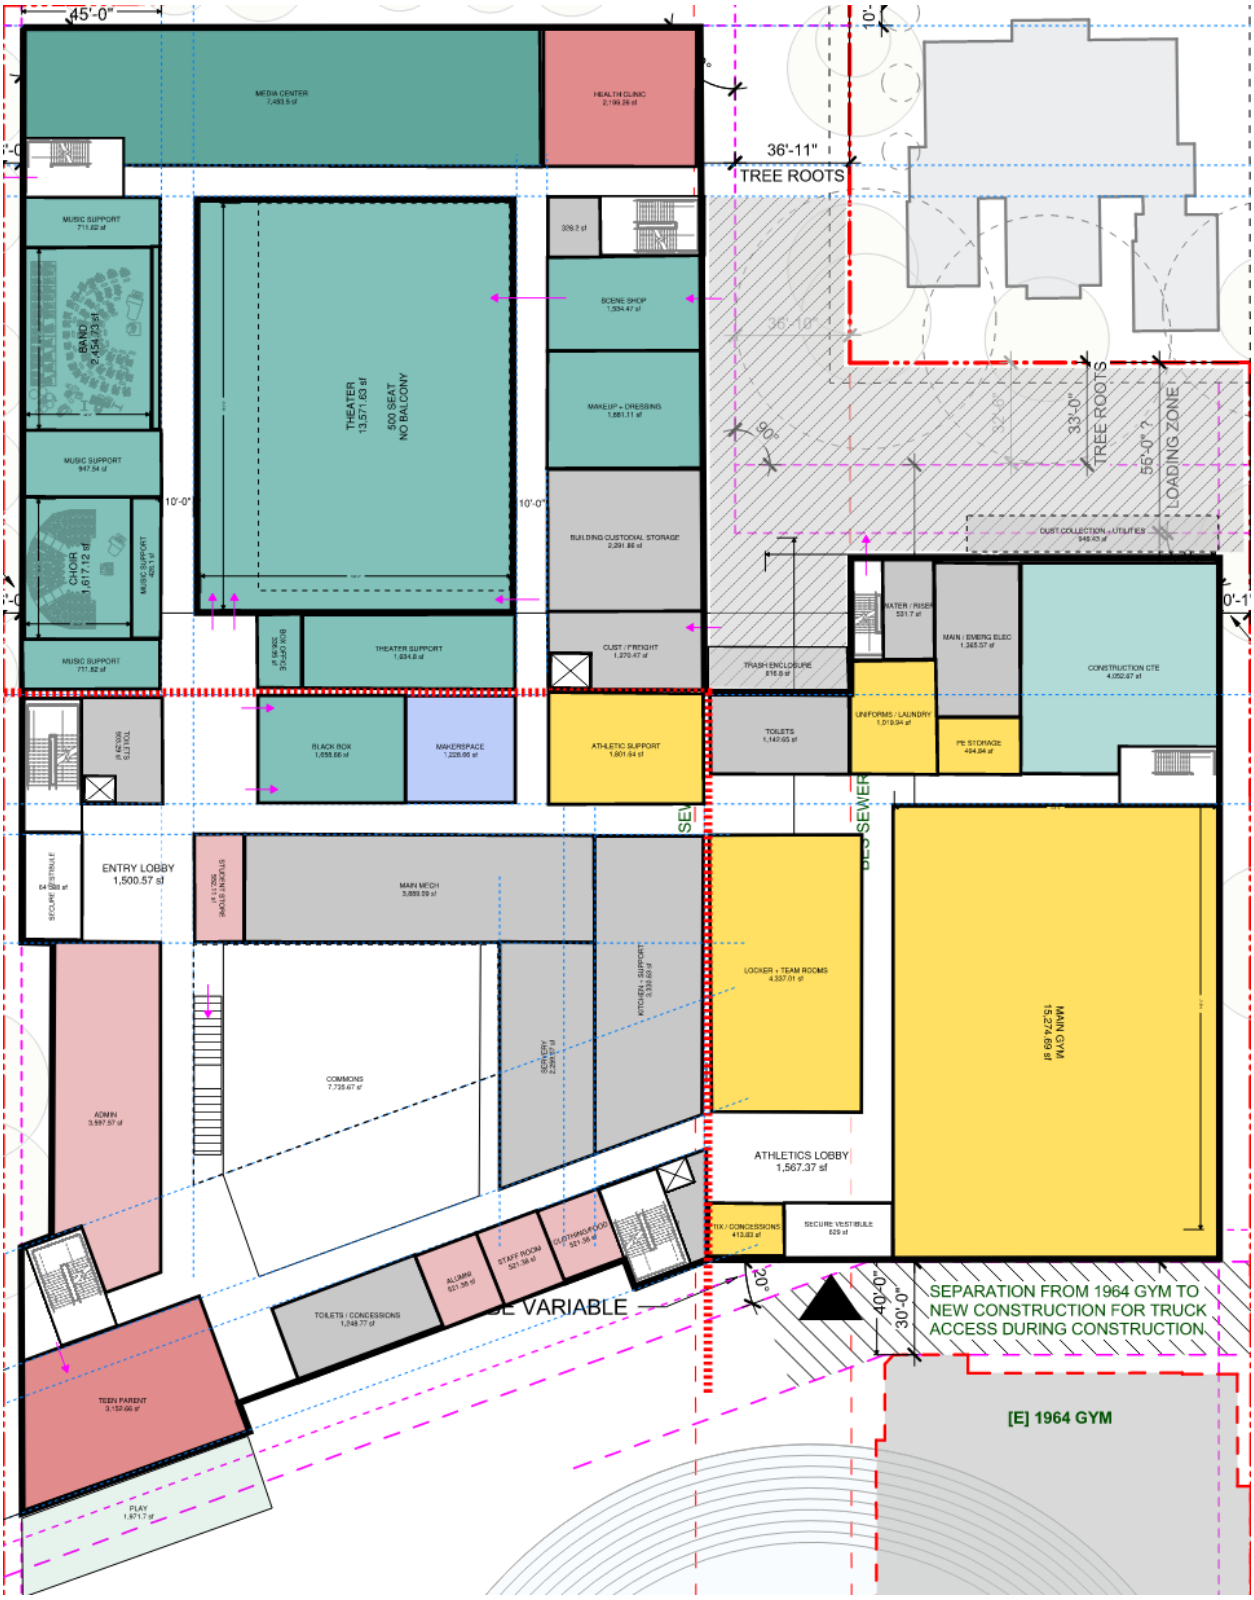


Figure 1 – First Floor Concept Design

Exhibit A

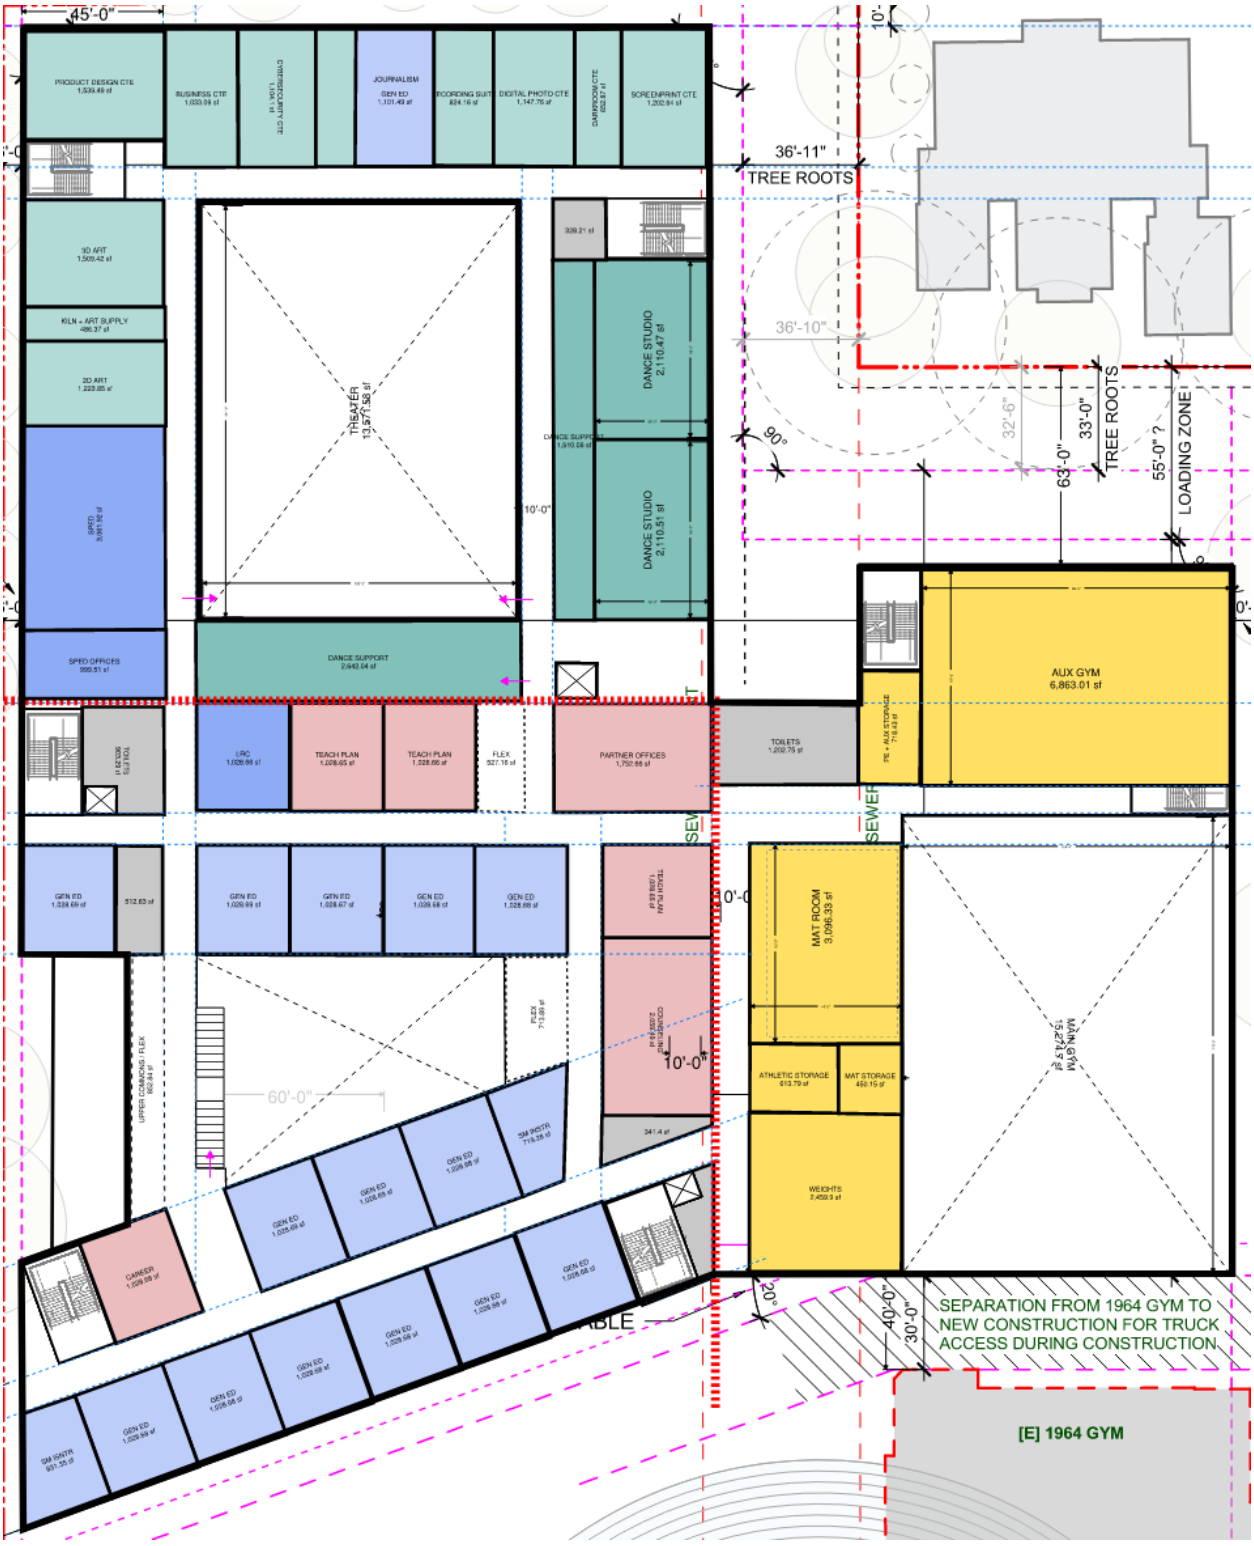


Figure 2 – Second Floor Concept Design

Exhibit A

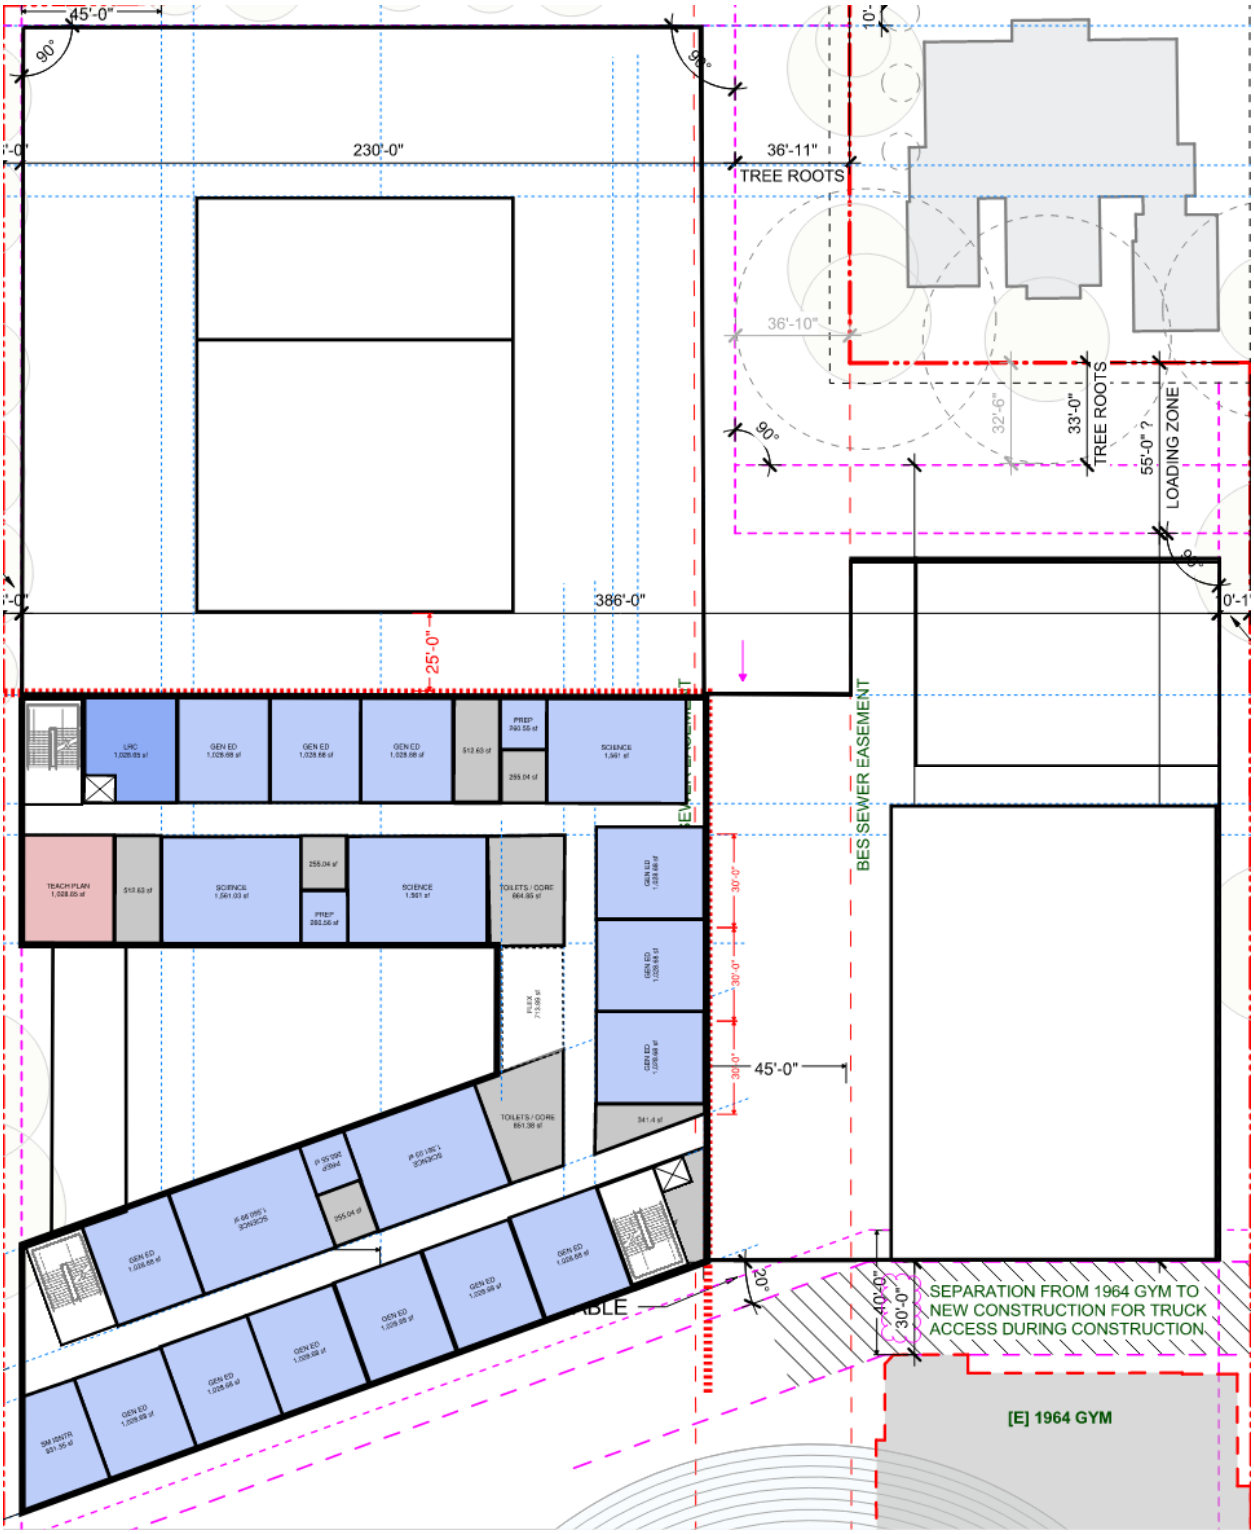


Figure 3 – Third Floor Concept Design

Exhibit A

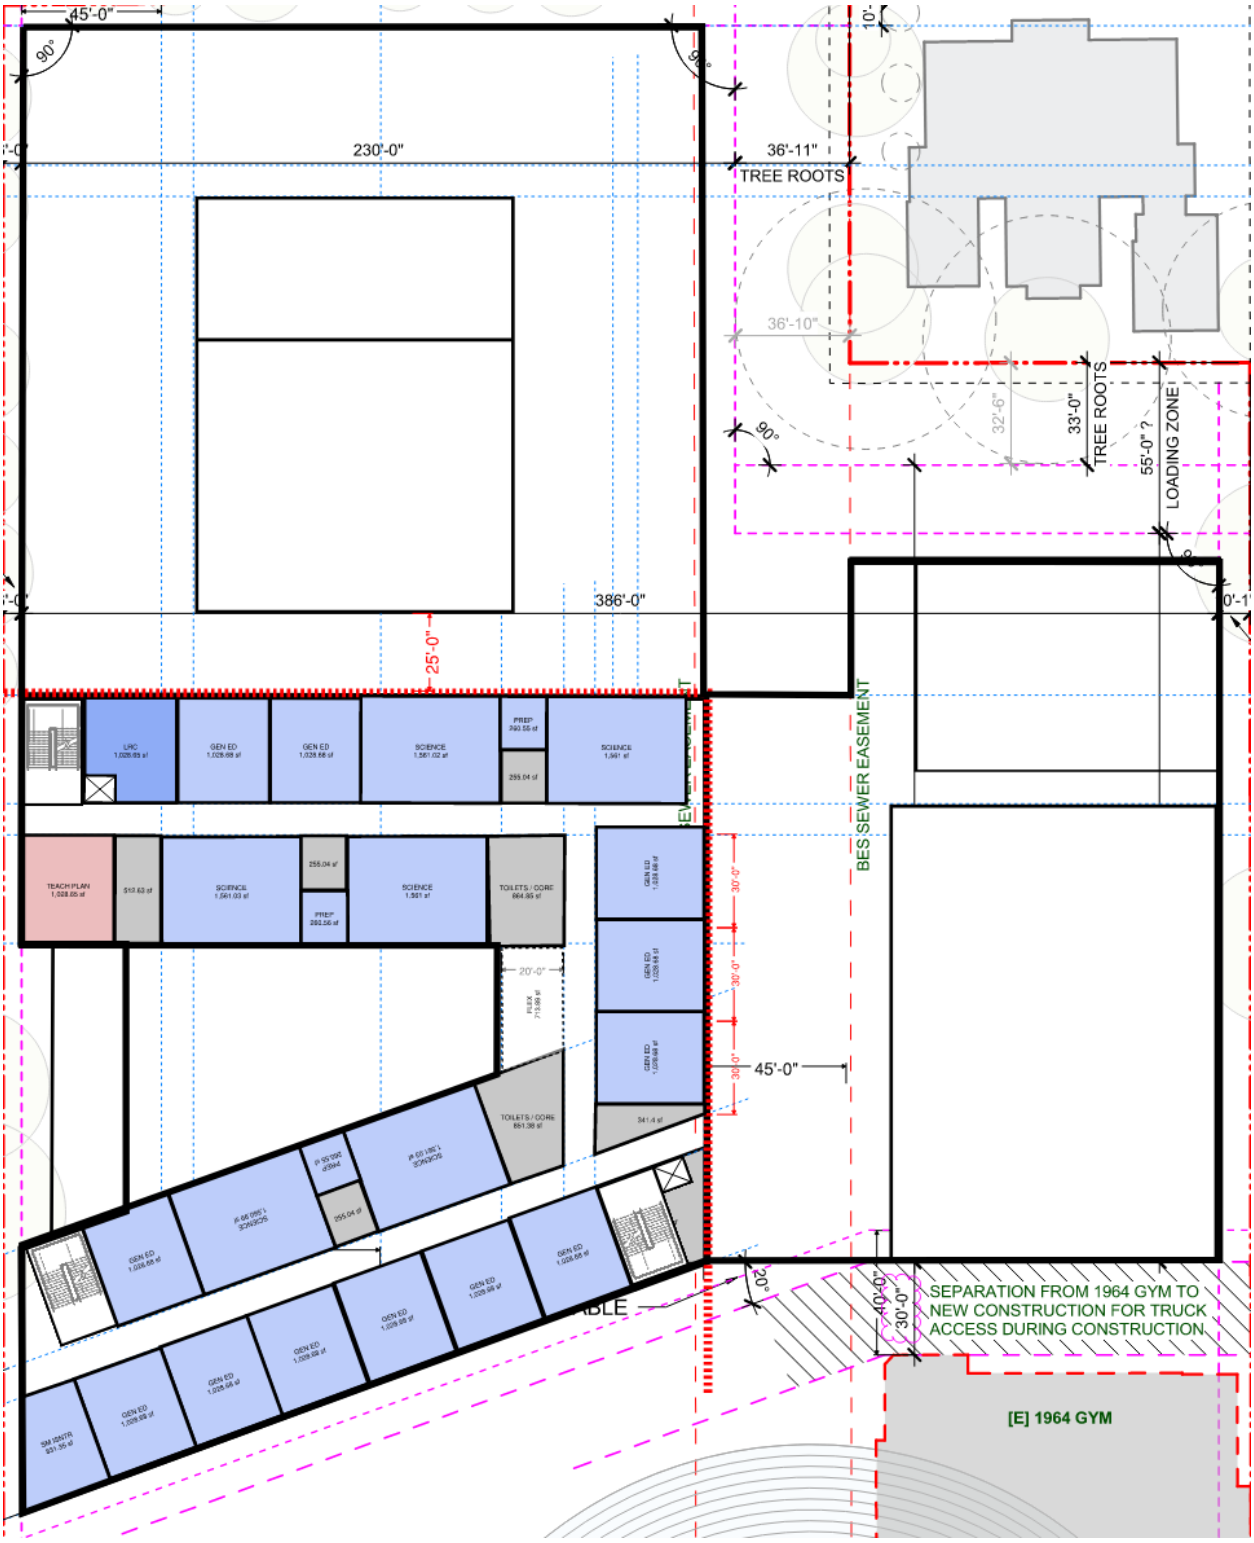


Figure 4 – Fourth Floor Concept Design

STRUCTURAL SYSTEM RECOMMENDATIONS

Classroom Building

The classroom building will be a 4-story structure. In previous studies, the design team found that a mass timber structure worked well for the classroom building and was a cost savings to the project when compared with a steel structure. We continue to recommend this building as a mass timber structure. The reduction in cost comes from speed of erection, no concrete pours at the floors and no spray applied fire protection to the structural members.

The mass timber frame will have either 5-ply CLT or 2x6 DLT panels spanning to glulam beams supported by glulam columns. In the previous design, DLT was cost-feasible over CLT as the contractor had partnered with StructureCraft, the sole supplier of DLT in North America. If that relationship changes or tariffs with Canada are put in place, the cost of DLT could change, and we would need to reevaluate the use of DLT versus CLT.

The lateral load-resisting system for the classroom building will consist of either buckling-restrained braced frames or special moment-resisting frames. We think the structural cost of these two systems is similar, but once we understand the building's floor plan, further study is required.

The roof of the classroom building will be designed to support MEP equipment and to be solar ready per the OSSC code requirements. A tall steel-framed screen wall will conceal mechanical air-handling units and other miscellaneous MEP systems on the roof. We estimate the screen wall steel weight to be 10 psf. Concrete housekeeping pads will be needed under the mechanical units, and we estimate the thickness as 4”-6” depending on the acoustic analysis.

Public stairs shall be assumed to be steel framed with concrete treads and landings.

For cost estimating, we recommend using the framing, braced frames and foundation information provided in the 50% Design Development Drawings for the classroom building. This cost per square foot could be applied to the revised square footage of the classroom building.

Classroom Steel Framed Alternate

This alternate consists of elevated floor framing with a composite slab of 3 inches of reinforced concrete over a 3 inch, 20-gauge metal deck. The composite slab would be supported by steel wide flange beams at 10’ spacing and girders spanning 30’. The beams and girders would be supported by HSS and/or steel wide flange columns on a 30’ x 30’ grid. The roof would be steel framed with 1½ inch, 18-gauge steel roof deck. We estimate that the approximate steel weight of the classroom areas would be 13 psf for the floors and 10 psf for the roof. This includes columns, connections, and miscellaneous steel.

Concrete on metal deck with steel beams and columns weighs more than timber deck with plywood and glulam beams and columns. Due to the increased structural weight, the spread footings in the classroom areas would increase by about 25% if changing to an all steel-framed system.

Performing Arts

We recommend that the theater be steel-framed, as shown in the 50% Design Development Drawings provided in December 2024. Although the theater's size may be reduced, the structural system cost on a square-foot basis should be approximately the same.

Gym, Aux Gym and Support Space

We recommend constructing the gymnasium with CMU perimeter walls and a metal deck over steel trusses at the roof. The CMU could be exposed on the interior face, reducing the cost of interior finishes. Additionally, CMU is very durable for the use of the space. Steel trusses are the most cost-effective and structurally efficient for the long-span roof. The weight of the steel roof would be approximately 11 psf.

CMU can be slow to erect, and concrete tilt panels could be an alternative. Based on previous studies, we think the site logistics of having enough area to pour the panels could be challenging. If tilt panels were utilized, they would be 12" thick panels with 150 lbs per cubic yard of reinforcing.

Another alternative is to provide an all steel-framed gym. The roof would be constructed of 1 ½ 18-gauge metal deck over long-span steel trusses supported by steel columns. Buckling restrained braced frames would be provided for the seismic force resisting system. Where there is a second floor, it would consist of a composite slab of 3 inches of reinforced concrete over a 3 inch, 20-gauge metal deck. The composite slab would be supported by steel wide flange beams at 10' spacing and girders spanning 30'. The beams and girders would be supported by HSS and/or steel wide flange columns on a 30' x 30' grid. We estimate that the approximate steel weight of the gym and surrounding areas would be 13 psf for the floors and 11 psf for the roof. This includes columns, connections, and miscellaneous steel.

Seismic Resilience

The new school buildings are designed as Risk Category IV structures in response to the PPS Resilience Measures Document dated May 9, 2024. Non-structural components like MEP systems will not be designed to Risk Category IV.

If building separation is required between the classroom building to the south and the gym/theater building to the north, it is possible to design the school with the gym and auditorium as Risk Category IV and the classroom portion to the south as Risk Category III. Based on our previous studies, we expect the added cost for Risk Category IV structure to be approximately $5 per square foot. Therefore, we estimate that this strategy could save the project approximately $675,000.

This strategy was recently used at Lincoln High School where we designed the 6-story classroom building as Risk Category III and the adjoining theater/gym building as Risk Category IV.

Foundation System

The building's foundations are based on recommendations provided by GRI in the Geotechnical Investigation report dated February 27, 2025. Based on this report, the classroom building, gymnasium, performing arts wing, grandstand, and site structures are supported on conventional spread footings established in firm, native soil or compacted structural fill.

For cost estimating, we recommend using the foundation sizes provided in the 50% DD set provided in December 2024. If portions of the building are changed to steel from mass timber, the spread footings would increase by about 25%.

The slab on grade will have a base layer and vapor-retarding membrane as recommended in the Geotechnical report.

Canopies

Canopy structures are located around the exterior of the buildings. The canopies are assumed to be steel-framed for durability and resistance to water. Provide a steel allowance of 15 psf for the canopy steel framing. This includes columns and allowance for connections and miscellaneous steel.

Exterior Walls

To reduce cost, we recommend limiting the use of brick. Brick is heavy and requires a stiff support structure to limit deflection. The weight of brick also increases the building's seismic mass, which increases seismic forces and therefore the lateral element sizes. We recommend trying to use a mixture of lightweight materials, including metal panels, GRFC, and glazing.

The backup system for the facade will be light gage metal stud framing that is supported on the ground floor and at each floor above. Stud framing will run past the roof to act as a parapet. Deflection heads are required at each floor line. Exterior studs supporting lightweight materials can be assumed to be 6" 16-gauge metal studs at the first floor, due to the increased height and 18 gauge at floors above.

Additional miscellaneous steel is required to support glazing systems in large open areas where no floor is provided, such as stairs. This steel weight is included in our estimate of steel weight at each floor.

Exterior studs to support brick veneer will need to be 16 gauge minimum. At locations of brick veneer, additional miscellaneous steel is required to support the brick in the form of steel lintels over the windows and brick relief angles at each floor line.

Provide the following additional allowances to the primary building structure to support brick veneer facades:

- At the mass timber-framed option, provide perimeter glulam beams and an additional 30 plf steel allowance along the building perimeter.
- At the all-steel option, provide an additional 0.5 psf of steel weight on each floor to accommodate increased beam stiffness and miscellaneous steel.

GEOTECHNICAL REPORT SUMMARY

GRI provided a final Geotechnical Investigation report dated February 27, 2025. Based on GRI's report, the site soil consists of non-engineered fill underlain by alluvial sand and gravel. The site soils are classified as Site Class D.

The risk of liquefaction, cyclic softening, lateral spreading, and slope instability is low at this site based on the subsurface conditions, topography, and site location. Reference "Foundation System" section of this narrative for additional information.

SITE STRUCTURES

Several small stand-alone one-story buildings are anticipated, including but not limited to:

- Grandstand
- Concession building for the grandstand
- Covered bike parking
- Track and field support building for ticketing and storage
- Batting facilities including dugouts and batting cages
- Trash enclosure

The site buildings are assumed to be fully grouted CMU walls with steel wide flange roof beams with metal deck. Interior steel HSS columns on spread footings may be required for some structures. Assume a 4-inch slab on grade at site buildings. Refer to the foundations section of this report for foundation information.

The trash enclosure is assumed to be a three-sided fully grouted CMU building with cold-formed joists and metal roof deck. Provide an appropriate allowance for steel gates and their support.

New foundations for flag poles and field netting for the athletic facilities will also be required. Provide appropriate allowances.

The security fence will be a cantilevered fence product with embedded round concrete footings.

Memo

Date:	March 14, 2025
Project:	Jefferson High School
To:	Bora
From:	PAE
Subject:	Concept Cost Package

The intent of this memo is to summarize the base MEP systems for the Jefferson HS Modernization project as part of the Concept Cost Reduction Study Phase 2. This is a high-level summary intended to inform the concept level pricing effort.

MECHANICAL SYSTEMS

Central Heating and Cooling Plant

Five 200-ton air to water heat pumps located on the roof (Based on Trane ACX (2-pipe)) will be the primary source of heating and cooling for the building. The heat pumps will feed into a 4-pipe (HWS/HWR/CHWS/CHWR) primary/secondary building distribution system. Chilled water will be distributed to all air handlers for cooling. Heating water will be distributed to all air handlers and throughout the building to each zone.

The plant will include two 700 kW electric boilers for backup heat. Plant equipment will also include primary and secondary pumps, buffer tanks, expansion tanks, glycol makeup, and other accessories as detailed in the 100% SD documents for the baseline central plant. This equipment will be in a ground level mechanical room with dedicated piping risers to each rooftop heat pump.

Air Distribution Systems

Rooftop variable-air-volume (VAV) custom air handlers (AHU) will be the source of air distribution to the building. The AHUs will include air-to-air heat recovery wheels, heating water coils, and chilled water coils. Combined airflow of the units is estimated to be around 295,000 cfm with a maximum size of 35,000 cfm per AHU. Sizing and quantity of AHUs will vary based on final building layout and programming.

Large commons spaces will be served by single zone VAV AHUs. Classrooms, office, and other smaller zones will be served by multizone VAV AHUs. Supply air will be fully ducted. Return air will utilize a plenum return system, with ducted inlets at the mechanical shaft on each level. Acoustical treatments (sound attenuators or sound lined ductwork) for return plenum ducted inlets to be provided as necessary per acoustical consultant recommendations.

Science labs, art rooms, and other high exhaust spaces will have single-pass 100% dedicated outside air (DOAS) VAV AHUs with heat recovery. Supply and exhaust air will be fully ducted.

Multizone systems will have single duct VAV terminal units with heating water reheat coils for individual zone temperature and ventilation control. No secondary zone cooling systems will be provided; chilled water will be limited to the air handlers.

Specialty & Miscellaneous Systems

Specialty exhaust will be provided based on final programming and equipment as detailed in the previous 100% SD documents. This will include a subsoil radon exhaust, exhaust for kilns, fume hoods, chemical storage rooms/cabinets, point of use dust collectors, and other fume and heat exhaust. An outdoor recirculating dust collector for the wood shop will support the construction CTE space.

Rooftop exhaust fans will serve each Type I and Type II hood in the kitchen located on level 1. Type I grease exhaust will be welded and fire wrapped. Type II heat/vapor exhaust will be aluminum or stainless steel.

Split systems will be provided for spaces with 24-hour cooling requirements such as MDF, IDF, and electrical rooms. Split systems will utilize A2L refrigerants distributed vertically within ventilated shafts with exhaust fans for each shaft at the roof.

Building Controls

Building controls, measurement and verification scope, and miscellaneous systems will be provided as detailed in the 100% SD documents.

Teen Parent Center

The teen parent center programming will be integrated into the high school building programming and no longer be its own dedicated building. The teen parent center programming will be served by VAV terminal units w/ reheat from a rooftop VAV AHU.

Remove the HVAC systems and controls detailed in the 100% SD documents, the chilled and heating water mains extended from the high school building, and the associated underground utility trench.

ELECTRICAL SYSTEMS

Main Building Electrical Service Size

The new building will be served by Pacificorp. Primary power will be routed from Pacificorp overhead lines located at the north or east of the site and dropped down to route to a new Pacificorp MV switch cabinet. From there, the primary feeds will extend out to transformer vaults. There will be a total of (3) primary service feeders from this switch cabinet to the transformers.

The switch vault will serve three (3) new utility transformers. Two (2) 4” conduits will be provided to each transformer vault.

Three (3) oil filled, pad mount transformers, will be located at the NE of the building in a utility yard. Pacificorp will confirm exact transformer quantity as design progresses. Each utility transformer will be pad-vault mounted with secondary feeds to three (3) 4000A, 277/480V EUSERC rated service switchboards at the exterior of the building and will contain the service disconnect and sub-feed circuit breaker to the feeder into the building. The vaults, primary and secondary conduits, and service switchboards with utility metering equipment will be provided by the project and installed per Pacificorp requirements. The utility (Pacificorp) will provide the primary conductors, pad mounted transformers, MV switch equipment, and the secondary conductors into the main switchboards.

The (3) service switchboards will feed sub-distribution panels in the electrical room.

March 14, 2025

Generator Size

Backup power will be provided by a 600kW/750kVA, 277/480V 3-phase diesel fired generator. The generator will be exterior mounted with weatherproof, sound attenuated enclosure and built in sub-base 24-hr fuel tank sized for operation at full load. A single feeder from the generator will be brought into the building to a 1200A, 277/480V emergency power main distribution switchboard. Separate transfer switches and distribution gear will be provided, a 225A, 277/480V system for emergency loads and a 600A, 277/480V system for standby loads. A remote docking station will be provided for connection of a temporary generator during maintenance of the system. A remote fuel filling station may be required pending the final location of the generator and its accessibility from the street by a fuel dispensing truck.

Hydrolyzed Vegetable Oil (HVO) will be investigated as a possible fossil fuel reducing source of fuel for the generators. HVO has a much longer shelf life and can be swapped 1 for 1 with diesel with no equipment necessary. HVO comes at a premium and may be more difficult to source than Diesel, however, is a more planet conscious fuel to use in backup generators.

Electrical loads on generator are as follows:

- NEC 700 (Code Required)
  - Egress and Exit Lighting
  - Fire Alarm
  - ERRCS
  - Generator Accessories (battery charger, block heater, etc.)
- NEC 695 (Code Required)
  - Fire Pump
  - Jockey Pump
- NEC 701 (Code Required)
  - None at this time.
- NEC 702 (Optional Standby)
  - MDF/IDF Rooms and associated cooling.
    - Intrusion Alarms
    - Clock Systems
    - Phone System
  - Walk-in Coolers and Freezers at the Kitchen.
  - One hand dryer per restroom.
  - Non-emergency lighting within selected areas:
    - Gymnasiums
    - Commons
    - Main Office
  - Heat trace Freeze Protection (recommended)

March 14, 2025

Photovoltaic System Size

A renewable power source using a Photovoltaic (PV) array will be provided for the facility. The PV array will be located on the roof and will be approximately 500 kW in size. The size noted is based on the concept level roof plan and preliminary rooftop mechanical system layouts. Exact PV array size will be verified and coordinated during design in later phases. Power inverters will be located within the building. PV system panel technology to be used is Crystal silicon construction with a minimum efficiency rating of 18.8 percent.

The PV system will be tied into one of the main distribution switchboards to offset usage.

PPS Standards Note:

— PV inverter output will have remote monitoring system.

— No energized PV conductors will route through the interior of the building where normally occupied by staff or students.

Exhibit A

THE BOOKIN GROUP LLC

Land Use & Institutional Planning

Project Management

Policy Analysis

JHS Cost Reduction Phase – Land Use Summary
Date: April 23, 2025

The following memo summarizes the research and conclusions that were made regarding Land Use and Zoning during the Cost Reduction Phase of the project (January – April 2025).

- **Land Use Schedule:** The development of the site will still require the same land use entitlements – A Conditional Use review for the entire site and a Historic Resource Review for the portion on the development that will be located within the Piedmont Historic District on the north end of the site. Additionally, the removal of the existing buildings on site will be subject to the 180-day Demolition Delay because of their historic status. PPS is still exploring the possibility of starting the south field(s) earlier by submitting a Type II Conditional Use review in September of 2025. The Type III Conditional Use review for the rest of the development would be submitted late 2025, followed shortly by the Type II Historic Resource Review.

  A second Pre-Application Conference would not be required if the Type III Review is submitted by December 3, 2026 (one year from the date of the last Pre-Application Conference). A new Early Assistance Appointment is generally not recommended unless the design changes significantly, since there would be little new information the City would provide for the cost of the appointment. A second Early Neighborhood Notification meeting is not required, and PPS has indicated that one will not likely be held due to the low attendance at the previous neighborhood meeting held in December 2024. An additional Design Advice Request is not required but could be optionally applied for to have the Historic Landmarks Commission weigh in on the new design.

- **South Field(s) Review:** The previous application for Type II Conditional Use review for the south baseball field was withdrawn from the City at the end of March 2025, to avoid the application expiring and all application fees being lost. A refund of $20,085 is being process by the City for this application.

  It appears that it may be possible to have both the baseball field, and the softball field included in the same Type II Conditional Use review with the new submittal. To avoid a Type III Conditional Use for these fields the exterior improvement area related to the fields must stay below 25,000 sq. ft. excluding areas of artificial turf. "Exterior improvements" are defined in the Zoning Code as: *"All improvements except buildings or other roofed structures…include surface parking and loading areas, paved and graveled areas…improved open areas such as plazas and walkways, but does not include vegetative landscaping, synthetic turf, natural geologic forms, or unimproved land."*

- **On-Site Tree Canopy:** The site must comply with the standards of Title 11 which require 25% of the site to be covered by tree canopy. Calculations of the previous design by Place found that the site could meet this standard, but it was very tight. Several of the trees that were included in this calculation may need to be removed from the updated plan (for example: trees in the Kerby Street pedestrian plaza and in the cross-block connection). Urban Forestry may be receptive to allowing a lower tree density standard for the site using the justification that so much of the outdoor area on the site will be artificial turf. However, this reduced

1020 SW Taylor St.
Suite 555
Portland, OR
97205

Telephone
503.241.2423

number must be negotiated with Urban Forestry and Planning and will require coordination from both review groups. It is suggested that PPS initiates talks with these reviewers about on-site tree density early since there is no official process or timeline for this request and no standard reduction that can be anticipated in the design.

- **Non Conforming Upgrades:** Per discussions with PPS, the required upgrades to the Humboldt Elementary site will not be deferred 10 years but rather completed as part of the last phase of the redevelopment of JHS. PPS may still need to enter into a covenant with the City to delay the upgrades at Humboldt a year or so to have them align with the final phases of construction. A more thorough assessment of the site conditions at Humboldt will be required to fully understand what upgrades will be necessary, which will need to include a site survey and an arborist report. The strategy for upgrades will need to be nailed by the submittal of the Type II Conditional Use for the south fields, since this would be the first project that will trigger the upgrades, so PPS is encouraged to begin this work as soon as possible.

  Because both schools are included in the definition of site, PPS has directed the team to look for opportunities to have the improvements made to the JHS site count toward the required upgrades at the Humboldt site. Probably the best opportunity for this would be in how the Adjustments included with the Conditional Use applications are structured and requested. The Adjustments could look at how the standards apply to the entire site (such as in the case of overall landscaping for example) and if the JHS site is over on standard the excess should be credited to the Humboldt site. It is recommended that PPS discuss this strategy with city planning staff, particularly because of how the City is calculating fees for the Adjustments (per frontage or element vs. per standard).

Exhibit A

EXHIBIT 9
REVISED COMPREHENSIVE PLAN COST MODEL

JEFFERSON HS MODERNIZATION

REVISED COMPREHENSIVE PLAN COST MODEL - 2025

Rider Levett Bucknall

UNIFORMAT LEVEL 3 SUMMARY

Ref	Description	**323,058** Incl. TPC & Grandstands GFA $/SF	100% SD Est. Rev.3 Nov - 2024	**300,823** Includes Grandstands GFA $/SF	Rev. Cost Model Total Cost $	Cost Delta ~ Cost Model - SD Rev.3	RLB COMMENTS ON COST VARIANCES b/w Rev. Comp Plan Cost Model and SD Rev.3 Est.
							In general, the total Building Gross Floor Area (GFA) reduction of 22,235 SF (from 317,951SF to 295,716SF) has cost savings overall.
A1010	Standard Foundations	$ 16.19	5,229,434	$ 17.30	5,204,238	(25,196)	Less overall building gross floor area
A1020	Special Foundations		Excl.	$ -	-	-	
A1030	Slab on Grade	$ 14.76	4,767,581	$ 16.31	4,906,423	138,842	Less overall building gross floor area
A2020	Basement Walls	$ 1.12	362,094	$ 1.20	360,988	(1,106)	
B1010	Floor Construction	$ 65.88	21,284,205	$ 66.62	20,040,828	(1,243,377)	Deleted Theater balcony floor structure
B1020	Roof Construction	$ 50.91	16,445,474	$ 53.11	15,976,710	(468,764)	Updated structural steel allowances per KPFF narrative 03/14/25
B2010	Exterior Walls	$ 50.61	16,351,503	$ 47.74	14,361,290	(1,990,213)	Updated mechanical screen wall steel psf per KPFF narrative Revised Façade SF based on less building GFA
B2020	Exterior Windows	$ 17.36	5,608,210	$ 16.92	5,089,925	(518,285)	Revised Windows SF based on less building GFA
B2030	Exterior Doors	$ 3.90	1,260,784	$ 3.88	1,167,193	(93,591)	Less overall building GFA
B3010	Roof Coverings	$ 17.74	5,732,151	$ 17.95	5,399,773	(332,378)	Deleted Teen Parent Center and Less overall building SF
C1010	Partitions	$ 48.42	15,640,975	$ 49.41	14,863,664	(777,311)	Updated costs based on area reductions to Classrooms, Gym, Theater
C1020	Interior Doors	$ 7.47	2,413,600	$ 7.87	2,367,477	(46,123)	Less overall building GFA
C1030	Specialties	$ 11.11	3,589,106	$ 10.14	3,050,345	(538,761)	Reduced lockers count Less overall building GFA
C2010	Stair Construction	$ 7.80	2,520,000	$ 7.05	2,120,802	(399,198)	Less egress stairs based on executive scope summary and updated pricing
C3010	Wall Finishes	$ 22.37	7,225,670	$ 21.81	6,560,950	(664,720)	Updated costs based on area reductions to Classrooms, Gym, Theater
C3020	Floor Finishes	$ 14.29	4,615,824	$ 14.28	4,295,752	(320,072)	Updated costs based on area reductions to Classrooms, Gym, Theater
C3030	Ceiling Finishes	$ 18.27	5,900,911	$ 17.07	5,135,049	(765,862)	Updated costs based on area reductions to Classrooms, Gym, Theater
D1010	Elevators and Lifts	$ 4.40	1,420,000	$ 4.07	1,224,350	(195,650)	Adjusted pricing per current market
D2010	Plumbing Fixtures	$ 1.82	588,455	$ 1.65	496,358	(92,097)	
D2020	Domestic Water Distribution	$ 5.25	1,694,962	$ 7.12	2,141,860	446,898	GFA generated variance--Price increase per GFA offsets due to higher sub pricing at reconciliation
D2030	Sanitary Waste	$ 4.63	1,495,428	$ 4.82	1,449,967	(45,461)	
D2040	Rain Water Drainage	$ 1.27	411,118	$ 1.37	412,128	1,010	
D2090	Other Plumbing Systems	$ 8.20	2,648,685	$ 8.65	2,602,119	(46,566)	
D3020	Heat Generating Systems	$ 9.44	3,048,983	$ 8.87	2,668,300	(380,683)	Primarily GFA generated variance affecting piping distribution
D3030	Cooling Generating Systems	$ 9.89	3,194,398	$ 15.87	4,774,061	1,579,663	Primarily GFA generated variance affecting piping distribution
D3040	Distribution Systems	$ 31.30	10,112,317	$ 25.68	7,725,135	(2,387,182)	Reduced CFM's per narrative, return air plenum based, ASHP capacities reduced
D3050	Terminal & Package Units	$ 7.86	2,540,100	$ 3.50	1,052,881	(1,487,220)	Switched to a standard VAV system, deleted fancoil units, radiant heating and more expensive convective panels
D3060	Controls & Instrumentation	$ 10.80	3,489,700	$ 11.60	3,489,547	(153)	GFA generated variance--Price increase per GFA offsets due to higher sub pricing at reconciliation
D3070	Systems Testing & Balancing	$ 0.98	317,951	$ 0.98	294,807	(23,144)	Primarily GFA generated variance
D3090	Other HVAC Systems and Equipment	$ 31.74	10,252,291	$ 18.44	5,547,176	(4,705,115)	Primarily GFA generated variances coupled with deletion of precontruction services allowance and ceiling fans.
D4040	Sprinklers	$ 7.95	2,568,051	$ 8.12	2,442,683	(125,368)	
D5010	Electrical Service & Distribution	$ 25.23	8,151,449	$ 21.32	6,413,546	(1,737,903)	
D5020	Lighting & Branch Wiring	$ 26.26	8,484,377	$ 26.56	7,989,859	(494,518)	
D5030	Communications & Security	$ 20.92	6,758,292	$ 21.27	6,398,505	(359,787)	
D5090	Other Electrical Services	$ 24.74	7,993,902	$ 22.46	6,756,485	(1,237,417)	
E1020	Institutional Equipment	$ 4.28	1,383,394	$ 4.60	1,383,786	392	
E1030	Vehicular Equipment	$ 0.08	25,000	$ 0.08	24,066	(934)	
E1090	Other Equipment	$ 29.72	9,599,951	$ 25.92	7,797,332	(1,802,619)	Theater seating decreased from 1000 to 500 Reduced A/V systems budget by 10%, as advised
E2010	Fixed Furnishings	$ 11.01	3,558,025	$ 11.17	3,360,193	(197,832)	Less building GFA
E2020	Moveable Furnishings		Excl.		-	-	
F2010	Building Elements Demolition	$ 20.18	6,520,500	$ 18.06	5,432,863	(1,087,637)	Reduced allowances due to potential open-bid competitiveness rather than limited consortium partners
F2020	Hazardous Components Abatement	$ 21.57	6,967,000	$ 20.34	6,118,740	(848,260)	Reduced allowances due to potential open-bid competitiveness rather than limited consortium partners
G1010	Site Clearing	$ 0.01	4,500	$ 0.01	4,500	-	
G1020	Site Demolition & Relocations	$ 4.40	1,422,069	$ 4.73	1,422,893	824	
G1030	Site Earthwork	$ 30.83	9,958,909	$ 32.96	9,915,126	(43,783)	Deleted West parking lot improvements Reduced improvements at cross block connection
G2010	Roadways	$ 0.87	282,628	$ 0.39	117,321	(165,307)	Deleted site improvements at Kerby Grove
G2020	Parking Lots	$ 1.00	324,375	$ 0.66	198,543	(125,832)	Reduced West parking lot site improvements
G2030	Pedestrian Paving	$ 5.97	1,929,241	$ 6.41	1,928,275	(966)	
G2040	Site Development	$ 25.74	8,316,076	$ 27.64	8,314,748	(1,328)	Deleted West parking lot improvements Reduced improvements at cross block connection
G2050	Landscaping	$ 3.85	1,243,327	$ 4.13	1,242,399	(928)	
G3010	Water Supply	$ 0.71	227,772	$ 0.76	228,625	853	
G3020	Sanitary Sewer	$ 0.18	57,610	$ 0.19	57,156	(454)	
G3030	Storm Sewer	$ 7.23	2,334,283	$ 7.31	2,199,016	(135,267)	Deleted West parking lot improvements
G3060	Fuel Distribution	$ 0.02	5,000	$ 0.02	6,016	1,016	
G4010	Electrical Distribution	$ 0.18	56,600	$ 0.19	57,156	556	
G4020	Site Lighting	$ 6.55	2,115,265	$ 6.87	2,066,654	(48,611)	Deleted West parking lot improvements
G4030	Site Communication and Security	$ 1.36	440,425	$ 1.46	439,202	(1,223)	
ESTIMATED NET COST		**776.62**	**250,889,931**	**754.91**	**227,095,783**	**(23,794,148)**	
MARGINS & ADJUSTMENTS							
	Design / Estimating Contingency	**6.9%**	17,247,295	7.0%	15,896,705	(1,350,590)	No change
	Escalation to Start of Construction - April 2025 to July 2026	**6.1%**	16,477,328	6.0%	14,579,549	(1,897,779)	Updated to date
	Escalation to Mid-point of Construction - July 2026 to May 2028 (10% - Discounted to reflect early buyout of Main Building)	**6.2%**	17,787,016	4.3%	11,204,358	(6,582,658)	Updated to date
	Tariffs Risk / Market Volatility Contingency		-	**0.0%**	-	-	Excluded per direction from Bora
	CM/GC Contingency (5%)	**4.9%**	14,895,079	5.0%	13,438,820	(1,456,259)	No change
	General Conditions/General Requirements (49 months duration)	**16.8%**	53,175,430		-	(53,175,430)	
	General Conditions (49 months duration)		-	9.0%	25,399,369	25,399,369	Allowance optimized based on benchmarking other CMGC projects in PNW region
	General Requirements (49 months duration)		-	7.0%	21,533,021	21,533,021	
	Cranes and hoisting - Incl. Above		Incl.		-	-	
	Bonds & Insurance (3%)	**3.0%**	11,114,163	3.0%	9,874,428	(1,239,735)	No change
	Overhead & Profit (3.5%)	**3.5%**	13,355,518	3.5%	11,865,771	(1,489,747)	Fee could be an opportunity for small reduction.
	Preconstruction Services Allowance	**0.4%**	1,470,000		1,500,000	30,000	
	Preconstruction Services - Sept. 24 to Aug 25 - to match CMGC, as advised	**0.6%**	2,333,921		Excl.	(2,333,921)	Deleted
	Solar/Green Energy Allowance - Included in Est. Detail		Incl.		Incl.	-	
	Total Estimated Construction Cost (in current dollars)	**$ 1,234.29**	**$ 398,745,681**	**$ 1,171.41**	**$ 352,387,804**	**(46,357,877)**	
	Owner Contingency - Excluded, as Advised		Excl.		Excl.		
ESTIMATED TOTAL COST		**$ 1,234.29**	**$ 398,745,681**	**$ 1,171.41**	**$ 352,387,804**	**$ (46,357,877)**	

Exhibit A

EXHIBIT 9
REVISED COMPREHENSIVE PLAN COST MODEL

JEFFERSON HS MODERNIZATION

REVISED COMPREHENSIVE PLAN COST MODEL - APRIL 2025

UNIFORMAT LEVEL 3 SUMMARY		323,058			300,823	
Ref	**Description**	**GFA $/SF**	**100% SD Est. Rev.3 Nov - 2024**		**GFA1 $/SF**	**Rev. Cost Model Total Cost $**
A1010	Standard Foundations	$ 16.19	5,229,434	$	17.30	5,204,238
A1020	Special Foundations		Excl.	$	-	-
A1030	Slab on Grade	$ 14.76	4,767,581	$	16.31	4,906,423
A2020	Basement Walls	$ 1.12	362,094	$	1.20	360,988
B1010	Floor Construction	$ 65.88	21,284,205	$	66.62	20,040,828
B1020	Roof Construction	$ 50.91	16,445,474	$	53.11	15,976,710
B2010	Exterior Walls	$ 50.61	16,351,503	$	47.74	14,361,290
B2020	Exterior Windows	$ 17.36	5,608,210	$	16.92	5,089,925
B2030	Exterior Doors	$ 3.90	1,260,784	$	3.88	1,167,193
B3010	Roof Coverings	$ 17.74	5,732,151	$	17.95	5,399,773
C1010	Partitions	$ 48.42	15,640,975	$	49.41	14,863,664
C1020	Interior Doors	$ 7.47	2,413,600	$	7.87	2,367,477
C1030	Specialties	$ 11.11	3,589,106	$	10.14	3,050,345
C2010	Stair Construction	$ 7.80	2,520,000	$	7.05	2,120,802
C3010	Wall Finishes	$ 22.37	7,225,670	$	21.81	6,560,950
C3020	Floor Finishes	$ 14.29	4,615,824	$	14.28	4,295,752
C3030	Ceiling Finishes	$ 18.27	5,900,911	$	17.07	5,135,049
D1010	Elevators and Lifts	$ 4.40	1,420,000	$	4.07	1,224,350
D2010	Plumbing Fixtures	$ 1.82	588,455	$	1.65	496,358
D2020	Domestic Water Distribution	$ 5.25	1,694,962	$	7.12	2,141,860
D2030	Sanitary Waste	$ 4.63	1,495,428	$	4.82	1,449,967
D2040	Rain Water Drainage	$ 1.27	411,118	$	1.37	412,128
D2090	Other Plumbing Systems	$ 8.20	2,648,685	$	8.65	2,602,119
D3020	Heat Generating Systems	$ 9.44	3,048,983	$	8.87	2,668,300
D3030	Cooling Generating Systems	$ 9.89	3,194,398	$	15.87	4,774,061
D3040	Distribution Systems	$ 31.30	10,112,317	$	25.68	7,725,135
D3050	Terminal & Package Units	$ 7.86	2,540,100	$	3.50	1,052,881
D3060	Controls & Instrumentation	$ 10.80	3,489,700	$	11.60	3,489,547
D3070	Systems Testing & Balancing	$ 0.98	317,951	$	0.98	294,807
D3090	Other HVAC Systems and Equipment	$ 31.74	10,252,291	$	18.44	5,547,176
D4040	Sprinklers	$ 7.95	2,568,051	$	8.12	2,442,683
D5010	Electrical Service & Distribution	$ 25.23	8,151,449	$	21.32	6,413,546
D5020	Lighting & Branch Wiring	$ 26.26	8,484,377	$	26.56	7,989,859
D5030	Communications & Security	$ 20.92	6,758,292	$	21.27	6,398,505
D5090	Other Electrical Services	$ 24.74	7,993,902	$	22.46	6,756,485
E1020	Institutional Equipment	$ 4.28	1,383,394	$	4.60	1,383,786
E1030	Vehicular Equipment	$ 0.08	25,000	$	0.08	24,066
E1090	Other Equipment	$ 29.72	9,599,951	$	25.92	7,797,332
E2010	Fixed Furnishings	$ 11.01	3,558,025	$	11.17	3,360,193
E2020	Moveable Furnishings		Excl.			-
F2010	Building Elements Demolition	$ 20.18	6,520,500	$	18.06	5,432,863
F2020	Hazardous Components Abatement	$ 21.57	6,967,000	$	20.34	6,118,740
ESTIMATED NET COST		**687.72**	**222,171,851**		**661.18**	**198,898,151**
MARGINS & ADJUSTMENTS						
Design / Estimating Contingency		**6.9%**	17,247,295		7.0%	13,922,871
Escalation to Start of Construction - April 2025 to July 2026		**6.1%**	16,477,328		6.0%	12,769,261
Escalation to Mid-point of Construction - July 2026 to May 2028 (10% - Discounted to reflect early buyout of Main Building)		**6.2%**	17,787,016		4.3%	9,813,155
Tariffs Risk / Market Volatility Contingency					**0.0%**	-
CM/GC Contingency (5%)		**4.9%**	14,895,079		5.0%	11,770,172
General Conditions/General Requirements (49 months duration)		**16.8%**	53,175,430			
General Conditions (49 months duration)			-		9.0%	22,245,625
General Requirements (49 months duration)			-		7.0%	18,859,346
Cranes and hoisting - Incl. Above			Incl.			-
Bonds & Insurance (3%)		**3.0%**	11,114,163		3.0%	8,648,357
Overhead & Profit (3.5%)		**3.5%**	13,355,518		3.5%	10,392,443
Preconstruction Services Allowance		**0.4%**	1,470,000			1,250,000
Preconstruction Services - Sept. 24 to Aug 25 - to match CMGC, as advised		**0.6%**	2,333,921			-
Solar/Green Energy Allowance - Included in Est. Detail			Incl.			Incl.
Total Estimated Construction Cost (in current dollars)		**$ 1,234.29**	**$ 370,027,601**		**$ 1,025.75**	**$ 308,569,381**
Owner Contingency - Excluded, as Advised			Excl.			Excl.
ESTIMATED TOTAL COST		**$ 1,234.29**	**$ 370,027,601**		**$ 1,025.75**	**$ 308,569,381**

Exhibit A

JEFFERSON HS MODERNIZATION

REVISED COMPREHENSIVE PLAN COST MODEL - APRIL 2025

UNIFORMAT LEVEL 3 SUMMARY		323,058			300,823	
Ref	**Description**		**GFA $/SF**	**100% SD Est. Rev.3 Nov - 2024**	**GFA1 $/SF**	**Rev. Cost Model Total Cost $**
G1010	Site Clearing	$	0.01	4,500	$ 0.01	4,500
G1020	Site Demolition & Relocations	$	4.40	1,422,069	$ 4.73	1,422,893
G1030	Site Earthwork	$	30.83	9,958,909	$ 32.96	9,915,126
G2010	Roadways	$	0.87	282,628	$ 0.39	117,321
G2020	Parking Lots	$	1.00	324,375	$ 0.66	198,543
G2030	Pedestrian Paving	$	5.97	1,929,241	$ 6.41	1,928,275
G2040	Site Development	$	25.74	8,316,076	$ 27.64	8,314,748
G2050	Landscaping	$	3.85	1,243,327	$ 4.13	1,242,399
G3010	Water Supply	$	0.71	227,772	$ 0.76	228,625
G3020	Sanitary Sewer	$	0.18	57,610	$ 0.19	57,156
G3030	Storm Sewer	$	7.23	2,334,283	$ 7.31	2,199,016
G3060	Fuel Distribution	$	0.02	5,000	$ 0.02	6,016
G4010	Electrical Distribution	$	0.18	56,600	$ 0.19	57,156
G4020	Site Lighting	$	6.55	2,115,265	$ 6.87	2,066,654
G4030	Site Communication and Security	$	1.36	440,425	$ 1.46	439,202
ESTIMATED NET COST			**88.90**	**28,718,080**	**93.73**	**28,197,632**
MARGINS & ADJUSTMENTS						
	Design / Estimating Contingency		**6.9%**	17,247,295	7.0%	1,973,834
	Escalation to Start of Construction - April 2025 to July 2026		**6.1%**	16,477,328	6.0%	1,810,288
	Escalation to Mid-point of Construction - July 2026 to May 2028 (10% - Discounted to reflect early buyout of Main Building)		**6.2%**	17,787,016	4.3%	1,391,203
	Tariffs Risk / Market Volatility Contingency				**0.0%**	-
	CM/GC Contingency (5%)		**4.9%**	14,895,079	5.0%	1,668,648
	General Conditions/General Requirements (49 months duration)		**16.8%**	53,175,430		
					9.0%	3,153,744
					7.0%	2,673,674
	Cranes and hoisting - Incl. Above			Incl.		-
	Bonds & Insurance (3%)		**3.0%**	11,114,163	3.0%	1,226,071
	Overhead & Profit (3.5%)		**3.5%**	13,355,518	3.5%	1,473,328
	Preconstruction Services Allowance		**0.4%**	1,470,000		250,000
	Preconstruction Services - Sept. 24 to Aug 25 - to match CMGC, as advised		**0.6%**	2,333,921		-
	Solar/Green Energy Allowance - Included in Est. Detail			Incl.		Incl.
Total Estimated Construction Cost (in current dollars)		**$**	**1,234.29**	**$ 176,573,830**	**$ 145.66**	**$ 43,818,422**
	Owner Contingency - Excluded, as Advised			Excl.		Excl.
ESTIMATED TOTAL COST		**$**	**1,234.29**	**$ 176,573,830**	**$ 145.66**	**$ 43,818,422**


Exhibit A

EXHIBIT 10
DRAFT CONSTRUCTION SCHEDULE

Jefferson HS Modernization

RLB Rider Levett Bucknall

Activity ID	Activity Name	Original Duration	Start	Finish
Jefferson HS Modernization		1420	04/21/25	12/24/30
Milestones and Summaries		985	01/15/27	12/24/30
MIL-1000	Early Fields Completed	0		01/15/27
MIL-1010	New Building Ready for Use	0		08/31/29*
MIL-1020	Phase 3 Complete	0		12/24/30
Design		446	04/21/25	02/02/27
Early Fields		231	04/21/25	03/24/26
DES-EF-1000	Develop 100% Design Documents-Early Fields	90	04/21/25*	08/27/25
DES-EF-1010	Review 100% Design Documents-Early Fields	10	08/28/25	09/11/25
DES-EF-1020	Develop 50% Construction Documents- Early Fields	70	08/28/25	12/09/25
DES-EF-1030	Review 50% Construction Documents- Early Fields	10	12/10/25	12/23/25
DES-EF-1040	Develop 100% Construction Documents- Early Fields	60	12/10/25	03/09/26
DES-EF-1050	Review 100% Construction Documents - Early Fields	10	03/10/26	03/23/26
DES-EF-1060	Issue IFC Documents- Baseball and Softball Fields	1	03/24/26	03/24/26
New School Building		446	04/21/25	02/02/27
DES-NB-1000	Develop 100% Schematic Design- New School Building	110	04/21/25	09/25/25
DES-NB-1010	Review 100% Schematic Design- New School Building	10	09/26/25	10/09/25
DES-NB-1020	Develop 25% Design Development- New School Building	50	09/26/25	12/09/25
DES-NB-1030	100% SD Cost Estimate - New School Building	30	10/10/25	11/24/25
DES-NB-1040	Develop 100% Design Development- New School Building	80	12/10/25	04/06/26
DES-NB-1050	Review 100% Design Development- New School Building	10	04/07/26	04/20/26
DES-NB-1060	100% CD Cost Estimate - New School Building	35	04/07/26	05/26/26
DES-NB-1070	Develop 50% Construction Development- New School Building	90	04/07/26	08/13/26
DES-NB-1080	Review 50% Construction Development- New School Building	10	08/14/26	08/27/26
DES-NB-1090	Develop 100% Construction Development- New School Building	70	08/14/26	11/24/26
DES-NB-1100	Review 100% Construction Development- New School Building	20	11/25/26	12/23/26
DES-NB-1110	CD Comment Reconciliation	25	12/24/26	02/01/27
DES-NB-1120	Issue IFC Documents	1	02/02/27	02/02/27
Permits		355	09/12/25	02/16/27
PER-1000	Type II Conditional Use- Early Fields	60	09/12/25	12/09/25
PER-1010	Permit A- Early Fields	80	12/10/25	04/06/26
PER-1020	Demolition Permit for Permit A	80	12/10/25	04/06/26
PER-1030	Type III Conditional Use	125	12/10/25	06/09/26
PER-1040	Type II- Historic Review	90	02/02/26	06/09/26
PER-1050	Demolition Permit for Remaining Works	80	06/10/26	10/02/26
PER-1060	Permit B- Foundation to Grade	90	06/10/26	10/19/26
PER-1070	HRI Removal	120	06/10/26	12/02/26
PER-1080	Permit C- Building Permit	80	10/20/26	02/16/27
Contract Procurements		210	12/10/25	10/09/26
PRC-1000	Early Fields GMP	40	12/10/25	02/06/26
PRC-1010	New Building 50% CD GMP-	40	08/14/26	10/09/26
Construction		1180	04/07/26	12/24/30
Phase 1- Early Fields		195	04/07/26	01/15/27
CON-EF-1000	Softball Field Construction	85	04/07/26	08/06/26

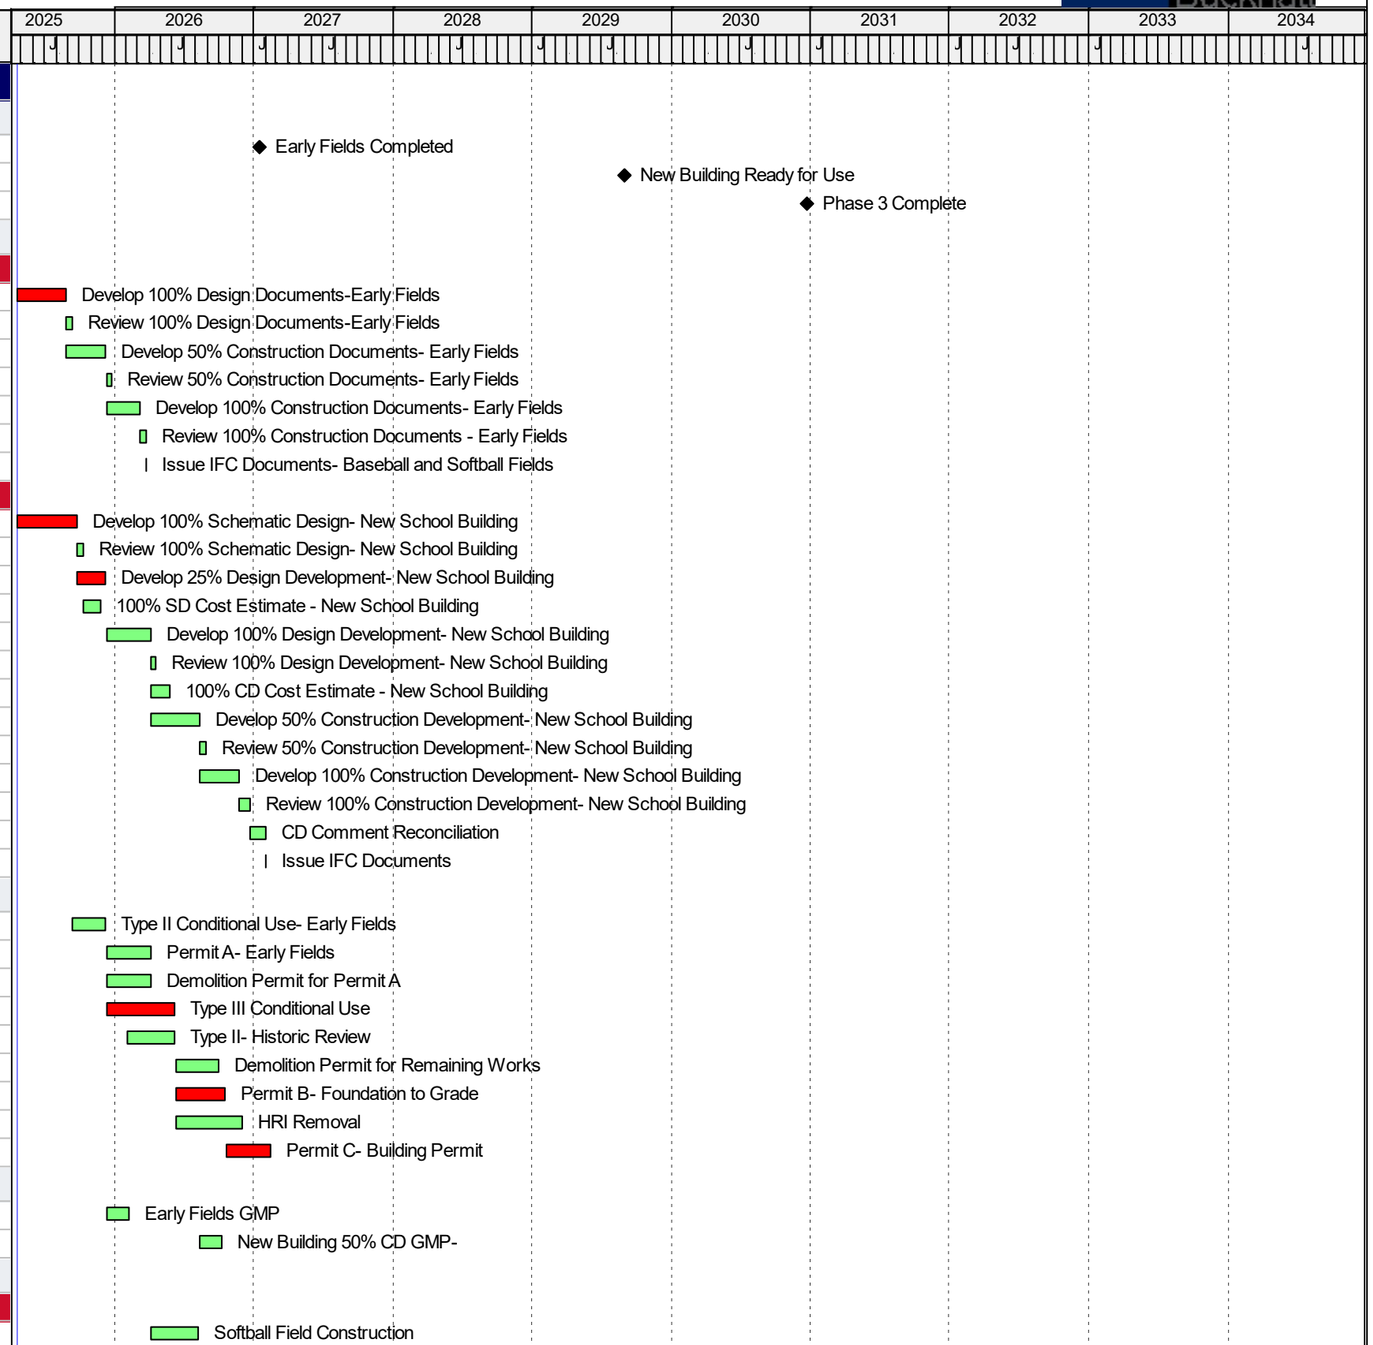

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone

Data Date: 04/21/25

Date	Revision	Checked	Approved


Exhibit A

EXHIBIT 10
DRAFT CONSTRUCTION SCHEDULE

Jefferson HS Modernization

RLB Rider Levett Bucknall

Activity ID	Activity Name	Original Duration	Start	Finish
CON-EF-1010	Baseball Field Construction	110	08/07/26	01/15/27
Phase 2- New Building Construction		718	10/20/26	08/31/29
CON-NB-1000	Site Preparation / Mobilization	80	10/20/26	02/16/27
CON-NB-1010	Foundations / Slab on Grade/ UG MEP	90	02/17/27	06/24/27
CON-NB-1020	Structure	150	06/25/27	02/01/28
CON-NB-1030	Exterior Skin	240	08/30/27	08/14/28
CON-NB-1040	Roof	200	09/28/27	07/17/28
CON-NB-1050	Rough In / Framing and Interior Finishes	390	10/27/27	05/17/29
CON-NB-1060	Site Work	200	02/02/28	11/15/28
CON-NB-1070	New Building Punch, Commissioning and TCO	50	04/06/29	06/15/29
CON-NB-1080	Move New Items From Old Building into New Building	40	06/18/29	08/14/29
CON-NB-1090	Contingency	13	08/15/29	08/31/29
Phase 3- Demo, Track, Fields and Site Works		340	08/15/29	12/24/30
CON-TF-1000	Current Building Demolition / Abatement	150	08/15/29	03/22/30
CON-TF-1010	Building Football / Tennis Fields	150	02/08/30	09/12/30
CON-TF-1020	Site Works	60	06/04/30	08/28/30
CON-TF-1030	Punch, Commissioning and Close out	70	09/13/30	12/24/30

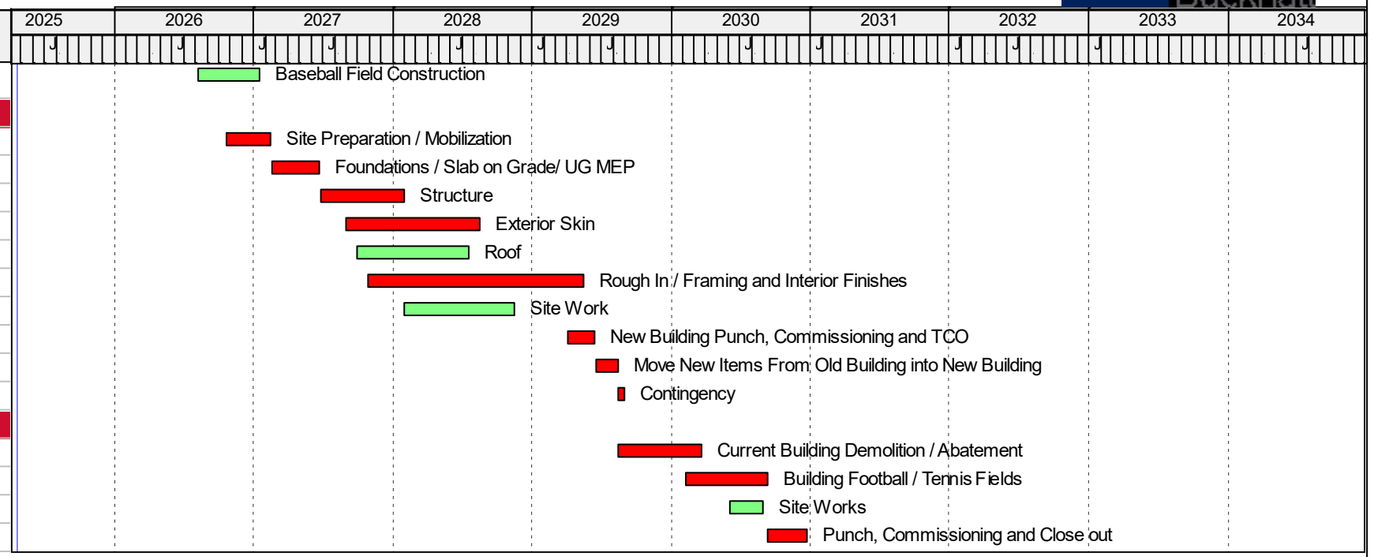

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone

Data Date: 04/21/25

Date	Revision	Checked	Approved
