


Jefferson High School Modernization

PPS School Board Meeting

October 14th, 2025


PORTLAND PUBLIC SCHOOLS

Current Plan Overview

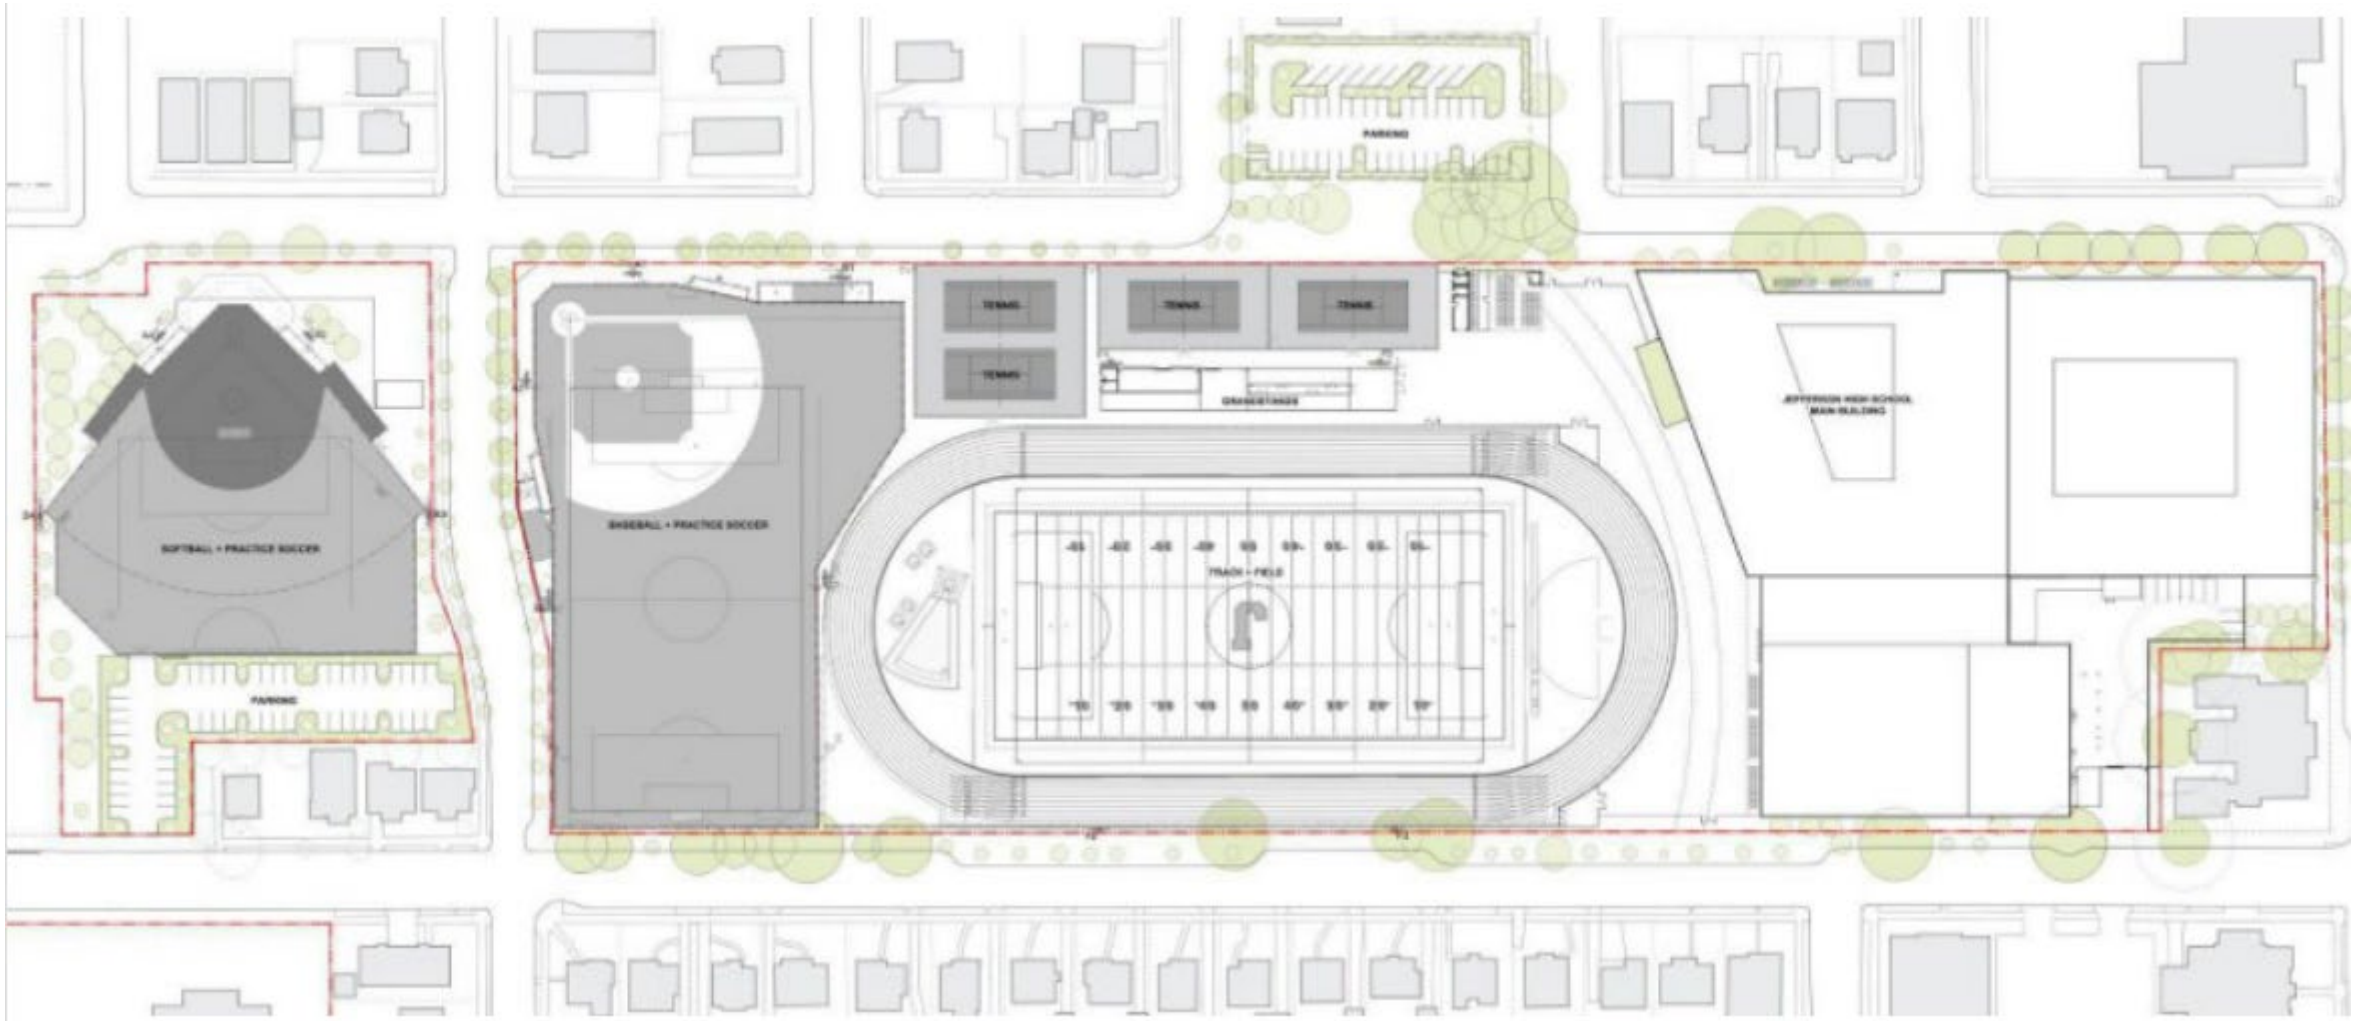


Cost Reduction Study Review

Previous Design

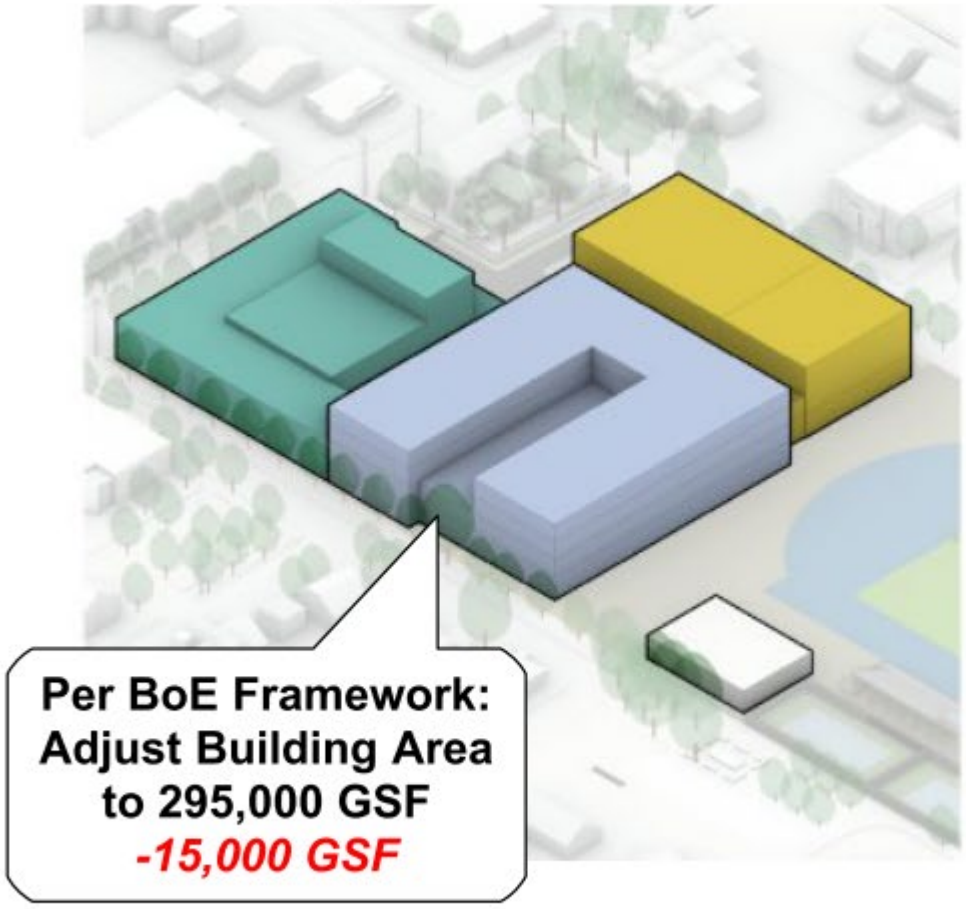


Updated Design

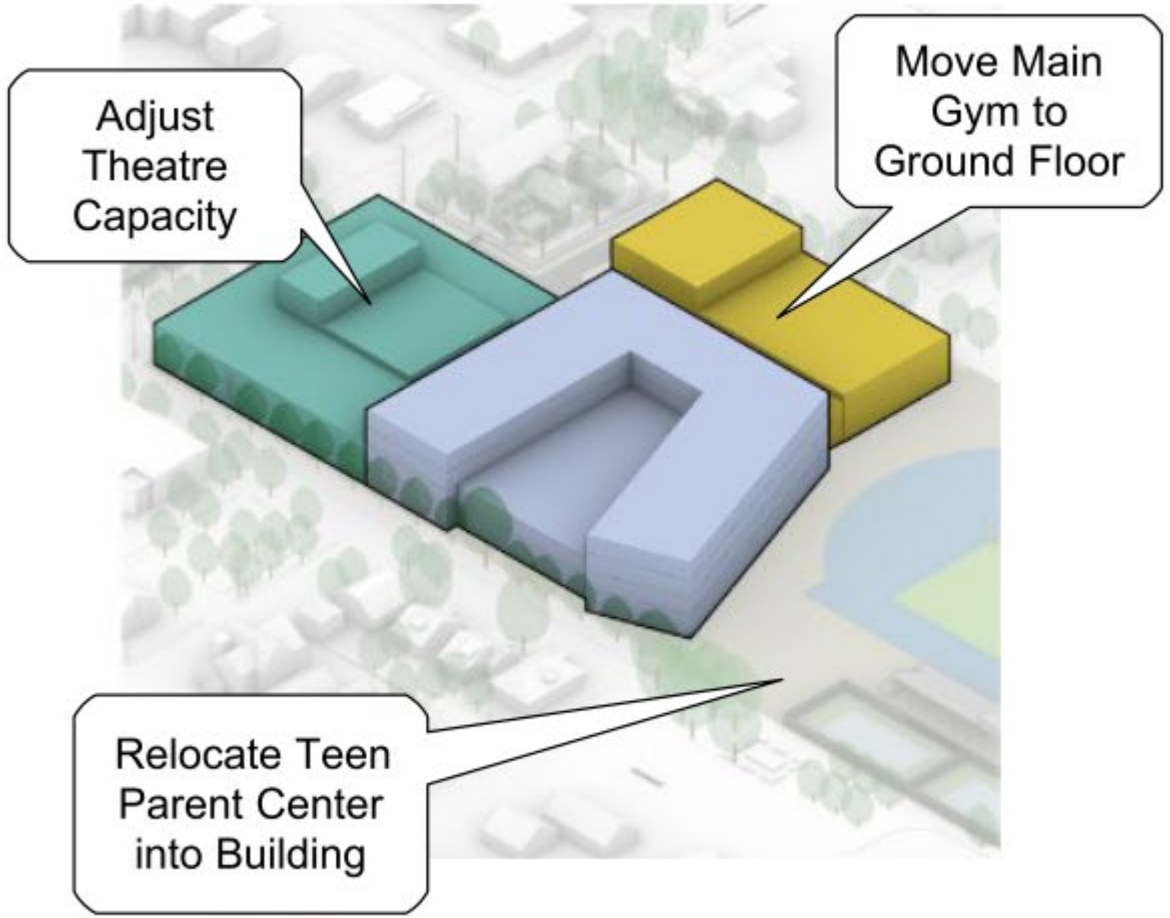


ACADEMICS PERFORMING ARTS ATHLETICS

Floor Plan Overview – Level 1

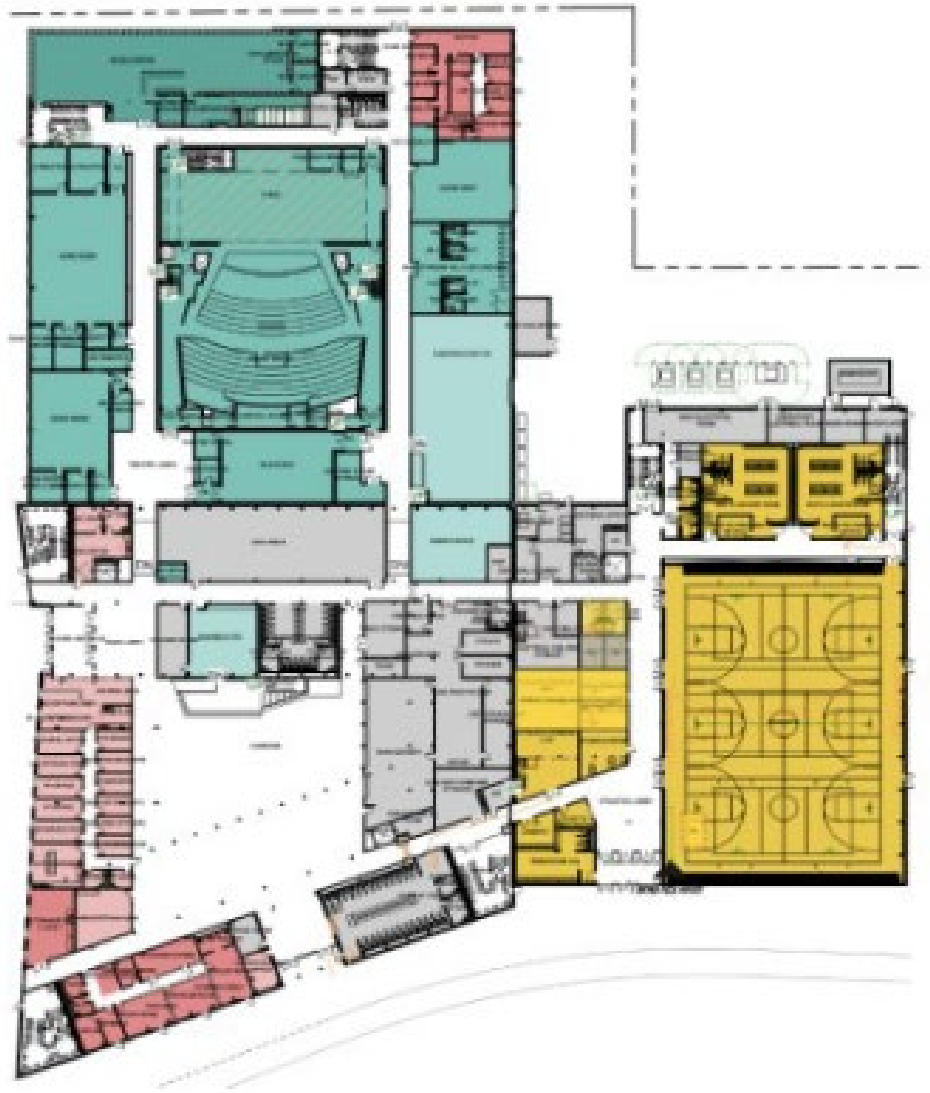


- ADMIN, COUNSELING & CAREER
- COMMUNITY & PARTNERS
- GENERAL CLASSROOMS & SCIENCE
- SPED
- FINE / GRAPHIC ARTS & CTE
- PERFORMING ARTS
- MEDIA CENTER
- ATHLETICS
- BUILDING SUPPORT

Floor Plan Overview – Levels 2 through 4

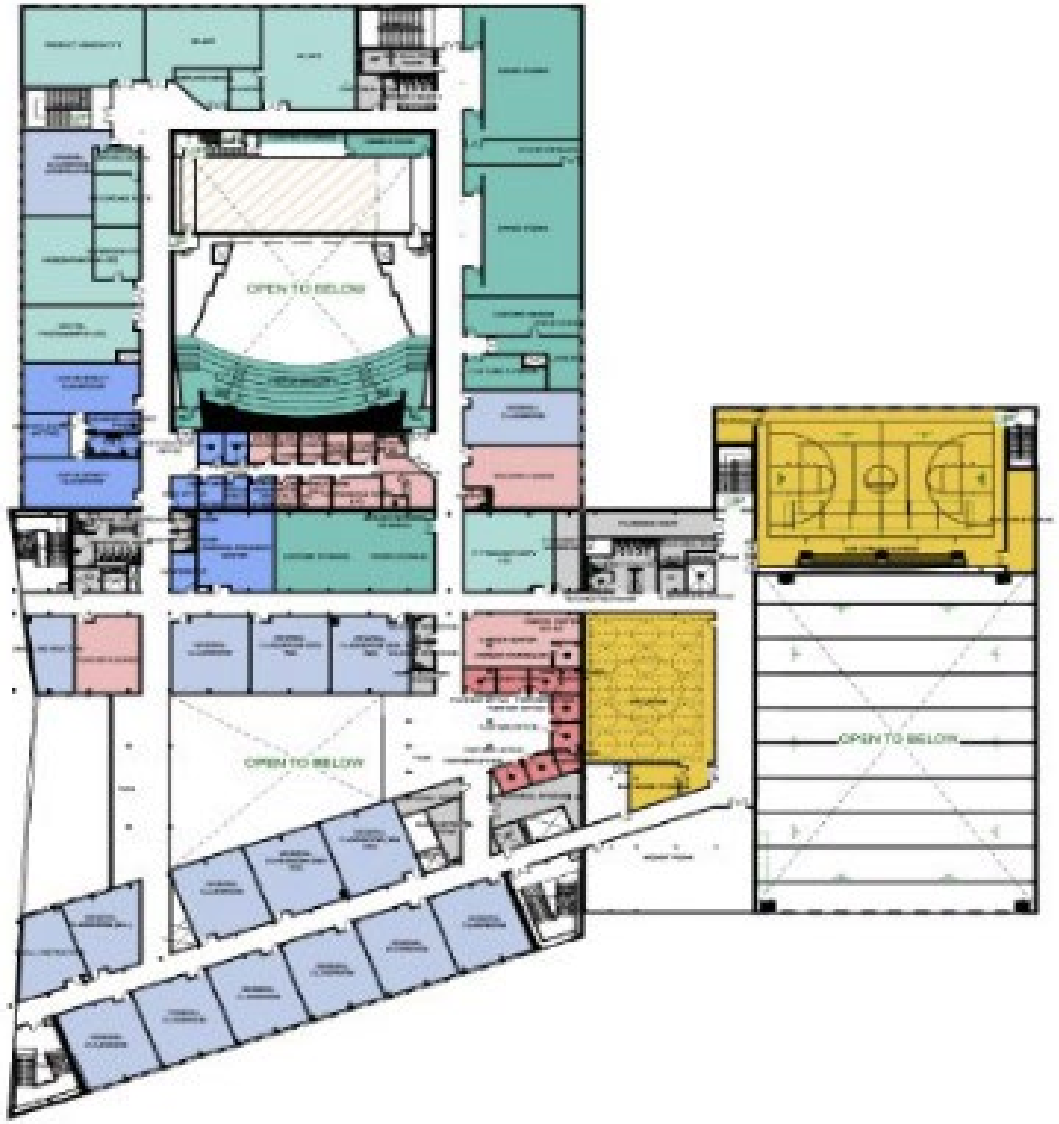



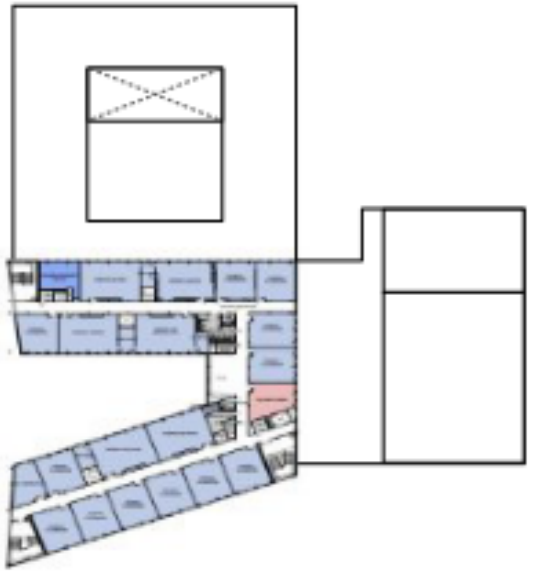


PPS Comprehensive Education Specifications


Ed Spec Minimum
Building Area
284,190 GSF

Previous Design – 50% DD
(EdSpec+)
Building Area
311,139 GSF

2025 Comprehensive Plan
Building Area
299,044 GSF
-Reduction of 12,095 SF from 50% DD
-5,233 GSF of additional Mech/Elec for All Elec
-293,811 GSF

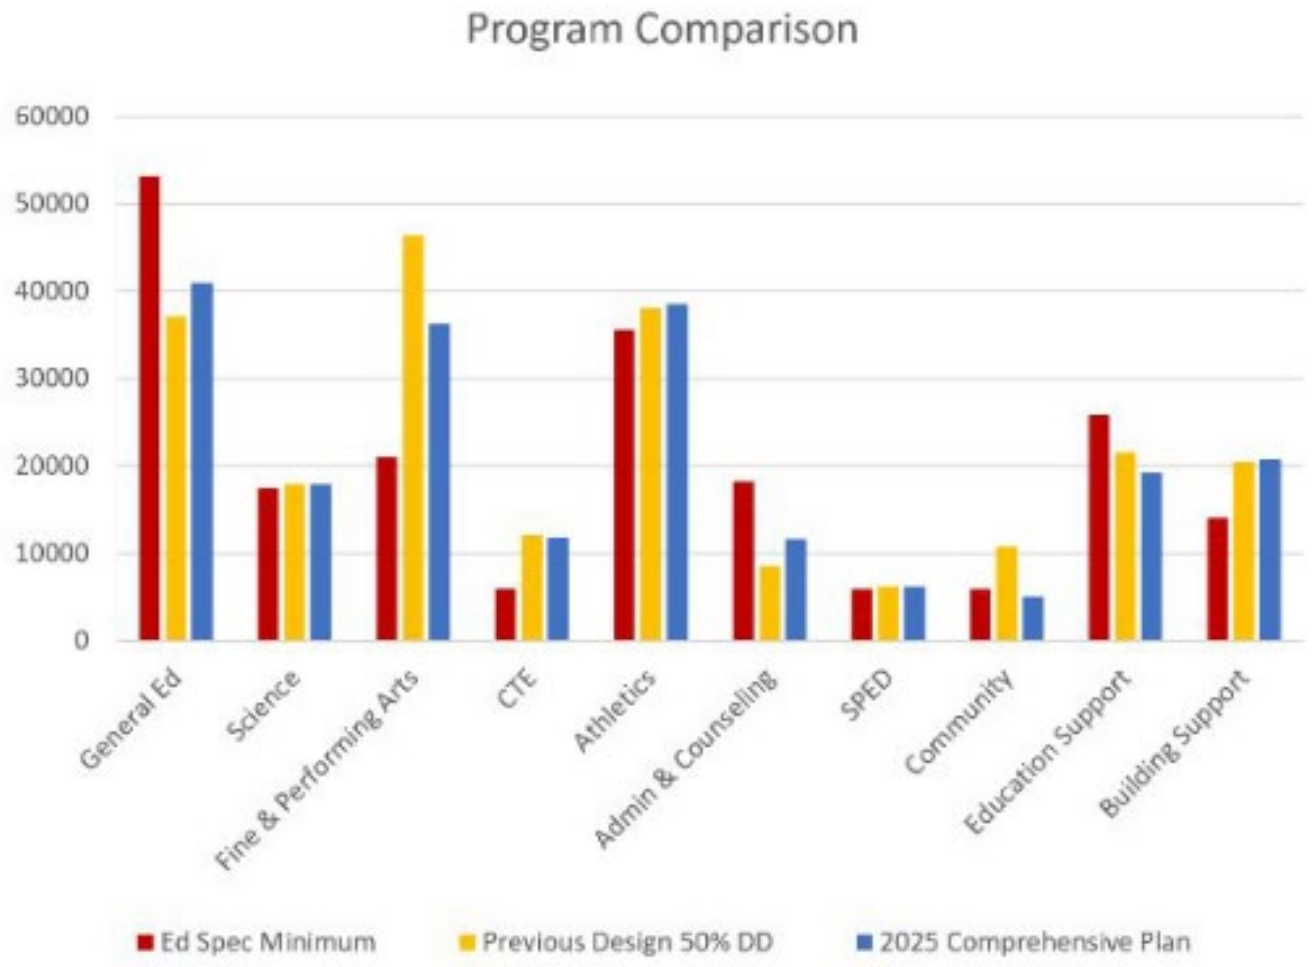

Jefferson HS Overall Project Schedule

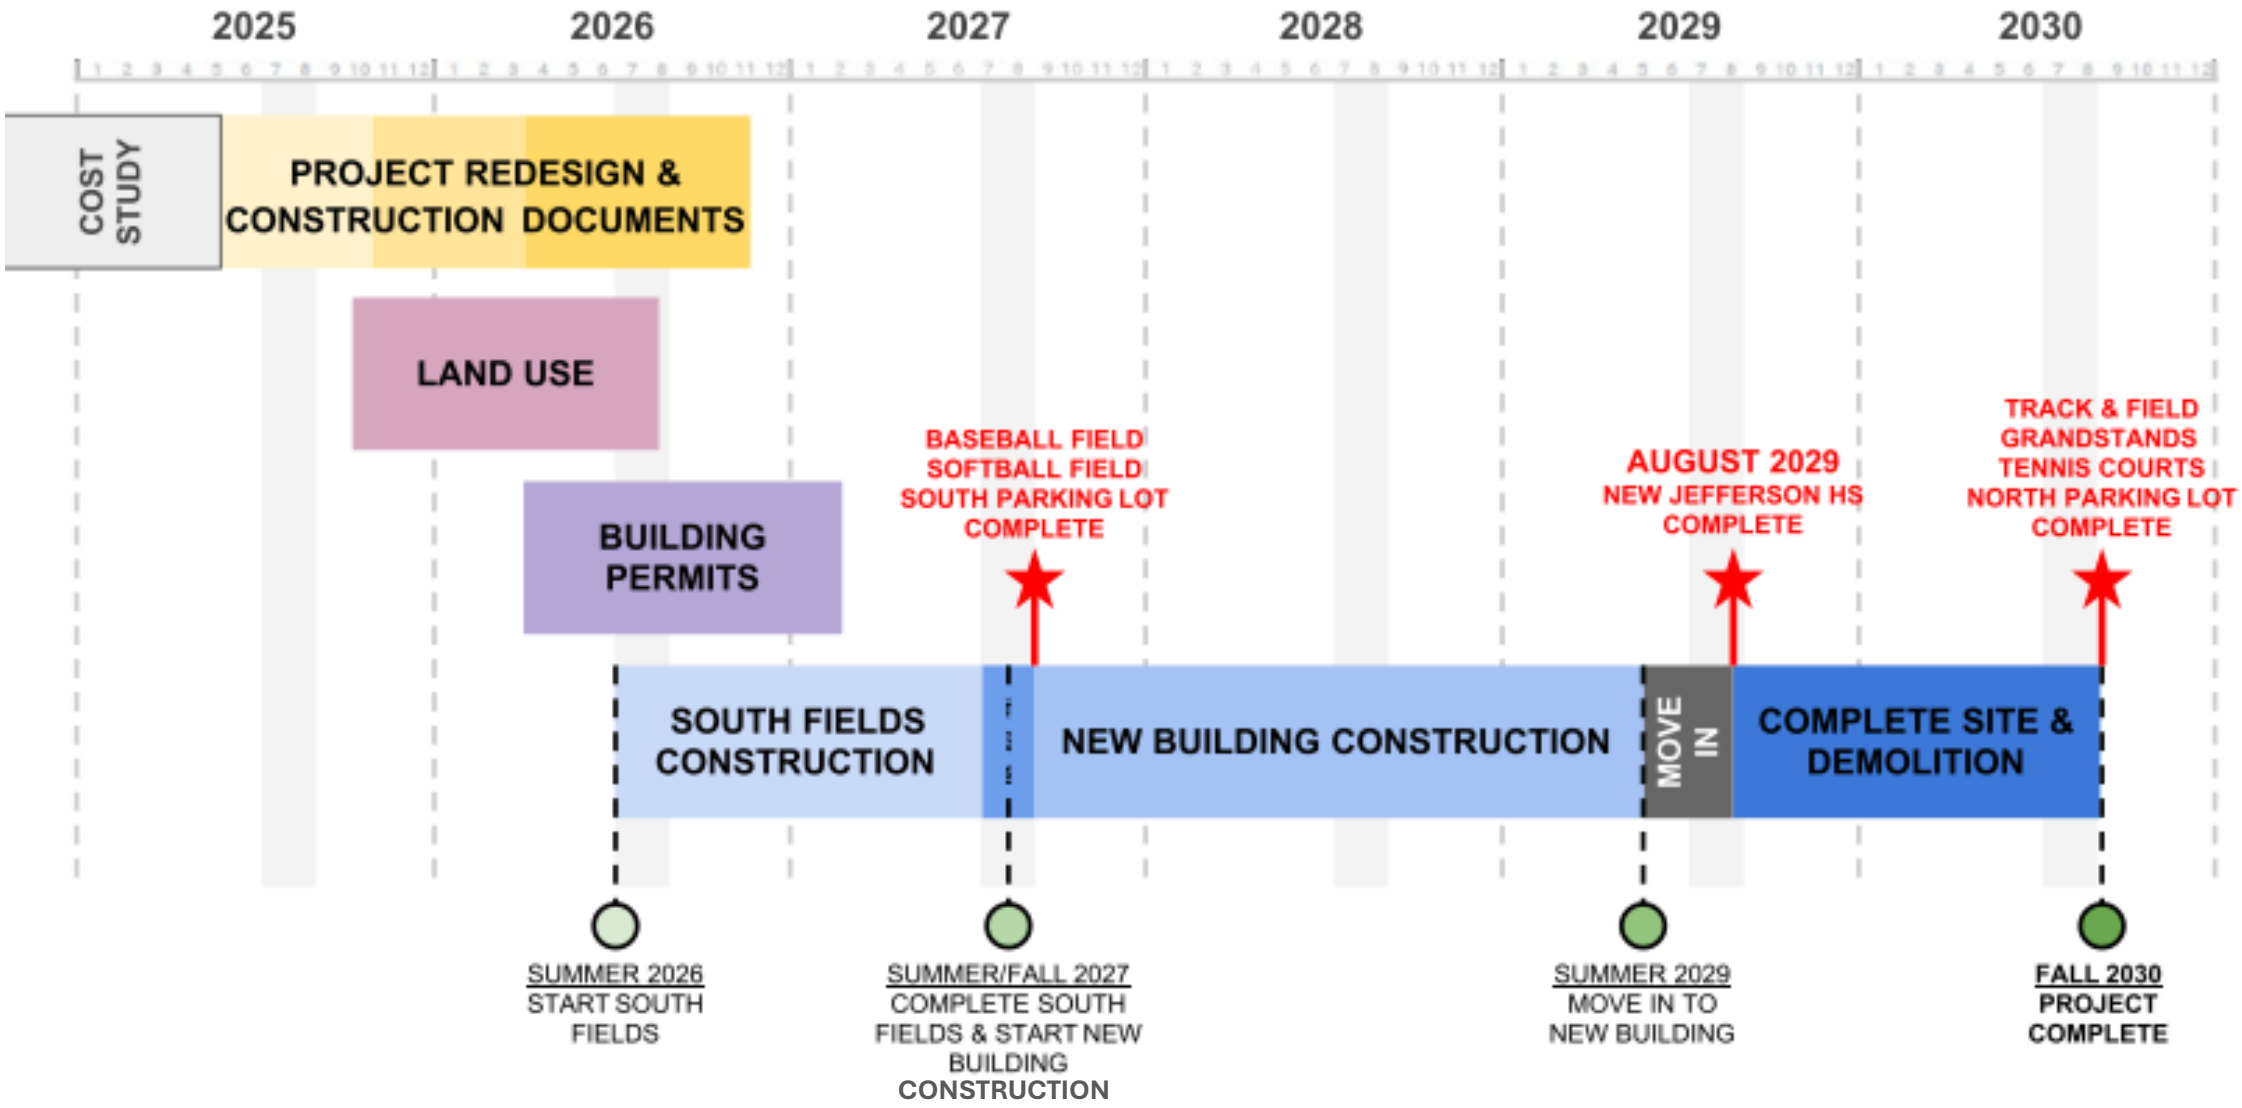

Updated Budget Summary

JHS MODERNIZATION BUDGET SUMMARY		2022	2023	2025
COMPONENT	**COMMENTS**	**BOE APPROVED COMPREHENSIVE PLAN**	**BOE APPROVED PROJECT PIVOT**	**CURRENT REVISED COMPREHENSIVE PLAN**
Hard Cost	Building & Site Work 2025: Includes actuals paid-to-date to CM/GC	$ 284,185,237	$ 407,397,113	$ 357,601,866
1.5% Green Energy Tech		$ 3,450,423	Included in Hard Cost Estimate	
Subtotal		**$ 287,635,660**	**$ 407,397,113**	**$ 357,601,866**
Owner Direct Hard Costs	Potential additional public improvements,hazardous materials abatement not included in Hard Cost 2025: Added allowance for potential additional off-site improvements	**$ 3,422,000**	**$ 1,900,000**	**$ 3,900,000**
TOTAL HARD COSTS		**$ 291,057,660**	**$ 409,297,113**	**$ 361,501,866**
Soft Costs	Approx. 12% of Hard Costs (includes design, engineering,consultant services, permitting,moving, insurance) 2025: Includes Added Redesign Costs	$ 33,338,529	$ 42,007,914	$ 50,513,864
Fixtures, Furniture & Equipment, including technology	Approx. $34 per SF	$ 8,360,250	$ 9,988,000	$ 10,500,000
Moves / Swing Space / Temp Facilities		n/a	n/a	$ 800,000
Contingency	2022: 10% of Total Costs (additional 5% CM/GC contingency included in Hard Cost Estimate) 2023: 10% minus $16,669,553 CM/GC contingencyincluded in Hard Cost Estimate 2025: 10% of Total Costs (additional 5% CM/GC contingency included in Hard Cost Estimate)	$ 33,243,561	$ 29,459,770	$ 42,691,769
Escalation	Included in Hard & Soft Costs	Included in Hard & Soft Costs Above		
TOTAL PROJECT BUDGET		**$ 366,000,000**	**$ 490,752,797**	**$ 466,007,500**
SAVINGS FROM 2023 DESIGN				**$ (24,745,297)**

Next Steps

- Schematic Design (SD) Phase Approval: REVIEW PHASE
  - Document review by internal OSM staff
  - Page turn reviews by district stakeholders
  - Estimating by RLB (Design Team Estimating Consultant)

- New CM/GC Contractor – COLAS/HOFFMAN
  - Contractor Estimating based on 8/29/25 SD drawings
  - Construction Logistics/Phasing/Schedule Workshops/OACs

- Community Engagement
  - Back to School Nights
  - Community Information Session: October 15th @ Jefferson
