


Cleveland High School Modernization

Comprehensive Plan Update

October 14th, 2025

PORTLAND PUBLIC SCHOOLS

Site Opportunities and Constraints

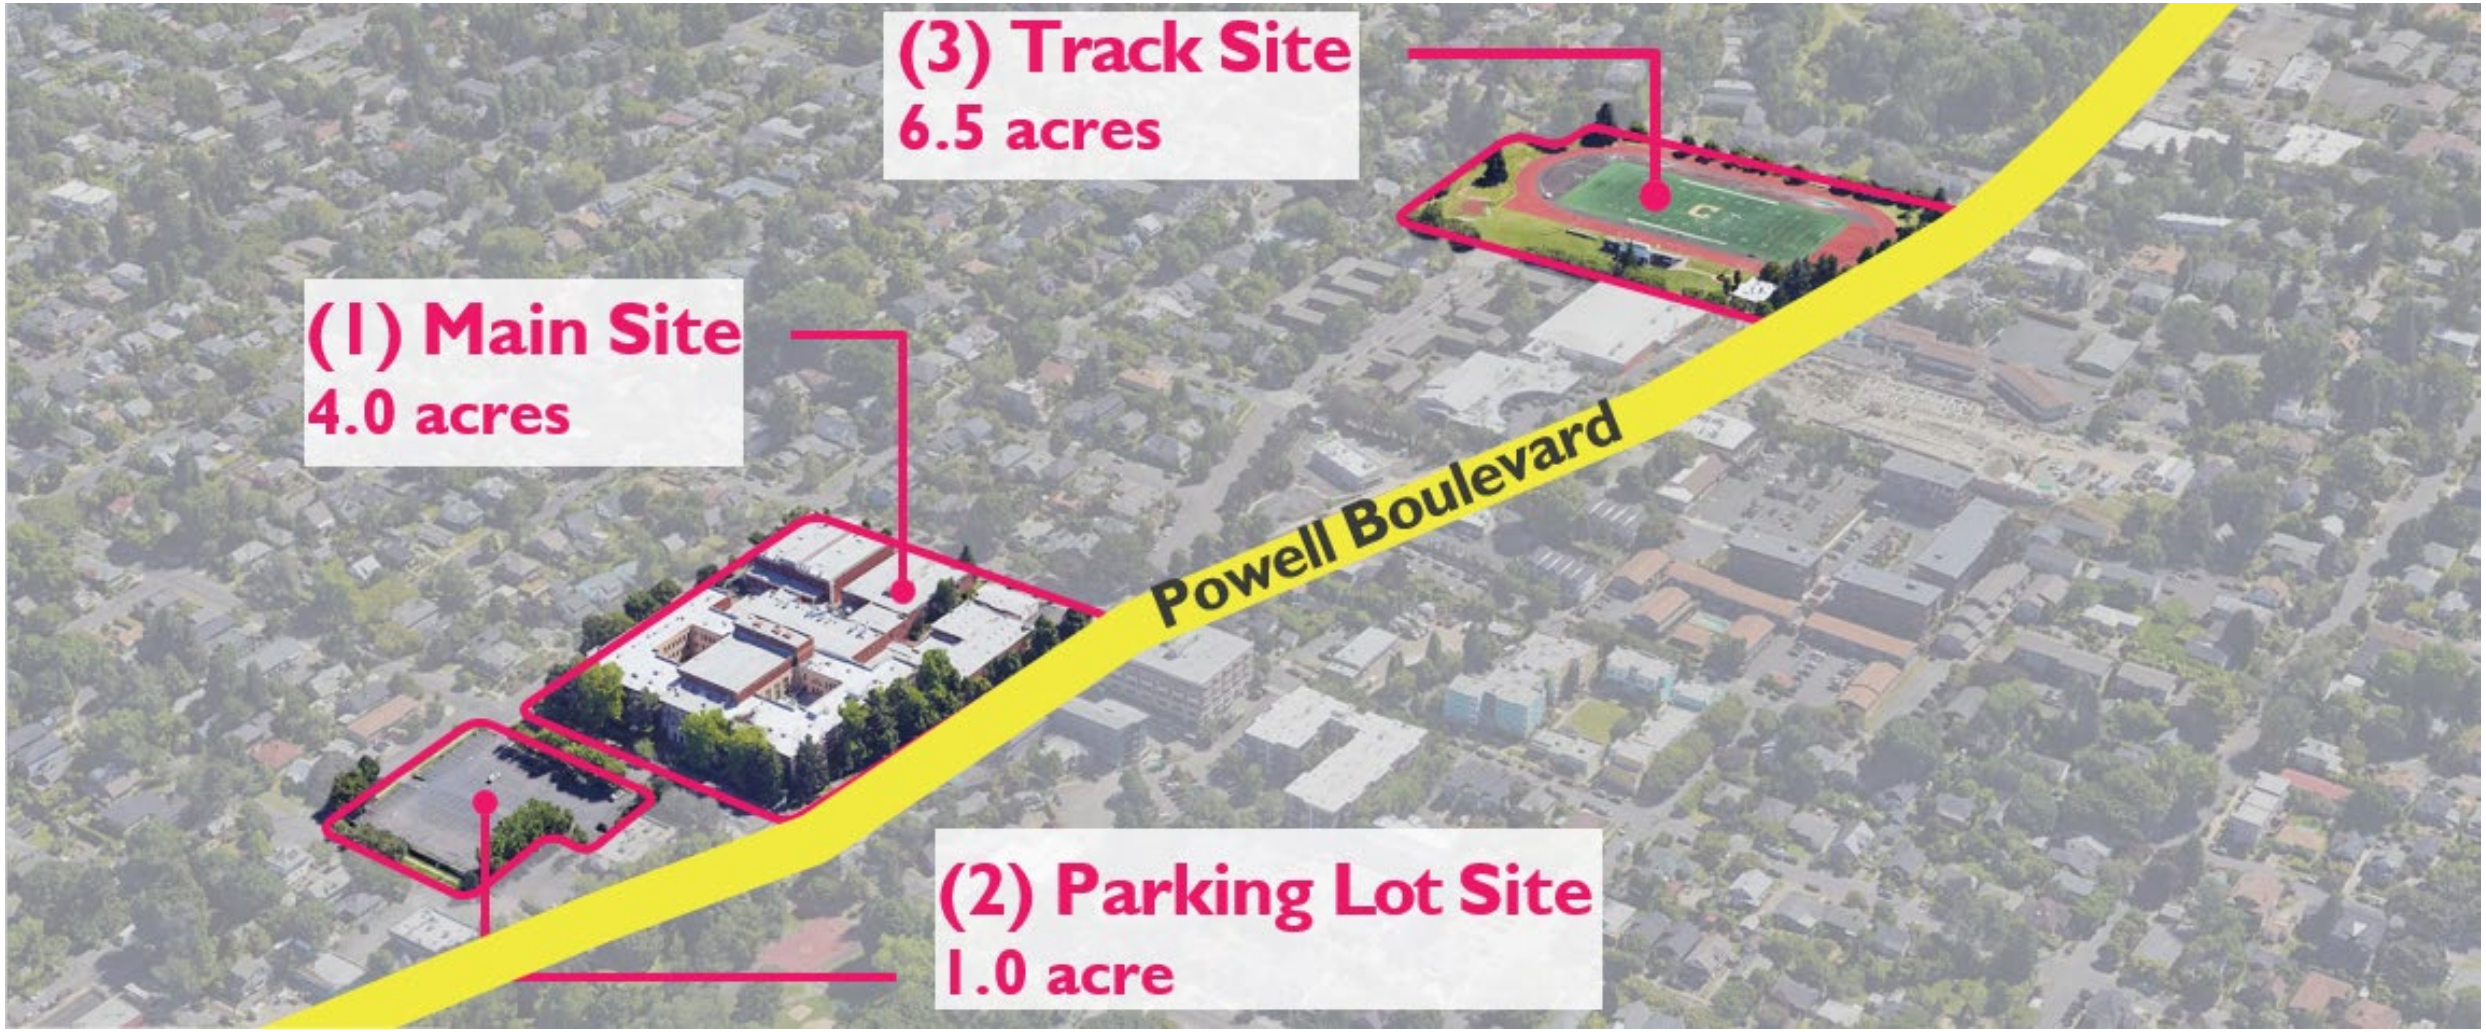

Site Opportunities & Constraints / Proposed Design




CURRENT CHS BUILDING
254,000 SF

- 4-acre Main Site; smallest in district
- On Powell Boulevard (state highway)
- 2-3 story configuration fills entire site
- No secure outdoor space for students
- No extra space for construction logistics
- Opportunity to create secure open space in new design
- Opportunity to reduce construction logistics costs with smaller building footprint



PROPOSED BUILDING
APPROX. 297,000 SF

Area Program Comparison

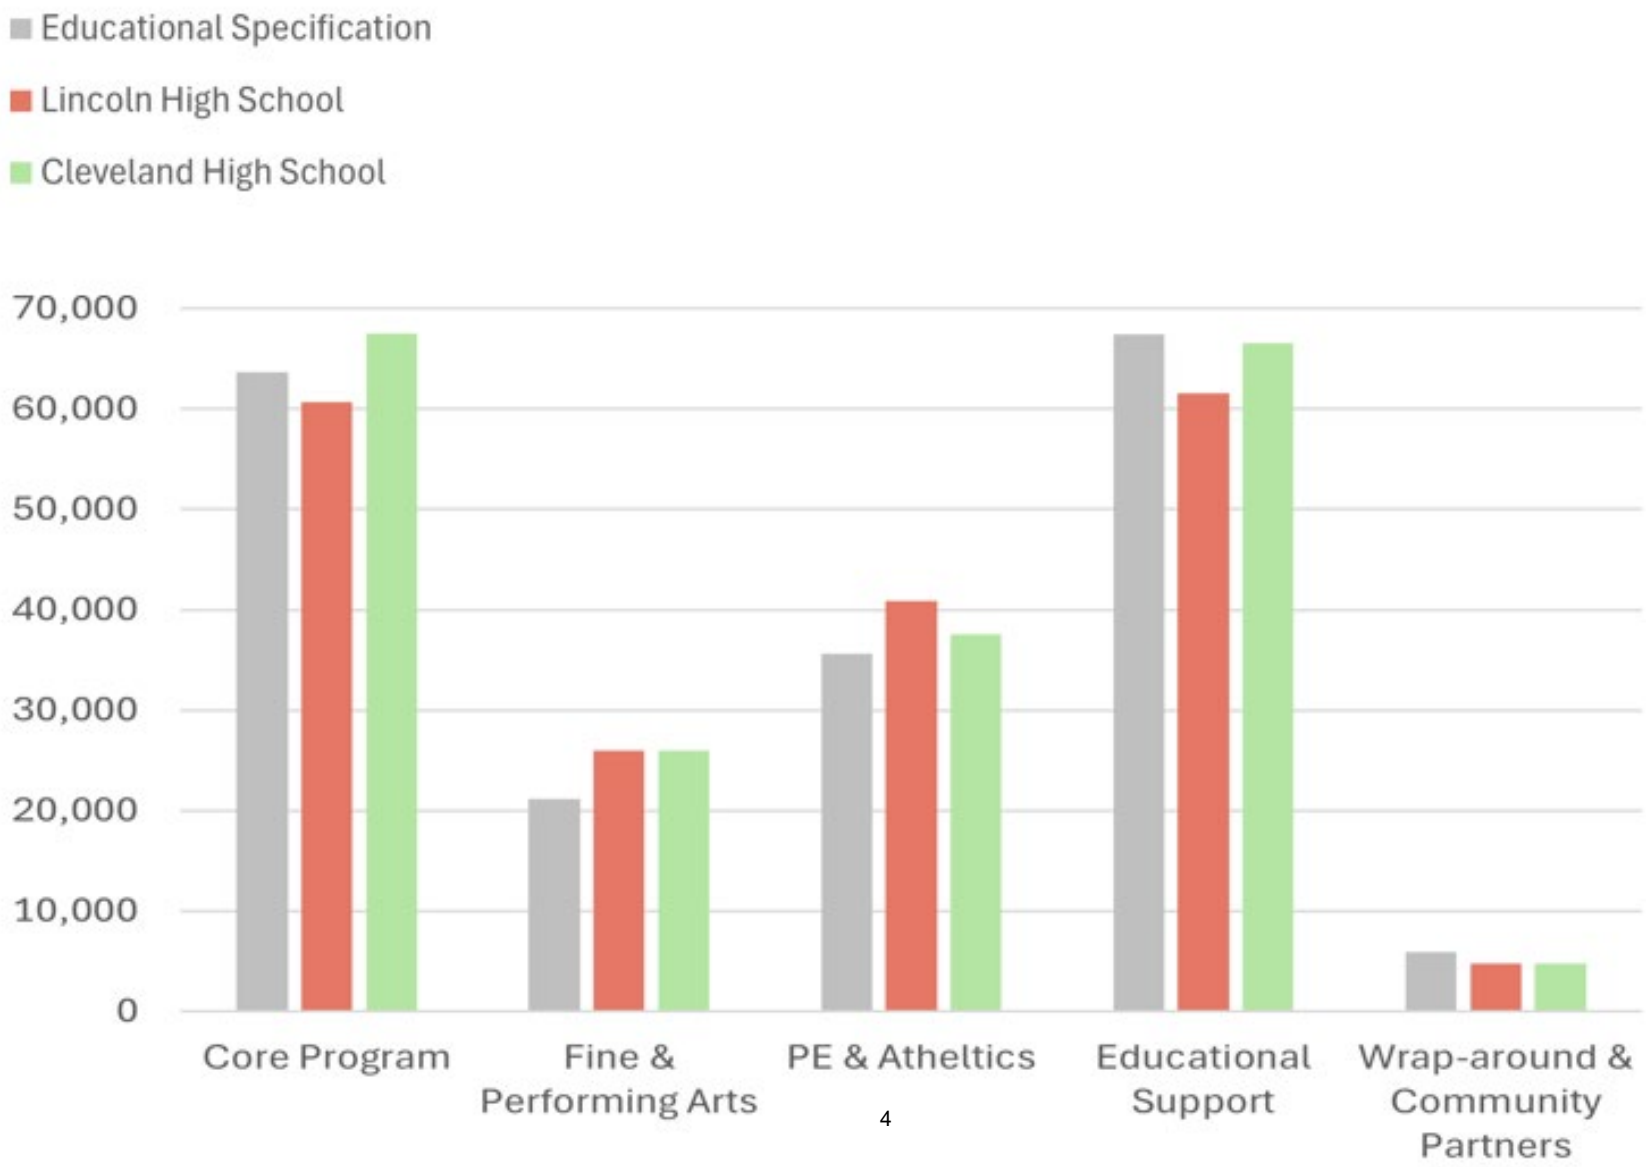

Building Design: Floor Plan Updates

L01

- FLEX LEARNING
- SPED + LRC
- CTE
- VISUAL + PERFORMING ARTS
- WRAP-AROUND SERVICES
- GYM + ATHLETICS
- MISCELLANEOUS
- CUSTODIAL



L02

- ADMIN / STUDENT SPACE
- COUNSELING / CAREER
- FLEX LEARNING
- SPED + LRC
- GENERAL CLASSROOMS
- VISUAL + PERFORMING ARTS
- STUDENT COMMONS
- GYM + ATHLETICS
- MISCELLANEOUS
- CUSTODIAL



Building Design: Floor Plan Updates

L03

- ADMIN / STUDENT SPACE
- LIBRARY / MEDIA CENTER
- FLEX LEARNING
- SPED + LRC
- GENERAL CLASSROOMS
- CTE
- VISUAL + PERFORMING ARTS
- MISCELLANEOUS
- CUSTODIAL



L04


- ADMIN / STUDENT SPACE
- FLEX LEARNING
- SPED + LRC
- GENERAL CLASSROOMS
- CTE
- MISCELLANEOUS
- CUSTODIAL



Building Design: Floor Plan Updates

Updated Athletic Fields

- Reduced size of Field House
- Number of team rooms from 3 to 2
- Storage building is now an Add Alternate
- Batting Facility/Multi-purpose space
- New Practice Field
- Updated Field lighting
- Replacement of Main Field turf

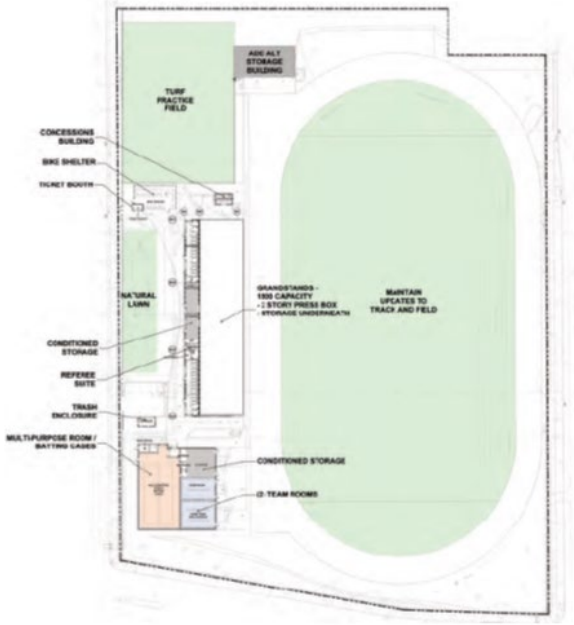


Potential Powell Park Improvements

- Baseball Field & Multi-Purpose Field for Soccer and Lacrosse
- Separate Softball Field



CHS Overall Project Schedule

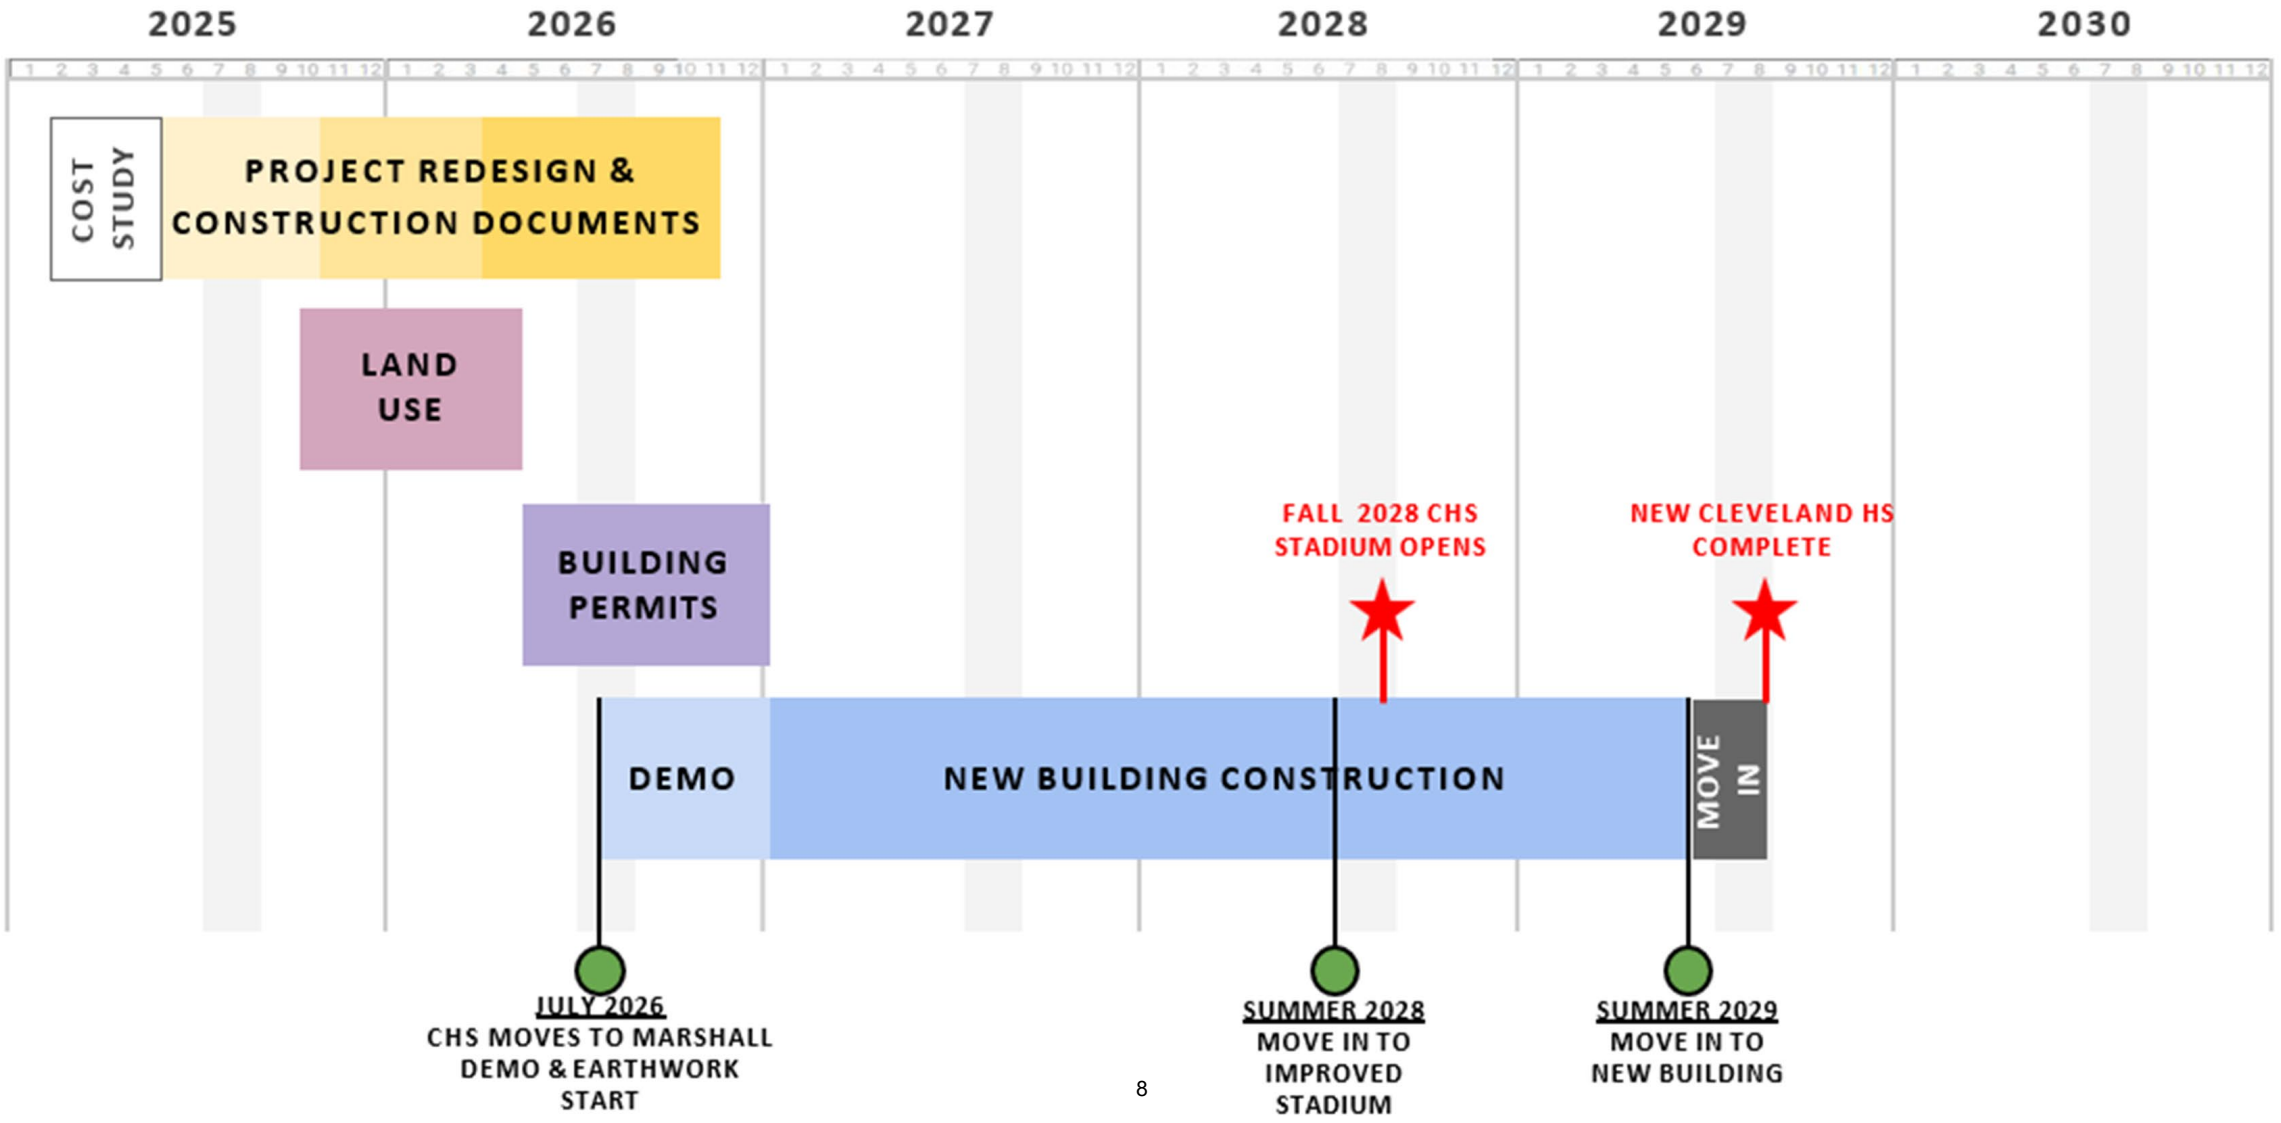

Updated Project Budget

CHS MODERNIZATION BUDGET SUMMARY

		2024	2025
COMPONENT	**COMMENTS**	**BOE APPROVED COMPREHENSIVE PLAN**	**REVISED COMPREHENSIVE PLAN**
Hard Cost	Building & Site Work 2025: Includes actuals paid-to-date to CM/GC	$ 377,654,178	$ 364,284,431
1.5% Green Energy Tech		$ 5,664,813	$5,529,547
Subtotal		**$ 383,318,991**	**$ 369,813,978**
Owner Direct Hard Costs	Off site improvements, utility costs not included above	**$ 1,650,000**	**$ 1,200,000**
TOTAL HARD COSTS		$ 384,968,991	**$ 371,013,978**
Soft Costs	Approx. 9.5% of Hard Costs	$ 33,155,000	$ 34,580,000
Fixtures, Furniture & Equipment, including technology	Approx. $34/SF	$ 8,700,000	$ 10,000,000
Moves / Swing Space / Temp Facilities		$500,000	$1,500,000
Contingency	10% of Total Costs (additional 5% CM/GC contingency included in Hard Cost Estimate)	$ 41,320,859	$ 40,459,782
Escalation	Included in Hard & Soft Costs		
MAIN BUILDING BUDGET		**$ 468,644,850**	**$ 457,553,760**
SAVINGS FROM 2024 DESIGN			**$(11,091,090)**
OFF SITE ATHLETIC FIELDS	Work may include fields at Powell park and/or Hosford MS		**$15,000,000**
TOTAL PROJECT BUDGET			**$472,553,760**

Next Steps

- Design Development Phase
  - Ongoing design review with PPS stakeholder
  - 75% DD milestone documents to be issued October 24th
  - New cost estimates to follow 75% documents

- Preconstruction Services – CMGC
  - Skanska to issue trade partner preconstruction service contracts with MEPO and Framing subcontractors

- Community Engagement
  - Design Advisory Group (DAG) - September 18th, 2025
  - Community Design Workshop - October 4th, 2025
  - Sellwood MS - October 16th, 2025
