Bond Program Update



PORTLAND
Public Schools

Date January 13, 2026


Current Tasks

- Meeting cadence and collaboration with Program Directors
- Procurement schedule
- Project timeline schedules




Procurement Schedule

Activity Name	Duration	Start	Finish
PROCUREMENT			
PHASE 1 Program Geotechnical Services			
BID ADVERTISEMENT POSTED	0	09-Jan-26*	
DEADLINE ISSUING ADDENDA	0	23-Jan-26*	
RFP OPENING DATE	0	29-Jan-26*	
NOTICE TO AWARD ISSUED	0	13-Feb-26*	
AGENDA DEADLINE TO PPS	0	24-Mar-26*	
PPS BOARD MEETING	0	14-Apr-26*	
PHASE 2 Program Testing & Balancing, Traffic Control Services			
BID ADVERTISEMENT POSTED	0	16-Jan-26*	
DEADLINE ISSUING ADDENDA	0	30-Jan-26*	
RFP OPENING DATE	0	05-Feb-26*	
NOTICE TO AWARD ISSUED	0	20-Feb-26*	
AGENDA DEADLINE TO PPS	0	07-Apr-26*	
PPS BOARD MEETING	0	28-Apr-26*	
PHASE 3 Program - Structural/Civil Engineering Services, Cx Services, Surveying, Envelope Consultant, Job Order Contracting - GC, Zoning/Planning/Permitting A&E			
BID ADVERTISEMENT POSTED	0	23-Jan-26*	
DEADLINE ISSUING ADDENDA	0	09-Feb-26*	
RFP OPENING DATE	0	23-Feb-26*	
NOTICE TO AWARD ISSUED	0	09-Mar-26*	
AGENDA DEADLINE TO PPS	0	21-Apr-26*	
PPS BOARD MEETING	0	12-May-26*	

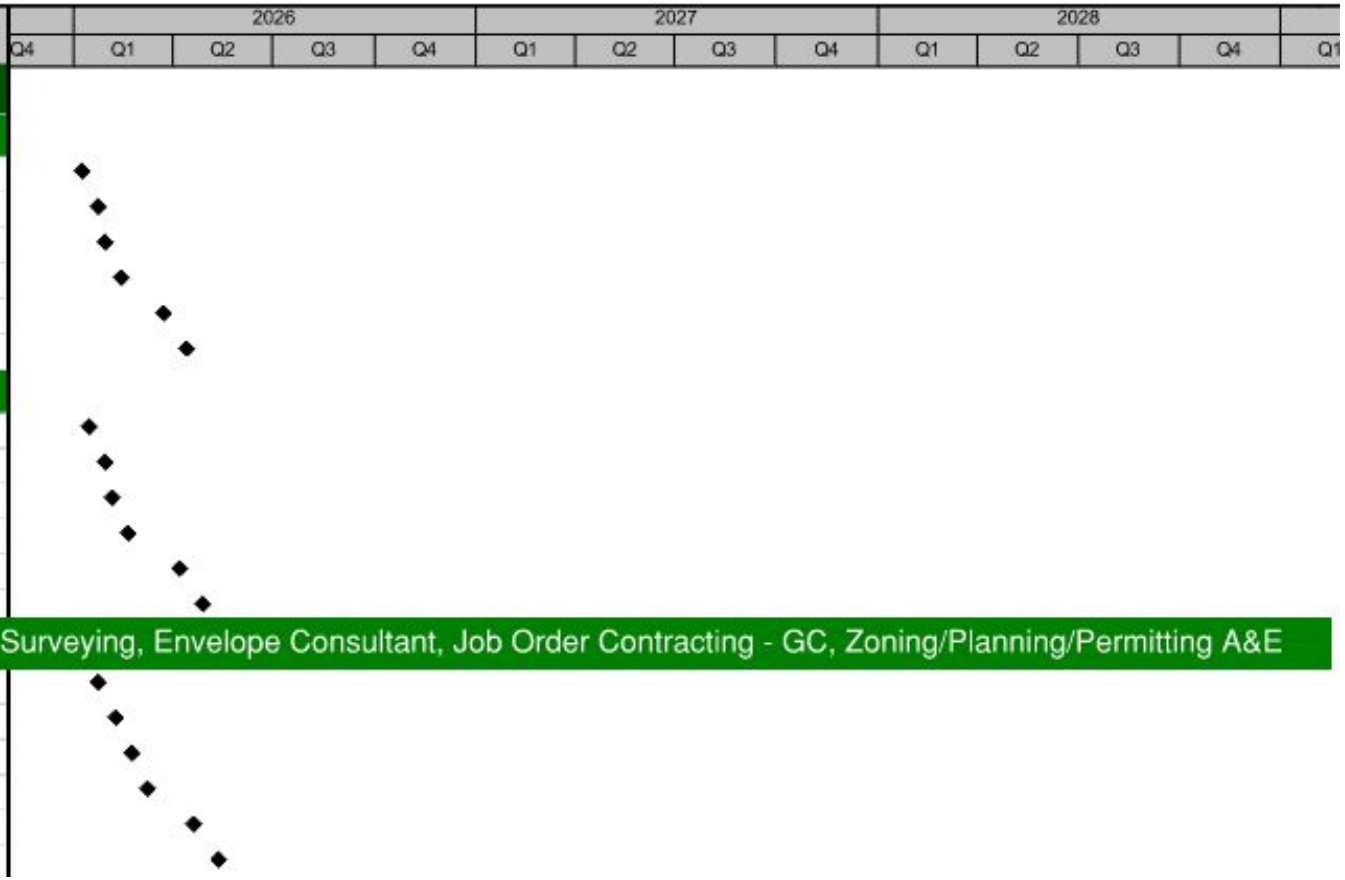


CHS Overall Project Schedule

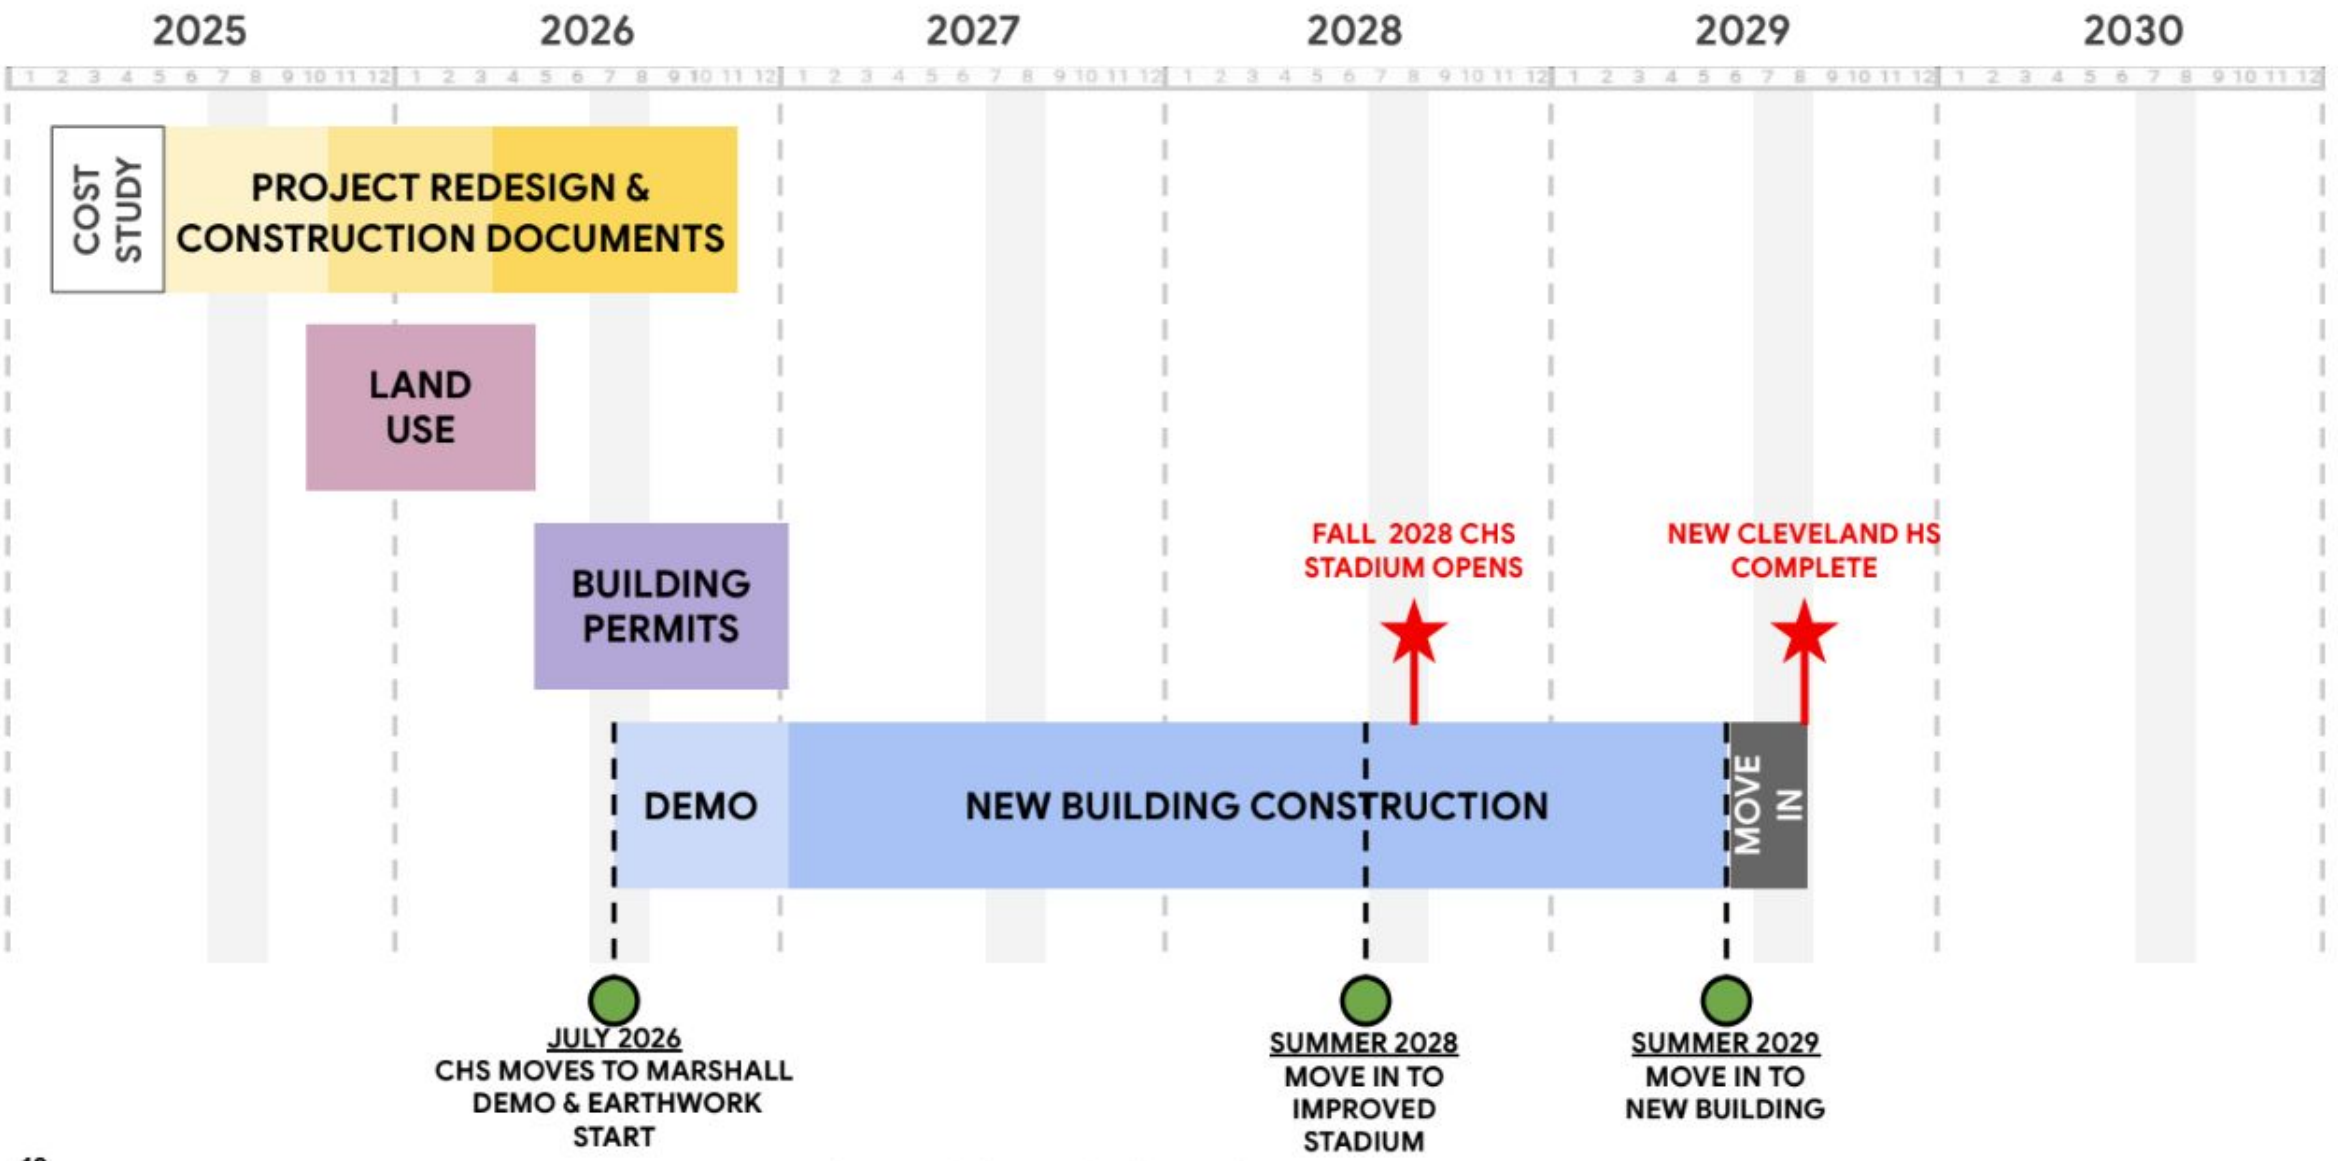


Jefferson High School

Overall Project Schedule

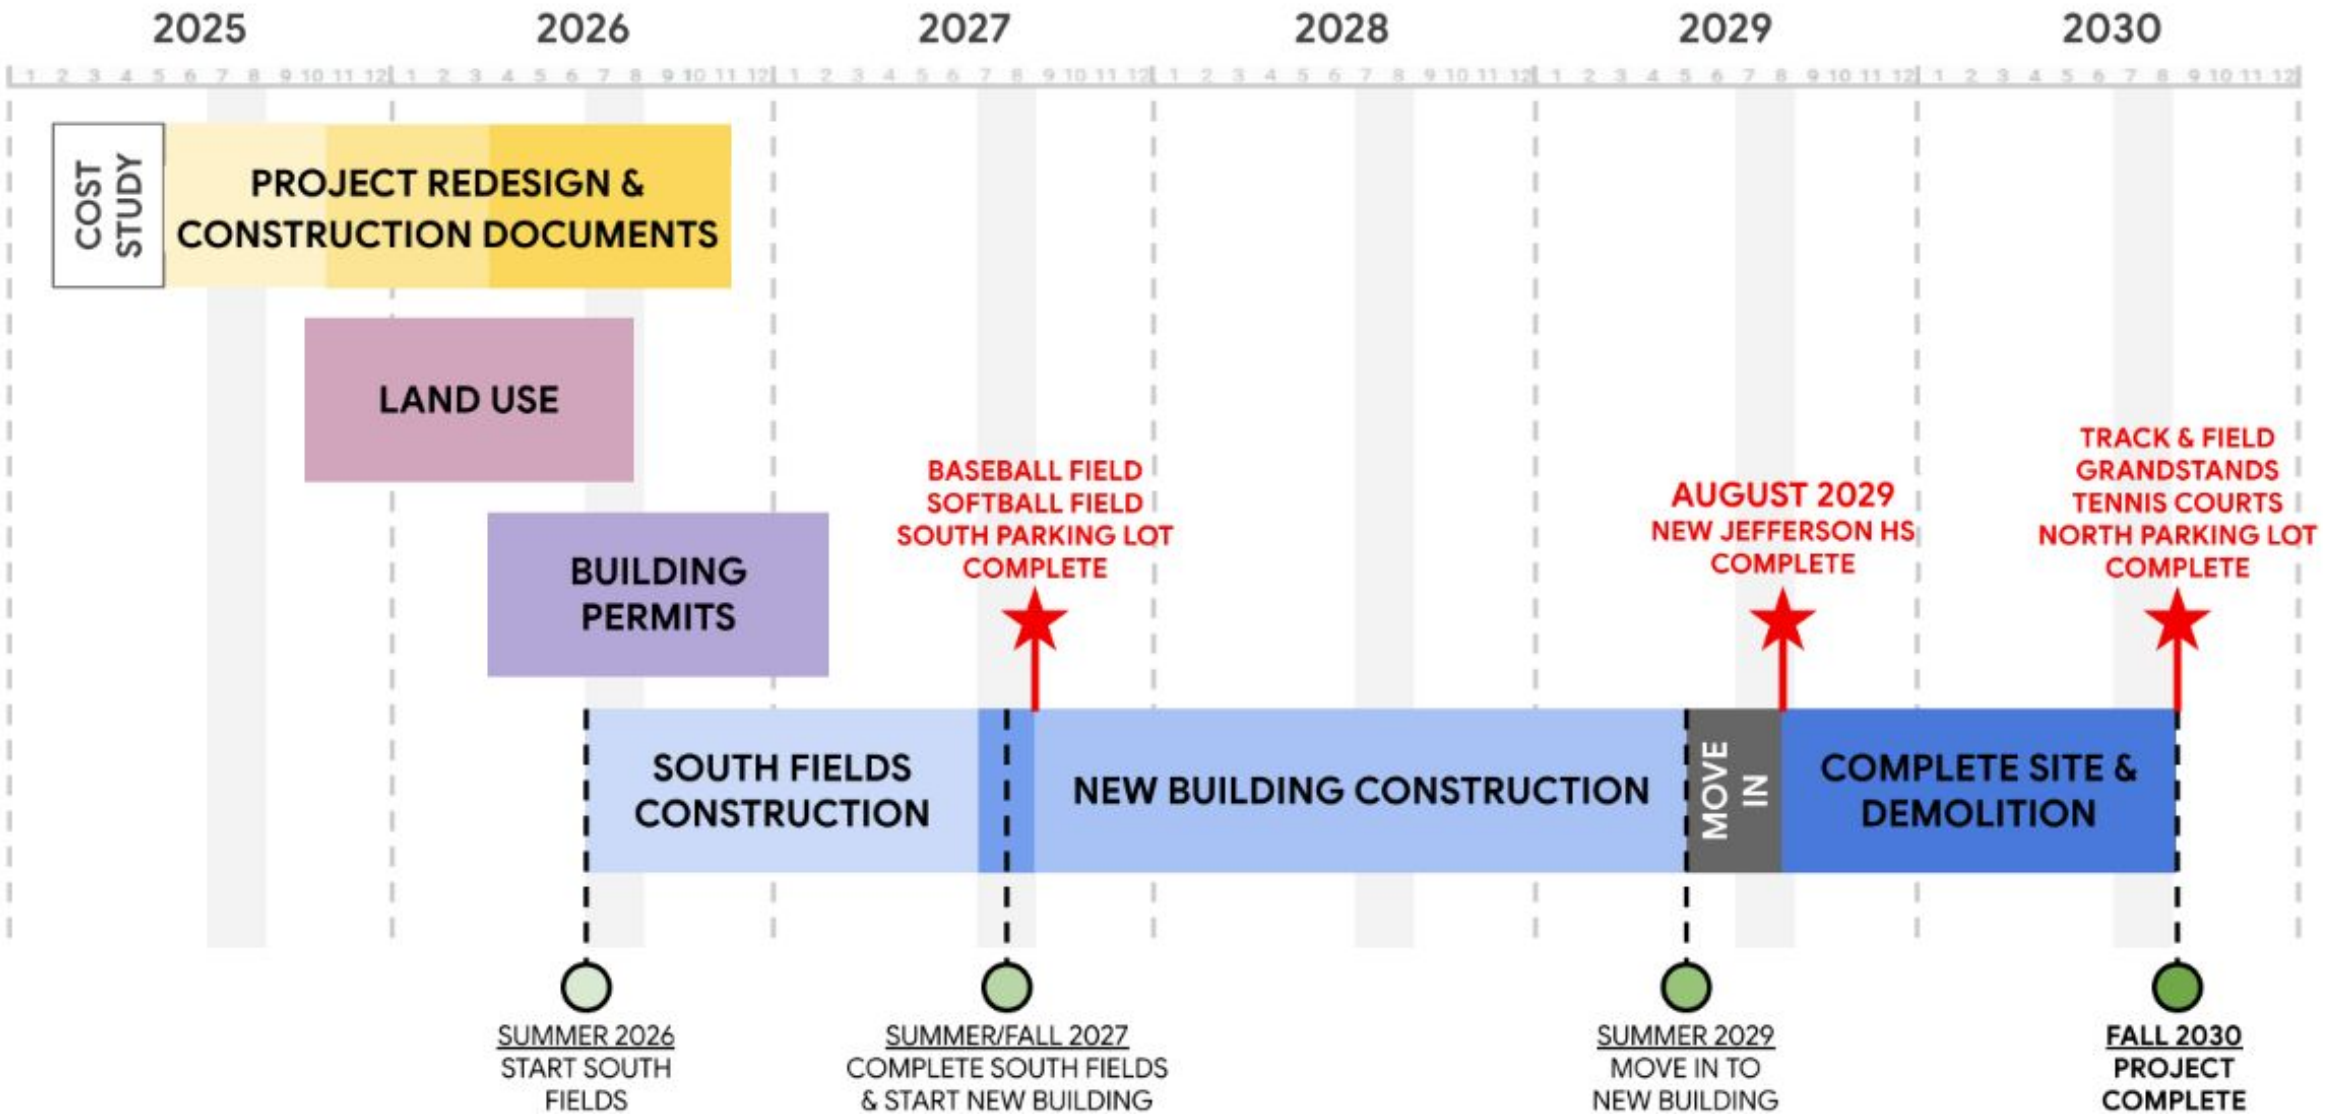

IBW Overall Project Schedule

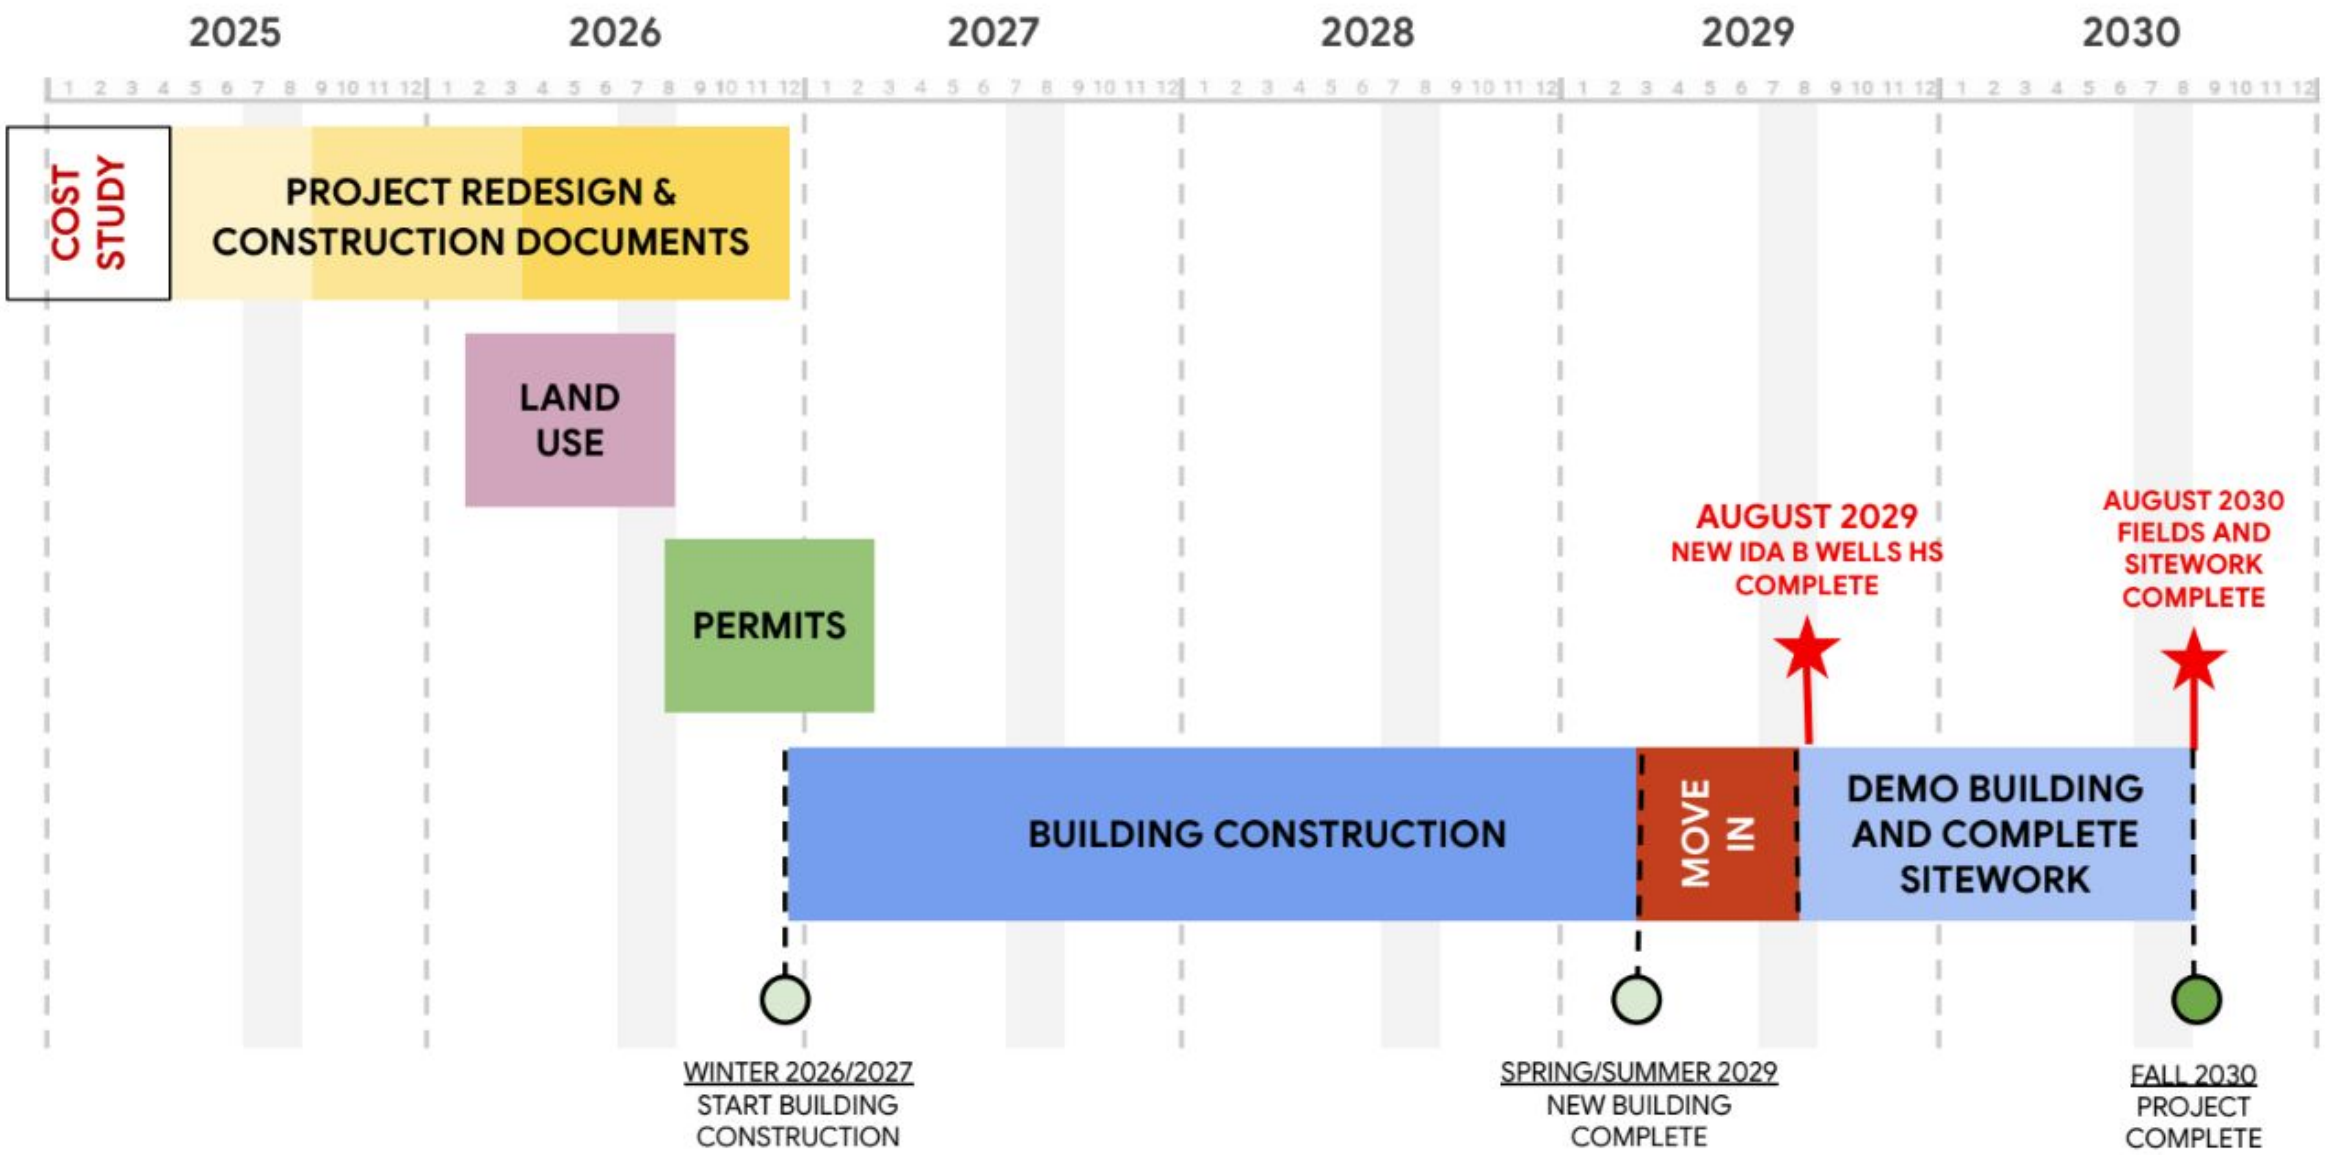



Bond Program Dashboard

Bond Measure

Deselect all	2012 Bond	2017 Bond	2020 Bond	2025 Bond

Total Funds	Spent to Date	Outstd. Encumbrance	Available Funds	Percent Available
4.6bn	2.0bn	167.7M	2.4bn	52%

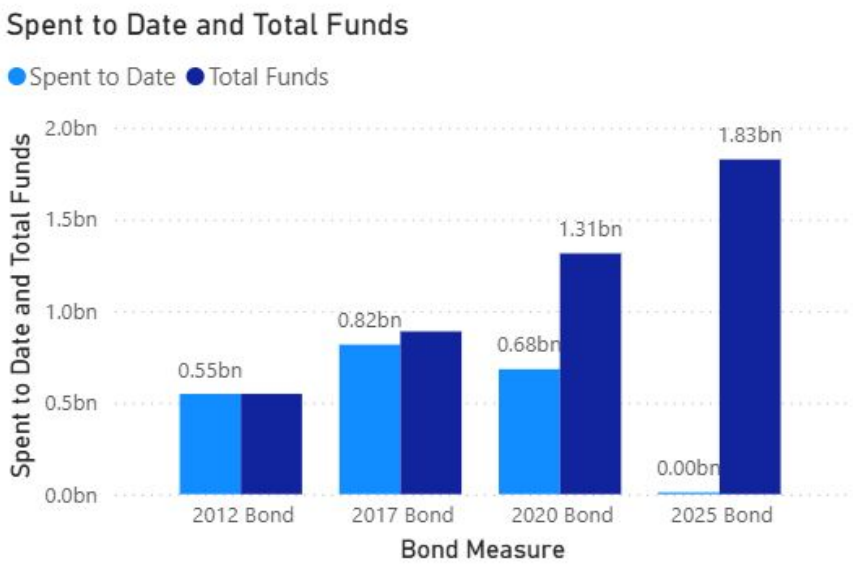

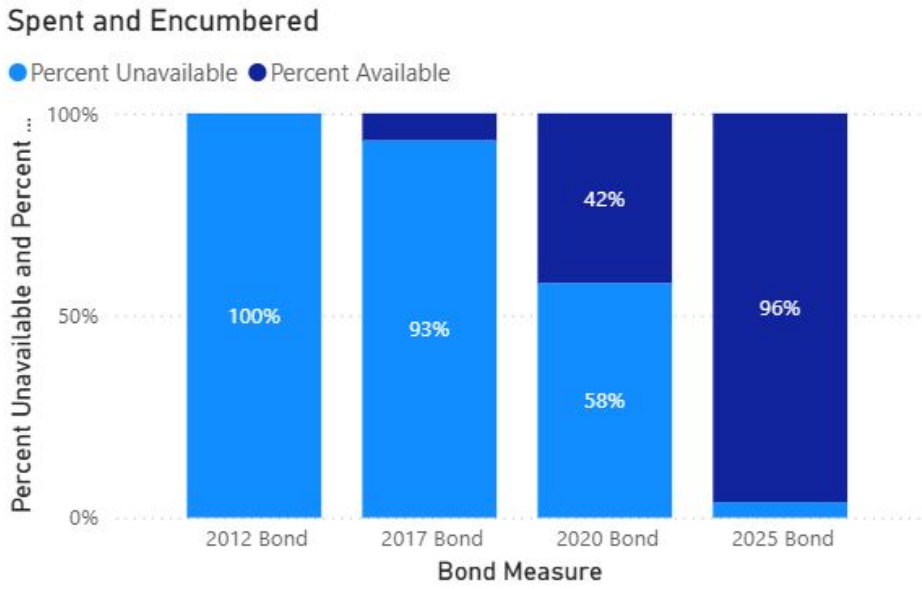


2012 Dashboard


Modernization: Franklin HS, Grant HS, Roosevelt HS and Faubion PK-8
Middle School Science Upgrades
Consolidated Projects: Accessibility, Seismic

Bond Measure

Select all	2012 Bond	2017 Bond	2020 Bond	2025 Bond


Total Funds	Spent to Date	Outstd. Encumbrance	Available Funds	Percent Available
547.8M	547.4M	77.3K	403.5K	0%

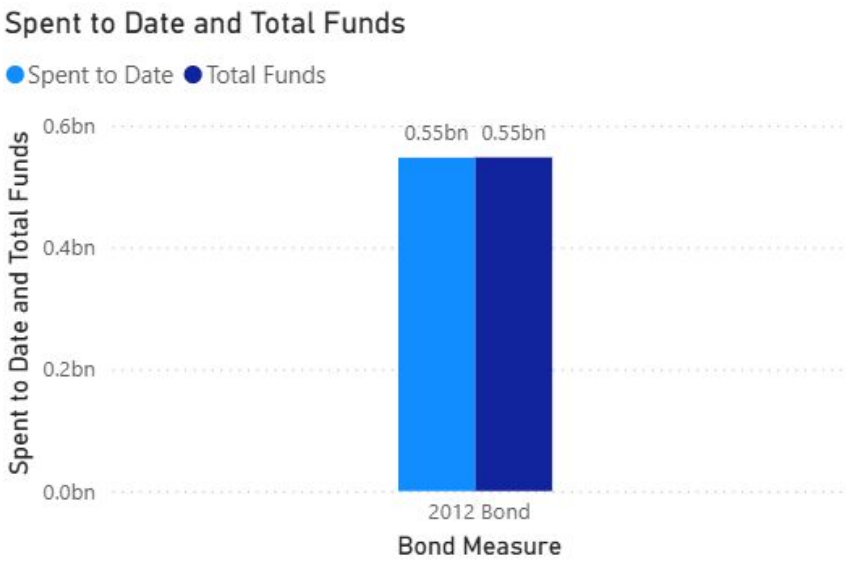

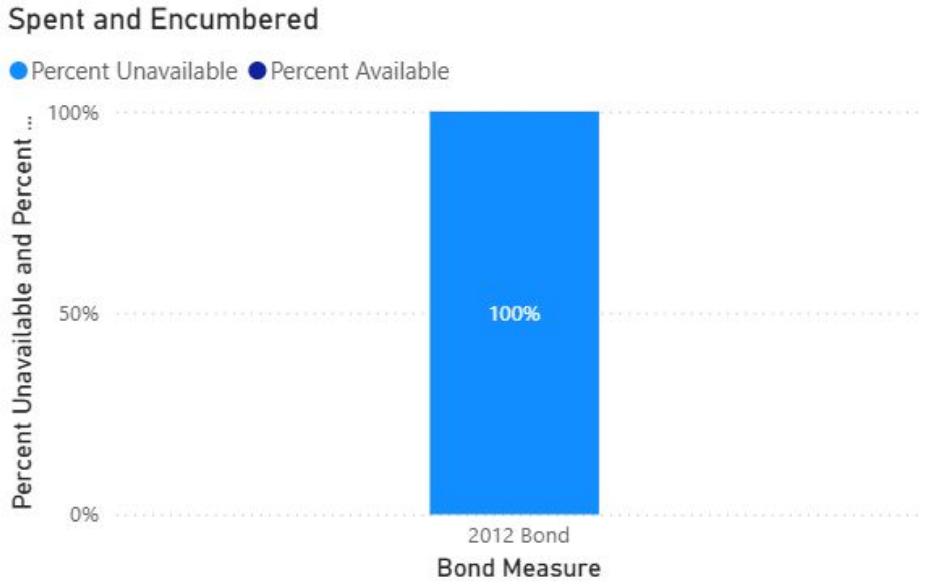

2012 Bond Program Project Status

Total Projects	Pre-Planning	Design Phase	Construction	Post Construction	Completed
33	1	0	6	2	24

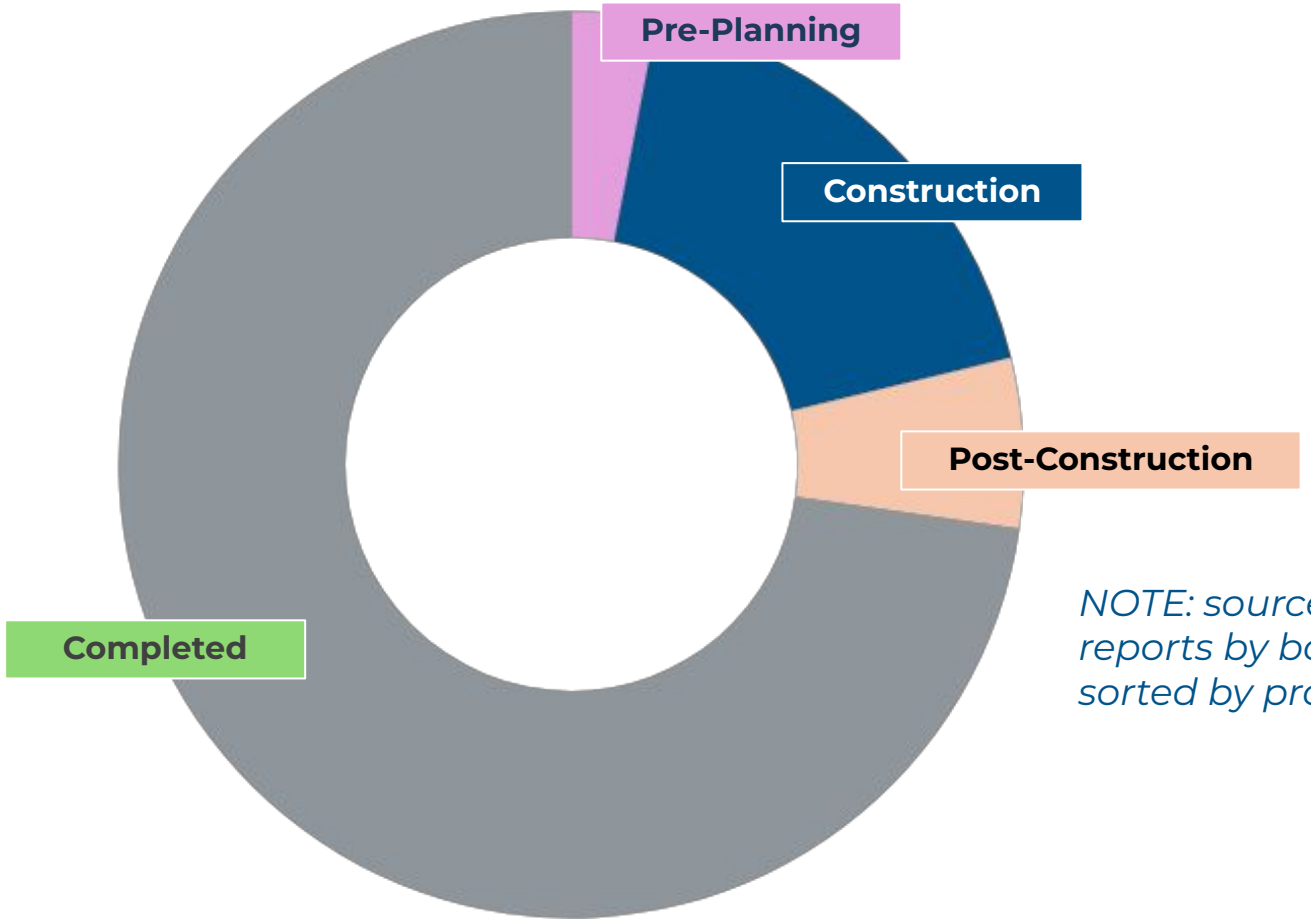

NOTE: source data: Ebuilder reports by bond measure, sorted by project status


2017 Dashboard


Modernizations: Benson Polytechnic, Lincoln, McDaniel, Kellogg Middle School and Multiple Pathways to Graduation
Consolidated: Water Quality, Security Upgrades, New Roofs, Asbestos Abatement, Radon remediation, Lead Paint Stabilization, Life Safety Upgrades, Accessibility, Seismic

Bond Measure

Select all	2012 Bond	**2017 Bond**	2020 Bond	2025 Bond


Total Funds	Spent to Date	Outstd. Encumbrance	Available Funds	Percent Available
888.5M	**816.3M**	**13.0M**	**59.5M**	**7%**

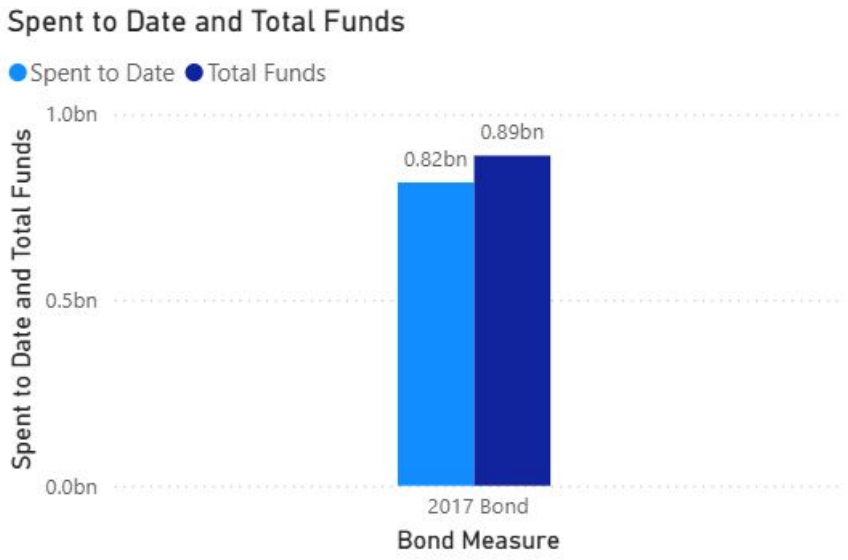

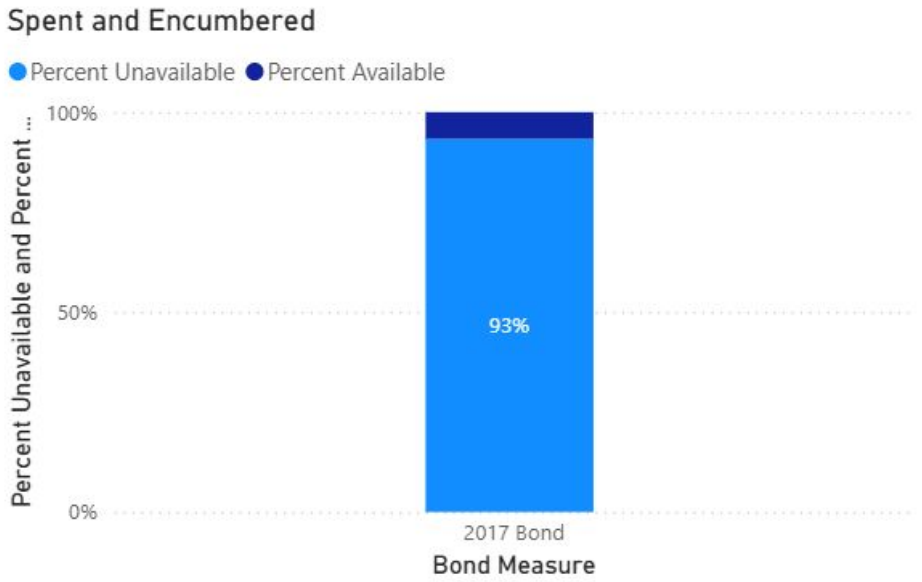

2017 Bond Program Project Status

Total Projects	Pre-Planning	Design Phase	Construction	Post Construction	Completed
175			46	26	103

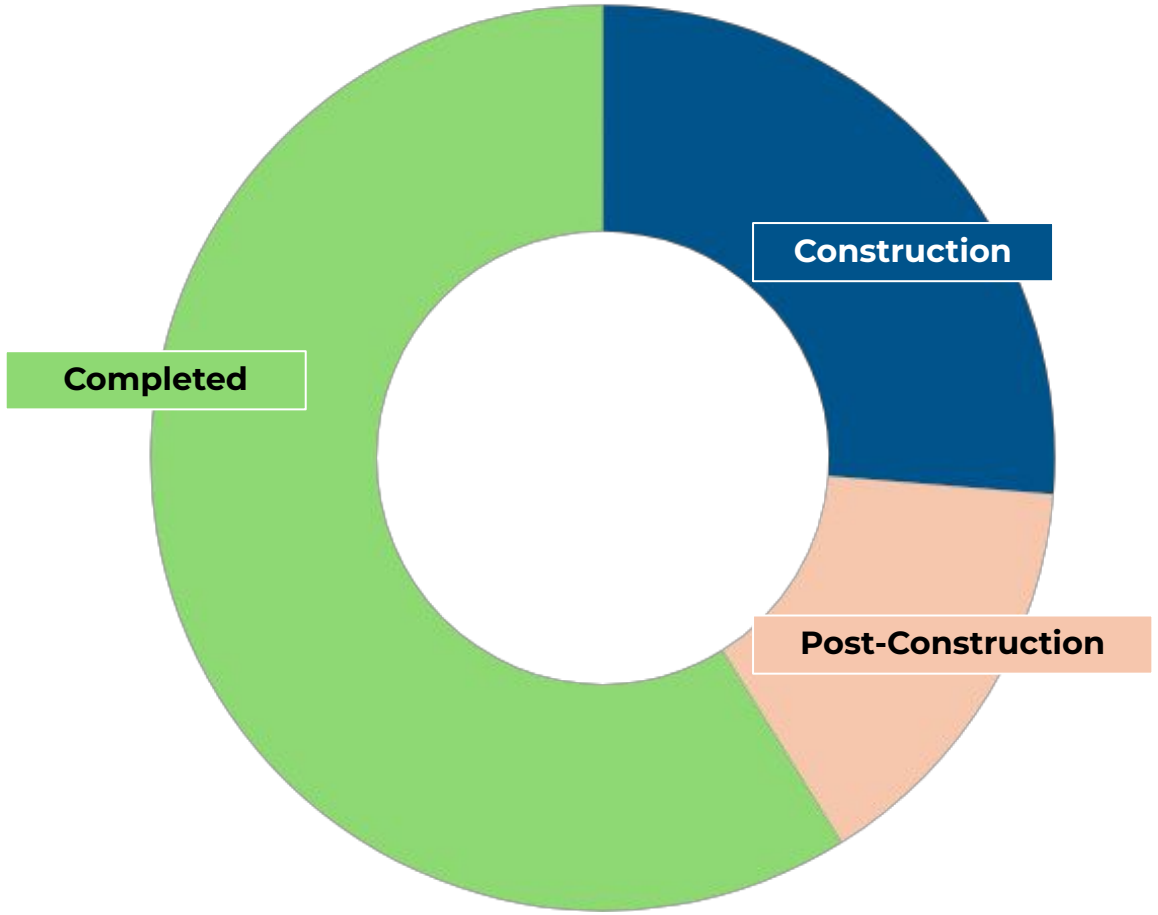

NOTE: source data: Ebuilder reports by bond measure, sorted by project status


2020 Dashboard


Modernizations: Jefferson HS. Pre-Planning/Design Ida B Wells and Cleveland High School, The Center of Black Excellence.
Consolidated: Curriculum Materials, New Technology for classroom and distance learning

Bond Measure

Select all	2012 Bond	2017 Bond	2020 Bond	2025 Bond


Total Funds	Spent to Date	Outstd. Encumbrance	Available Funds	Percent Available
1.3bn	682.2M	85.6M	551.7M	42%

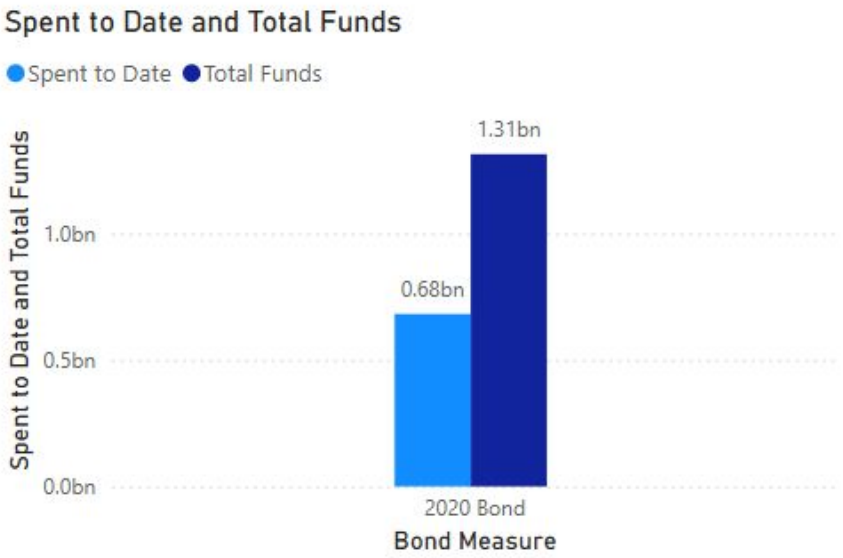

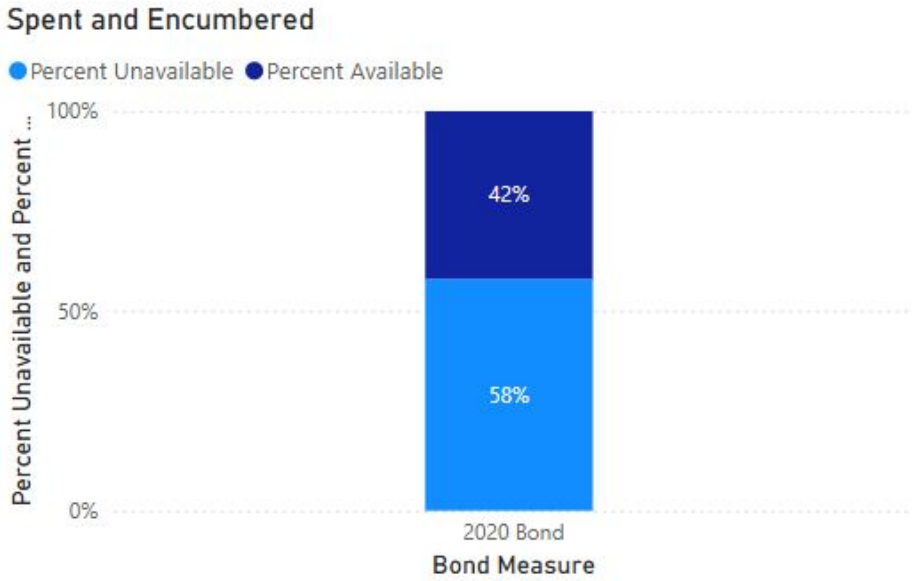

2020 Bond Program Project Status

Total Projects	Pre-Planning	Design Phase	Construction	Post Construction	Completed
103*	1	3	61	3	35

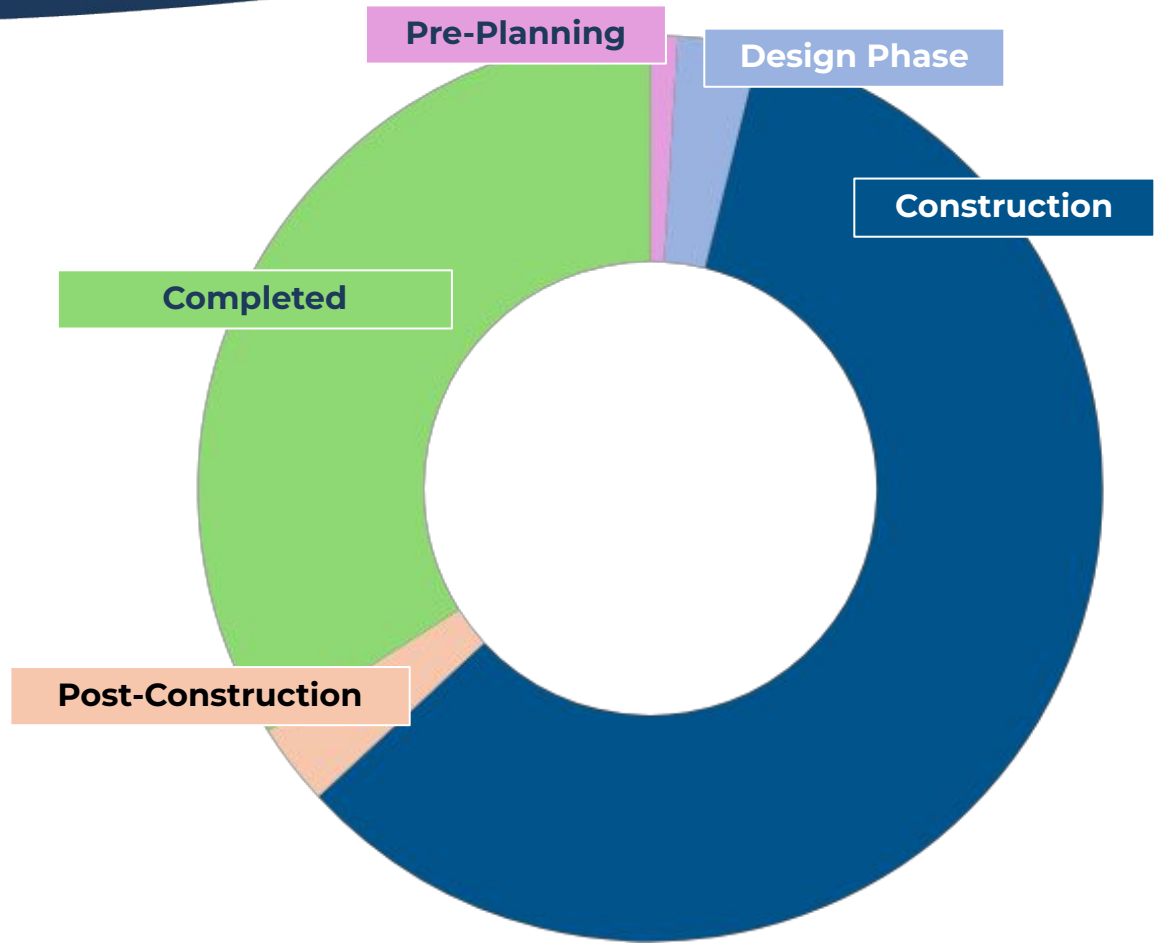

**Approximately $551 M remaining to be scheduled for 2020 Bond.*

NOTE: source data: Ebuilder reports by bond measure, sorted by project status

2025 Dashboard


Modernizations: Cleveland and Ida B. Wells


Consolidated:, Security upgrades, seismic, technology, improvements for Roosevelt, Lincoln, Franklin and Grant and create athletic hub facilities at Jackson Middle School and Marshall campus.

Bond Measure

Select all	2012 Bond	2017 Bond	2020 Bond	2025 Bond


Total Funds	Spent to Date	Outstd. Encumbrance	Available Funds	Percent Available
1.8bn	177.1K	69.1M	1.8bn	96%

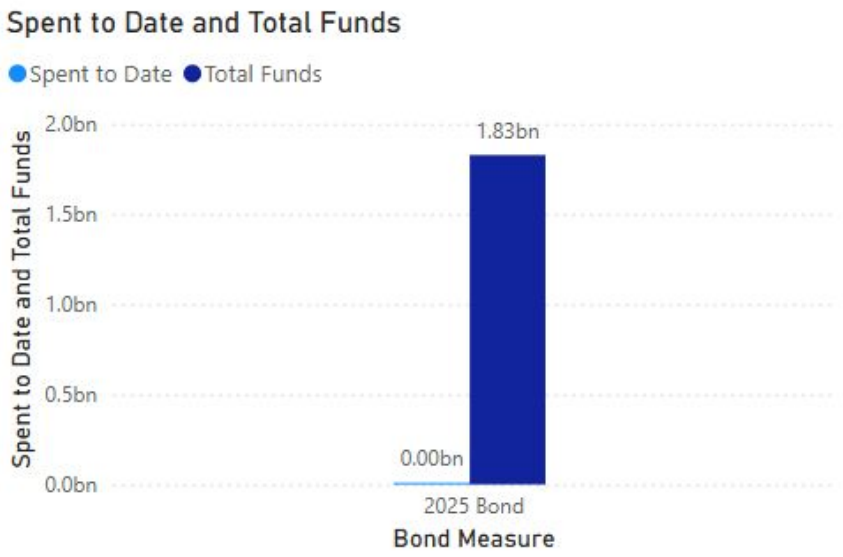

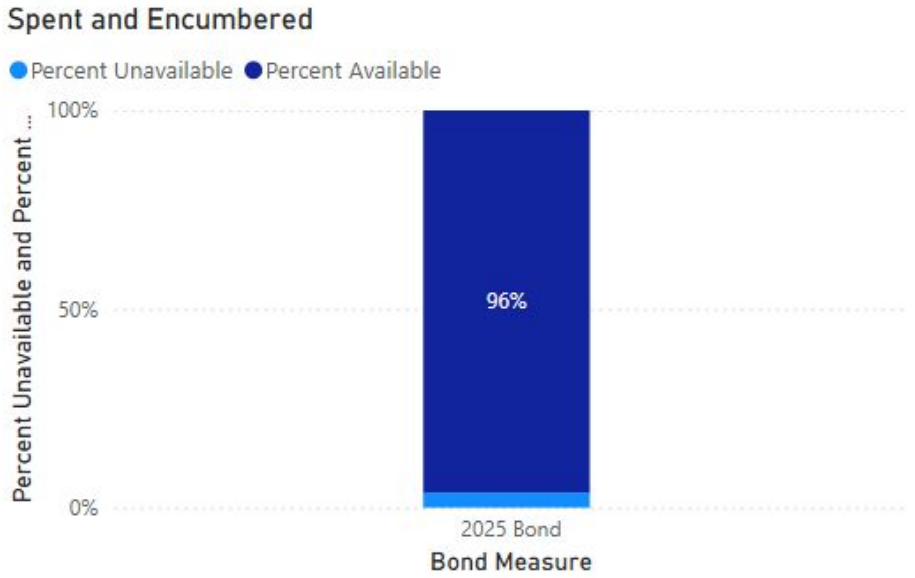

2025 Bond Program Project Status

Total Projects	Pre-Planning	Design Phase	Construction Phase	Post-Construction	Completed
12*	12		0	0	0

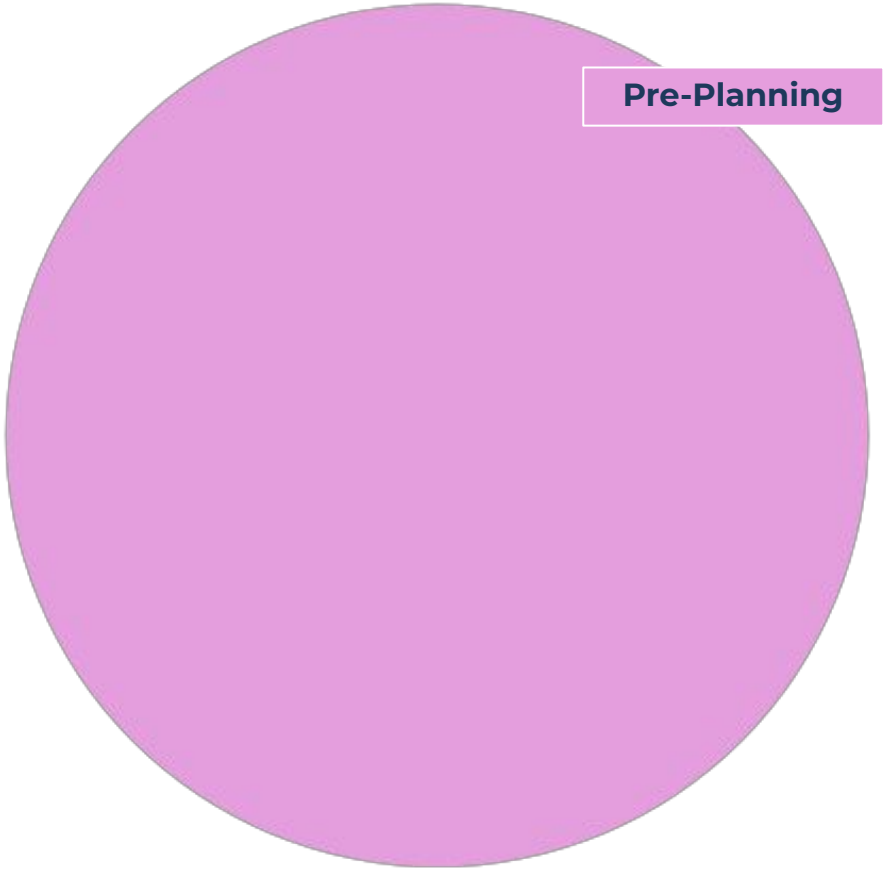

**Deferred Maintenance and Priority Scope specifically called out in the approved Bond have not yet been fully identified. Projects will increase as the program progresses.*

Questions
Thank you



Contact us

PPS.NET pubinfo@pps.net (503) 916-2000 501 N Dixion, Portland, OR 97227



PORTLAND
Public Schools
