Bond Program Update



PORTLAND
Public Schools

Date February 10, 2026

Bond Team Wins!

Modernizations:

- Cleveland and Jefferson have completed the Design Development Phase with Ida B. following in spring.
- Marshall track and field resurfacing has started and is scheduled to be complete by end of April!

Controls:

- Business Operations is producing has moved from quarterly cash flow reports to monthly.
- There has been increased collaboration with Finance
- There is a pending rollout of a new bond compensability standard operating procedure (SOP) which will result in improved BAC reporting.
- Improved cost controls in Ebuilder (project management database).

Bond Team Wins!

Communications:

- Bond project webpage updates are in progress. Webpages for modernizations and consolidated projects are being redesigned to be more user-friendly with easy to find, up-to-date information.

Consolidated:

- Duniway Re-Roof: Received final sign-off on all permits associated with the project and are moving into project closeout.
- Grant Lights: Expected to start construction **March 2026** (dependent on receipt of permit).
- **Jackson & Marshall HUB Athletic Fields:** Field & Turf scope set to start Q2 2026.

Technology

Portland Public Schools has selected MicroK12 as our partner for the upcoming Chromebook refresh to replace student devices which no longer meet instructional needs. This work includes investments in updated student laptops and classroom technology across the district.


The refresh is part of our broader modernization efforts and is aligned with August start of school.

This approach differs from past cycles by co-designing the rollout with school-based leaders to reduce risk of disruption to students and instruction. Building principals, senior directors of schools, and school business managers are helping shape processes for a 1:1 Chromebook model at high schools, cart-based models for grades 6–8, and age-appropriate access in earlier grades so that device distribution and management fit each school's operations and student needs.

OTIS is dedicated to refining logistics with the appropriate stakeholders, to fully develop a go forward plan by end of February.



CHS Overall Project Schedule

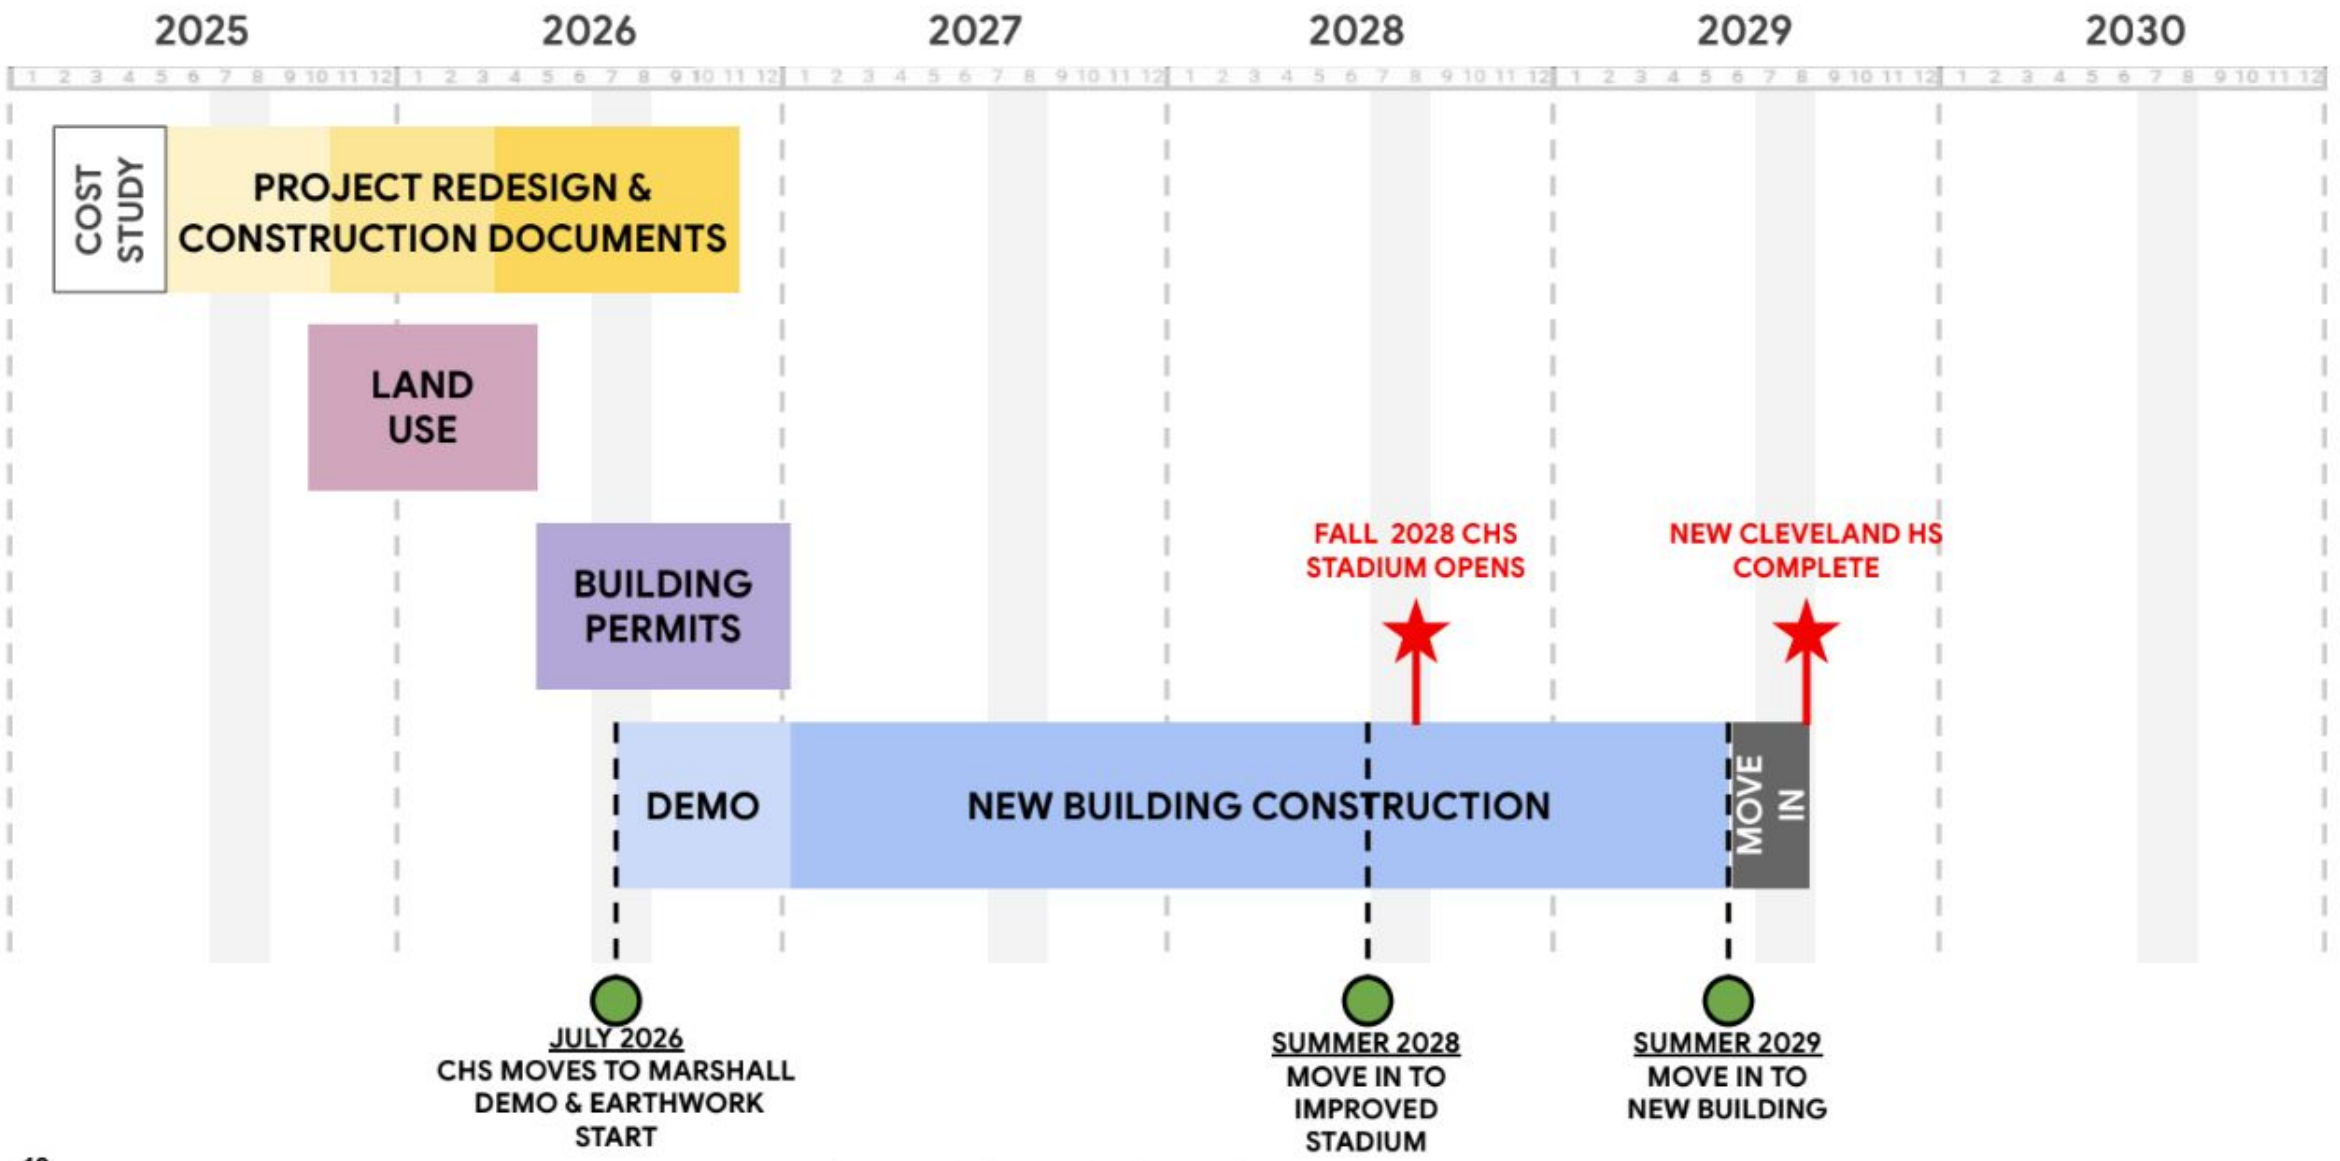


Cleveland High School

- Design Development milestone achieved in mid January 2026. Due to value engineering efforts (VE) and alternate indoor running track in the gym was accepted. The Construction Document phase has started.
- Improvements scheduled to start at Marshall in preparation for Cleveland High School with completion in June 2026.
- Construction scheduled to begin in June 2026.

Jefferson High School


Overall Project Schedule

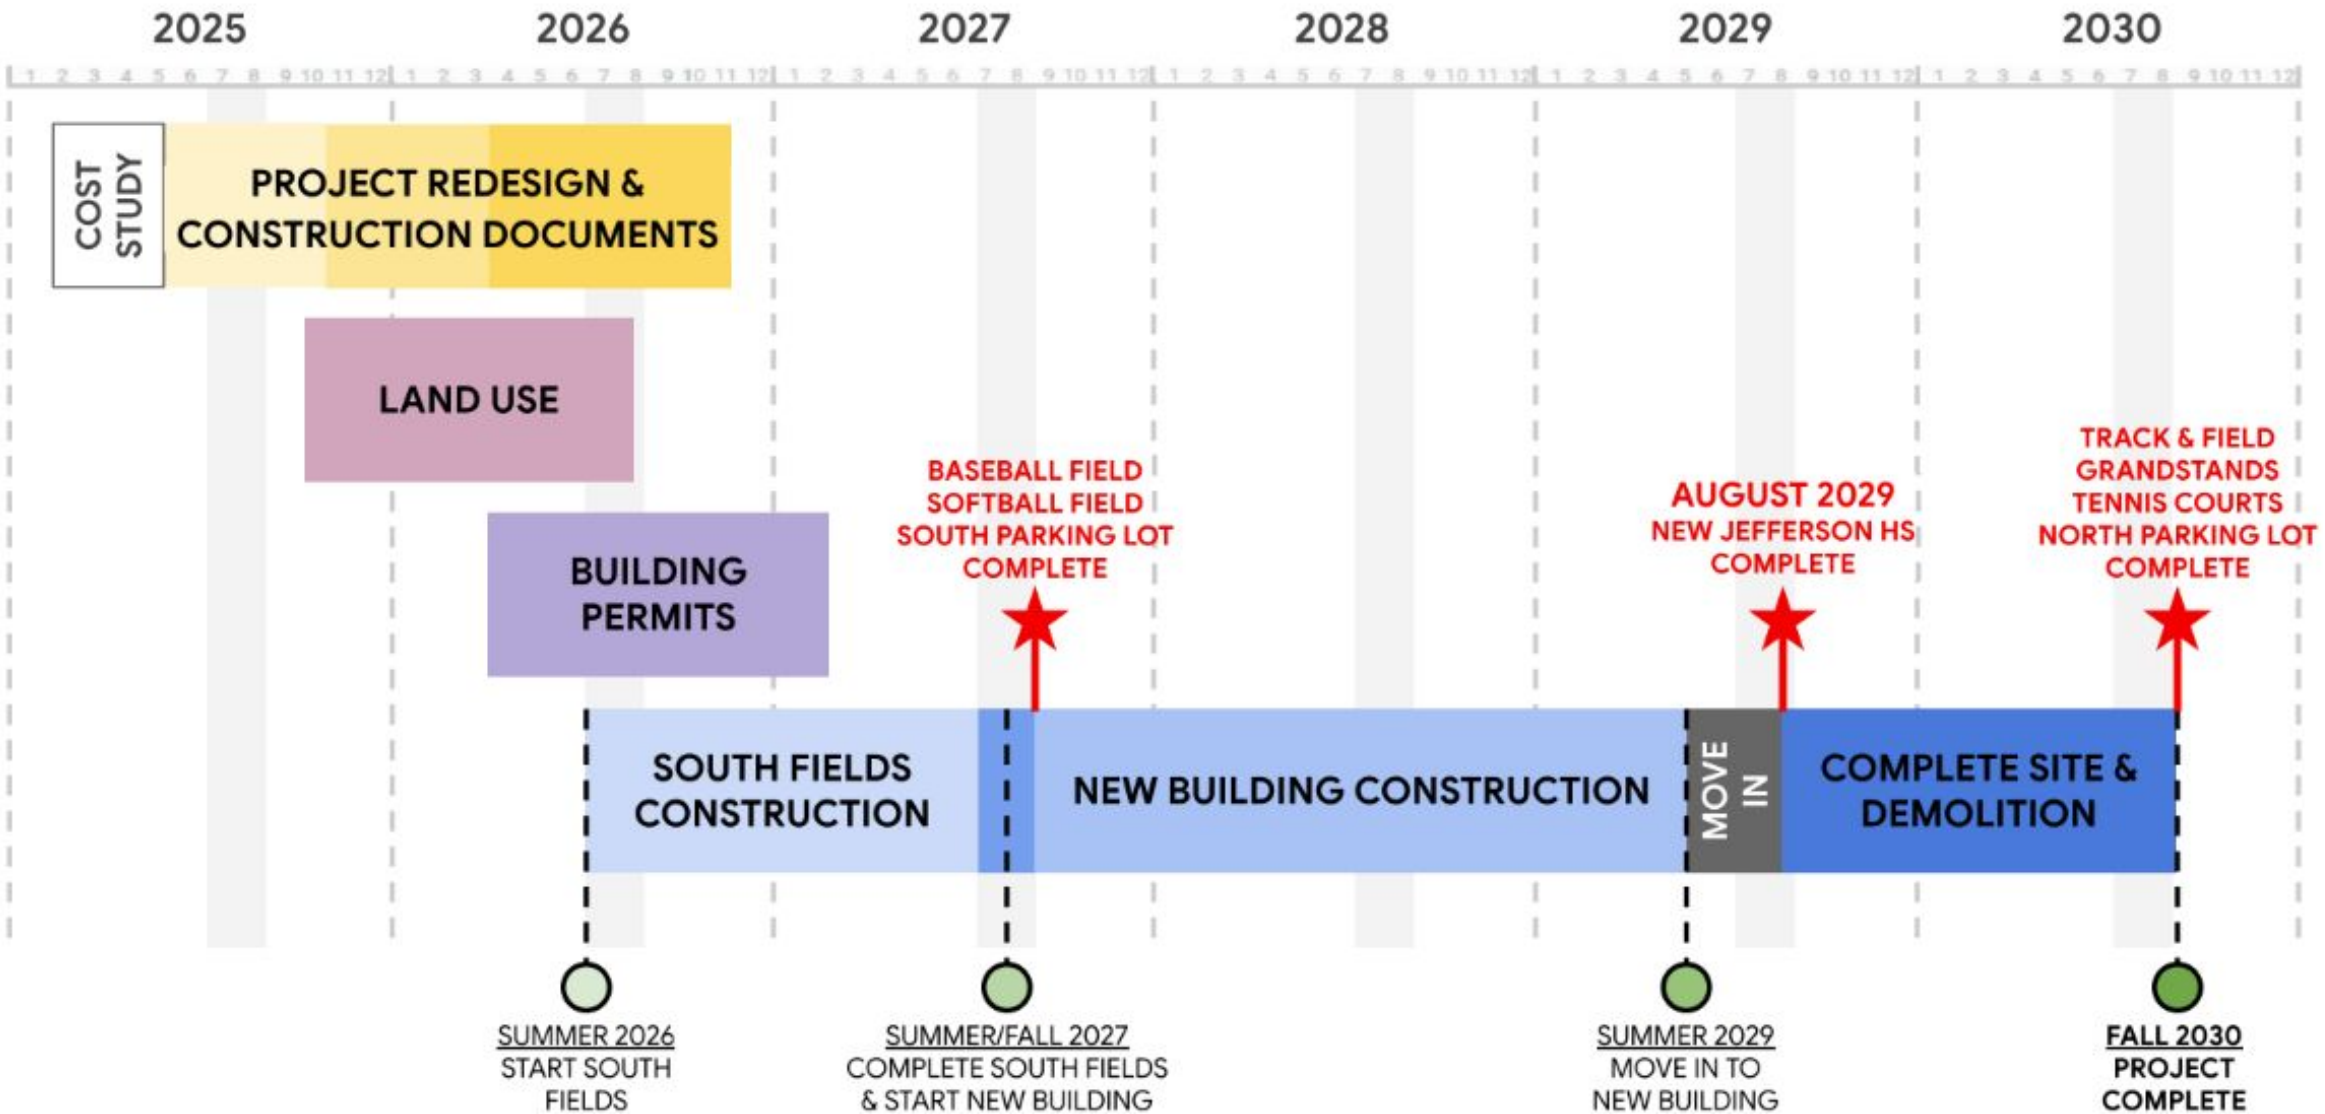

Jefferson High School

- Project is reaching the final stages of the Type III conditional use process with a hearing scheduled for February 11.
- Major milestone: Design Development is complete and documents have been received.
- Early fields scope is out to bid for a scheduled late spring construction start.
- Project team led several Community Information Sessions through the end of last year and will continue with additional engagement in the spring.
- Groundbreaking date TBD.

IBW Overall Project Schedule

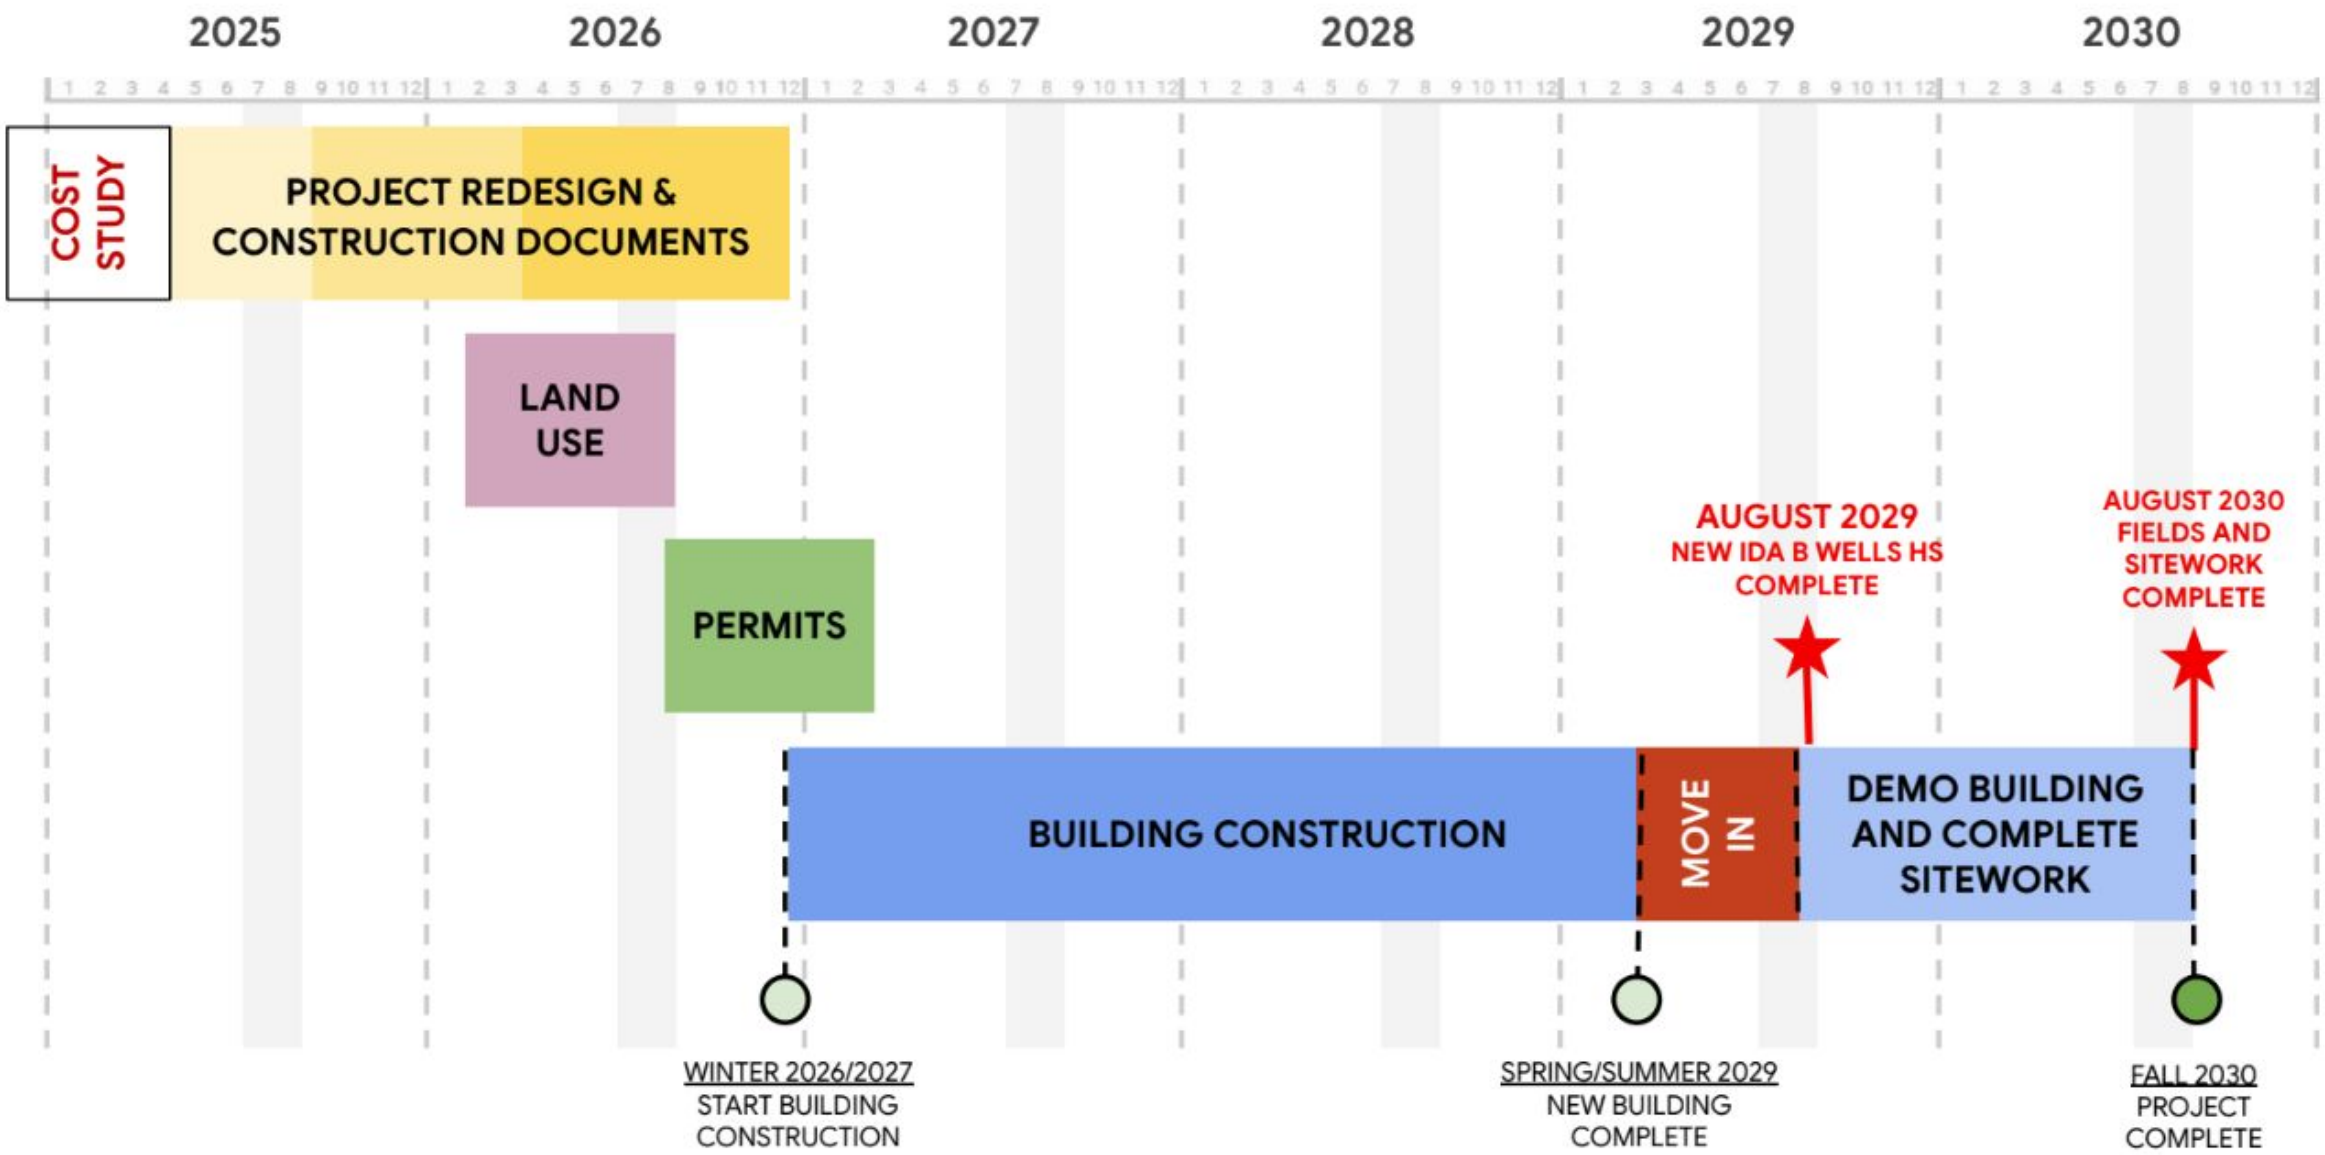

Ida B. Wells High School

- Feb 4th Community Design Workshop
- Design Development phase underway, deliverable scheduled for Spring 2026.
- Construction start scheduled for December 2026.
- Groundbreaking date TBD.

Consolidated Projects Update

2017 Bond

Roofs:

- Vestal re-roof
- Marshall re-roof

Consolidated Projects Update

2020 Bond

HVAC/Controls:

- Bridger and Kelly (Mechanical): Final commissioning report received and the project is moving into closeout.

ADA and SPED Upgrades:

- ADA and Special Education upgrade projects are **scheduled for completion 02/12/2026**.

Seismic:


- Award and completion of design for Chavez, Marshall, Vestal and Woodmere.


Bond Program Dashboard

Bond Measure

Deselect all	2012 Bond	2017 Bond	2020 Bond	2025 Bond

Total Funds	Spent to Date	Outstd. Encumbrance	Available Funds	Percent Available
4.6bn	2.1bn	184.7M	2.4bn	51%

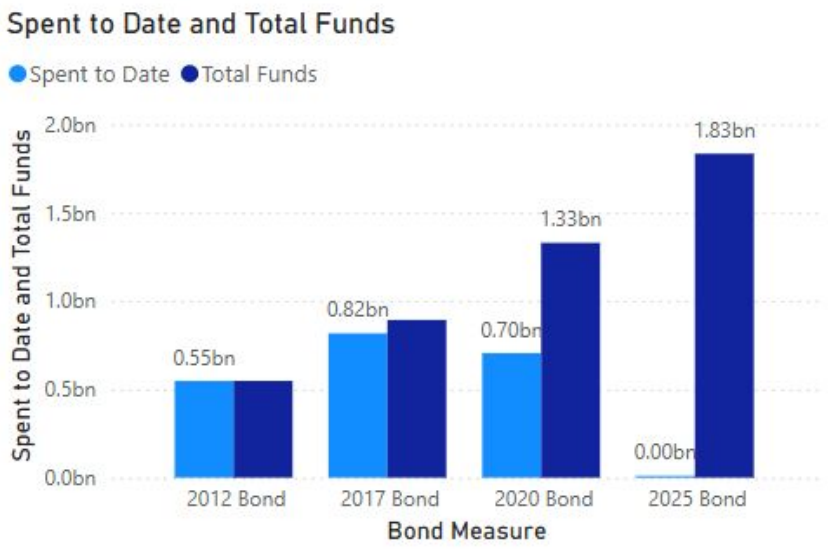

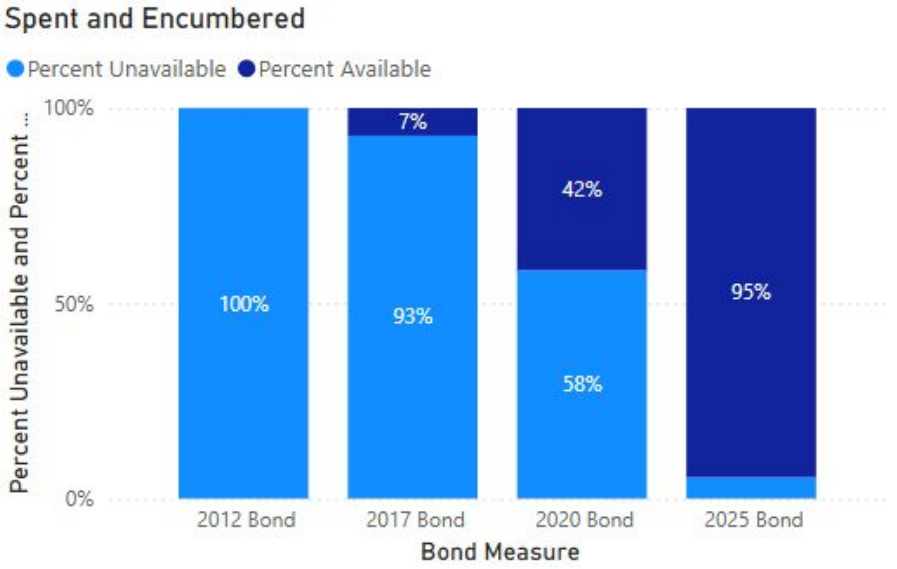


2012 Dashboard


Modernization: Franklin HS, Grant HS, Roosevelt HS and Faubion PK-8
Middle School Science Upgrades
Consolidated Projects: Accessibility, Seismic

Bond Measure

Select all | **2012 Bond** | 2017 Bond | 2020 Bond | 2025 Bond


Total Funds	Spent to Date	Outstd. Encumbrance	Available Funds	Percent Available
547.8M	547.4M	51.0K	403.5K	0%

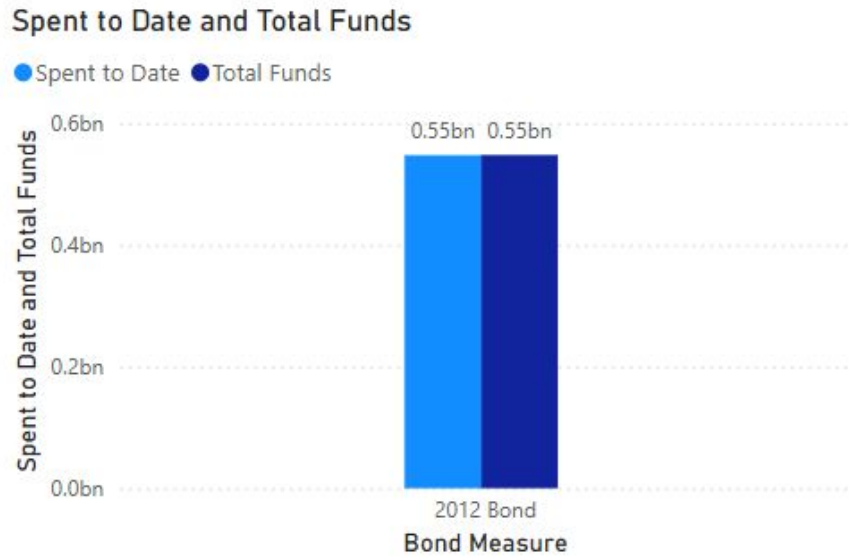

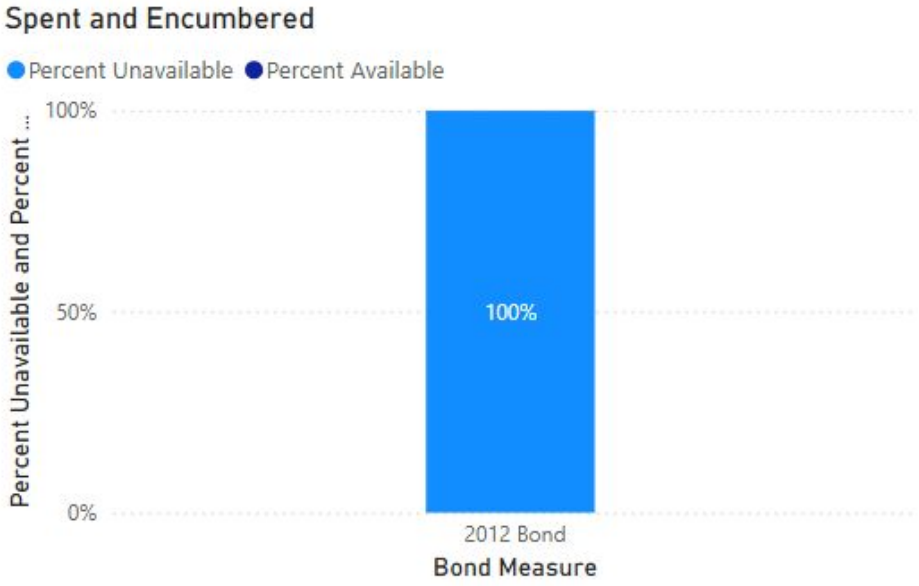

2012 Bond Program Project Status

Total Projects	Pre-Planning	Design Phase	Construction	Post Construction	Completed
33	0	0	8	2	23

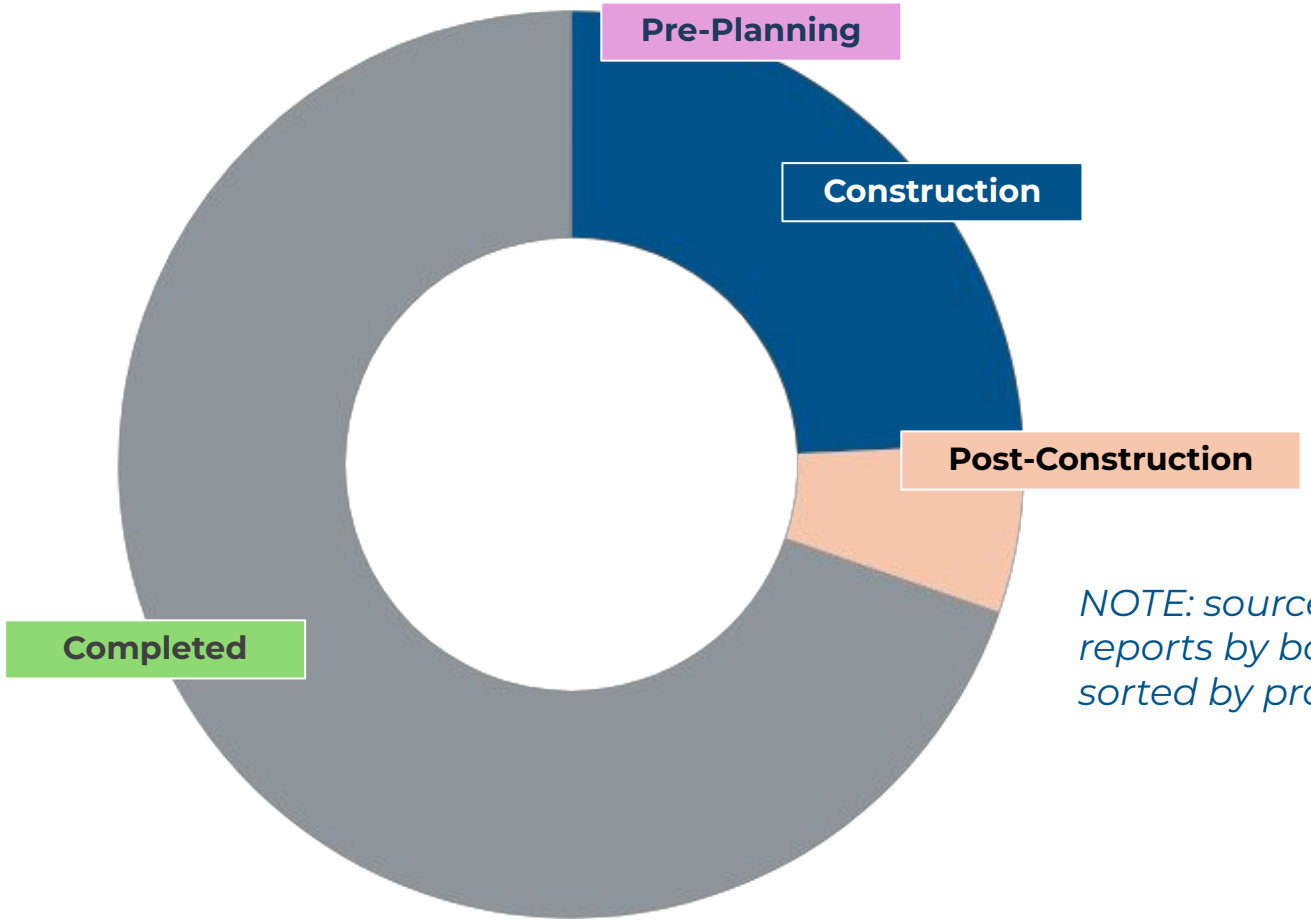

NOTE: source data: Ebuilder reports by bond measure, sorted by project status


2017 Dashboard


Modernizations: Benson Polytechnic, Lincoln, McDaniel, Kellogg Middle School and Multiple Pathways to Graduation
Consolidated: Water Quality, Security Upgrades, New Roofs, Asbestos Abatement, Radon remediation, Lead Paint Stabilization, Life Safety Upgrades, Accessibility, Seismic

Bond Measure

Deselect all | 2012 Bond | **2017 Bond** | 2020 Bond | 2025 Bond


Total Funds	Spent to Date	Outstd. Encumbrance	Available Funds	Percent Available
892.6M	816.9M	12.8M	63.3M	7%

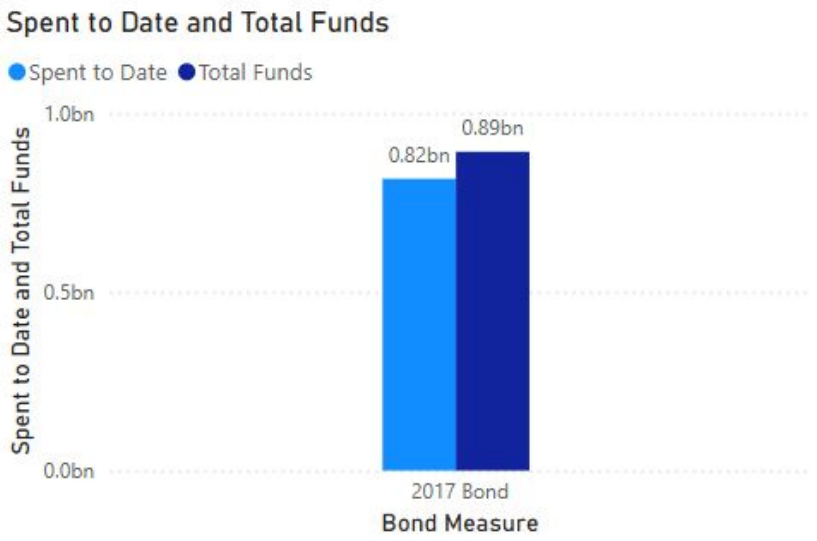

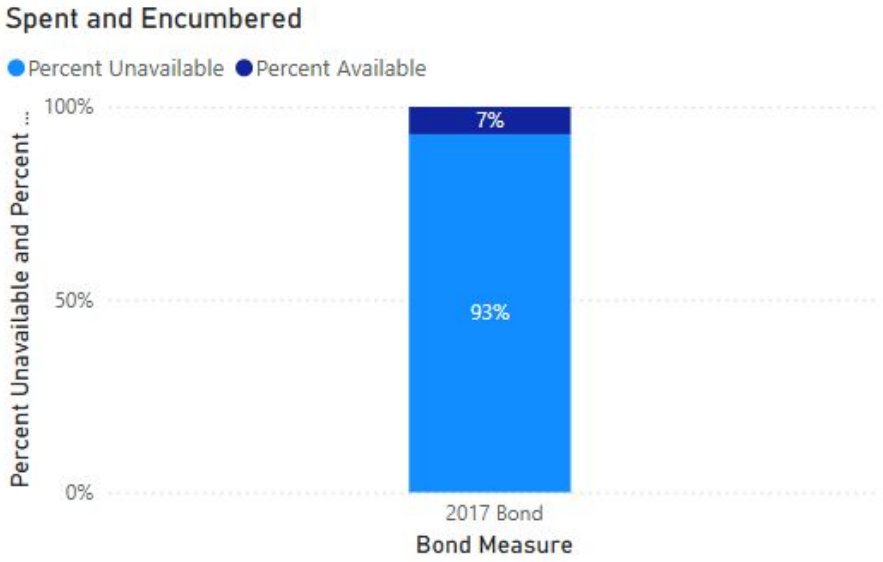

2017 Bond Program Project Status

Total Projects	Pre-Planning	Design Phase	Construction	Post Construction	Completed
175			48	17	110

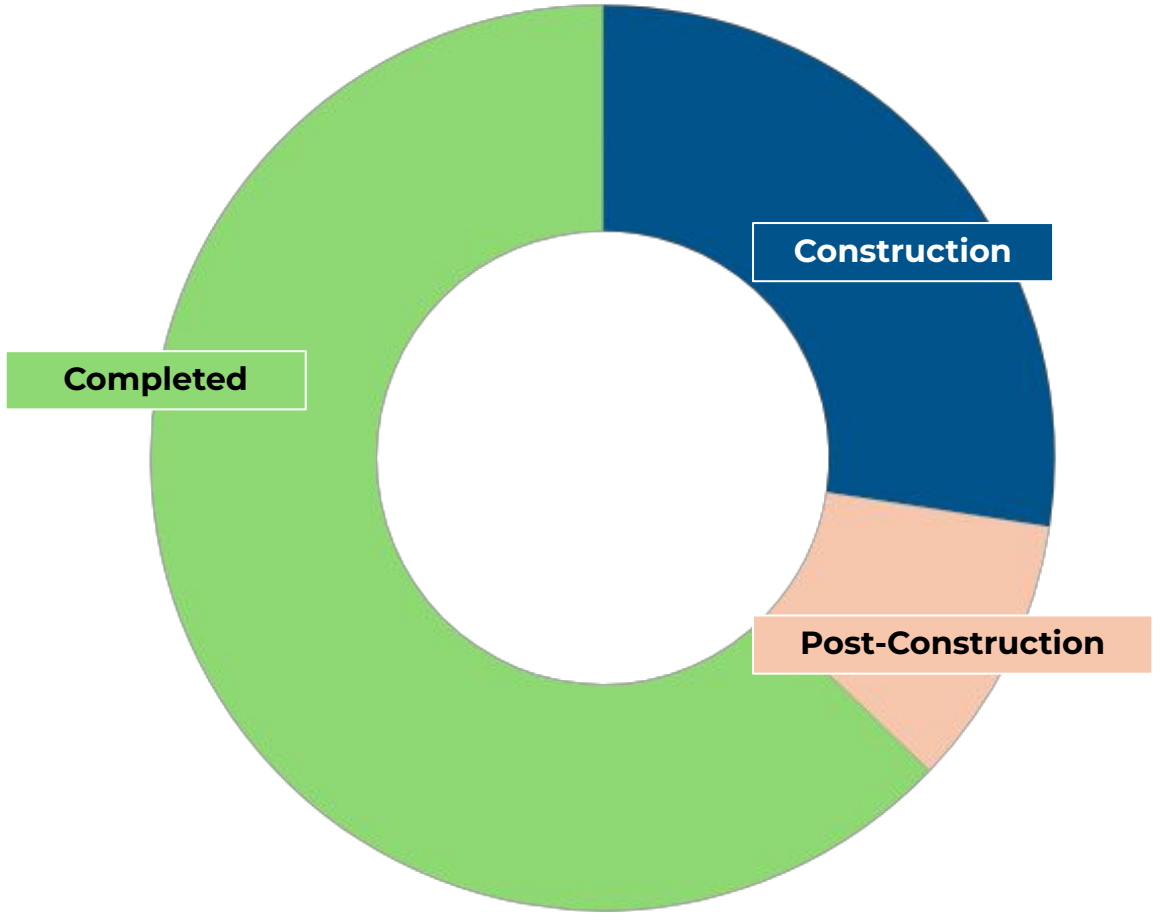

NOTE: source data: Ebuilder reports by bond measure, sorted by project status


2020 Dashboard


Modernizations: Jefferson HS. Pre-Planning/Design Ida B Wells and Cleveland High School, The Center of Black Excellence.
Consolidated: Curriculum Materials, New Technology for classroom and distance learning

Bond Measure

Deselect all	2012 Bond	2017 Bond	**2020 Bond**	2025 Bond


Total Funds	Spent to Date	Outstd. Encumbrance	Available Funds	Percent Available
1.3bn	**704.8M**	**73.6M**	**552.1M**	**42%**

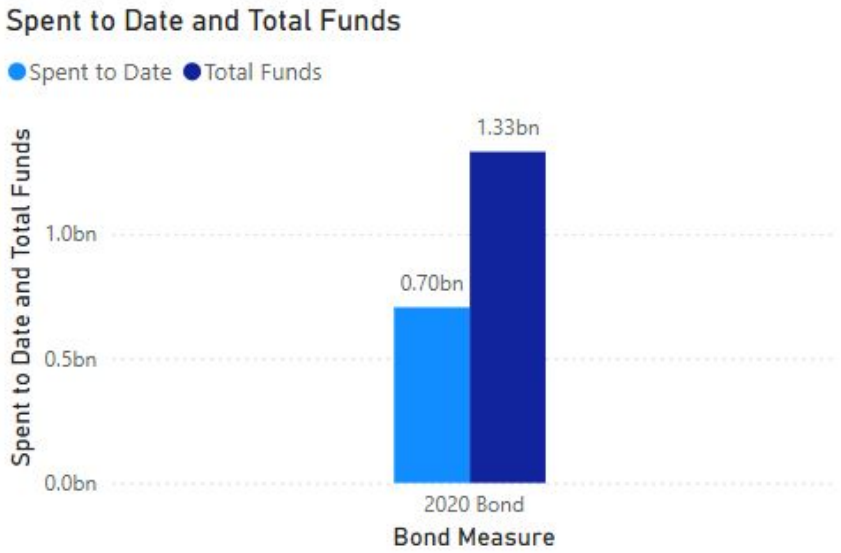

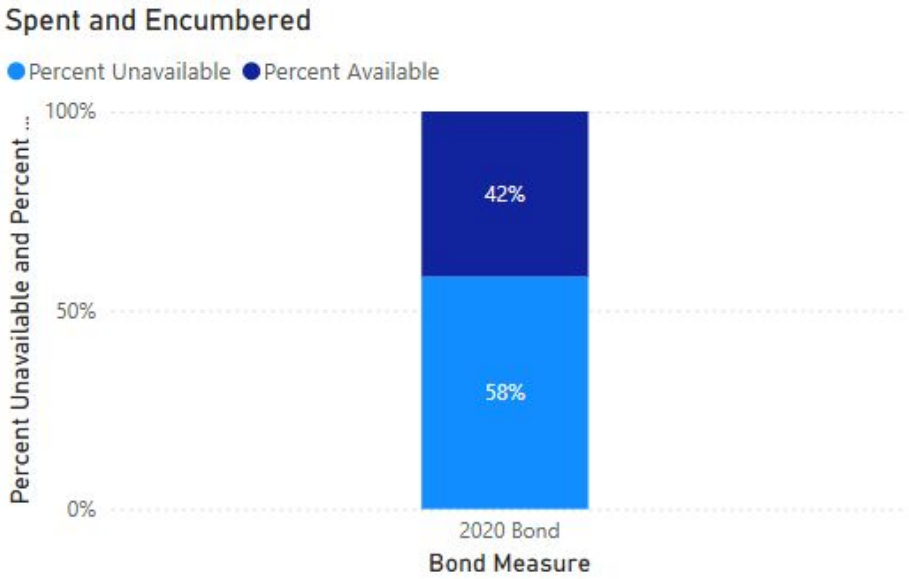

2020 Bond Program Project Status

Total Projects	Pre-Planning	Design Phase	Construction	Post Construction	Completed
103*	1	0	61	2	39

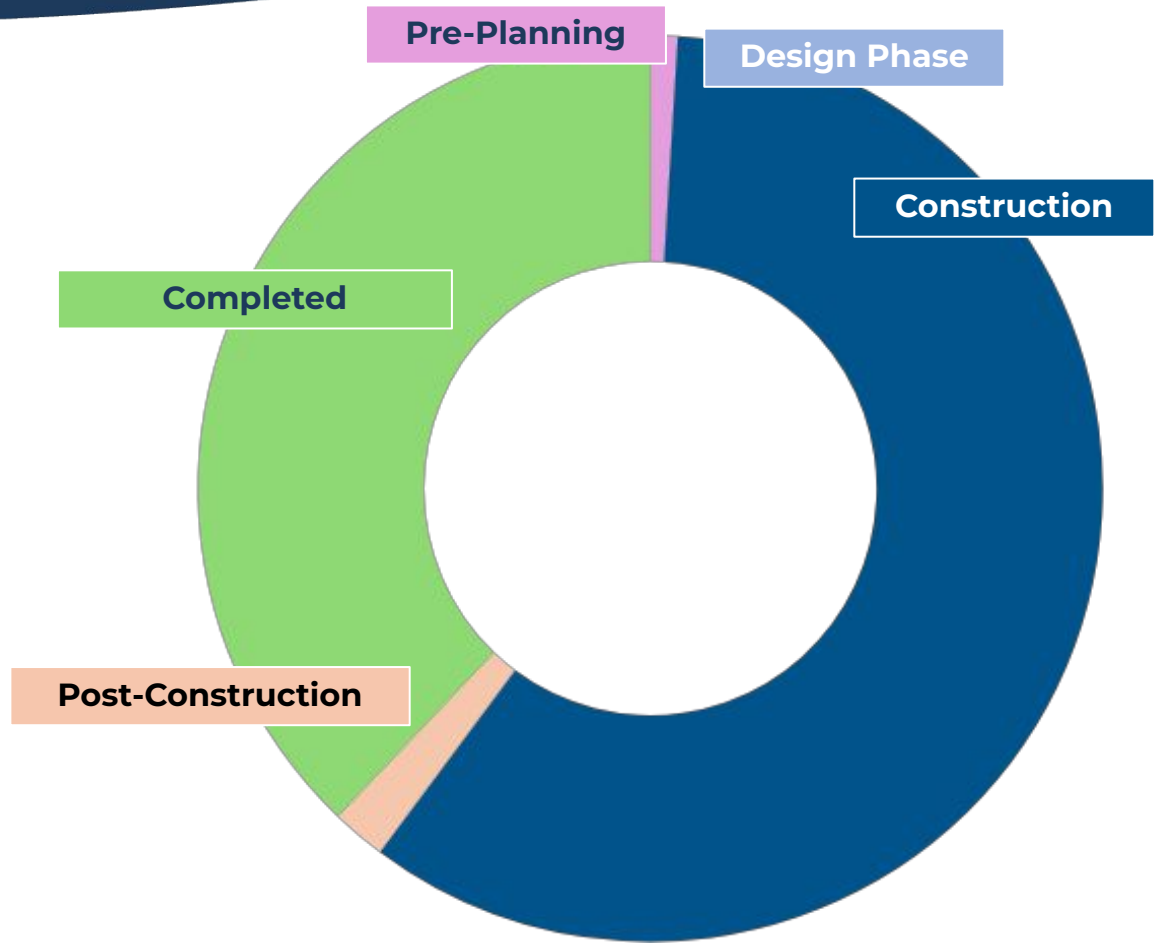


Approximately $551 M remaining to be scheduled for 2020 Bond.

NOTE: source data: Ebuilder reports by bond measure, sorted by project status

2025 Dashboard


Modernizations: Cleveland and Ida B. Wells

Consolidated:, Security upgrades, seismic, technology, improvements for Roosevelt, Lincoln, Franklin and Grant and create athletic hub facilities at Jackson Middle School and Marshall campus.

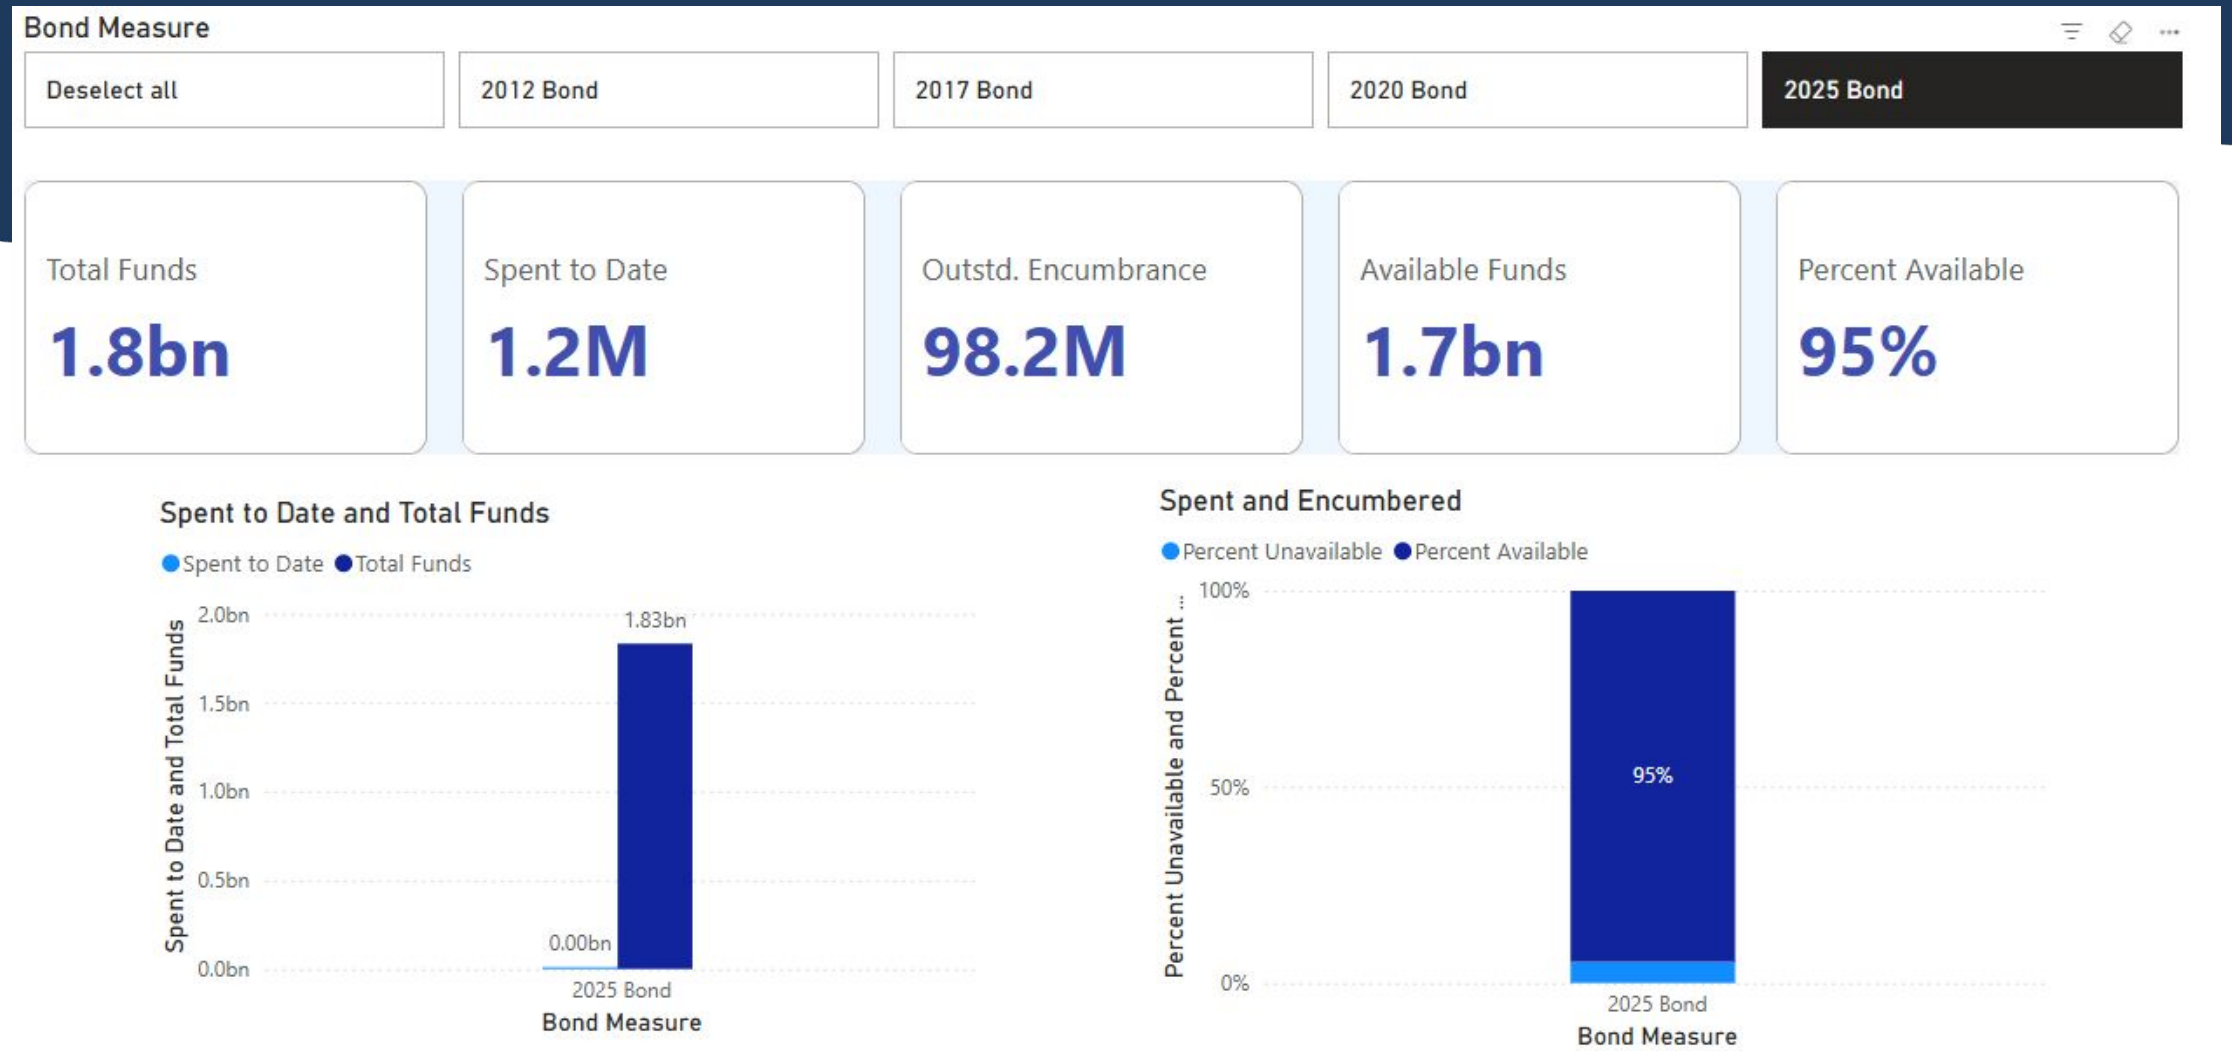

2025 Bond Program Project Status

Total Projects	Pre-Planning	Design Phase	Construction Phase	Post-Construction	Completed
12*	12		0	0	0

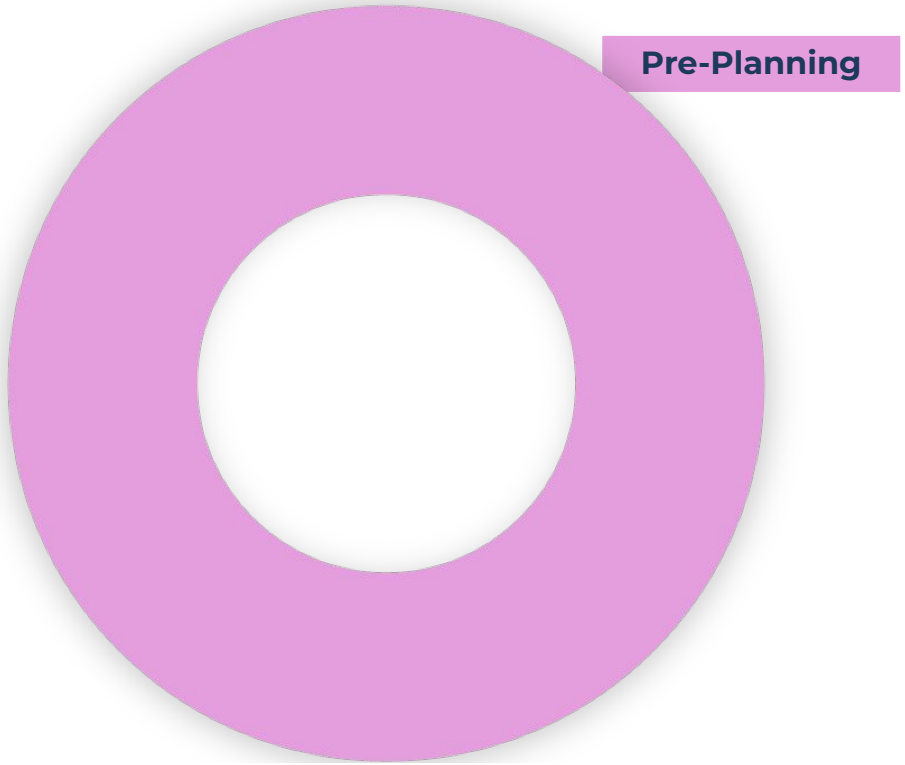

** Total projects will increase as the program progresses.*

Questions
Thank you



Contact us

PPS.NET pubinfo@pps.net (503) 916-2000 501 N Dixion, Portland, OR 97227



PORTLAND
Public Schools
