Bond Program Update



PORTLAND
Public Schools

Date March 10, 2026


Agenda

- Program Status Update
- Schedule Update
- Program Budget Update
- Project Updates

Program Status Update

2012 Bond Program Project Status

Total Projects	Pre-Planning	Design Phase	Construction	Post Construction	Completed
33	0	0	8	2	23

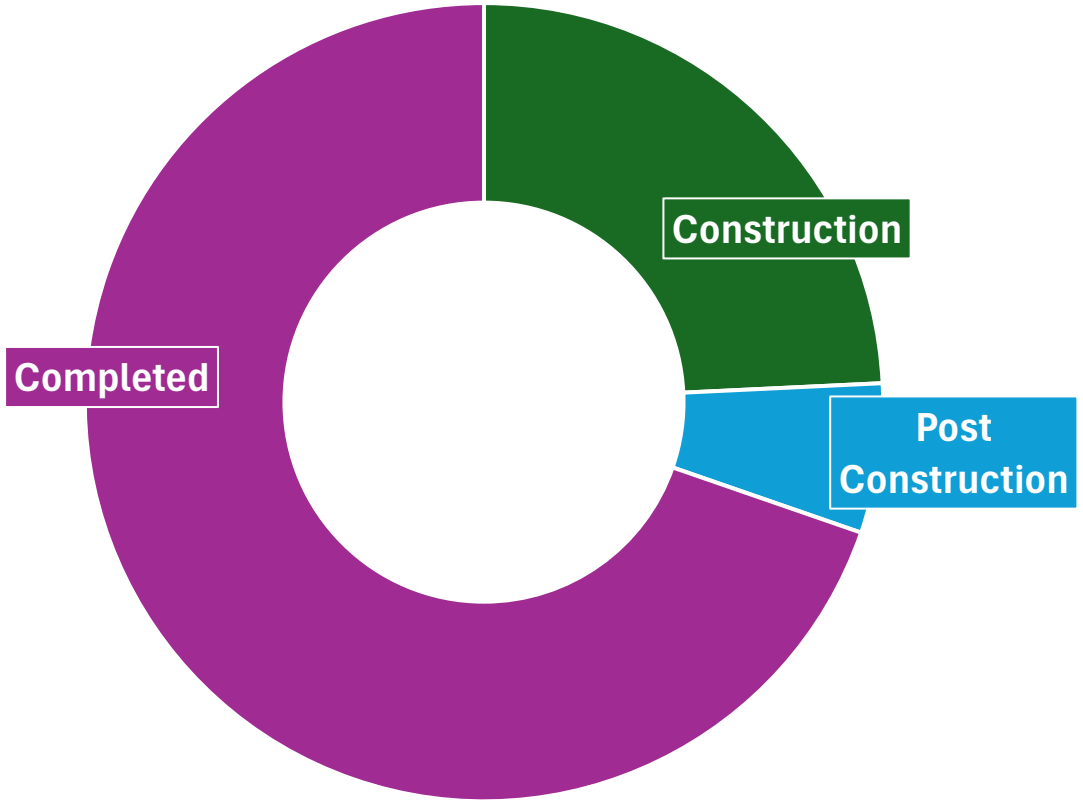


NOTE: source data: Ebuilder reports by bond measure, sorted by project status.

Audit of Project Completion and Closeout statuses is currently ongoing.

2017 Bond Program Project Status

Total Projects	Pre-Planning	Design Phase	Construction	Post Construction	Completed
175	0	0	48	17	110

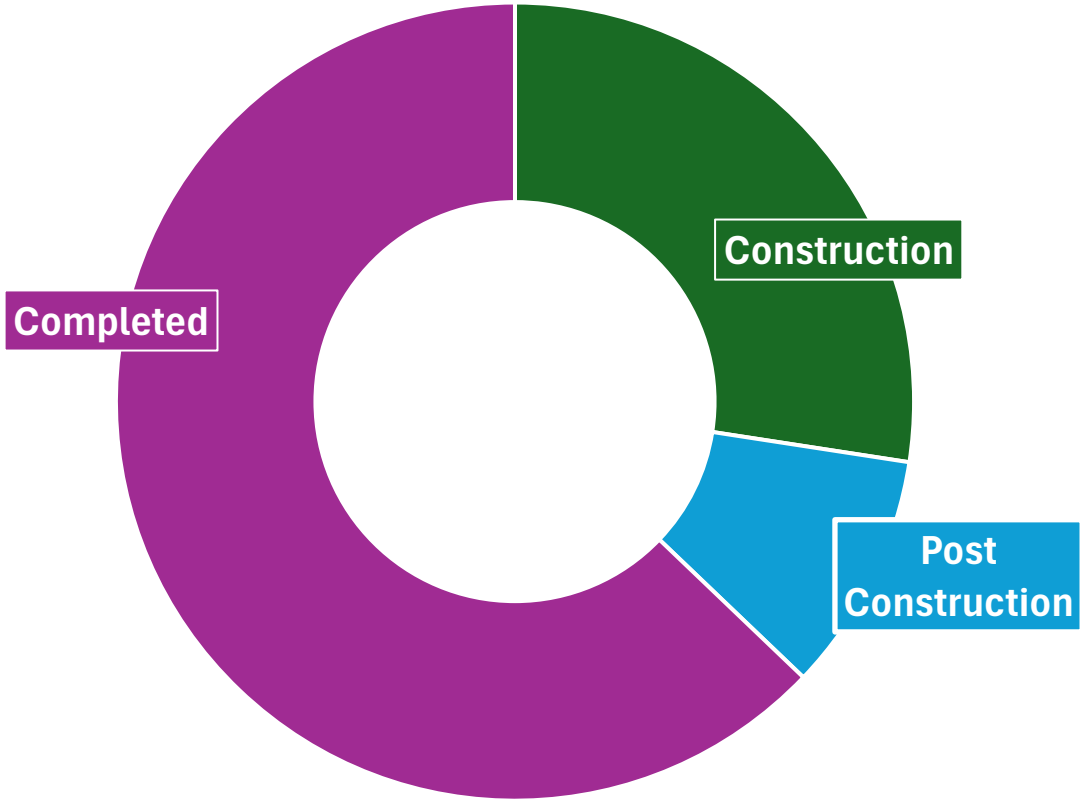


NOTE: source data: Ebuilder reports by bond measure, sorted by project status.

Audit of Project Completion and Closeout statuses is currently ongoing.

2020 Bond Program Project Status

Total Projects	Pre-Planning	Design Phase	Construction	Post Construction	Completed
103*	1	0	61	2	39

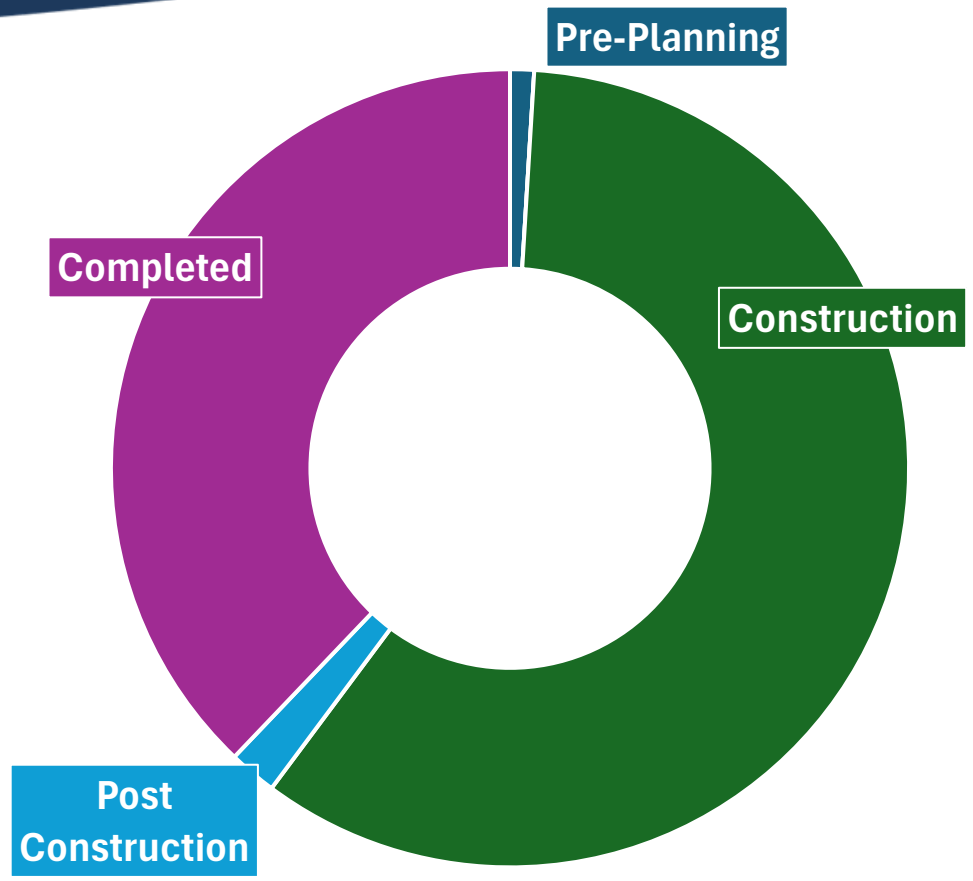


**Approximately $547 M remaining to be scheduled for 2020 Bond.*

NOTE: source data: Ebuilder reports by bond measure, sorted by project status.

Audit of Project Completion and Closeout statuses is currently ongoing.

2025 Bond Program Project Status


Total Projects	Pre-Planning	Design Phase	Construction	Post Construction	Completed
14*	9	5	0	0	0

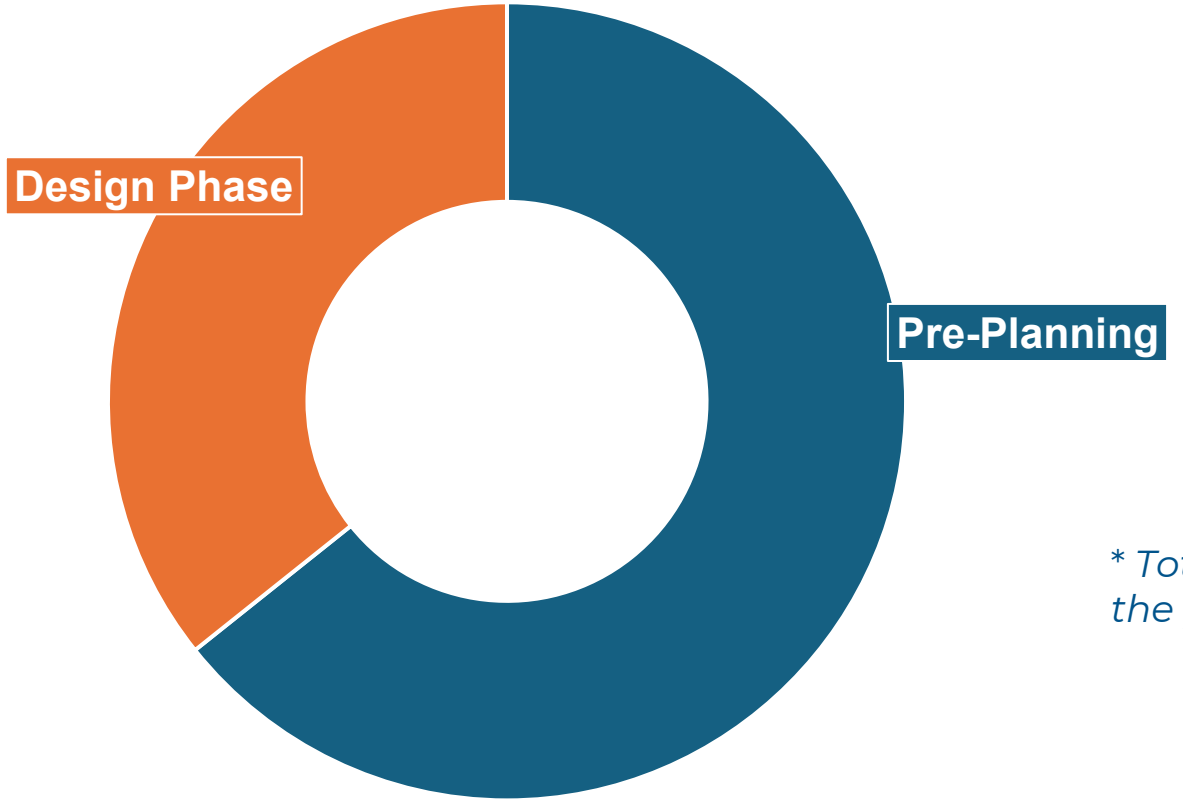

** Total projects will increase as the program progresses.*

Schedule and Budget Update

2025 Bond Schedule

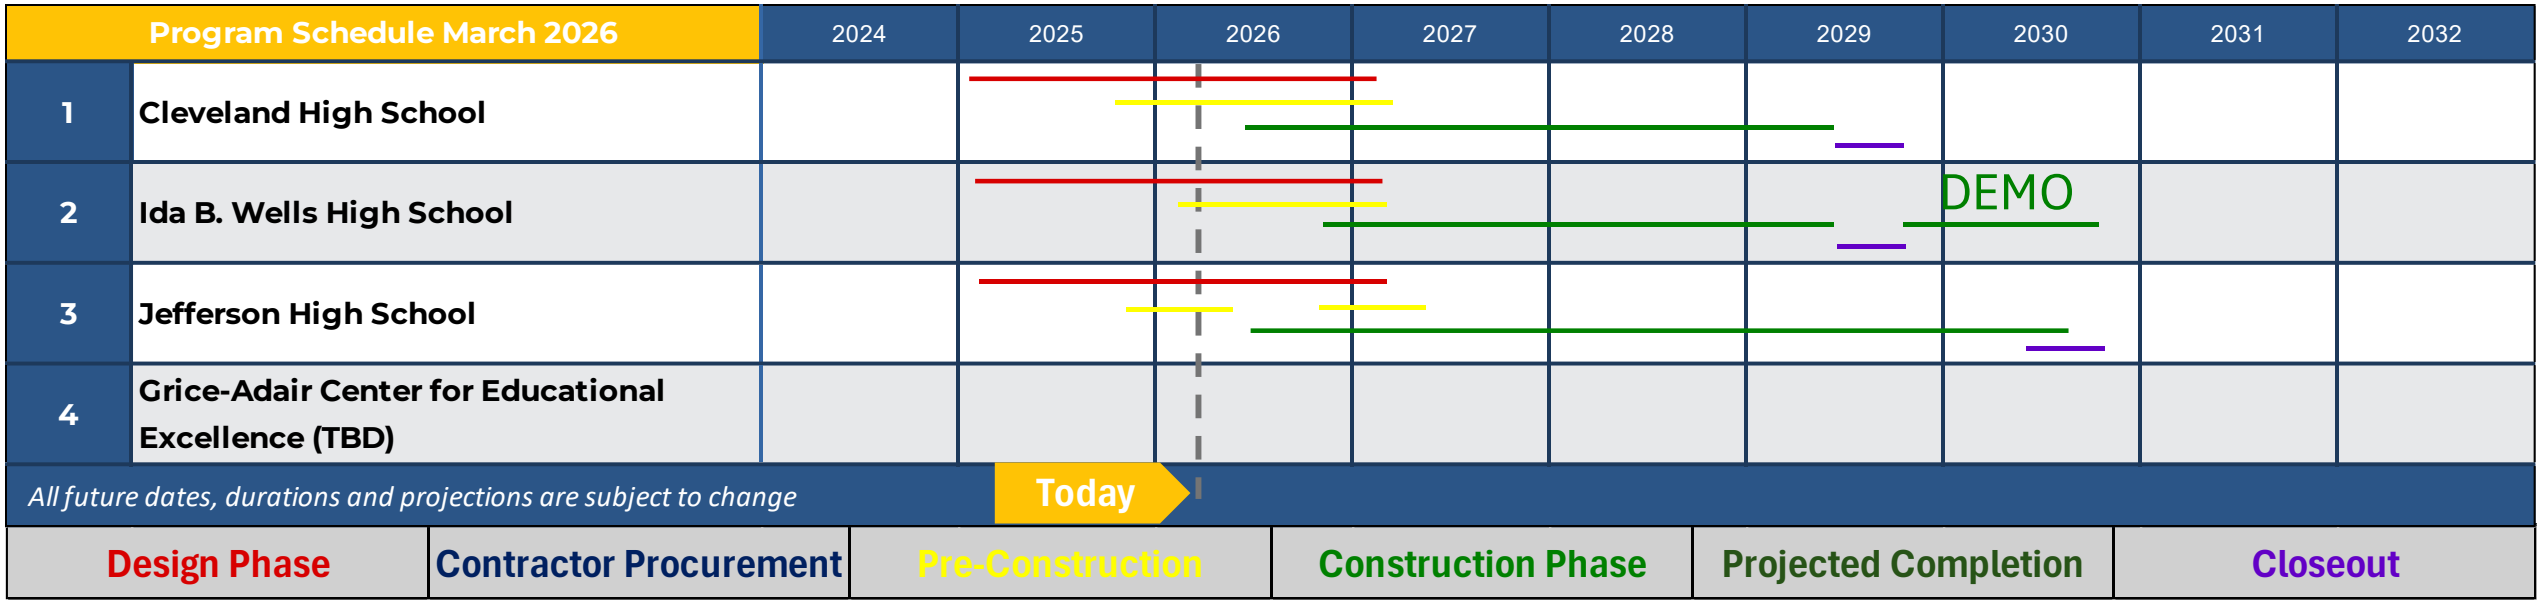



Bond Program Dashboard

Bond Measure

Deselect all | 2012 Bond | 2017 Bond | 2020 Bond | 2025 Bond


Total Funds	Spent to Date	Outstd. Encumbrance	Available Funds	Percent Available
4.6bn	2.1bn	184.7M	2.4bn	51%

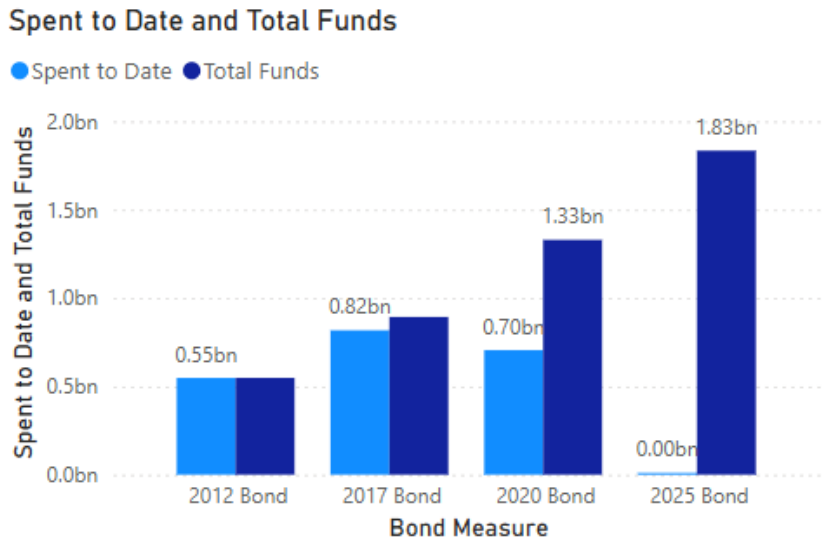

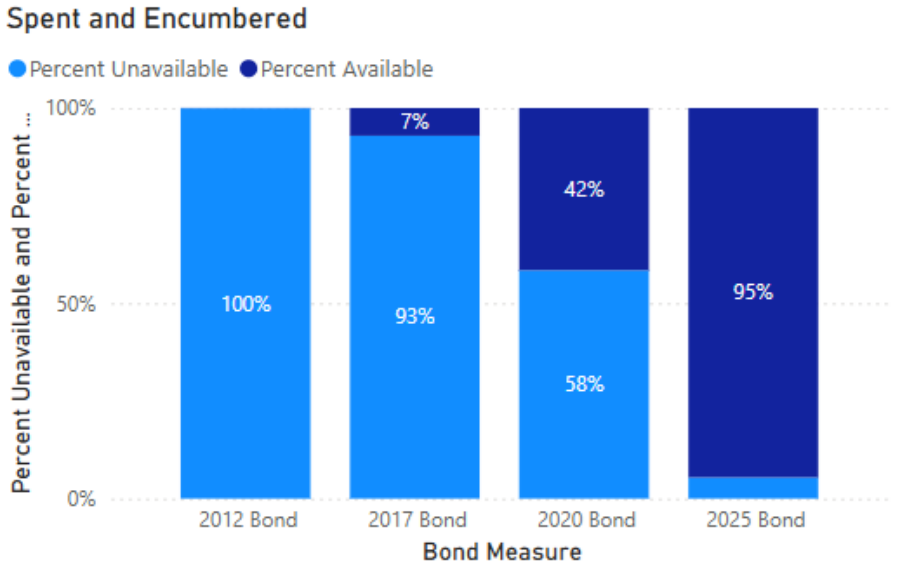


2012 Bond Program Status – Budget Update - Overview

Project	Budget	Outstanding Encumbrance	Amount Paid to Date	Remaining Balance
Franklin HS Mod	$110,950,414	$0	$110,950,414	$0
Grant HS Mod	$155,300,188	$0	$155,300,188	$0
Roosevelt HS Mod	$97,128,043	$0	$97,128,043	$0
Faubion Replace	$30,653,663	$0	$30,653,663	$0
Grant Upper Field	$3,170,988	$0	$3,170,988	$0
RHS Phase IV	$6,153,741	$0	$6,153,741	$0
Other Projects	$112,710,428	$0	$112,710,428	$0
Grant & Franklin Add Ons	$204,140	$50,989	$26,272	$126,879
Administration	$31,284,018	$0	$31,284,018	$0
Contingency	$276,627	$0	$902	$275,725
PPS 2012 Bond Program Total	**$547,832,250**	**$50,989**	**$547,378,657**	**$402,604**

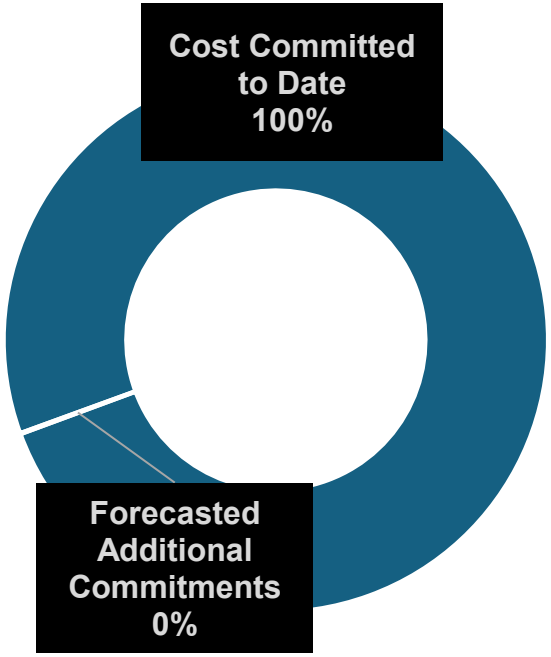

2017 Bond Program Status – Budget Update - Overview

Project	Budget	Outstanding Encumbrance	Amount Paid to Date	Remaining Balance
Benson HS Mod	$146,614,560	$128,434	$143,349,657	$3,136,469
Benson Add Ons	$2,865,020	$1,377,272	$43,638	$1,444,110
Benson Swings	$12,199,595	$0	$12,199,595	$0
Lincoln HS Repl	$240,836,448	$5,976,292	$224,096,580	$10,763,576
Kellogg MS Replace	$57,648,703	$0	$57,648,703	$0
McDanial Mod	$197,000,000	$17,217	$196,810,045	$172,738
Health & Safety	$165,165,443	$4,075,520	$120,728,735	$40,361,188
Athletics	$5,000,000	$174,034	$2,278,729	$2,547,237
Administration	$61,087,301	$555,845	$60,520,902	$10,554
Contingency	$4,221,725	$0	$0	$4,221,725
PPS 2017 Bond Program Total	**$892,638,795**	**$12,304,614**	**$817,676,587**	**$62,657,594**

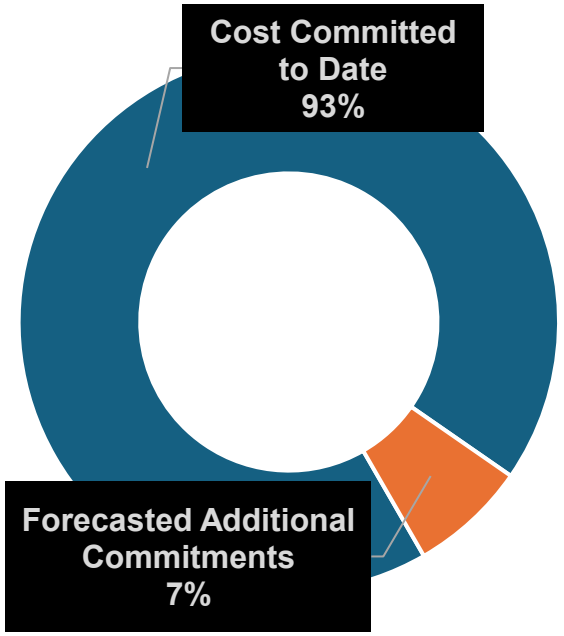


2020 Bond Program Status – Budget Update - Overview

Project	Budget Managed by PROCEDEO	Budget Managed by PPS	Outstanding Encumbrance	Amount Paid to Date	Remaining Balance
Benson 2020 Funds		$164,903,890	$1,141,041	$162,293,196	$1,469,654
Jefferson HS	$366,152,175		$19,209,047	$26,846,946	$320,096,183
CEE	$60,000,000		$1,700	$16,222,680	$43,775,620
Cleveland HS – Design	$25,784,000		$3,131,413	$12,770,499	$9,882,088
Cleveland Swing Site	$137,500		$18,046	$89,180	$30,274
Wells HS – Design	$25,318,534		$5,923,384	$13,663,029	$5,732,121
Roosevelt PhV – Design		$2,000,000	$1,035	$97,625	$1,901,340
MPG Building		$80,447,075	$265,462	$77,944,969	$2,236,645
Curriculum		$63,319,191	$1,126,803	$54,365,370	$7,827,018
Technology		$136,100,000	$23,959,026	$83,074,487	$29,066,486
Infra Projects		$261,139,814	$15,348,115	$229,941,008	$15,850,691
Administration		$63,198,640	$1,661,964	$32,031,061	$29,505,615
2017 Bond Balance		$0	$0	$0	$0
Contingency – OSM		$67,565,814	$0	$0	$67,565,814
Unallocated Funds		$12,515,089	$0	$0	$12,515,089
PPS 2020 Bond Program Total	**$477,392,209**	**$851,189,513**	**$71,787,036**	**$709,340,048**	**$547,454,638**



2025 Bond Program Status – Budget Update - Overview

Project	Budget Managed by PROCEDEO	Budget Managed by PPS	Outstanding Encumbrance	Amount Paid to Date	Remaining Balance
Priority Scope		$190,000,000	$3,296,135	$0	$186,703,865
Athletics		$79,000,000	$1,637,892	$111,100	$77,251,008
Technology		$176,000,000	$28,066,686	$1,942,396	$145,990,918
Physical Education		$10,000,000	$0	$0	$10,000,000
Curriculum		$56,000,000	$0	$0	$56,000,000
Jefferson HS Modernization	$100,000,000		$0	$0	$100,000,000
Cleveland HS Modernization	$449,229,760		$3,395,497	$94,114	$445,740,149
Ida B Wells HS Modernization	$432,000,000		$0	$0	$432,000,000
Elementary & Middle Schools		$168,770,240	$0	$0	$168,770,240
Admin		$83,050,000	$60,841,932	$1,214,008	$20,994,060
Contingency		$83,050,000	$0	$0	$83,050,000
PPS 2020 Bond Program Total	**$981,229,760**	**$845,870,240**	**$97,238,142**	**$3,361,618**	**$1,726,500,240**

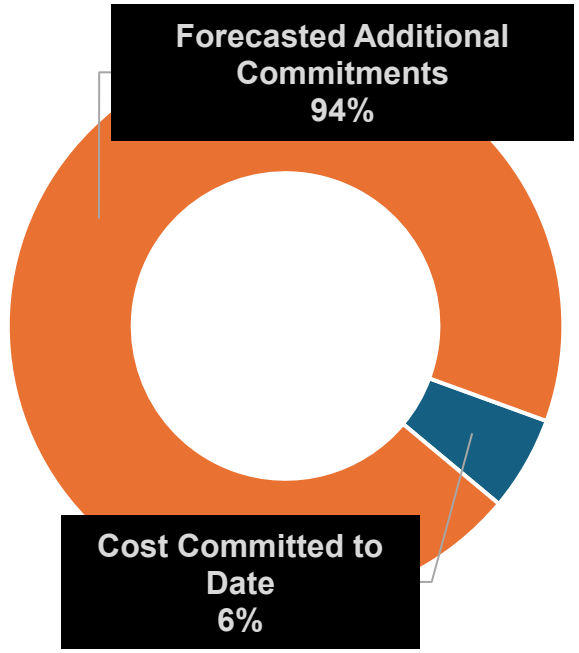

Project Updates

Cleveland HS Modernization

3400 SE 26th Ave, Portland, OR 97202

Senior CM
Drew Schott

Contractor (CMGC)
Skanska

PPS Zone 6
Stephanie Engelsman

Architect
Mahlum

Project Budget

Total Budget	CMGC GMP
$472,553,760	GMP: TBD

Project Overview

Current Phase: In Design
Scope: New Facility
New Facility: 297,000 SF
Construction Start: Summer 2026
Tentative Sub Com: Summer 2029
GMP Construction Timeline: TBD

General Scope

- ✓ 2 new four-story buildings connected by a skybridge
- ✓ Dynamic outdoor courtyard
- ✓ New arts theater, black box theater, 2 gyms, and dance and wrestling studios
- ✓ Improvements to track and athletic fields

Project Status

Design Procurement
100%

Design
50%

DDs Complete

Construction
0%

Construction NTP
Pending

Project Update

1	Improvements for Marshall starting in March for swing site moves in June.
2	Groundbreaking at 10am on June 13, 2026.

Project Floor Plan

See next slide for floor plans


PROCEDEO | PORTLAND Public Schools

Cleveland HS

Floor Plans Levels 1-4

L01

- FLEX LEARNING
- SPED + LRC
- CTE
- VISUAL + PERFORMING ARTS
- WRAP-AROUND SERVICES
- GYM + ATHLETICS
- MISCELLANEOUS
- CUSTODIAL

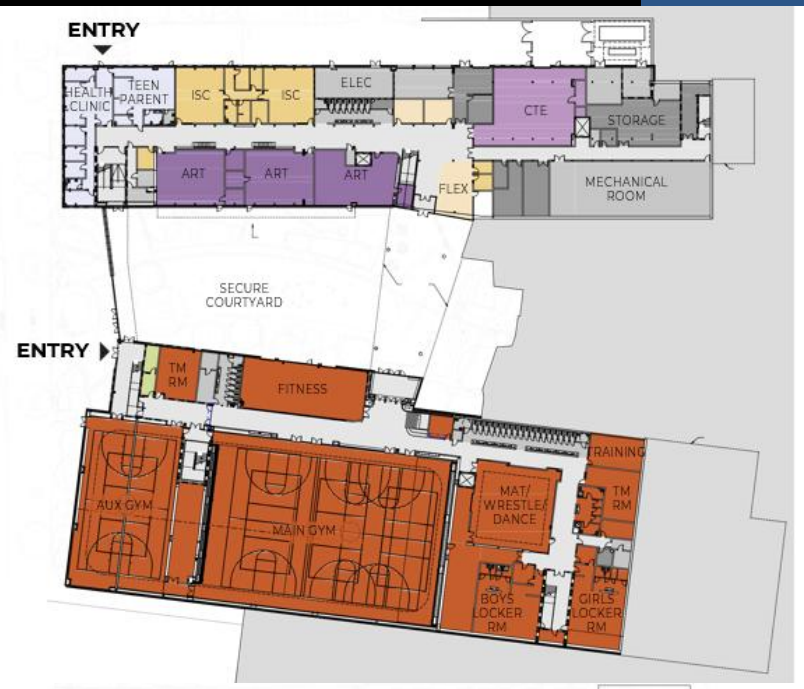

L02

- ADMIN / STUDENT SPACE
- COUNSELING / CAREER
- FLEX LEARNING
- SPED + LRC
- GENERAL CLASSROOMS
- VISUAL + PERFORMING ARTS
- STUDENT COMMONS
- GYM + ATHLETICS
- MISCELLANEOUS
- CUSTODIAL



L03

- ADMIN / STUDENT SPACE
- LIBRARY / MEDIA CENTER
- FLEX LEARNING
- SPED + LRC
- GENERAL CLASSROOMS
- CTE
- VISUAL + PERFORMING ARTS
- MISCELLANEOUS
- CUSTODIAL



L04

- ADMIN / STUDENT SPACE
- FLEX LEARNING
- SPED + LRC
- GENERAL CLASSROOMS
- CTE
- MISCELLANEOUS
- CUSTODIAL



Cleveland HS



Conceptual Rendering of Classroom

Conceptual Rendering of Exterior

In Design

Cleveland HS

Conceptual Rendering of Aerial View



In Design

Jefferson HS Modernization

5210 N Kerby Ave, Portland, OR 97217

Senior CM
Drew Schott

Contractor (CMGC)
Colas Hoffman

PPS Zone 2
Michelle DePass

Architect
BORA & LEVER

Project Budget

Total Budget	CMGC GMP
$466,007,500	GMP: $TBD

Project Overview

Current Phase: In Design
Scope: New Facility
New Facility: 299,485 SF
Construction Start: Spring 2026
Tentative Sub Com: Fall 2030
GMP Construction Timeline: TBD

General Scope

- ✓ New all-electric multi-story building
- ✓ Includes a theater, health center, teen parent center, and dance studios
- ✓ Track and field relocated to the site of the current structure
- ✓ New softball field and baseball/soccer multiuse field

Project Status

Design Procurement
100%

Design
50%

DDs Complete

Construction
0%

Construction NTP
Pending

Project Update

1	Design Development is complete and documents have been received.
2	Groundbreaking at 10am on May 29, 2026.

Project Floor Plan

See next slide for floor plans

PROCEDEO | PORTLAND Public Schools

Jefferson HS


Floor Plans Levels 1-4



Level 1



Level 2

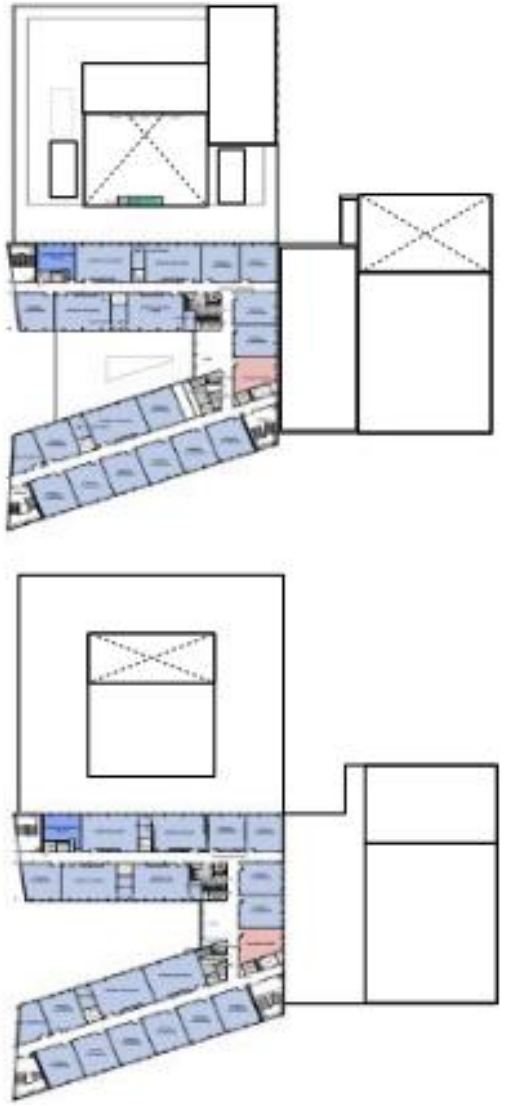

Levels 3-4

Jefferson HS

Conceptual Rendering of Exterior



In Design

Jefferson HS

Conceptual Rendering of Interior



In Design

Ida B Wells HS Modernization

1151 SW Vermont St, Portland, OR 97219

Senior CM
Drew Schott

Contractor (CMGC)
Hoffman Construction

PPS Zone 1
Christy Splitt

Architect
BORA Architects

Project Budget

Total Budget	CMGC GMP
$449,350,000	GMP: $TBD

Project Overview

Current Phase: In Design
Scope: New Facility
New Facility: 283,867 SF
Construction Start: Winter 2026
Tentative Sub Com: Fall 2030
GMP Construction Timeline: TBD

General Scope

- ✓ New four-story building including instructional spaces for Career Technical Education programs
- ✓ New performing arts, commons, and outdoor spaces
- ✓ Full complement of athletic fields and upgrade of existing fields on the Rieke side
- ✓ The existing pool is not in the scope, but a new pool support building is included

Project Status

Design Procurement
100%

Design
50%

DDs Complete

Construction
0%

Construction NTP
Pending

Project Update

1	Page turn sessions are being scheduled with Stakeholders to review Design Development drawings.
2	Groundbreaking date to be determined.


Project Floor Plan

See next slide for floor plans


Ida B Wells HS

Floor Plans Levels 0-3


LEVEL 0

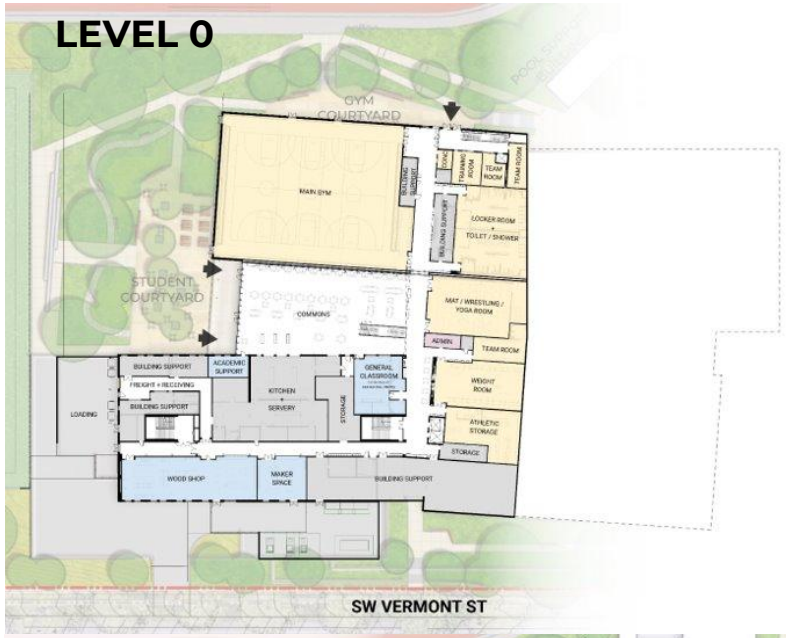

LEVEL 1 (Main Entrance)

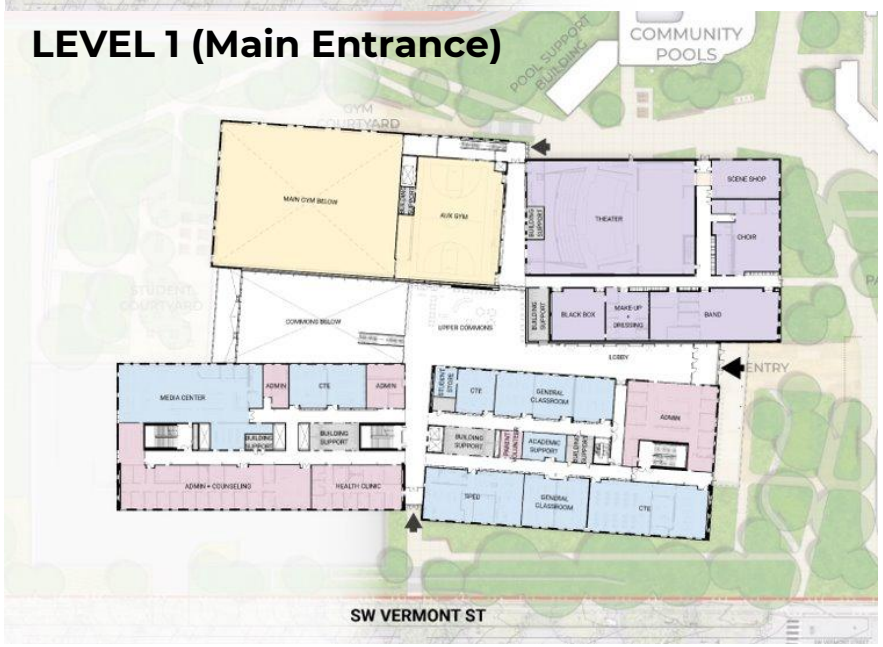

LEVEL 2

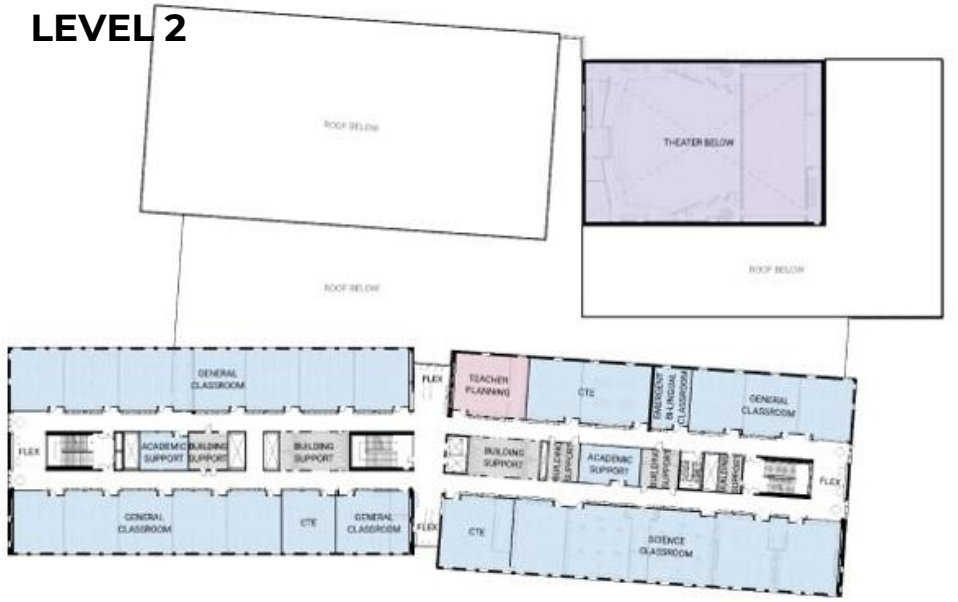

LEVEL 3



Ida B Wells HS



Conceptual Rendering of Aerial View

In Design

Ida B Wells HS

Conceptual Rendering of Exterior



In Design

Grice-Adair Center for Educational Excellence

1 N. Fremont St, Portland, OR 97227

Senior CM
Drew Schott

Contractor (CMGC)
TBD

Architect
TBD

Project Budget

Total Budget	CMGC GMP
$60,000,000	GMP: $TBD

Project Overview

Current Phase: Planning
Scope: Renovations
Renovations: TBD
Construction Start: TBD
Tentative Sub Com: TBD
GMP Construction Timeline: TBD

General Scope

✓ TBD

Project Status

Design Procurement
75%

Design
0%

Construction
0%

Construction NTP
Pending


Project Update

1	PPS purchased the 1 North building on 12/15
2	18 Architect Engineering firms currently being qualified from RFP process. Board approval targeted for 4/2026
3	Programming upon architectural award

Grice-Adair Center

Exterior



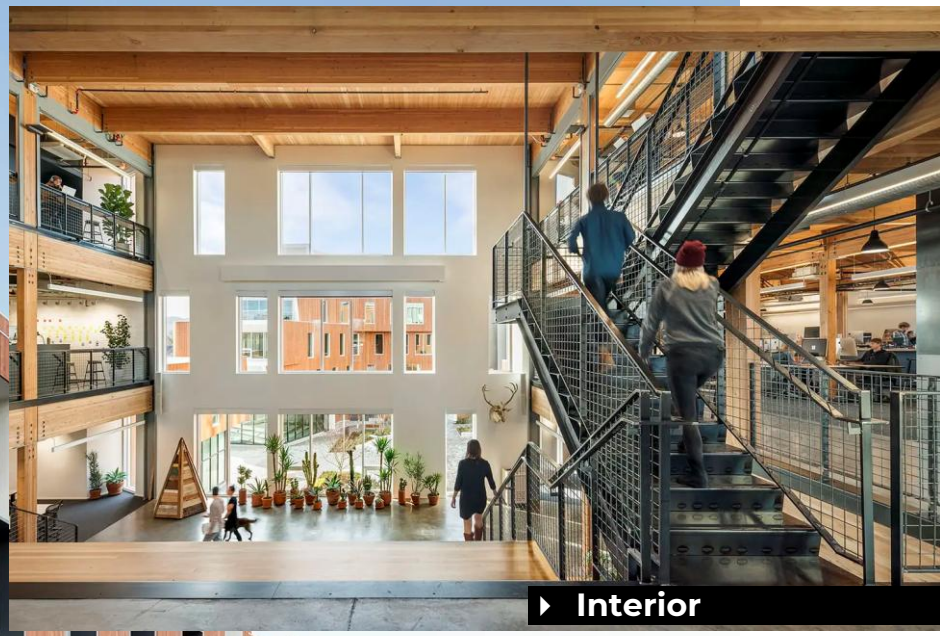


Interior

Planning

Grice-Adair Center

Courtyard Exterior

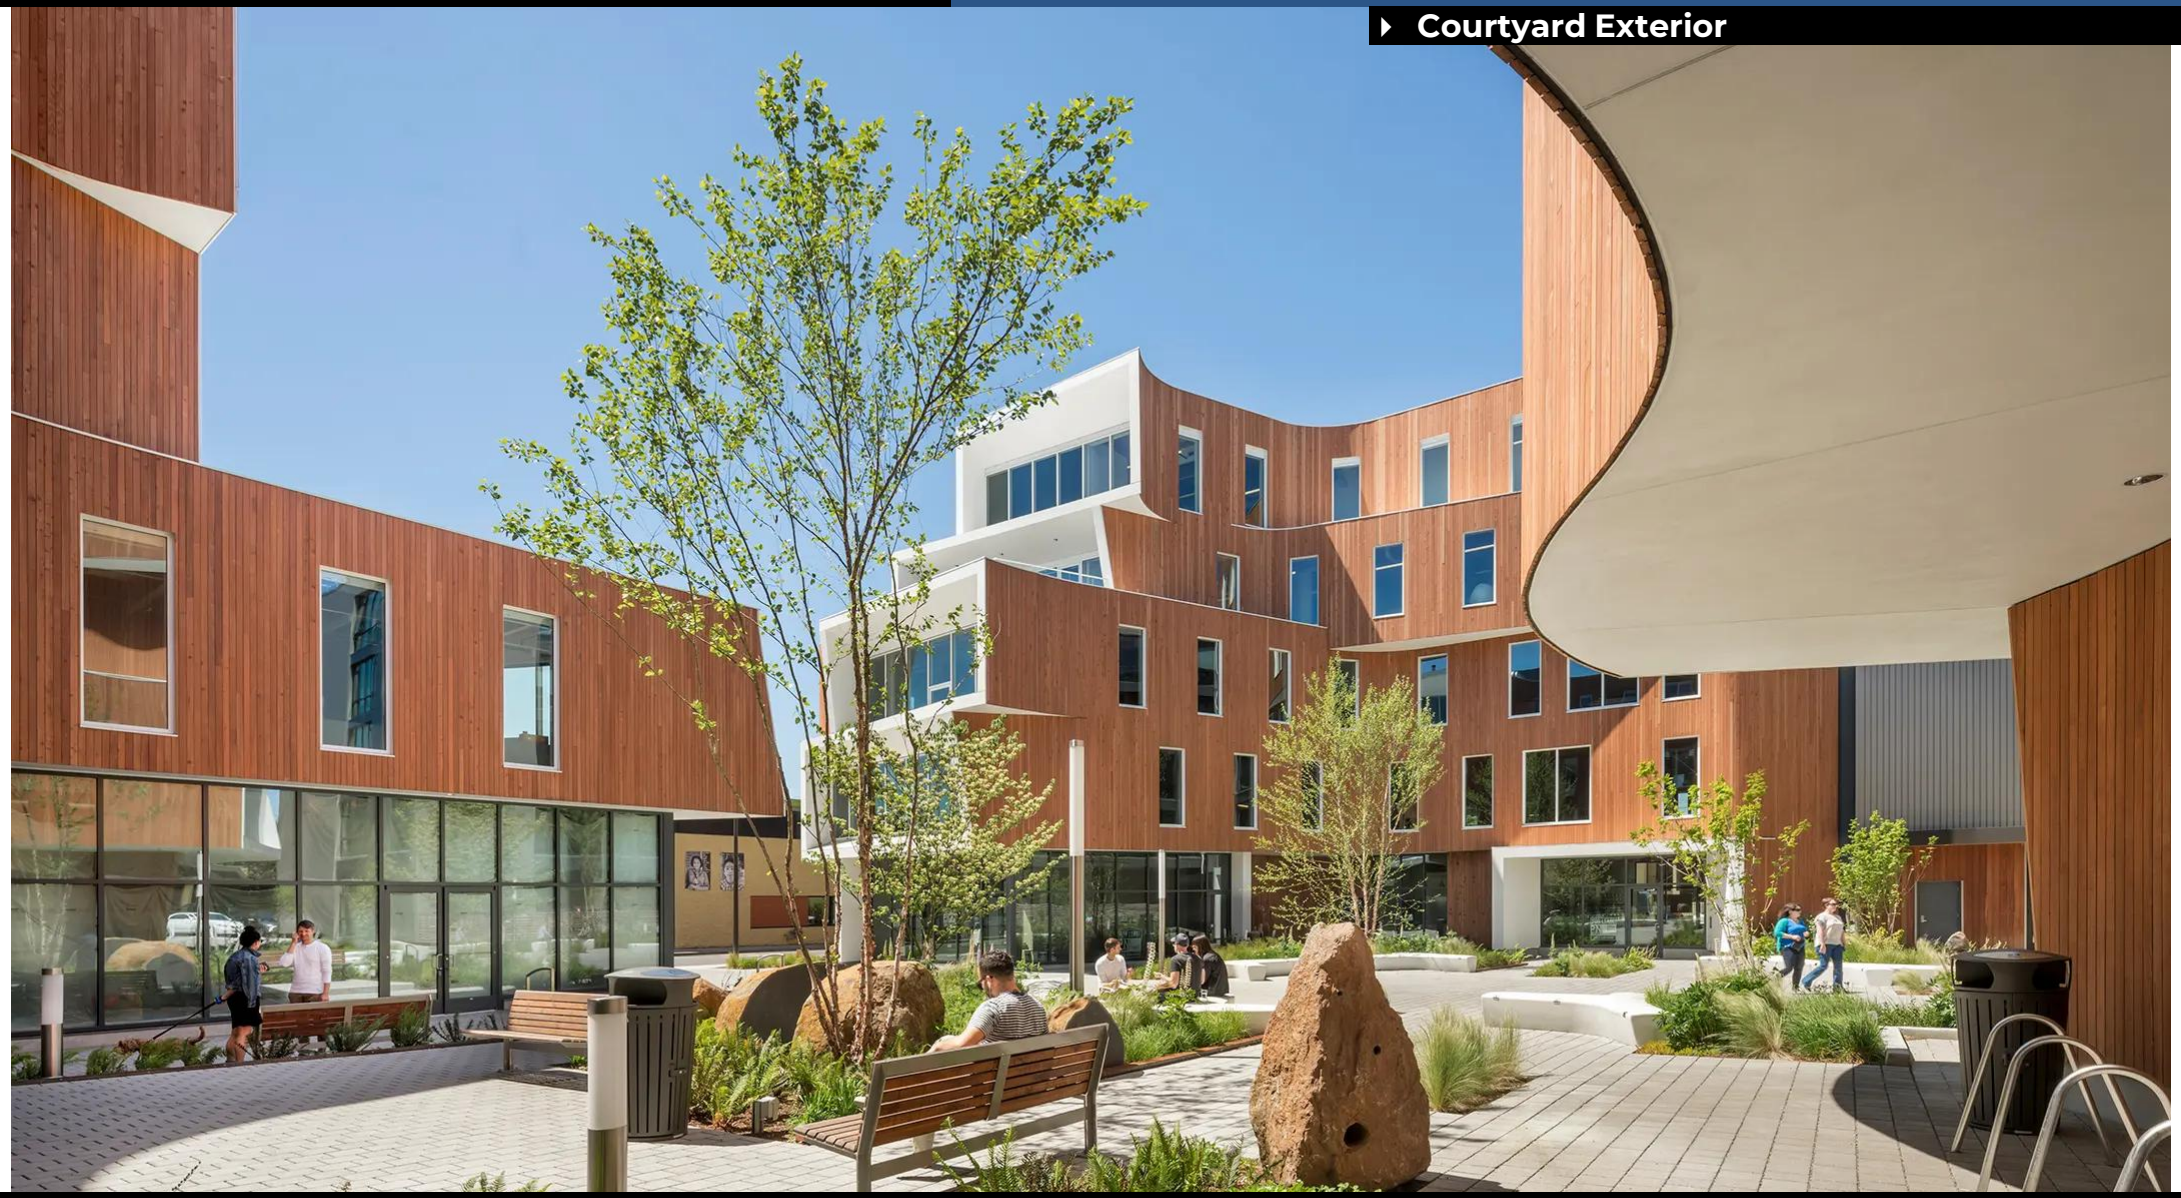

Consolidated Projects Update

2017 Bond

Re-Roofs w/ Seismic Add Alternate

- Vestal bid due on the 6th
- Marshall, Chavez, and Woodmere bids due on the week of the 9th.

Consolidated Projects Update

2020 Bond

HVAC/Controls

- Bridger and Kelly (Mechanical) in close-out

SPED

- ADA-SPED upgrade projects in close-out

Consolidated Projects Update

2025 Bond

Grant HS

- Permanent Lighting – Directional boring, poles, and lighting installation planned for Spring ‘26, with potential operational readiness as early as April ‘26 and full completion by May ‘26.

Athletics

- Powell Park, Franklin, Lincoln, and Roosevelt fields remain high-priority project carryovers with planned seating and field upgrades.

Consolidated Projects Update

2025 Bond

Marshall MS Athletics Hub

- Turf field, track, tennis court resurfacing and lighting upgrades are in progress; future upper-field redevelopment (multi-sport, baseball-primary, turf complex) is pending land use and AE procurement, likely 2027 to start construction.

Jackson MS Athletics Hub

- The Schematic Design (SD) phase is underway (Notice to Proceed was issued 2/11/26). Track and field reconstruction and drainage scheduled to start June ‘26 as part of a larger multi-phase athletics modernization. The second phase of work to address multi-use field and subsidiary facility needs in queue for land use submission with a planned start in November ‘26.

Questions
Thank you



Contact us

PPS.NET pubinfo@pps.net (503) 916-2000 501 N Dixion, Portland, OR 97227



PORTLAND
Public Schools
