PORTLAND Public Schools

Facility Improvement & Oversight Committee

March 17, 2026



Agenda

- Jefferson High School - Shell Option Update
- 2025 Bond Athletic Projects Update
  - Schedule
  - Project Details
- Audit Items - Status Update
- Bond Program Procurement Update
- Modernization Land Use Update



Jefferson HS Update

Jefferson HS - Shell Option Update


In December 2025 Directive to Evaluate expedited student occupancy on the 1st–2nd floors of new building while completing 3rd–4th floors.

Criteria Identified for Feasibility

- Schedule
- Accommodation
- Cost
- Operational concessions for early occupancy

Schedule:

- During the feasibility study the team was able to identify efficiencies within the proposed schedule
- Students able to occupy the site 6 weeks earlier (July ‘29 vs. August ‘29) but the time saved is only over summer break.

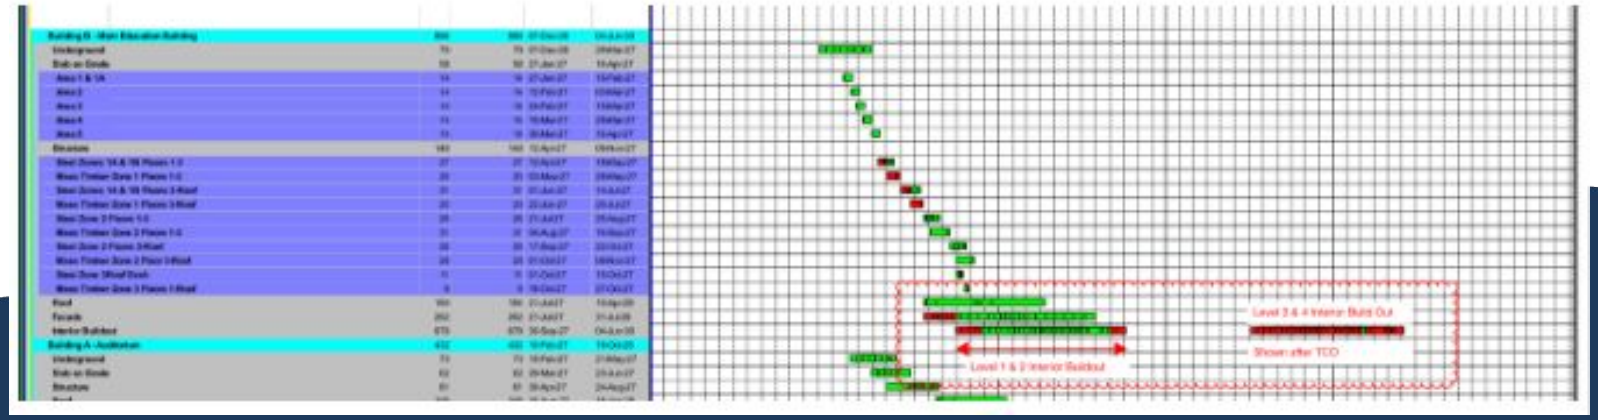

Jefferson HS - Shell Option Update

Accommodation:

- Expected increased enrollment would be able to be accommodate on 1st and 2nd Floors for the ‘28-’29 school year. Projected enrollment of 770 students at 85% utilization.
- 6 Temporary Science labs would be needed, and could be accommodated in CTE and General Education classrooms.

Cost:

- Although by shortening the schedule we would identify savings within General Conditions/General Requirements for the project approximately $500,000. Due to the the potential for increased labor inefficiencies, the NET outcome for expedited would have been a potential increase to the project budget of approximately $600,000.00.

Operational Concessions for Early Occupancy:


- Increased noise, dust and safety considerations inherent to active construction
- Temporary instructional spaces
- Site constraints, parking, logistics

Conclusion:

Technically feasible but due to the minimal schedule advantage identified throughout feasibility study, Leadership, along with RISE’s full agreement, has determined the best course of action is to remain on the current project schedule with an anticipated move -in date of **August 2029.**

Jefferson High School

Overall Project Schedule

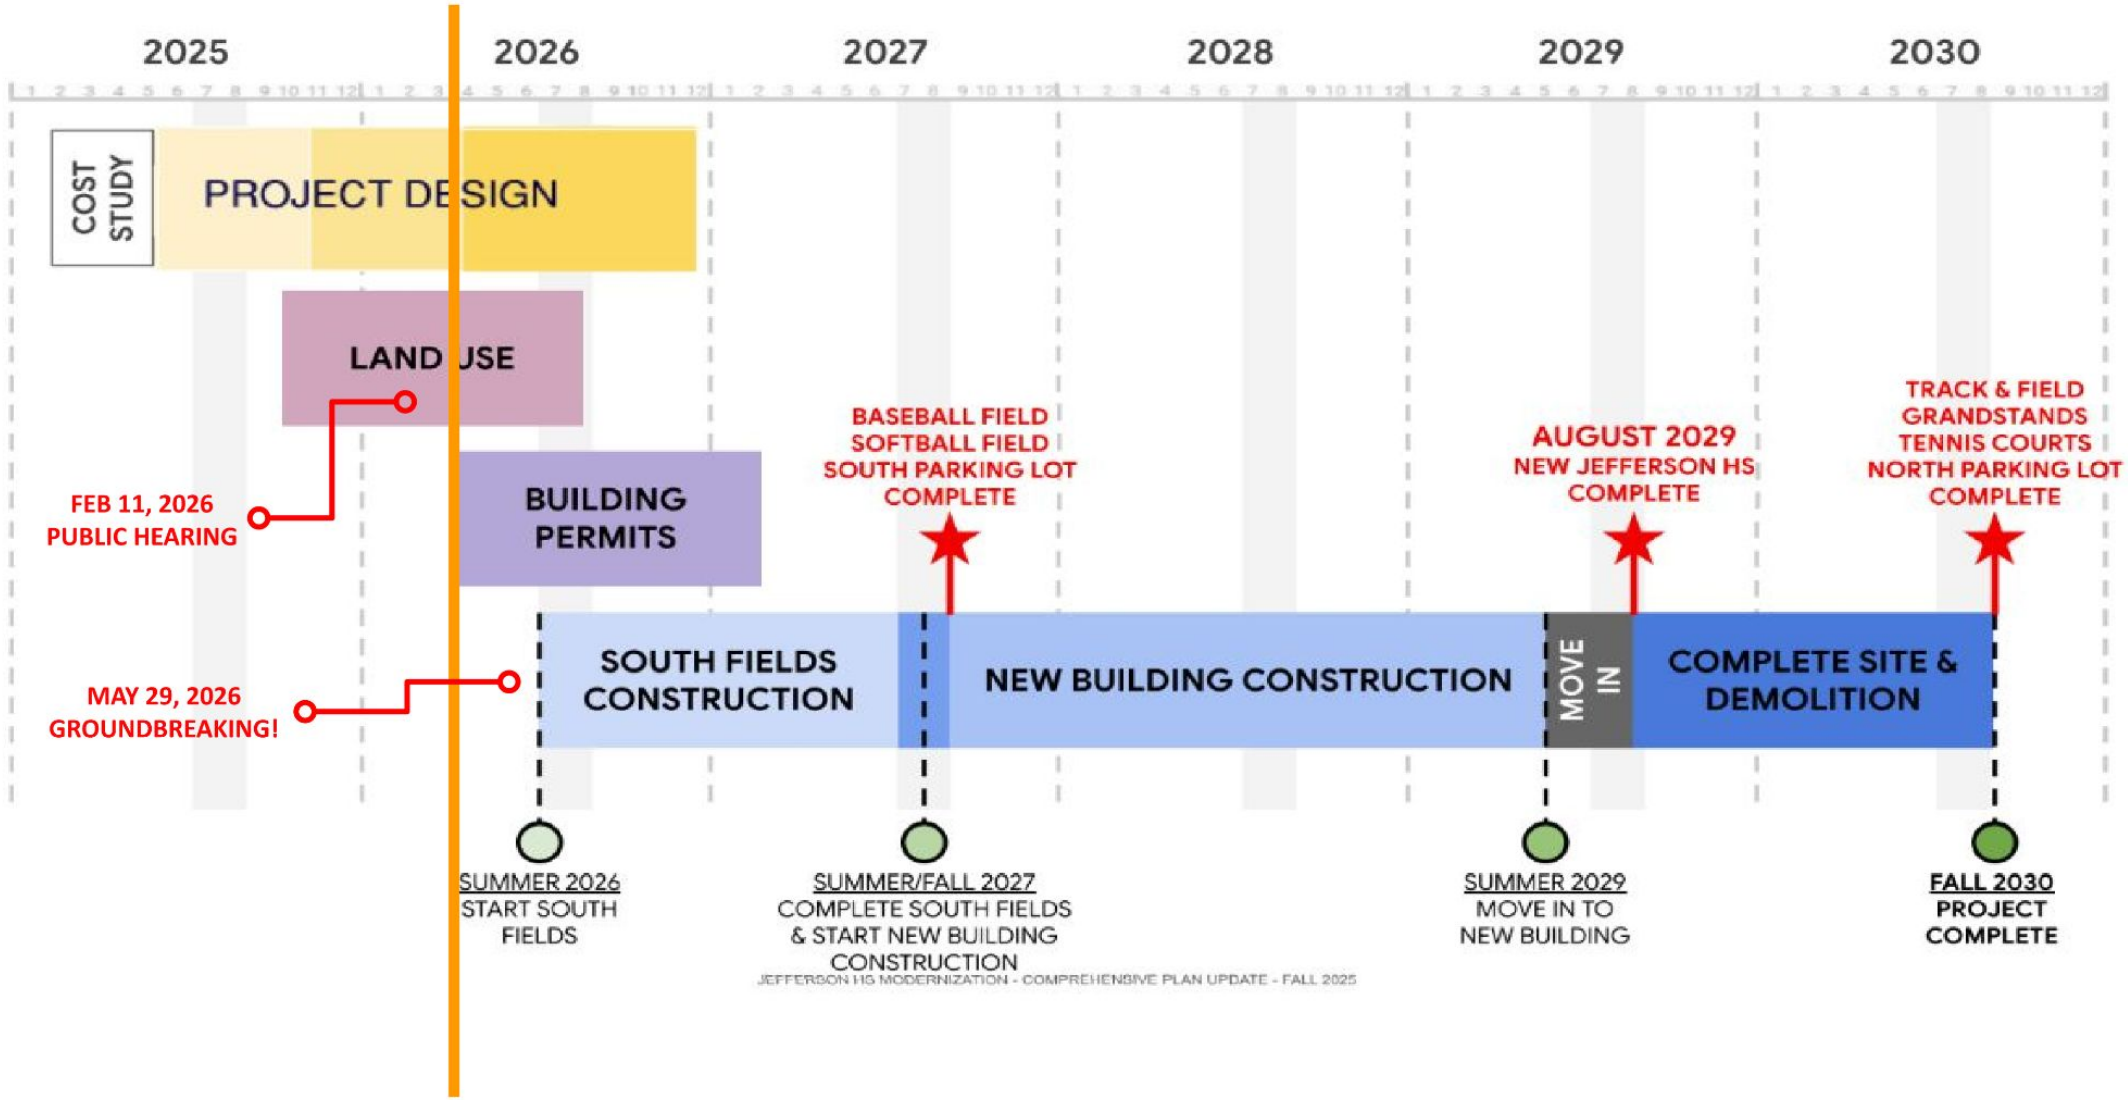

Athletics Updates

Major Athletic Updates - Grant Bowl

Lighting Installation (Phase 1)

- Scheduled Spring start to construction
- Power/Utility supplier received an executed contract in Late February
- Currently working through mobilization efforts

Seating Upgrades (Phase 2)

- Increased capacity, improved restroom facilities, and improved concessions facilities
- Currently in Pre-Planning, schedules still being developed

Major Athletic Updates - Jackson Hub

Track and Field Reconstruction (Phase 0)

- Reconstruction of track, new Track & Field equipment, and other site improvements
- Design Drawings on track to begin on 3/9 with Construction to start this Summer

Multi-Use Turf Field (Phase 1A)

- Construction of new multi-use field striped for soccer, baseball, softball, and lacrosse
- Schematic Design on track to begin in Late March

Batting Facility (Phase 1B)

- Construction of new indoor batting facility and storage
- Currently in Pre-Planning, schedules still being developed

Major Athletic Updates - Marshall Hub

Track & Field and Tennis Court Upgrades (Phase 1)

- Resurfaced track, synthetic turf on football field, resurfaced tennis courts, lighting improvements
- Construction underway
- Scheduled to be complete in May

Multi-Use Turf Field (Phase 2)

- Construction of new multi-use field striped for soccer, baseball, softball, and lacrosse
- Currently in Pre-Planning, schedules still being developed

Major Athletic Updates - Marshall Hub



Major Athletic Updates - Marshall Hub



Major Athletic Updates - Marshall Hub



Major Athletic Updates - Powell Park

Baseball Field Enhancements

- New synthetic turf field, improved bleachers, improved lighting
- Used by Cleveland HS, owned by Portland Parks & Recreation
- PPS currently coordinating with the City to develop a long-term agreement to improve the field

Major Athletic Updates - Roosevelt HS

Baseball and Softball Field Enhancements; Grandstand Improvement

- New synthetic turf field, new hitting facility, rebuilt grandstand

- Currently in Pre-Planning, schedules still being developed

Major Athletic Updates - Franklin HS

Baseball and Softball Field Enhancements

- Improved synthetic turf field and bleachers, new hitting facility
- Currently in Pre-Planning, schedules still being developed


Major Athletic Updates-W Sylvan/Lincoln

Multi-Use Field Enhancements

- New synthetic turf multi-use field striped for soccer, baseball, softball, and lacrosse with lighting
- Facilities will be available to both West Sylvan MS and Lincoln HS
- Currently in Pre-Planning, schedules still being developed

Athletics Schedule

Activity Name	Duration	Start	Finish
Portland PS Bond Program			
ATHLETIC FACILITIES			
GRANT HS LIGHTS			
DESIGN	37	01-Jan-25 A	28-Feb-25 A
LAND USE PERMIT	150	01-Mar-25 A	08-Aug-25 A
PERMITTING	65	21-Nov-25 A	16-Feb-26 A
CONSTRUCTION	45	02-Mar-26	01-May-26
CLOSE-OUT	10	06-May-26	19-May-26
MARSHALL MS HUB			
CONSTRUCTION	195	01-Jan-26 A	30-Apr-26
PERMITTING	66	01-Jan-26 A	01-Jan-26 A
DESIGN	35	01-Jan-26 A	01-Jan-26 A
CLOSE-OUT	5	05-May-26	11-May-26
HUB FIELD AND LIGHTS			
LAND USE PERMIT	70	01-Jan-26 A	01-Jan-26 A
MARSHALL SWING SPACE WORK	60	01-Jan-26 A	30-Apr-26
A/E PROCUREMENT	34	01-Jan-26 A	01-Jan-26 A
UPPER FIELD (MULTI-USE)			
A/E PROCUREMENT	34	05-Jan-26 A	23-Mar-26
LAND USE PERMIT	203	24-Mar-26	31-Dec-26
JACKSON MS HUB			
PHASE 0			
LAND USE PERMIT	43	01-Jan-24 A	10-Sep-24 A
DESIGN	37	11-Feb-26 A	24-Apr-26
DIRECT SELECT / COOP PROCUREMENT	25	11-Feb-26 A	27-Mar-26
PERMITTING	26	27-Apr-26	01-Jun-26
CONSTRUCTION	107	02-Jun-26	28-Oct-26
PHASE 1A			
DESIGN	37	11-Feb-26 A	30-Jul-26
LAND USE PERMIT	55	27-Apr-26*	10-Jul-26
PERMITTING	77	31-Jul-26	16-Nov-26
CONSTRUCTION	107	17-Nov-26	14-Apr-27
PHASE 1B			
DESIGN	238	01-Apr-26	26-Feb-27
PERMITTING	119	17-Nov-26	30-Apr-27
CONSTRUCTION	154	01-Jun-27	31-Dec-27
CLOSE-OUT	8	05-Jan-28	14-Jan-28
POWELL PARK			
P&R NEGOTIATIONS	105	05-Jan-26 A	29-May-26
DESIGN	20	01-Jun-26	26-Jun-26
LAND USE PERMIT	60	29-Jun-26	18-Sep-26
PERMITTING	60	21-Sep-26	11-Dec-26
CONSTRUCTION	196	14-Dec-26	13-Sep-27
CLOSE-OUT	5	16-Sep-27	22-Sep-27
JEFFERSON FIELD			
DESIGN (BORA)	0	01-Sep-25 A	30-Sep-25 A
LAND USE PERMIT	150	01-Oct-25 A	27-Aug-26
PERMITTING	238	01-Dec-26	28-Oct-27
CONSTRUCTION - PHASE 1	132	29-Oct-27	01-May-28
CONSTRUCTION - PHASE 2	260	05-Jul-29	03-Jul-30
CLOSE-OUT	5	08-Jul-30	12-Jul-30

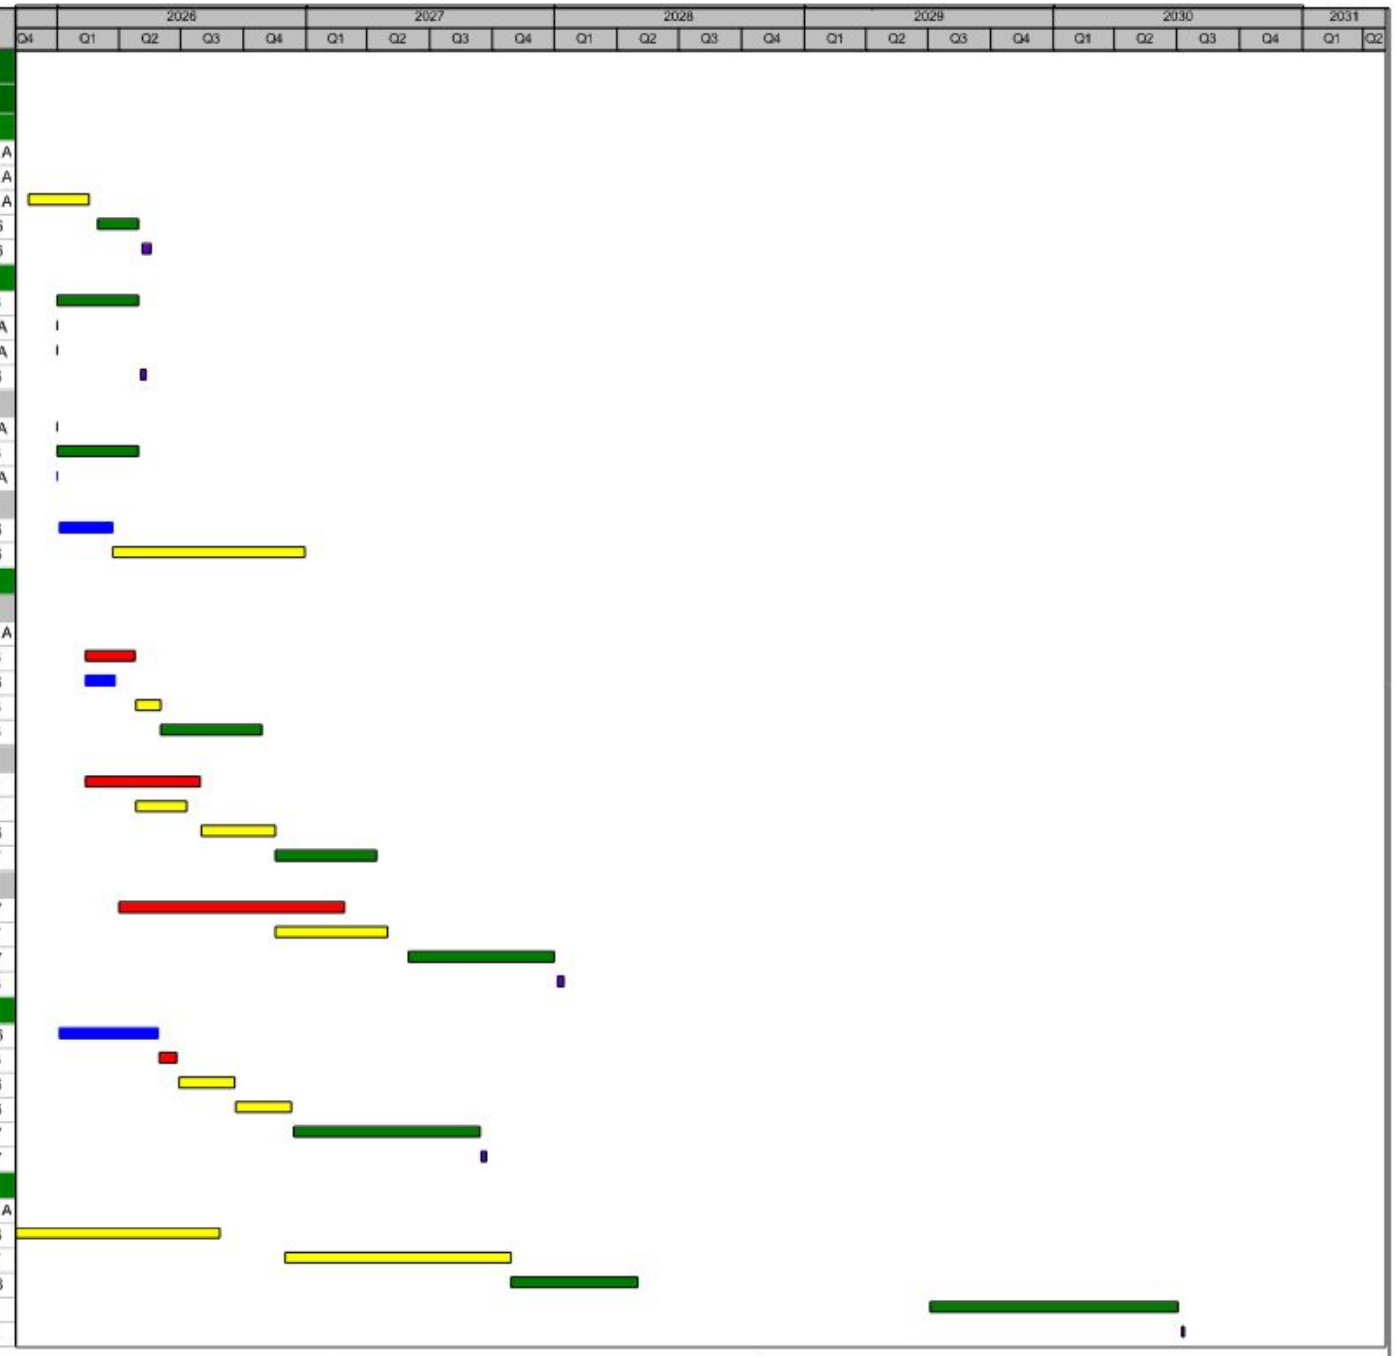


PROCUREMENT
DESIGN
PERMITTING
CONSTRUCTION
CLOSE-OUT & W...
MILESTONE

Portland PS
Bond Summary

Data Date 23-Feb-26
Run Date 23-Feb-26

Activity Name	Duration	Start	Finish
Portland PS Bond Program			
ATHLETIC FACILITIES			
ROOSEVELT HS SB TURF			
A/E PROCUREMENT	43	01-May-26	30-Jun-26
DESIGN	22	01-Jul-26	30-Jul-26
LAND USE PERMIT	240	31-Jul-26	01-Jul-27
PERMITTING	131	02-Jul-27	31-Dec-27
CONSTRUCTION	130	03-Jan-28	30-Jun-28
CLOSE-OUT	5	05-Jul-28	11-Jul-28
ROOSEVELT HS GRANDSTAND			
A/E PROCUREMENT	43	01-May-26	30-Jun-26
DESIGN	44	01-Jul-26	31-Aug-26
LAND USE PERMIT	240	01-Sep-26	02-Aug-27
PERMITTING	196	03-Aug-27	02-May-28
CONSTRUCTION	197	03-May-28	01-Feb-29
CLOSE-OUT	5	06-Feb-29	12-Feb-29
FRANKLIN FIELD			
A/E PROCUREMENT	43	01-May-26	30-Jun-26
DESIGN	44	01-Jul-26	31-Aug-26
LAND USE PERMIT	240	01-Sep-26	02-Aug-27
PERMITTING	195	03-Aug-27	01-May-28
CONSTRUCTION	196	02-May-28	30-Jan-29
CLOSE-OUT	5	02-Feb-29	08-Feb-29
WEST SYLVAN MS FIELD			
A/E PROCUREMENT	43	01-May-26	30-Jun-26
DESIGN	105	01-Jul-26	24-Nov-26
LAND USE PERMIT	240	25-Nov-26	26-Oct-27
PERMITTING	195	27-Oct-27	25-Jul-28
CONSTRUCTION	197	26-Jul-28	26-Apr-29
CLOSE-OUT	5	01-May-29	07-May-29
GRANT HS SEATING			
A/E PROCUREMENT	43	01-May-26	30-Jun-26
DESIGN	217	01-Jul-26	29-Apr-27
LAND USE PERMIT	240	30-Apr-27	30-Mar-28
PERMITTING	132	31-Mar-28	02-Oct-28
CONSTRUCTION	129	03-Oct-28	30-Mar-29
CLOSE-OUT	5	04-Apr-29	10-Apr-29

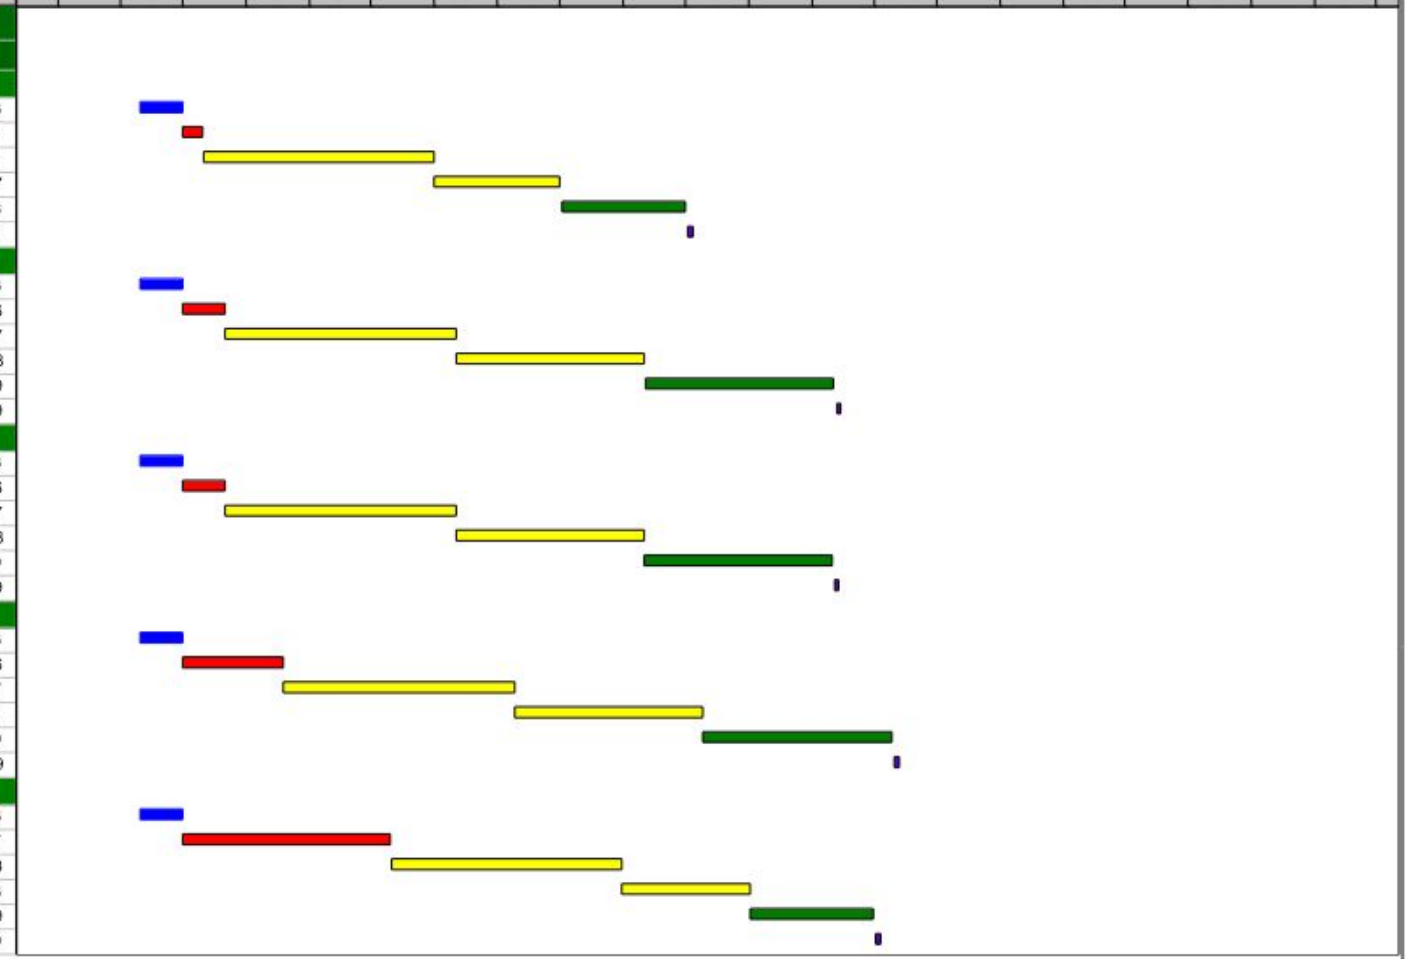

PROCUREMENT PERMITTING CLOSE-OUT & W...
DESIGN CONSTRUCTION MILESTONE

Portland PS
Bond Summary

Data Date	**23-Feb-26**
Run Date	**23-Feb-26**

Audit Updates

Bond Audit Recommendation

Year 2 - Recommendation #7 - 2017 Bond Program

Conduct a post-project completion analysis for the Madison and Lincoln High School projects to evaluate benefits and challenges of the CM/GC delivery method overall, as well as specific aspects such as timing of Guaranteed Maximum Price (GMP) contract amendments and make process changes as warranted. The evaluation should consider components suggested by ORS279.103 and provide a comparison of actual project cost against original project estimates, change order number, value and type, as well as descriptions of success and failures during design and construction.

Implementation – Complete

- Gather examples of ORS 279C.355 compliant post-project evaluations for CM/GC projects completed by other contracting agencies
- Develop post-project evaluation template for CM/GC projects
- Gather "Findings in Support of Alternative Contracting Methodology" documents for Lincoln and McDaniel (Formerly Madison)
- Gather applicable data from eBuilder Analyze data, write narratives, and assemble reports

Bond Audit Recommendation

Year 2 - Recommendation #8 - 2017 Bond Program
Memorialize and discuss underlying rationale and decisions related to the timing of GMP negotiations with the Bond Accountability Committee, and present to the Board for future CM/GC GMP contract amendments as appropriate.

Implementation – Complete
RISE already discusses GMP timing extensively during Bond Accountability Committee (BAC) meetings, but will look to include it as a specific update at BAC meetings for projects that have not yet completed their GMP negotiations. The Bond Accountability Committee provides a report to the Board quarterly, and RISE also provides all BAC meeting materials and minutes to the Board as part of RISE's quarterly report.



Bond Audit Recommendation

Year 4 - Recommendation #1 – 2017/2020 Bond Program

Complete development of and memorialize policies, procedures, and e-Builder processes related to construction closeout as well as train project staff on new closeout protocols before the remaining 2017 Bond projects are completed.

Implementation – Complete

- Gather requirements and design project closeout workflow, step actors, required documents
- Develop document templates
- Develop eBuilder project closeout process
- Develop training materials, conduct training with staff
- Identify pilot projects and execute pilot
- Make adjustments following pilot project
- Go live with project closeout process for all projects

Bond Audit Recommendation

Year 4 - Recommendation #6 – 2017/2020 Bond Program
Require general contractors to consistently report specific safety performance data to RISE.

Implementation – Complete

- Update the Project Status Update process in eBuilder to add required safety performance data fields
- Develop and deliver training to project management staff
- Update contracts to require contractors to report on standard safety metrics at regular intervals



Procurement and Land Use Updates

Procurement Schedule

Activity Name	Start	Finish	2026				
			JAN	FEB	MAR	APR	MAY
PROCUREMENT							
PHASE 1 | Program Geotechnical Services							
Bid Advertisement Posted	1/13/2026	1/13/2026					
Deadline Issuing Addenda	1/26/2026	1/26/2026					
RFP Opening Date	1/29/2026	1/29/2026					
Notice to Award Issued	2/13/2026	2/13/2026					
Agenda Deadline to PPS	3/24/2026	3/24/2026					
PPS Board Meeting	**4/14/2026**	**4/14/2026**					
PHASE 2 | Construction Testing Materials, Traffic Control Services, A/E Services, Structural and Civil, HVAC Test and Balance							
Bid Advertisement Posted	1/20/2026	1/20/2026					
Deadline Issuing Addenda	2/5/2026	2/26/2026					
RFP Opening Date	2/10/2026	3/3/2026					
Notice to Award Issued	2/20/2026	3/13/2026					
Agenda Deadline to PPS	4/1/2026	4/1/2026					
PPS Board Meeting	**4/28/2026**	**4/28/2026**					
PHASE 3 | Cx Services, Surveying, Envelope Consultant, Zoning/Planning/Permitting A&E							
Bid Advertisement Posted	1/26/2026	1/28/2026					
Deadline Issuing Addenda	2/12/2026	2/26/2026					
RFP Opening Date	2/24/2026	3/4/2026					
Notice to Award Issued	3/2/2026	3/16/2026					
Agenda Deadline to PPS	4/15/2026	4/15/2026					
PPS Board Meeting	**5/12/2026**	**5/12/2026**					

Land Use Status

- **Cleveland High School**
  - Milestone achievement: Conditional Use Hearing on 3/4/2026
  - Timeline for approval of conditional use permit: May 2026

- **Ida B. Wells High School**
  - Milestone achievement: Anticipated timeline for land use permit application March 2026
  - Timeline for land use hearing: June 2026

- **Jefferson High School**
  - Milestone achievement: Conditional Use Hearing on 2/11/2026, decision on 2/26/2026
  - Milestone achievement: Historic Resource Review approval on 3/4/2026
  - Anticipated issuance of conditional use permit: March 2026

- **Next steps in land use: IBW hearing early this summer!**

Questions?

