PROCEDEO

TABLE OF CONTENTS

02 EXECUTIVE SUMMARY

13 EXHIBIT A

14 EXHIBIT B

17 EXHIBIT C

APPENDIX

ATTACHMENT A

ATTACHMENT B

ATTACHMENT C

ATTACHMENT D

ATTACHMENT E

ATTACHMENT F

ATTACHMENT G

ATTACHMENT H

ATTACHMENT I

ATTACHMENT J

ATTACHMENT K

ATTACHMENT L

ATTACHMENT M

ATTACHMENT N

PROCEDEO

To: Dr. Jon Franco

From: Sarah R. Norman. Executive Director - RISE

Date: [Insert Date]

Re: Jefferson High School – Early Occupancy **Feasibility Review**

Executive Summary

In November 2025, PROCEDEO was tasked by PPS Leadership to perform a **feasibility study** to explore the Jefferson High School (JHS) early shell option presented in PROCEDEO's report to Dr. Armstrong on October 22, 2025. The exploration proceeded with the goal of identifying feasibility and challenges of Shell Option – trying to identify any expedited occupancy for Jefferson Students and Community. The Study involved a collaborative effort, and preliminary review (from a feasibility standpoint) to support early occupancy of JHS.

PROCEDEO in collaboration with Bora Architects, Colas/Hoffman Construction, and existing OSM Staff initiated structured workshops to evaluate the feasibility of **early occupancy of Jefferson High School (JHS)** while **maintaining the integrity of the approved design, permits, and construction plan.** Therefore, allowing the team to explore the option without having any impact on existing design/construction timelines already in motion for Jefferson High School.

December 17, 2025, marked the first of a series of collaborative and creative workshops led by PROCEDEO and focused on:

- Validating baseline schedule assumptions, sequencing, and constraints
- Investigating feasibility of early occupancy of Levels 1 and 2
- Identifying schedule, cost, safety, and operational impacts
- Establishing next steps and decision points for PPS leadership

The 1st workshop was a chance to bring all team members up to speed on current design development, land use, permitting, construction logistical challenges and schedules.

- Team agreement #1 at first workshop, all ideas were on the table, however no work should stop on current approved plan for Jefferson High School.
- Team agreed that feasibility needed to be detailed but also expedited as to not cause major disruptions to Design and Construction teams. It was settled that the team would work to a deadline of the first week of February to deliver a report to Leadership for review and decisions.
- All Team members left the meeting with homework assignments to report back in our following workshop held on January 22nd.
- In between each workshop multiple conversations took place among team members so our workshop on the 22nd would be productive and a decision point in meeting our targeted deadline of the first week in February.


The January 22, 2026, workshop #2 was dedicated to reviewing the documentation resulting from the December 17th workshop starting with the feasibility study phased occupancy schedule scenario presented by Colas Hoffman.

Item #1 - ***Confirm schedule validity from a constructability and staging standpoint, including whether the 1st and 2nd floors can be occupied by August 2028 or Dec 2028 (mid-school year)***


Key Findings

Colas-Hoffman Schedules

- Current Baseline Schedule: Student-ready August 15, 2029

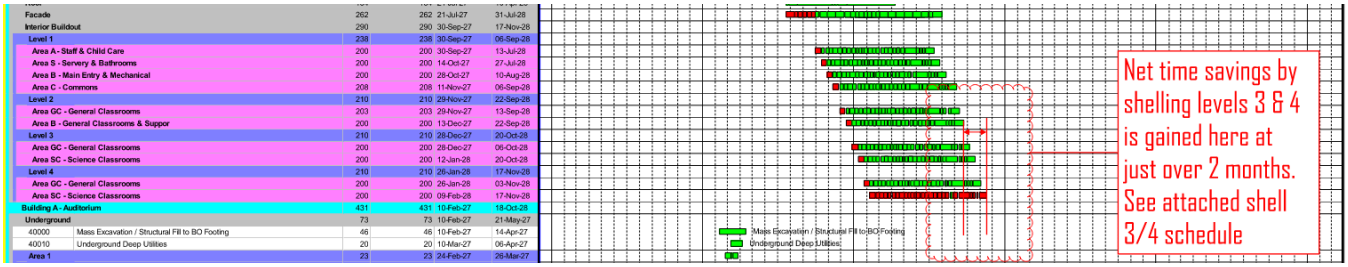

- Feasibility Study Phased Occupancy Schedule: Levels 1 & 2 student-ready July 5, 2029

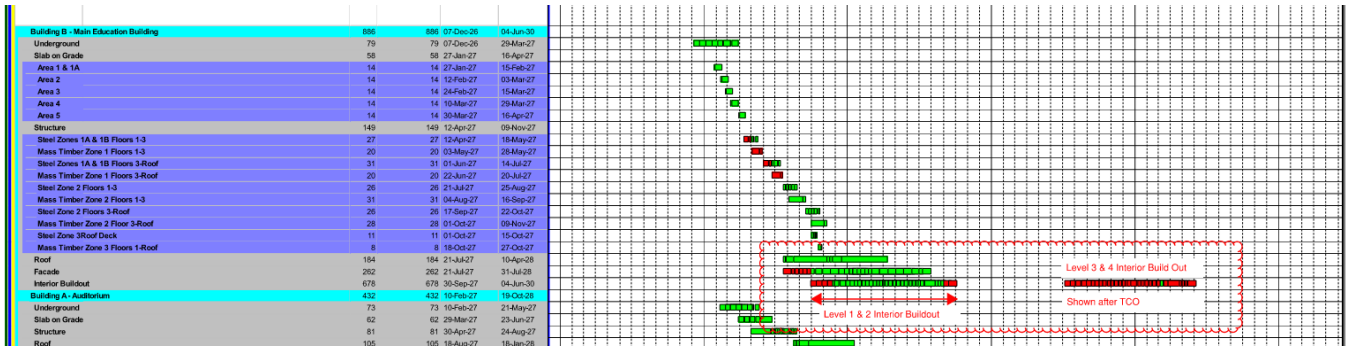

full schedule analysis from Colas-Hoffman including in Appendix

Colas-Hoffman Schedule review resulted in only 6 weeks in the phased occupancy approach

Colas-Hoffman said they may be able to expedite schedule by (3) Months. Identifying Student move-in Date as June 2029, however due to it being the summer months it did not offer much advantage to utilization of the 1st and 2nd floors.

PROCEDEO – 3rd Party Schedule review results - After a joint review with Procedeo's schedule consultant the following was found.

- Critical path activities revealed potential improvement starting with Design and Permitting.
- Several design related tasks can be compressed to save some time on the critical path. These items are as follows:
  - 100% DD approval is shown to be complete 3/27/26. 2-3 weeks can be recognized by shortening this review duration.
  - 50% foundation to grade drawings are due to be submitted for pricing on 7/17/26 with the permit submittal starting 8/3/26. Scheduling these tasks concurrently can save approximately 3 weeks. However, the permit duration of 4 months is a risk as it is dependent on the City review process.
  - The PPS document review (DD, 50% CD's, 100% CD's) durations are excessive. By shortening the owner review durations the critical path can be reduced.
- Occupancy of the new building is currently has a duration of 70 calendar days and is on the critical path. Simply by reducing this duration to 40 days will save 30 days on the critical path.

Other schedule options explored was changing the work week to 5 – 10 hour days and 6 – 10 hoy days. The results of this exercise are as follows:

- 5-10 hour days resulted in a reduced schedule of 2 month. The premium for this option would be approximately $17,000,000.
- 6-10 hour days resulted in a reduced schedule of 3 months. The premium for this option would be approximately $23,000,000.

Schedule conclusion

After review and making the above adjustments, the schedule can be reduced by over a month.

The overall risk in achieving any option outlined in this summary is solely driven by City approvals and issuance of required permits.

The other main constraint found was schedule issues revolving around working on an occupied site and the inherent restrictions that impacts deliveries and site constraints.

Item #2 – *Confirm increase enrollment numbers with PPS and the ability for increased enrollment would fit on 1st and 2nd floors*.

Key Findings

- PROCEDEO received targeted enrollment numbers from Margaret Calvert (PPS) as follows on January 6, 2025:
    - The enrollment estimates for 2027-28 and 2028-29 will be heavy in the freshmen and sophomore students. Chemistry for sophomores has the largest need for fume hoods. (offerings book also provided)
    - The increase would look like this:
        - 2027-28 total population 552 (with the freshman class being 200, sophomore class 120ish) (6-7 sections for freshmen science and 4 for sophomores)
        - 2028-29 total population 770 (with a freshman class at about 220 and sophomores now closer to 200) (7-8 sections for freshmen and 6-7 for sophomores)
        - If we assume a class size of 30, there would be about 4 sections of chemistry in 2027-28, increasing to 6 in 2028-29.

- PPS assumes that all freshmen - juniors need to take science these years. We also assume that the increase in students is primarily in the freshmen year as students roll up.

With the above provided information, PROCEDEO shared with BORA to confirm utilization on 1st and 2nd floors during this time should early delivery be available.

- For school year '28-'29 Jefferson High School would need a projected total of 6 science labs at 100% utilization with (2) having fume hood capability due to it being the sophomore Chemistry

BORA findings

Below is the early occupancy utilization table put together for the 1st and 2nd floors.

Early Occupation of First & Second Floors
770 students at 85% Utilization with Adjustments

	Total SF	/	SF/TS	=	TS	*	Util	*	Students Per Classroom Range		=	Student - low	Student - high	Includes:	Replaces:
General Classroom			950		15		85%	*	20	30		255	383	[16] General Classrooms	[1] VAPA****
Temporary Science			1,500		2		85%	*	20	30		34	51	[2] Temp Science "Labs" at full size	[1] CTE, [2] General Education
Temporary Science (Undersized)			1,100		2		85%	*	15	22	**	26	37	[2] Temp Science "Labs" at reduced size	[1] CTE, [1] Maker Space
Specialized Instruction			*varies*		8		75%		20	30		120	180	[4] VAPA + [4] CTE	
Dance			*2,000*		2		85%	*	20	30		34	51	[2] Dance Studios	
PE/Athletics			*varies*		4		35%	***	20	30		28	42	[1] Main Gym, [1] Aux Gym, [1] Mat Rm, [1] Weight Rm	
Special Education			*varies*		3		70%		15	24		32	50	[2] Int skills + [1] LRC	
Small Instructional			500		-		0%		15	20		-	-	No Small Instruction	
Total	**281,098**				**36**							**528**	**794**		

* Supported by [3] Teacher Collaboration rooms
** Reduced student capacity with reduced room size
*** Assume half utilization at 770 students for room qty sized for 1700 students
**** Assume JHS will continue to not offer Choir in 2028

Occupancy utilization schedule for 100% occupancy along with Early Occupancy table above included in appendix

Occupancy table explanation

- The projected enrollment of 770 students put into utilization table and calculated at 85% utilization per PPS standards identified the need for a total (4) temporary Science classrooms
- BORA Identified potential options on the 1st and 2nd floor that could accommodate these classrooms on a temporary basis (swing) during the '28-'29 School year – recommendations as follows:
    - 1 CTE Room
    - 2 General Education rooms
    - 1 CTE Room
    - 1 Makers Space

Overall, we would be able to accommodate students on the 1st and 2nd floors for science.

Item #3 - Identify any cost impacts associated with early occupancy and confirm whether those impacts can be mitigated within the current project budget.

Key Findings

Colas-Hoffman provided the explanation below and breakdown associated with labor and schedule:

COLAS HOFFMAN CONSTRUCTION

Labor inefficiency operating in an occupied classroom building for the 6 weeks overlap

Subcontractors' labor will be less efficient through the construction of the upper floors due to access constraints and restrictions. Assumes access routes around and within the building will be closed to construction. With no exterior material hoist available for stocking materials and moving personnel the wait times for the interior elevator will be slow.

125 workers on site x 30 work days (6 weeks) x 8 hrs/day = 30,000 craft labor hours

Average labor rate including project markups = $160/hr

Assumed inefficiency of 20%

30,000 hours x 20% inefficiency x $160/hr = $960,000

Reduced general conditions / general requirements in Phase 3 related to earlier finish

Baseline Schedule – Phase 3 Finish September 5, 2030

Phased Occupancy Schedule – Phase 3 Finish July 25, 2030

Reduce Phase 3 General Conditions by 1.5 Months: $267,832/mo x 1.5 mo = $401,748

In summary, implementing the Phased Occupancy Schedule will result in an estimated increase to the project cost of:

$960,000 labor efficiency loss - $401,748 Reduced GCs/GRs = **$558,252 increase**

Full letter from Colas-Hoffman provided in Appendix

Explanation of the above table:

- Colas-Hoffman concluded that due to limited trade access to 3rd and 4th floors during phase occupancy would cause inefficiencies resulting in added labor cost to the projects by trades.
- Colas-Hoffman acknowledges savings of 1.5 months of General Conditions totaling: $401,748.00.

- Colas- Hoffman however concedes that although there is an identified savings in GC's the add of the labor cost due to accessibility constraints results in an overall Project cost ADD of $558,252.00

Item #4 – What early occupancy impacts will be felt by the students, community, and administration

The team talked in detail about pros and cons of early occupancy, attempting to leave no stone unturned for such a crucial decision.

The Team noted the following:

- Increased noise, dust, and safety considerations inherent to active construction
- Temporary instructional spaces (including science classrooms) would operate below programmed sizes in some cases, and some functionality would be limited
- Site constraints, parking, logistics to accommodate continued construction while school is occupied

Operational Impacts in Phased Occupancy Scenario Presented by Bora

- Temporary Science considerations in rooms with at least (1) sink. Additional temporary equipment/furniture would need to be used to make these spaces function.
- The temporary Science rooms will be below the programmed 1,500sf
- The temporary use assumes that JHS will continue to not offer Choir
- JHS currently has a "Screen-printing" course. This room is considered as a temporary Science room because of its larger size and access to sinks.
- Per the current JHS enrollment numbers, (38) students are enrolled in Special Education Courses.

Conclusion

Based on the current **feasibility study and analysis:**

- Colas-Hoffman has concluded that early occupancy **does not provide a meaningful schedule advantage** as time savings was identified however it was only identified in summer months, therefore as it relates to student move-in there is no advantage.
- Bora verified increased student enrollment can be accommodated on 1st & 2nd floor, however there will be operational trade-offs.
- Colas-Hoffman concluded that cost evaluation of schedule and labor was not cost efficient to the overall project budget.
- While the cost of most of these options is extensive these are worse case scenarios. The cost for these options cannot be 100% verified until the project is priced in a competitive environment and a full execution plan is issued with bid packages.

Moving Forward

PROCEDEO recommends:

PPS leadership considers the feasibility of the information provided above, as it impacts schedule, operational utilization, and cost.

PROCEDEO provides the following options for your consideration:

- Option 1 – Abandon the pursuit of Shell Early Occupancy option and stay the course of an August 2029 move-in to completely modernized Jefferson High School

- Option 2 – Direct the PROCEDEO to direct project team to continue to pursuit Shell Early occupancy option, acknowledging the mid-year move in, operational concessions and cost associated with early occupancy.

Both Options above are challenging as is the overall Jefferson Project, considering the current state of design and permit coordination with the City. The team was successful in identifying some ability to expedite the overall schedule and verified student accommodations on first and 2nd floor is obtainable for the '28- '29 school year. The Project team remains focused and ready to support which every option leadership decides to deploy.

Respectfully submitted,

Sarah R. Norman

Executive Director

2025 JHS Design and Construction Schedule

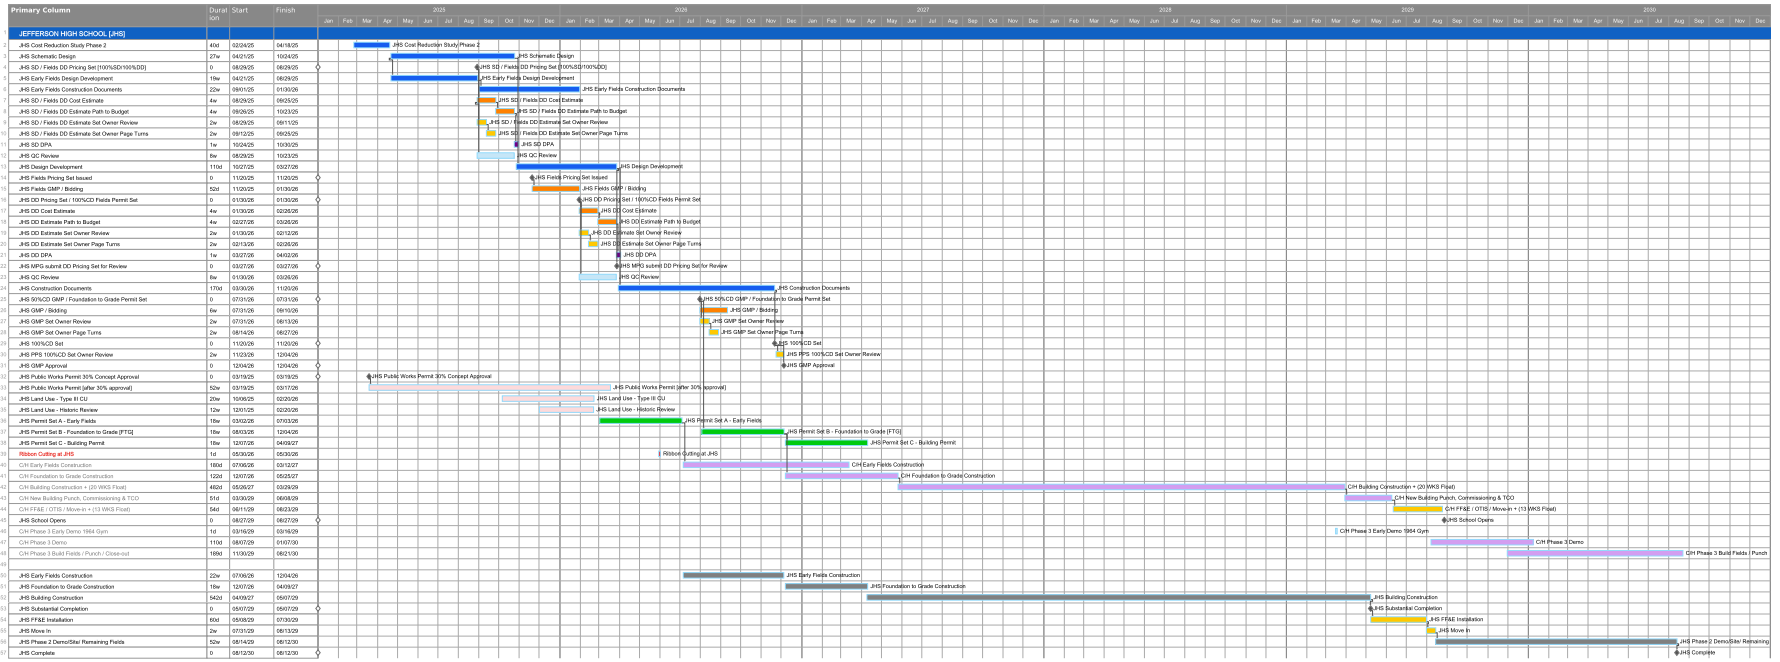


Exhibit B – Collaborative deep dive into Bora & Colas/Hoffman's current project schedule

Set A/Phase 1 – Early Fields Package

Schedule Status (End 2025):

- Design completion for Set A: End Jan 2026
- Land Use / Zoning (Lighting + PA):
    - Baseline schedule: March 2026
    - Actual: submitted Oct 2025; incompleteness review completed; PPS responses received, Bora is packaging and submitting this week.
    - Target: deemed complete → Public hearing mid–late April 2026
- Permit review (Type III CU): ~16 weeks best case
    - City 1st review: 6 wks → Bora response: 3 wks
    - City 2nd review: 3 wks → Bora response: 2 wks
    - No 3rd round anticipated
- Construction start: July 2026
- Duration: 8 months → Construction Completion: March 2027

Key Risks:

- Best-case permitting only; need worst-case scenario
- Rain and weather impacts on field construction
- Neighbor/public opposition during Type III CU hearing

Planning & Risk Mitigation:

1. Procedeo POC: to coordinate neighbor notices, public outreach, and hearings
2. Bora/Colas Hoffman: Early coordination with utilities (new power line, easements, contracts)
3. Bora/ Colas Hoffman: Investigate fenced utility/storage areas (SUE, existing feeds)
4. Procedeo POC: Collect City/utility contacts and commitments, ensure follow ups and planning is in place.

Set B/Phase 2 – Utilities & Early Foundations

Schedule:

- City permit submission: July 2026 (4-month review)
- Construction start: Dec 2026
- Duration: 6 months → Construction Completion: June 2027

Risks:

- Tight site / staging areas

- Utility agreements, unforeseen subsurface conditions
- Surveys required to avoid surprises and stop work

Planning & Risk Mitigation:

1. Colas Hoffman: Site Logistics & Access
    - Detailed site plan: staging, delivery, pedestrian separation
    - Coordinate with school operations
2. Colas Hoffman/Bora/Procedeo: Utilities & Subsurface Investigation
    - Conduct SUE survey
    - Coordinate with utility companies (easements, connections)
3. Colas Hoffman: Scheduling & Phasing
    - Integrate GMPs and master schedule
    - Account for weather, school calendar
4. Colas Hoffman/Bora/Procedeo: Permitting & Approvals
    - Confirm permits/approvals prior to mobilization
    - Procedeo: Assign permit POC
5. Procedeo: Coordination & Communication
    - Single POC for City, utilities, school, contractors
    - Regular coordination and documented decisions, **who needed to do what and by when!**
6. Colas Hoffman: Design Review & Validation
    - Verify constructability and phasing alignment
    - Conduct risk review workshops

Set C/Phase 3 – 4-Story Building Construction

Schedule:

- Design completion: Nov 2026
- Permit: 4 months
- Construction start: June 2027
- Duration: 22 months after Phase 2

Set C/Phase 4 – Demo existing gym, Demo existing Jeff and new track and field

- Construction start: May 2029
- Duration: Approx. 16 months after phase 3

Procedeo Concerns for current phasing from a logistical point of view:

- Staging areas and site logistics – Colas Hoffman to provide asap.

Proposed GMP / Phasing Strategy

GMP	Scope	Notes
GMP 1	Fields (Phase 1 – softball & baseball)	Consider splitting fields if staging required in one of the fields
GMP 2	Utilities & foundation	Set B
GMP 3A	Building 1st & 2nd floors	Early occupancy investigation
GMP 3B	Building 3rd & 4th floors	Full build-out
GMP 4	Track, fields, and site work	Phase 4, includes deferred fields

All GMPs should be **reflected as distinct phases in schedule and timeline.**

All GMPs should be within the CCL approved for this project.

Exhibit C – Early Occupancy Investigation

Early Occupancy – 1st & 2nd Floors (Aug 2028)

1. Minimum Completion Requirements for 1st & 2nd Floors (Early Occupancy) – need to confirm requirements with the fire marshal.

To safely occupy the first two floors, the following must be fully installed, operational, and inspected:

Structural & Envelope

- Complete building structural shell for all floors (slabs, columns, beams)
- Building Envelope should be completed.
- Secure temporary or permanent barriers between occupied and under-construction areas

Life Safety Systems

- Fire sprinkler system fully operational and tested for all floors.
- Fire alarm system installed and functional for all floors (confirm with Fire Marshal).
- Emergency egress for 1st and 2nd floors: stairs, ramps, exit doors, signage, and lighting fully installed and code-compliant.
- Exterior scaffolding or stair towers in place to support 3rd & 4th floor construction without interfering with student/staff access on lower floors.
- Smoke/CO detectors installed and tested on 1st and 2nd floors (verify upper floors with Fire Marshal).
- Access control and security systems fully installed for the entire building.

Mechanical, Electrical, Plumbing (MEP)

- HVAC systems functional for the entire building.
- Plumbing: restrooms, drinking fountains, and other water systems fully functional in 1st and 2nd floors.
- Electrical: lighting, outlets, and emergency power (as required by code and fire marshal)
- IT/Data/PA systems sufficient for basic school operations
- Any temporary utilities (power, water) since upper floors are still under construction

Safety & Accessibility

- Floors 1 & 2 fully accessible (ADA compliant paths, elevators operational if needed)
- Barriers or enclosures to prevent access to 3rd/4th floors
- Temporary dust control measures (plastic sheeting, negative air machines if needed)
- Safe routing for students and staff, including fire and egress planning

2. Contractor Requirements to Continue Work on 3rd & 4th Floors Safely

To **minimize disruption and maintain safety** while upper floors are under construction:

Site Separation

- Fully **enclose or segregate construction zones** from occupied areas
    - Fire-rated temporary walls or barriers
    - Dust control: plastic sheeting, negative air, or temporary partitions
- Temporary access routes for construction workers, equipment, and deliveries **separate from students and staff via scaffolding stair towers.**

Noise & Vibration Control

- Limit high-noise activities during school hours (hammering, saws, drilling)
- Schedule noisy work during off-hours, evenings, or school breaks
- Use quieter construction methods where possible

Safety Measures

- Guardrails, fall protection for upper floors
- Secure tools, materials, and equipment to prevent falling debris
- Clearly marked signage and restricted zones
- Coordination with school administration for emergency planning

MEP Coordination

- Ensure utilities serving the 1st & 2nd floors are fully functional and isolated from ongoing work above
- Prevent contamination of occupied systems by construction dust or debris

Material & Logistics Management

- Staging areas for materials must **not interfere with school operations**
- Deliveries should avoid occupied floor access points
- Use of lifts with controlled access to avoid pedestrian conflicts

Inspection & Certification

- Floors 1 & 2 inspected and approved for occupancy
- Life safety systems certified and tested independently of upper floors

3. Summary Table – Minimum Early Occupancy vs. Upper Floor Work

Category	Early Occupancy (1st & 2nd floors)	Upper Floor Work (3rd & 4th floors)
Structural	Complete shell for occupied floors	Continue framing/floor slabs as per schedule
Life Safety	Fire alarm & sprinklers operational	Ensure separate systems, protect occupied floors
Mechanical	HVAC functional	Work above can proceed if isolation maintained
Electrical	Lighting, outlets, PA, emergency power	Isolation from floors below
Plumbing	Restrooms, water fountains functional	Connections above, no disruption below
Finishes	Safe floors, walls, ceilings	Partial/unfinished above, protected with barriers
Safety	ADA access, egress, barriers	Guardrails, fall protection, restricted zones
Noise / Dust	Minimized, school-safe	Enclosures, dust barriers, off-hour noisy work
Access	Controlled routes for students/staff	Separate construction access, staging zones

Key Takeaways:

1. Exploring early occupancy is intended to support students, meet district goals, and align with public expectations, and should not impact the current design or permit timeline.
2. If early occupancy is deemed feasible, Bora's scope, fee, and schedule remain unchanged.
3. The 1st and 2nd floors must be fully safe, functional, and code-compliant, with all required life safety and MEP systems operational prior to occupancy.
4. Construction on the 3rd and 4th floors may continue only with clearly defined physical separation, dust and noise controls, and controlled logistics that protect students, staff, and daily operations.
5. Any early occupancy approach must be financially feasible and achievable within the current project budget.

Next Steps / Required Actions

1. Colas/Hoffman to confirm schedule validity from a constructability and staging standpoint, including whether the 1st and 2nd floors can be occupied by August 2028.
2. Colas/Hoffman to identify any cost impacts associated with early occupancy and confirm whether those impacts can be mitigated within the current project budget. Early turnover of Phase 3 and reduced construction duration therefore reducing general conditions may help offset potential costs (refer to Exhibit A).
3. Colas/Hoffman to provide detailed construction phasing plans, including:
   Staging areas by phase
   Entry and exit paths for material delivery and offloading
4. Colas/Hoffman to provide a realistic, phase-based schedule for all packages, including:
   Floor-by-floor construction durations
   Demolition of the existing gym
   FFE, move in and PA coordination
   Inspections and AHJ approvals
5. Bora to confirm the number of students that can be accommodated on the 1st and 2nd floors, assuming temporary science instruction in CTE spaces, subject to PPS approval.
   Temporary science setup (one-year duration):
   Level 1 CTE lab and Level 2 IT/Cybersecurity lab
   Mobile FFE including tables, chemical carts, portable eyewash, and plug-in equipment
   Pros: fast deployment, flexible use, lower cost
   Cons: limited plumbing and ventilation, restricted chemistry use
6. Procedeo / OSM to confirm the temporary science lab approach with PPS.

COLAS HOFFMAN CONSTRUCTION

1/15/2026

Jefferson High School Early Occupancy Schedule and Cost Study

On December 17, 2025 the Jefferson High School OAC team met to review the Option 1 “Shell” from the Procedeo report of October 22, 2025 and to discuss the feasibility of early occupancy of the classroom building. In the meeting Colas Hoffman was asked to study the schedule and cost of the early occupancy plan. Below are those two questions from the meeting minutes, with answers from the schedule study.

Confirm schedule validity from a constructability and staging standpoint, including whether the 1st and 2nd floors can be occupied by August 2028 or Dec 2028 (mid-school year)

Included in the following pages are roll-up summaries of the Baseline Schedule and the Phased Occupancy Schedule. Fully detailed reports of each schedule are also attached to the email in which this memo was distributed. Below are the Student Ready dates for each option:

Baseline Schedule – Student Ready August 15, 2029

Phased Occupancy Schedule – L1 & L2 Student Ready July 5, 2029

The study concluded that this strategy would get the building student ready **6 weeks earlier**, and that date happens to be during Summer Break. This is because the baseline schedule assumes an overlapping chase sequence of trades moving up the four stories of the classroom building.

Identify any cost impacts associated with early occupancy and confirm whether those impacts can be mitigated within the current project budget. Early turnover of Phase 3 and reduced construction duration therefore reducing general conditions may help offset potential costs (refer to Exhibit A)

The enclosed phased occupancy schedule shows level 3 and 4 delayed to start construction after move-in, which was the understanding from the meeting conversation. That schedule shows the project completing later than the baseline schedule. A different option would be to continue level 3 and 4 buildout without a gap/delay. The cost study below assumes no delay to the level 3 and level 4 buildout.

Labor inefficiency operating in an occupied classroom building for the 6 weeks overlap

Subcontractors' labor will be less efficient through the construction of the upper floors due to access constraints and restrictions. Assumes access routes around and within the building will be closed to construction. With no exterior material hoist available for stocking materials and moving personnel the wait times for the interior elevator will be slow.

125 workers on site x 30 work days (6 weeks) x 8 hrs/day = 30,000 craft labor hours

Average labor rate including project markups = $160/hr

Assumed inefficiency of 20%

30,000 hours x 20% inefficiency x $160/hr = $960,000

Reduced general conditions / general requirements in Phase 3 related to earlier finish

Baseline Schedule – Phase 3 Finish September 5, 2030

Phased Occupancy Schedule – Phase 3 Finish July 25, 2030

Reduce Phase 3 General Conditions by 1.5 Months: $267,832/mo x 1.5 mo = $401,748

In summary, implementing the Phased Occupancy Schedule will result in an estimated increase to the project cost of:

$960,000 labor efficiency loss - $401,748 Reduced GCs/GRs = **$558,252 increase**

Jefferson High

BASELINE SCHEDULE SUMMARY

LAYOUT: Jefferson HS Summary_1....12-Jan-26....

Activity ID	Activity Name	Orig Dur	Remaining Duration	Start	Finish
Owner Milestones		724	724	08-May-26	15-Mar-29
MS0900	PPS Ground Breaking Ceremony	0	0	08-May-26*	
MS1000	Baseball / Softball Season Completion	0	0		01-Jun-26*
MS1010	Last Day of School 2026	0	0		12-Jun-26*
MS1020	First Day of Spring Practice Softball / Baseball	0	0	01-Mar-27*	
MS1030	Last Day of Basketball Practice / Early Gym Demo	0	0		15-Mar-29*
MS1040	Last Day of Football Practice	0	0		13-Nov-26*
PRECONSTRUCTION		731	658	19-Mar-25 A	05-Jul-28
Deign & Permitting from Bora		417	344	19-Mar-25 A	09-Apr-27
Design		331	258	01-Sep-25 A	08-Dec-26
Fields		114	41	01-Sep-25 A	30-Jan-26
New School Building		268	258	27-Oct-25 A	08-Dec-26
Permit		390	344	19-Mar-25 A	09-Apr-27
HCC		658	658	01-Dec-25	05-Jul-28
Contracts & Buyout		417	417	01-Dec-25	23-Jul-27
Trade Partner Selection for Precon Assist & Procurement		460	460	11-May-26	02-Mar-28
Mass Timber		190	190	11-May-26	09-Feb-27
Electrical		460	460	11-May-26	02-Mar-28
Mechanical / Plumbing		309	309	11-May-26	28-Jul-27
Fire Protection		442	442	11-May-26	07-Feb-28
Structural Steel Detailing		216	216	11-May-26	17-Mar-27
General Material Procurement		593	593	06-Mar-26	05-Jul-28
Early Fields Phase 1 Work		85	85	06-Mar-26	06-Jul-26
JHS Main Building Phase 2 Work		450	450	28-Sep-26	05-Jul-28
BIM Coordination		354	354	01-Dec-25	23-Apr-27
Early Fields		55	55	25-Mar-26	10-Jun-26
Timber 1		70	70	17-Jul-26	23-Oct-26
Timber 2		70	70	07-Aug-26	13-Nov-26
Timber 3		70	70	28-Aug-26	08-Dec-26
Timber 4		70	70	21-Sep-26	30-Dec-26
Timber 5		70	70	12-Oct-26	21-Jan-27
Architectural Routing (AR) @ MEP Timber Elements		248	248	01-Dec-25	20-Nov-26
DLT		60	60	09-Dec-26	04-Mar-27
Auditorium (A)		154	154	17-Jul-26	24-Feb-27
Main Building (B)		196	196	17-Jul-26	23-Apr-27
Gym (C)		154	154	17-Jul-26	24-Feb-27
Phase 3		90	90	23-Nov-26	01-Apr-27
PROCUREMENT		225	225	12-Oct-26	30-Aug-27
Mass Timber		225	225	12-Oct-26	30-Aug-27
Steel		170	170	12-Oct-26	11-Jun-27
Construction		1252	1206	15-Aug-25 A	05-Sep-30
Cons10000	Start of Construction	0	0	23-Jun-26	
Cons10010	Construction Duration	1045	1045	02-Jun-26	17-Jul-30
HCC		1252	1206	15-Aug-25 A	05-Sep-30
Pacific Power		546	500	15-Aug-25 A	18-Nov-27
Phase 1		218	218	13-Apr-26	19-Feb-27
Fld10000	Softball & Baseball Fields Mobilization, Site Fencing, Temp MEP & Vac Truck U	15	15	02-Jun-26	22-Jun-26
Fld10010	Site Survey / Set Controls / Underground Modeling / Clash Detection	35	35	13-Apr-26	01-Jun-26
Softball Field		130	130	10-Jul-26	14-Jan-27
Baseball Field		160	160	06-Jul-26	19-Feb-27
Fields Frontage Improvements		64	64	13-Jul-26	09-Oct-26
Phase 2		707	707	20-Nov-26	04-Sep-29
20000	Mobilization, Temp Power& Demo	10	10	20-Nov-26	07-Dec-26
Building B - Main Education Building		498	498	07-Dec-26	17-Nov-28
Underground		79	79	07-Dec-26	29-Mar-27
Slab on Grade		58	58	27-Jan-27	16-Apr-27
Area 1 & 1A		14	14	27-Jan-27	15-Feb-27
Area 2		14	14	12-Feb-27	03-Mar-27
Area 3		14	14	24-Feb-27	15-Mar-27
Area 4		14	14	10-Mar-27	29-Mar-27
Area 5		14	14	30-Mar-27	16-Apr-27
Structure		149	149	12-Apr-27	09-Nov-27
Steel Zones 1A & 1B Floors 1-3		27	27	12-Apr-27	18-May-27
Mass Timber Zone 1 Floors 1-3		20	20	03-May-27	28-May-27



Remaining Level of Effort | Actual Work | Critical Remaining Work
Actual Level of Effort | Remaining Work | Meeting Milestone

Jefferson High School 1.6.26


data date :01-Dec-25 Page 1 of 3 TASK filter: <100%.

Jefferson High

BASELINE SCHEDULE SUMMARY

LAYOUT: Jefferson HS Summary_1....12-Jan-26....

Activity ID	Activity Name	Orig Dur	Remaining Duration	Start	Finish
	Steel Zones 1A & 1B Floors 3-Roof	31	31	01-Jun-27	14-Jul-27
	Mass Timber Zone 1 Floors 3-Roof	20	20	22-Jun-27	20-Jul-27
	Steel Zone 2 Floors 1-3	26	26	21-Jul-27	25-Aug-27
	Mass Timber Zone 2 Floors 1-3	28	28	04-Aug-27	13-Sep-27
	Steel Zone 2 Floors 3-Roof	26	26	13-Sep-27	19-Oct-27
	Mass Timber Zone 2 Floor 3-Roof	31	31	27-Sep-27	09-Nov-27
	Steel Zone 3Roof Deck	11	11	27-Sep-27	12-Oct-27
	Mass Timber Zone 3 Floors 1-Roof	8	8	12-Oct-27	22-Oct-27
	Roof	184	184	21-Jul-27	10-Apr-28
	Facade	262	262	21-Jul-27	31-Jul-28
	Interior Buildout	290	290	30-Sep-27	17-Nov-28
	Level 1	238	238	30-Sep-27	06-Sep-28
	Area A - Staff & Child Care	200	200	30-Sep-27	13-Jul-28
	Area S - Servery & Bathrooms	200	200	14-Oct-27	27-Jul-28
	Area B - Main Entry & Mechanical	200	200	28-Oct-27	10-Aug-28
	Area C - Commons	208	208	11-Nov-27	06-Sep-28
	Level 2	210	210	29-Nov-27	22-Sep-28
	Area GC - General Classrooms	203	203	29-Nov-27	13-Sep-28
	Area B - General Classrooms & Suppor	200	200	13-Dec-27	22-Sep-28
	Level 3	210	210	28-Dec-27	20-Oct-28
	Area GC - General Classrooms	200	200	28-Dec-27	06-Oct-28
	Area SC - Science Classrooms	200	200	12-Jan-28	20-Oct-28
	Level 4	210	210	26-Jan-28	17-Nov-28
	Area GC - General Classrooms	200	200	26-Jan-28	03-Nov-28
	Area SC - Science Classrooms	200	200	09-Feb-28	17-Nov-28
	Building A - Auditorium	431	431	10-Feb-27	18-Oct-28
	Underground	73	73	10-Feb-27	21-May-27
40000	Mass Excavation / Structural Fill to BO Footing	46	46	10-Feb-27	14-Apr-27
40010	Underground Deep Utilities	20	20	10-Mar-27	06-Apr-27
	Area 1	23	23	24-Feb-27	26-Mar-27
	Area 2	23	23	10-Mar-27	09-Apr-27
	Area 3	23	23	24-Mar-27	23-Apr-27
	Area 4	23	23	07-Apr-27	07-May-27
	Area 5	23	23	21-Apr-27	21-May-27
	Slab on Grade	62	62	29-Mar-27	23-Jun-27
	Area 1	14	14	29-Mar-27	15-Apr-27
	Area 2	14	14	12-Apr-27	29-Apr-27
	Area 3	14	14	26-Apr-27	13-May-27
	Area 4	14	14	10-May-27	27-May-27
	Area 5	22	22	24-May-27	23-Jun-27
	Structure	80	80	30-Apr-27	23-Aug-27
	Roof	105	105	18-Aug-27	18-Jan-28
	Facade	152	152	12-Aug-27	17-Mar-28
	Interior Buildout	260	260	12-Oct-27	18-Oct-28
	Level 1	260	260	12-Oct-27	18-Oct-28
	Area TA - Theater Auxiliary	200	200	12-Oct-27	25-Jul-28
	Theater	250	250	26-Oct-27	18-Oct-28
	Level 2	200	200	26-Oct-27	08-Aug-28
	Area TA - Theater Auxiliary	200	200	26-Oct-27	08-Aug-28
	Building C - Gym	482	482	10-Feb-27	03-Jan-29
	Underground	60	60	10-Feb-27	04-May-27
	Slab on Grade	196	196	22-Mar-27	28-Dec-27
	Area 1	12	12	22-Mar-27	06-Apr-27
	Area 2	12	12	01-Apr-27	16-Apr-27
	Area 3	14	14	13-Apr-27	30-Apr-27
	Area 4	18	18	22-Oct-27	17-Nov-27
	Area 5	26	26	17-Nov-27	28-Dec-27
	Structure	194	194	26-Apr-27	31-Jan-28
	Roof	161	161	23-Sep-27	10-May-28
	Facade	145	145	31-Jan-28	23-Aug-28
	Interior Buildout	324	324	23-Sep-27	03-Jan-29
	Level 1 / Level 1 Mezzanine	324	324	23-Sep-27	03-Jan-29
	Area GA - Gym Auxiliary & Main Electrical / Lockers	200	200	23-Sep-27	06-Jul-28
	Area G - Gym	240	240	24-Jan-28	03-Jan-29
	Level 2	230	230	04-Oct-27	28-Aug-28
	Area GA - Auxiliary Gym & Weights	230	230	04-Oct-27	28-Aug-28

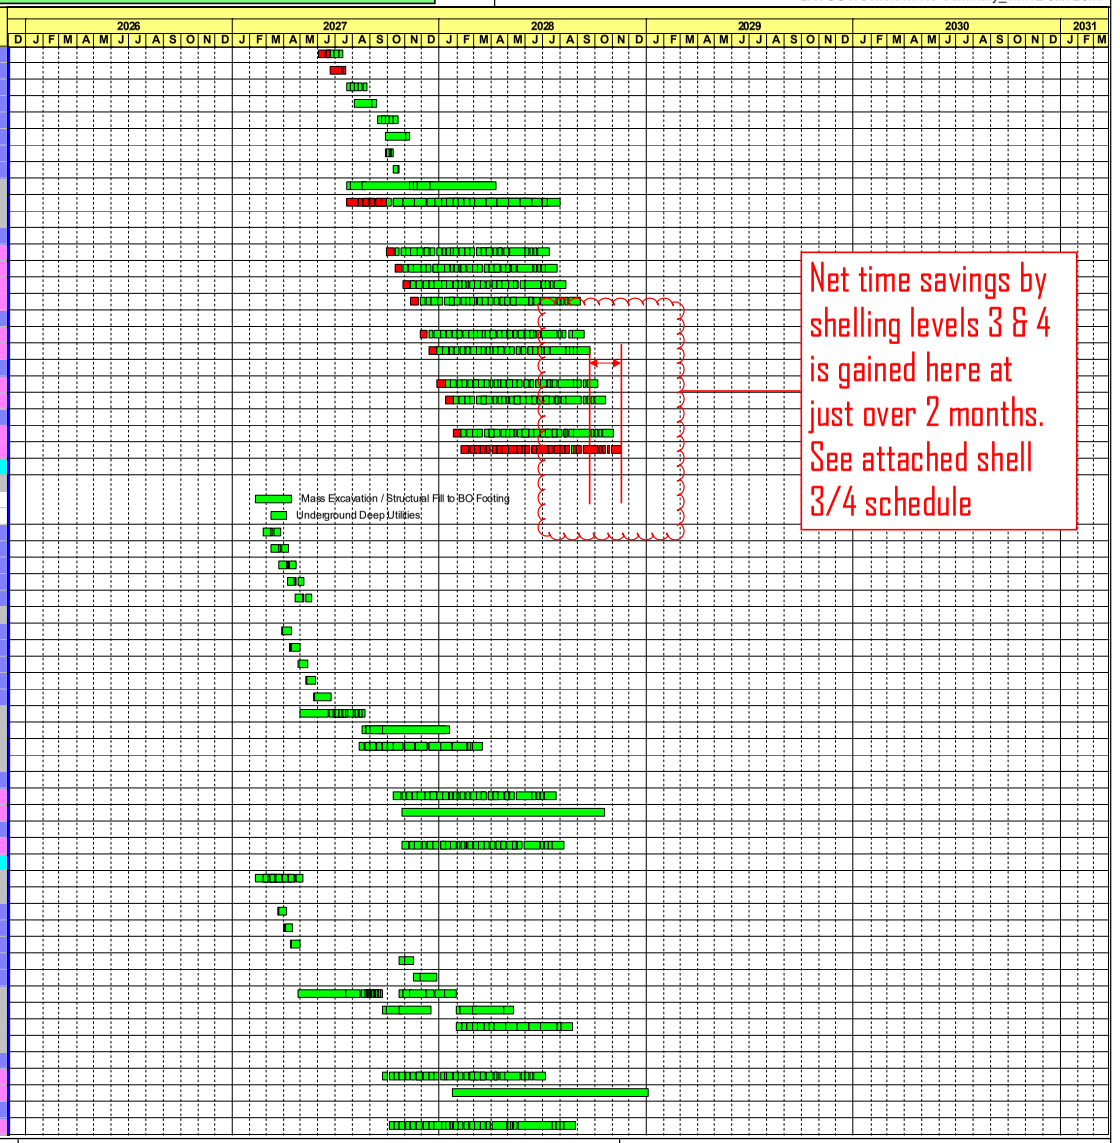

Net time savings by shelling levels 3 & 4 is gained here at just over 2 months. See attached shell 3/4 schedule

Remaining Level of Effort | Actual Work | Critical Remaining Work
Actual Level of Effort | Remaining Work | Meeting Milestone

Jefferson High School 1.6.26


data date :01-Dec-25 Page 2 of 3 TASK filter: <100%.

Jefferson High

BASELINE SCHEDULE SUMMARY

LAYOUT: Jefferson HS Summary_1....12-Jan-26....

Activity ID	Activity Name	Orig Dur	Remaining Duration	Start	Finish
Sidewalks / Landscaping		195	195	09-Feb-28	10-Nov-28
Commissioning		119	119	09-Aug-28	29-Jan-29
Closeout		153	153	30-Jan-29	04-Sep-29
90000	Weather Contingency	20	20	30-Jan-29	26-Feb-29
90010	New Building Punch	50	50	27-Feb-29	07-May-29
90015	TCO	0	0		07-May-29
90020	Otis / FF&E Install & Move-in (Aug 15 2029) **Student Ready**	70	70	08-May-29	15-Aug-29*
90030	Contingency	13	13	16-Aug-29	04-Sep-29
Phase 3		265	265	15-Aug-29	05-Sep-30
Hoisting		342	342	21-Dec-26	24-Apr-28



Current Baseline Schedule allows for Student Ready on 15August2029.

Remaining Level of Effort | Actual Work | Critical Remaining Work
Actual Level of Effort | Remaining Work | Meeting Milestone

Jefferson High School 1.6.26


data date :01-Dec-25 Page 3 of 3 TASK filter: <100%.

Jefferson High-1

PHASED OCCUPANCY SCHEDULE SUMMARY

LAYOUT: Jefferson HS Delay L3 L4 Summary....12-Jan-26....

Activity ID	Activity Name	Orig Dur	Remaining Duration	Start	Finish
Owner Milestones		724	724	08-May-26	15-Mar-29
MS0900	PPS Ground Breaking Ceremony	0	0	08-May-26*	
MS1000	Baseball / Softball Season Completion	0	0		01-Jun-26*
MS1010	Last Day of School 2026	0	0		12-Jun-26*
MS1020	First Day of Spring Practice Softball / Baseball	0	0	01-Mar-27*	
MS1030	Last Day of Basketball Practice / Early Gym Demo	0	0		15-Mar-29*
MS1040	Last Day of Football Practice	0	0		13-Nov-26*
PRECONSTRUCTION		731	658	19-Mar-25 A	05-Jul-28
Deign & Permitting from Bora		417	344	19-Mar-25 A	09-Apr-27
Design		331	258	01-Sep-25 A	08-Dec-26
Permit		390	344	19-Mar-25 A	09-Apr-27
HCC		658	658	01-Dec-25	05-Jul-28
Contracts & Buyout		417	417	01-Dec-25	23-Jul-27
Trade Partner Selection for Precon Assist & Procurement		460	460	11-May-26	02-Mar-28
General Material Procurement		593	593	06-Mar-26	05-Jul-28
BIM Coordination		354	354	01-Dec-25	23-Apr-27
PROCUREMENT		225	225	12-Oct-26	30-Aug-27
Construction		1308	1262	15-Aug-25 A	22-Nov-30
Cons10000	Start of Construction	0	0	23-Jun-26	
Cons10010	Construction Duration	1016	1016	02-Jun-26	04-Jun-30
HCC		1308	1262	15-Aug-25 A	22-Nov-30
Pacific Power		546	500	15-Aug-25 A	18-Nov-27
Phase 1		218	218	13-Apr-26	19-Feb-27
Phase 2		1015	1015	20-Nov-26	22-Nov-30
20000	Mobilization, Temp Power& Demo	10	10	20-Nov-26	07-Dec-26
Building B - Main Education Building		886	886	07-Dec-26	04-Jun-30
Underground		79	79	07-Dec-26	29-Mar-27
Slab on Grade		58	58	27-Jan-27	16-Apr-27
Area 1 & 1A		14	14	27-Jan-27	15-Feb-27
Area 2		14	14	12-Feb-27	03-Mar-27
Area 3		14	14	24-Feb-27	15-Mar-27
Area 4		14	14	10-Mar-27	29-Mar-27
Area 5		14	14	30-Mar-27	16-Apr-27
Structure		149	149	12-Apr-27	09-Nov-27
Steel Zones 1A & 1B Floors 1-3		27	27	12-Apr-27	18-May-27
Mass Timber Zone 1 Floors 1-3		20	20	03-May-27	28-May-27
Steel Zones 1A & 1B Floors 3-Roof		31	31	01-Jun-27	14-Jul-27
Mass Timber Zone 1 Floors 3-Roof		20	20	22-Jun-27	20-Jul-27
Steel Zone 2 Floors 1-3		26	26	21-Jul-27	25-Aug-27
Mass Timber Zone 2 Floors 1-3		31	31	04-Aug-27	16-Sep-27
Steel Zone 2 Floors 3-Roof		26	26	17-Sep-27	22-Oct-27
Mass Timber Zone 2 Floor 3-Roof		28	28	01-Oct-27	09-Nov-27
Steel Zone 3Roof Deck		11	11	01-Oct-27	15-Oct-27
Mass Timber Zone 3 Floors 1-Roof		8	8	18-Oct-27	27-Oct-27
Roof		184	184	21-Jul-27	10-Apr-28
Facade		262	262	21-Jul-27	31-Jul-28
Interior Buildout		678	678	30-Sep-27	04-Jun-30
Building A - Auditorium		432	432	10-Feb-27	19-Oct-28
Underground		73	73	10-Feb-27	21-May-27
Slab on Grade		62	62	29-Mar-27	23-Jun-27
Structure		81	81	30-Apr-27	24-Aug-27
Roof		105	105	18-Aug-27	18-Jan-28
Facade		152	152	13-Aug-27	20-Mar-28
Interior Buildout		260	260	13-Oct-27	19-Oct-28
Level 1		260	260	13-Oct-27	19-Oct-28
Level 2		200	200	27-Oct-27	09-Aug-28
Building C - Gym		485	485	10-Feb-27	08-Jan-29
Underground		60	60	10-Feb-27	04-May-27
Slab on Grade		199	199	22-Mar-27	03-Jan-28
Structure		197	197	26-Apr-27	03-Feb-28
Roof		164	164	23-Sep-27	15-May-28
Facade		145	145	04-Feb-28	28-Aug-28

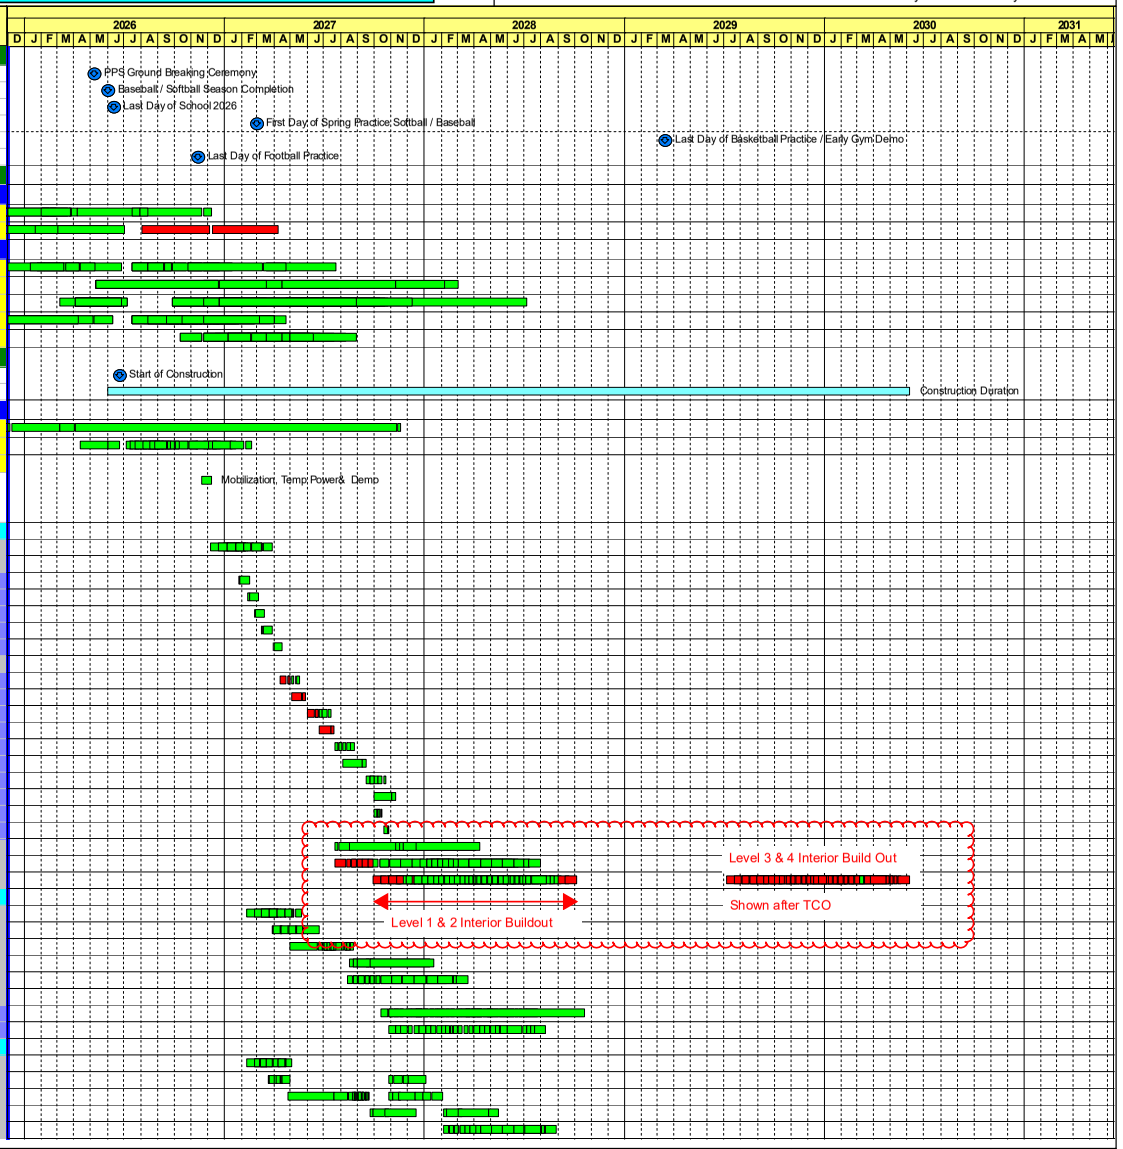

Remaining Level of Effort | Actual Work | Critical Remaining Work
Actual Level of Effort | Remaining Work | Meeting Milestone

Jefferson High School 1.6.26 - Delay L3 L4


data date :01-Dec-25 Page 1 of 2 TASK filter: <100%.

Jefferson High-1

PHASED OCCUPANCY SCHEDULE SUMMARY

LAYOUT: Jefferson HS Delay L3 L4 Summary....12-Jan-26....

Activity ID	Activity Name	Orig Dur	Remaining Duration	Start	Finish
Interior Buildout		327	327	23-Sep-27	08-Jan-29
Level 1 / Level 1 Mezzanine		327	327	23-Sep-27	08-Jan-29
Level 2		230	230	04-Oct-27	28-Aug-28
Sidewalks / Landscaping		194	194	10-Feb-28	10-Nov-28
Commissioning		187	187	23-Mar-28	15-Dec-28
Closeout		490	490	18-Dec-28	22-Nov-30
90000	Weather Contingency	20	20	18-Dec-28	16-Jan-29
90010	New Building Punch & Fire Life Safety FA Testing	50	50	17-Jan-29	27-Mar-29
90015	TCO Buildings A & B	0	0		27-Mar-29
90017	TCO Building C	0	0		08-Jan-29
90020	Otis / FF&E Install & Move-in	70	70	28-Mar-29	05-Jul-29*
90025	Teaching Ready / Start of Classes	0	0	06-Jul-29	
90030	Contingency	13	13	06-Jul-29	24-Jul-29
91000	L3 & L4 Punch & Life Safety FA Testing	50	50	05-Jun-30	15-Aug-30
91020	L3 & L4 FF&E Install & Move-in	70	70	16-Aug-30	22-Nov-30
Phase 3		265	265	05-Jul-29	25-Jul-30
Hoisting		345	345	21-Dec-26	27-Apr-28

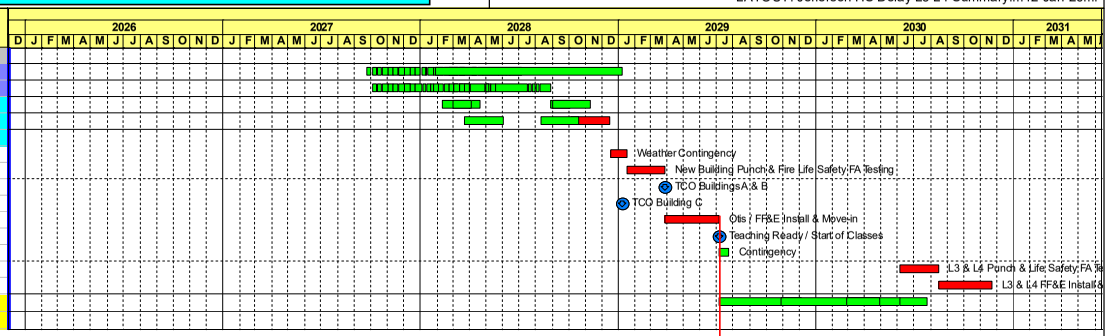

L3 &L4 Delay Schedule allows for Student Ready on 5July2029.

Remaining Level of Effort | Actual Work | Critical Remaining Work
Actual Level of Effort | Remaining Work | Meeting Milestone


Jefferson High School 1.6.26 - Delay L3 L4

data date :01-Dec-25 Page 2 of 2 TASK filter: <100%.

Jefferson High

LAYOUT: Jefferson HS....13-Jan-26....

Activity ID	Activity Name	Orig Dur	Remaining Duration	Start	Finish
Owner Milestones		724	724	08-May-26	15-Mar-29
MS0900	PPS Ground Breaking Ceremony	0	0	08-May-26*	
MS1000	Baseball / Softball Season Completion	0	0		01-Jun-26*
MS1010	Last Day of School 2026	0	0		12-Jun-26*
MS1020	First Day of Spring Practice Softball / Baseball	0	0	01-Mar-27*	
MS1030	Last Day of Basketball Practice / Early Gym Demo	0	0		15-Mar-29*
MS1040	Last Day of Football Practice	0	0		13-Nov-26*
PRECONSTRUCTION		731	658	19-Mar-25 A	05-Jul-28
Deign & Permitting from Bora		417	344	19-Mar-25 A	09-Apr-27
Design		331	258	01-Sep-25 A	08-Dec-26
Fields		114	41	01-Sep-25 A	30-Jan-26
D1200	JHS Early Fields Construction Documents	110	41	01-Sep-25 A	30-Jan-26
D1230	JHS Early Fields 100% CD Set	0	0		30-Jan-26*
New School Building		268	258	27-Oct-25 A	08-Dec-26
D1500	JHS Design Development	110	87	27-Oct-25 A	06-Apr-26
D1510	JHS DD Pricing Set (Structural / Arch Gridlock)	0	0		30-Jan-26
D1520	JHS DD Cost Estimate	35	35	02-Feb-26	20-Mar-26
D1530	JHS DD Estimate Set Owner Review	10	10	02-Feb-26	13-Feb-26
D1540	JHS DD Estimate Set Owner Page Turns	10	10	16-Feb-26	27-Feb-26
D1550	JHS DD DPA (Design Phase Approval)	5	5	23-Mar-26	27-Mar-26
D1560	JHS QC Review	40	40	30-Jan-26	26-Mar-26
D1570	JHS Construction Documents	161	161	07-Apr-26	20-Nov-26
D1580	JHS 50% CD Set (100% CD Foundation to Grade Structural)	0	0	17-Jul-26	
D1590	Design Deliverable 1 (AR) Fire Protection Head Placement For DLT Pen. Coor	0	0	17-Jul-26	
D1600	Design Deliverable 2 (AR) Light Layout For DLT Pen. Coord.	0	0	17-Jul-26	
D1610	Design Deliverable 3 (AR) Shaft Rollout For DLT Pen. Coord.	0	0	17-Jul-26	
D1620	Structural Frame 100% CD Connected Structural Model LOD 300	0	0	12-Oct-26*	
D1630	JHS 50% CD Set Owner Review	10	10	17-Jul-26	30-Jul-26
D1640	JHS 50% CD Set Owner Page Turn	10	10	31-Jul-26	13-Aug-26
D1645	JHS 75% MEP Design / Equipment Selection	0	0	01-Oct-26*	
D1650	JHS 100% CD Set	0	0		20-Nov-26
D1660	JHS PPS 100% CD Set Owner Review	10	10	23-Nov-26	08-Dec-26
Permit		390	344	19-Mar-25 A	09-Apr-27
PER0900	JHS MPG Submit 25% DD Documents for Review	0	0	01-Dec-25	
PER0910	JHS MPG Submit 100% DD Documents for Review	0	0	07-Apr-26	
PER0930	JHS Public Works Permit / Right of Way Scope	260	126	19-Mar-25 A	01-Jun-26
PER0940	JHS Land Use - Type III CU	100	77	06-Oct-25 A	23-Mar-26
PER0950	JHS Land Use - Historic Review	60	60	21-Jan-26*	14-Apr-26
PER1000	JHS Permit Set A: Early Fields	88	88	02-Mar-26*	02-Jul-26
PER1020	JHS Permit Set B: Foundation to Grade	87	87	03-Aug-26*	04-Dec-26
PER1040	JHS Permit Set C: Building Permit	85	85	10-Dec-26	09-Apr-27
HCC		658	658	01-Dec-25	05-Jul-28
Contracts & Buyout		417	417	01-Dec-25	23-Jul-27
BO60000	Sub Bids, Normalization & EWA Preparation (Early Fields)	45	45	01-Dec-25	05-Feb-26
BO60010	Early Work Amendment Execution (Early Fields)	20	20	06-Feb-26	05-Mar-26
BO60020	Phase 1 - Execute Critical Subcontracts (Early Fields)	20	20	06-Mar-26	02-Apr-26
BO60030	Athletic Field Specialties Long Lead Time	60	60	03-Apr-26	26-Jun-26
BO60040	MEPF Trade Partner RFP, Bids & PPS Amendment	56	56	23-Jan-26*	10-Apr-26
BO60050	PPS Amendment for MEPF Trade Partner District Approval	20	20	13-Apr-26	08-May-26
BO60060	Mass Timber RFP Bids & PPS Amendment	45	45	12-Jan-26*	13-Mar-26
BO60062	Mass Exc / UG Utilities / Foundations RFP Bids & Early Work Amendment	30	30	17-Jul-26	27-Aug-26
BO60064	EWA Mass Exc / UG Utilities / Foundations District Approval	20	20	28-Aug-26	25-Sep-26
BO60070	Early Work Amendment for Mass Timber District Approval	20	20	16-Mar-26	10-Apr-26
BO60080	Sub Bids, Normalization & Budget Preparation (Balance of Work)	70	70	17-Jul-26	23-Oct-26
BO60090	Phase 2 Early Work Amendment Execution District Appoval	20	20	26-Oct-26	20-Nov-26
BO60100	Balance of Work - Execute Critical Subcontracts & Start Submittals	20	20	23-Nov-26	22-Dec-26
BO60110	Steel Fab & Erect Sub Bids, Normalization Early Work Amendment	20	20	17-Jul-26	13-Aug-26
BO60120	Structural Steel Mill Order, Fab & Erect Early Work Amendment Execution by D	20	20	14-Aug-26	11-Sep-26
BO60130	Prepare & Release Mill Order	10	10	14-Sep-26	25-Sep-26
BO60140	Roll & Ship Steel to Fabricator	75	75	28-Sep-26	15-Jan-27
BO60150	Misc Iron / Stairs Procurement	90	90	18-Mar-27	23-Jul-27

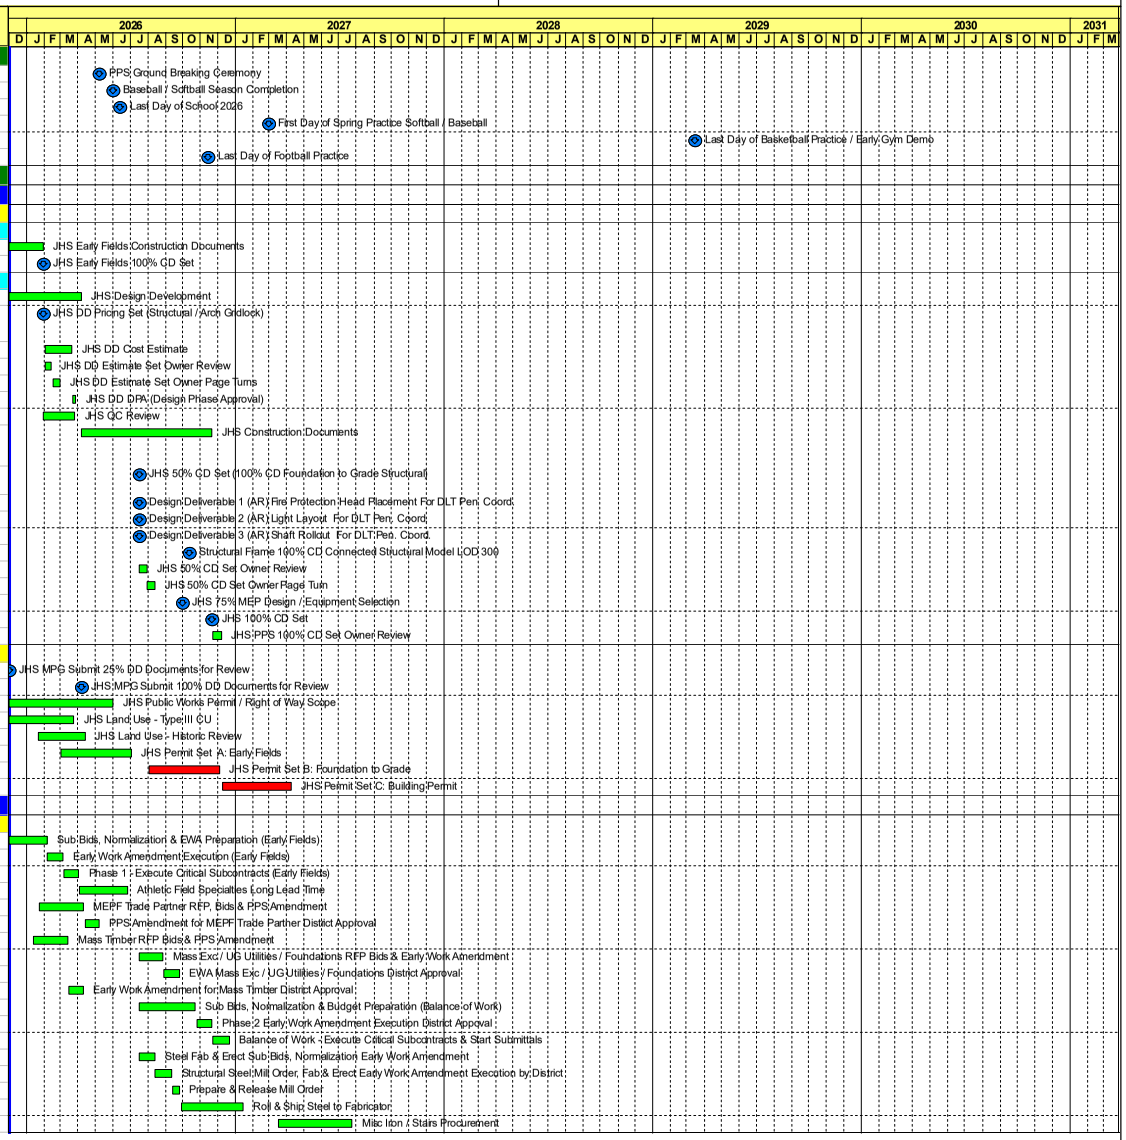

Remaining Level of Effort | Actual Work | Critical Remaining Work
Actual Level of Effort | Remaining Work | Meeting Milestone


Jefferson High School 1.6.26

data date :01-Dec-25 Page 1 of 19 TASK filter: <100%.

Jefferson High

LAYOUT: Jefferson HS....13-Jan-26....

Activity ID	Activity Name	Orig Dur	Remaining Duration	Start	Finish
BO60170	Full GMP Amendment Negotiation & Execution	95	95	26-Oct-26	11-Mar-27
BO60180	Early Start of Phase 2 Work	0	0	23-Dec-26	
BO60190	Balance of Work - Execute All Remaining Subcontractors	30	30	12-Mar-27	22-Apr-27
Trade Partner Selection for Precon Assist & Procurement		460	460	11-May-26	02-Mar-28
Mass Timber		190	190	11-May-26	09-Feb-27
TPS1200	Trade Partner Selection Complete - Mass Timber	0	0	11-May-26	
TPS1210	BIM Coordination for Timber	190	190	11-May-26	09-Feb-27
TPS1220	Select & Source Materials	100	100	11-May-26	30-Sep-26
Electrical		460	460	11-May-26	02-Mar-28
TPS1300	Trade Partner Selection Complete - Electrical	0	0	11-May-26	
TPS1310	Trade Partner Budgeting / VE & Early BIM Efforts & Temp Power Install	156	156	11-May-26	21-Dec-26
TPS1320	Electrical Switchgear & Emergency Generator Long Lead Equipment	323	323	23-Nov-26	02-Mar-28
TPS1330	Misc. Electrical & Data Submittals / Procurement	150	150	23-Dec-26	26-Jul-27
TPS1340	Misc Security &AV Submittals/ Procurement	150	150	23-Dec-26	26-Jul-27
Mechanical / Plumbing		309	309	11-May-26	28-Jul-27
TPS1400	Trade Partner Selection Complete - Mechanical / Plumbing	0	0	11-May-26	
TPS1410	Trade Partner Budgeting / VE & Early BIM Efforts & Temp Water Install	156	156	11-May-26	21-Dec-26
TPS1420	Major MEP Equipment Long Lead Equipment Submittals / Procurement	172	172	23-Nov-26	28-Jul-27
Fire Protection		442	442	11-May-26	07-Feb-28
TPS1600	Trade Partner Selection Complete- Fire Protection	0	0	11-May-26	
TPS1602	Trade Partner Budgeting / VE & Early BIM Efforts	156	156	11-May-26	21-Dec-26
TPS1610	Fire Pump Long Lead Submittals / Procurement	100	100	23-Nov-26	15-Apr-27
TPS1620	Fire Protection DFS Submittals / Approval	145	145	16-Apr-27	09-Nov-27
TPS1630	Fire Protection Submitals / Procurement	60	60	10-Nov-27	07-Feb-28
Structural Steel Detailing		216	216	11-May-26	17-Mar-27
TPS1700	Structural Steel Detailer Selection Complete	0	0	11-May-26	
TPS1710	Structural Steel Detailing BIM Efforts	156	156	11-May-26	21-Dec-26
TPS1720	Misc Iron / Stairs Detailing & Submittals	60	60	22-Dec-26	17-Mar-27
General Material Procurement		593	593	06-Mar-26	05-Jul-28
Early Fields Phase 1 Work		85	85	06-Mar-26	06-Jul-26
019000	Underground Utilities / Plumbing - Submittals / Procurement	60	60	03-Apr-26	26-Jun-26
019010	Rebar / Concrete - Submittals / Procurement	60	60	03-Apr-26	26-Jun-26
019020	Field Turf Products & Electrical / Data - Submittals / Procurement	65	65	06-Mar-26	05-Jun-26
019030	Site Furnishings - Submittals / Procurement	65	65	03-Apr-26	06-Jul-26
019040	Site Landscaping - Submittals / Procurement	65	65	03-Apr-26	06-Jul-26
019050	Curbs & Sidewalk & ROW - Submittals / Procurement	60	60	03-Apr-26	26-Jun-26
019060	Early Field Procurement Complete	0	0		06-Jul-26
JHS Main Building Phase 2 Work		450	450	28-Sep-26	05-Jul-28
019750	Early MEP Underground - Submittals / Procurement	45	45	28-Sep-26	01-Dec-26
019800	Gymnasium & Theatrical Specialties - Submittals / Procurement	120	120	23-Apr-27	12-Oct-27
020200	PV Panels - Submittals / Procurement	305	305	23-Apr-27	05-Jul-28
020300	Site Civil - Submittals / Procurement	60	60	28-Sep-26	22-Dec-26
020700	Foundation Reinforcing - Submittals / Procurement	65	65	28-Sep-26	30-Dec-26
020900	Utility Materials, Catch Basins & Vaults - Submittals / Procurement	43	43	28-Sep-26	25-Nov-26
021100	Underslab Plumbing - Procurement	45	45	23-Nov-26	28-Jan-27
021300	Underslab Electrical - Procurement	45	45	23-Nov-26	28-Jan-27
021700	Plumbing Fixtures, Tubs & Showers - Submittals / Procurement	127	127	23-Apr-27	21-Oct-27
021900	Finishes - Submittals / Procurement	130	130	23-Apr-27	26-Oct-27
022200	Elevator Rails, Platform & Equipment - Submittals / Procurement	85	85	23-Dec-26	22-Apr-27
022400	Elevator Cab Packages - Submittals / Procurement	127	127	23-Dec-26	22-Jun-27
022800	Glazing Systems - Submittals / Procurement	246	246	23-Dec-26	10-Dec-27
024165	Temp Roof - Submittals / Procurement	60	60	23-Dec-26	18-Mar-27
024170	Roofing - Submittals / Procurement	87	87	23-Dec-26	26-Apr-27
024190	Exterior Skin System - Submittals / Design / DFS Approval / Procurement	175	175	23-Dec-26	30-Aug-27
BIM Coordination		354	354	01-Dec-25	23-Apr-27
Early Fields		55	55	25-Mar-26	10-Jun-26
D1130	Survey Coordination	55	55	25-Mar-26	10-Jun-26
D1140	Civil Modeling	21	21	08-Apr-26	06-May-26
D1150	Civil Coordination	24	24	07-May-26	10-Jun-26
D1160	IFF Underground	0	0		10-Jun-26
Timber 1		70	70	17-Jul-26	23-Oct-26
BIM1000	T1 - Populate Model	15	15	17-Jul-26	06-Aug-26
BIM1010	T1 - Initial Space Coordination with MEP	15	15	07-Aug-26	27-Aug-26
BIM1020	T1 - Initial Clash Detection	15	15	28-Aug-26	18-Sep-26
BIM1030	T1 - Penetration Coordination	10	10	21-Sep-26	02-Oct-26

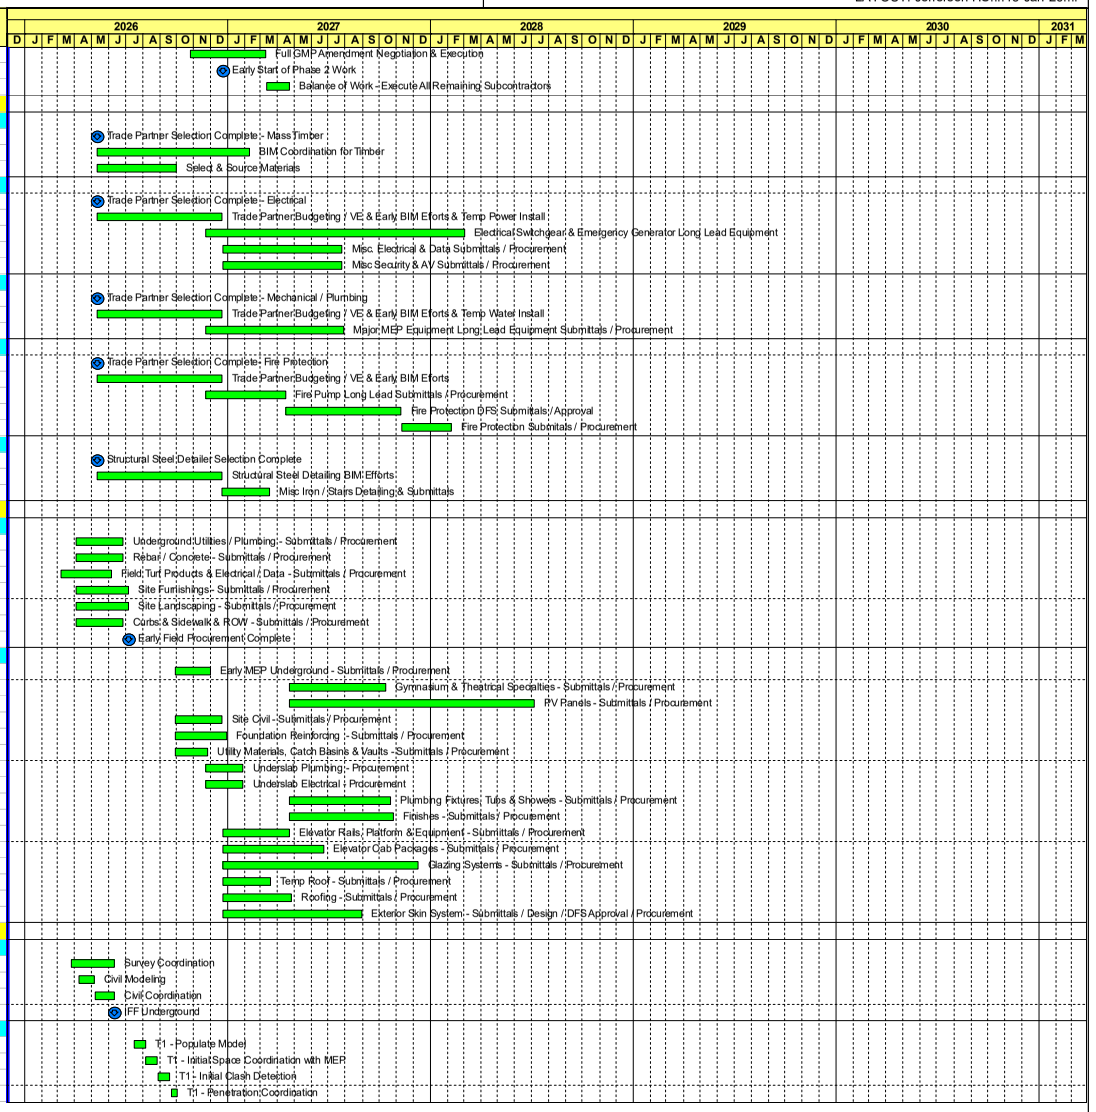

Remaining Level of Effort | Actual Work | Critical Remaining Work

Actual Level of Effort | Remaining Work | Meeting Milestone

Jefferson High School 1.6.26

data date :01-Dec-25 Page 2 of 19 TASK filter: <100%.

Jefferson High

LAYOUT: Jefferson HS....13-Jan-26....

Activity ID	Activity Name	Orig Dur	Remaining Duration	Start	Finish
BIM1040	T1 - Issue Penetration Drawings Clashes Resolved	5	5	05-Oct-26	09-Oct-26
BIM1050	T1 - Structural Penetration Coordination & Approval	10	10	12-Oct-26	23-Oct-26
Timber 2		70	70	07-Aug-26	13-Nov-26
BIM2000	T2 - Populate Model	15	15	07-Aug-26	27-Aug-26
BIM2010	T2 - Initial Space Coordination with MEP	15	15	28-Aug-26	18-Sep-26
BIM2020	T2 - Initial Clash Detection	15	15	21-Sep-26	09-Oct-26
BIM2030	T2 - Penetration Coordination	10	10	12-Oct-26	23-Oct-26
BIM2040	T2 - Issue Penetration Drawings Clashes Resolved	5	5	26-Oct-26	30-Oct-26
BIM2050	T2 - Structural Penetration Coordination & Approval	10	10	02-Nov-26	13-Nov-26
Timber 3		70	70	28-Aug-26	08-Dec-26
BIM3000	T3 - Populate Model	15	15	28-Aug-26	18-Sep-26
BIM3010	T3 - Initial Space Coordination with MEP	15	15	21-Sep-26	09-Oct-26
BIM3020	T3 - Initial Clash Detection	15	15	12-Oct-26	30-Oct-26
BIM3030	T3 - Penetration Coordination	10	10	02-Nov-26	13-Nov-26
BIM3040	T3 - Issue Penetration Drawings Clashes Resolved	5	5	16-Nov-26	20-Nov-26
BIM3050	T3 - Structural Penetration Coordination & Approval	10	10	23-Nov-26	08-Dec-26
Timber 4		70	70	21-Sep-26	30-Dec-26
BIM4000	T4 - Populate Model	15	15	21-Sep-26	09-Oct-26
BIM4010	T4 - Initial Space Coordination with MEP	15	15	12-Oct-26	30-Oct-26
BIM4020	T4 - Initial Clash Detection	15	15	02-Nov-26	20-Nov-26
BIM4030	T4 - Penetration Coordination	10	10	23-Nov-26	08-Dec-26
BIM4040	T4 - Issue Penetration Drawings Clashes Resolved	5	5	09-Dec-26	15-Dec-26
BIM4050	T4 - Structural Penetration Coordination & Approval	10	10	16-Dec-26	30-Dec-26
Timber 5		70	70	12-Oct-26	21-Jan-27
BIM5000	T5 - Populate Model	15	15	12-Oct-26	30-Oct-26
BIM5010	T5 - Initial Space Coordination with MEP	15	15	02-Nov-26	20-Nov-26
BIM5020	T5 - Initial Clash Detection	15	15	23-Nov-26	15-Dec-26
BIM5030	T5 - Penetration Coordination	10	10	16-Dec-26	30-Dec-26
BIM5040	T5 - Issue Penetration Drawings Clashes Resolved	5	5	31-Dec-26	07-Jan-27
BIM5050	T5 - Structural Penetration Coordination & Approval	10	10	08-Jan-27	21-Jan-27
Architectural Routing (AR) @ MEP Timber Elements		248	248	01-Dec-25	20-Nov-26
BIM6000	T1 AR Populate / Coordinate	90	90	17-Jul-26	20-Nov-26
BIM6010	T1 IFFAR	0	0		20-Nov-26
BIM6020	T2 AR Populate / Coordinate	90	90	01-Dec-25	09-Apr-26
BIM6030	T2 IFFAR	0	0		09-Apr-26
BIM6040	T3 AR Populate / Coordinate	90	90	01-Dec-25	09-Apr-26
BIM6050	T3 IFFAR	0	0		09-Apr-26
BIM6060	T4 AR Populate / Coordinate	90	90	01-Dec-25	09-Apr-26
BIM6070	T4 IFFAR	0	0		09-Apr-26
BIM6080	T5 AR Populate / Coordinate	90	90	01-Dec-25	09-Apr-26
BIM6090	T5 IFFAR	0	0		09-Apr-26
DLT		60	60	09-Dec-26	04-Mar-27
BIM7000	MEP Connection Coordination / Architectural Ceiling Layout	60	60	09-Dec-26	04-Mar-27
Auditorium (A)		154	154	17-Jul-26	24-Feb-27
BIM8000	Aud UG Populate / Coordinate / Clash Resolution / Submit & Approve	70	70	17-Jul-26	23-Oct-26
BIM8010	IFF Aud UG	0	0		23-Oct-26
BIM8020	Aud L1 Populate / Coordinate / Clash Resolution / Submit & Approve	90	90	14-Aug-26	22-Dec-26
BIM8030	IFF Aud L1	0	0		22-Dec-26
BIM8040	Aud L2 Populate / Coordinate / Clash Resolution / Submit & Approve	90	90	17-Sep-26	26-Jan-27
BIM8050	IFF Aud L2	0	0		26-Jan-27
BIM8060	Aud L3 Populate / Coordinate / Clash Resolution / Submit & Approve	90	90	16-Oct-26	24-Feb-27
BIM8070	IFF Aud L3	0	0		24-Feb-27
Main Building (B)		196	196	17-Jul-26	23-Apr-27
BIM9000	MB UG Populate / Coordinate / Clash Resolution / Submit & Approve	90	90	17-Jul-26	20-Nov-26
BIM9010	IFF MB UG	0	0		20-Nov-26
BIM9020	MB L1 Populate / Coordinate / Clash Resolution / Submit & Approve	90	90	14-Aug-26	22-Dec-26
BIM9030	IFF MB L1	0	0		22-Dec-26
BIM9040	MB L2 Populate / Coordinate / Clash Resolution / Submit & Approve	90	90	17-Sep-26	26-Jan-27
BIM9050	IFF MB L2	0	0		26-Jan-27
BIM9060	MB L3 Populate / Coordinate / Clash Resolution / Submit & Approve	90	90	16-Oct-26	24-Feb-27
BIM9070	IFF MB L3	0	0		24-Feb-27
BIM9080	MB L4 Populate / Coordinate / Clash Resolution / Submit & Approve	90	90	16-Nov-26	25-Mar-27
BIM9090	IFF MB L4	0	0		25-Mar-27
BIM9100	MB L5 Populate / Coordinate / Clash Resolution / Submit & Approve	90	90	17-Dec-26	23-Apr-27
BIM9110	IFF MB L5	0	0		23-Apr-27
Gym (C)		154	154	17-Jul-26	24-Feb-27



Remaining Level of Effort | Actual Work | Critical Remaining Work

Actual Level of Effort | Remaining Work | Meeting Milestone


Jefferson High School 1.6.26

data date :01-Dec-25 Page 3 of 19 TASK filter: <100%.

Jefferson High

LAYOUT: Jefferson HS....13-Jan-26....

Activity ID	Activity Name	Orig Dur	Remaining Duration	Start	Finish
BIM10000	Gym UG Populate / Coordinate / Clash Resolution / Submit & Approve	70	70	17-Jul-26	23-Oct-26
BIM10010	IFF Gym UG	0	0		23-Oct-26
BIM10020	Gym L1 Populate / Coordinate / Clash Resolution / Submit & Approve	90	90	14-Aug-26	22-Dec-26
BIM10030	IFF Gym L1	0	0		22-Dec-26
BIM10040	Gym L2 Populate / Coordinate / Clash Resolution / Submit & Approve	90	90	17-Sep-26	26-Jan-27
BIM10050	IFF Gym L2	0	0		26-Jan-27
BIM10060	Gym L3 Populate / Coordinate / Clash Resolution / Submit & Approve	90	90	16-Oct-26	24-Feb-27
BIM10070	IFF Gym L3	0	0		24-Feb-27
Phase 3		90	90	23-Nov-26	01-Apr-27
BIM11000	Building / Football / Tennis Fields Populate / Coordinate / Clash Resolution	90	90	23-Nov-26	01-Apr-27
BIM11010	IFF FB / TF / Submit & Approve	20	20	05-Mar-27	01-Apr-27
PROCUREMENT		225	225	12-Oct-26	30-Aug-27
Mass Timber		225	225	12-Oct-26	30-Aug-27
Proc9000	Detail, Submit, Approve Mass Timber - Zone 1	85	85	12-Oct-26	11-Feb-27
Proc9010	Fab & Deliver Mas Timber - Zone 1	80	80	12-Feb-27	04-Jun-27
Timber 1		165	165	12-Oct-26	04-Jun-27
Proc1000	T1 -Populate Beams & Columns	15	15	12-Oct-26	30-Oct-26
Proc1010	T1 - Populate DLT Plank	15	15	02-Nov-26	20-Nov-26
Proc1020	T1 - Connect Timber	15	15	23-Nov-26	15-Dec-26
Proc1030	T1 - Incorporate Penetrations	10	10	16-Dec-26	30-Dec-26
Proc1040	T1 - Detail & Submit	15	15	31-Dec-26	21-Jan-27
Proc1050	T1 - Approve Submittal	15	15	22-Jan-27	11-Feb-27
Proc1060	T1 - Fabricate & Deliver	80	80	12-Feb-27	04-Jun-27
Timber 2		165	165	02-Nov-26	25-Jun-27
Proc2000	T2 -Poulate Beams & Columns	15	15	02-Nov-26	20-Nov-26
Proc2010	T2 - Populate DLT Plank	15	15	23-Nov-26	15-Dec-26
Proc2020	T2 - Connect Timber	15	15	16-Dec-26	07-Jan-27
Proc2030	T2 - Incorporate Penetrations	10	10	08-Jan-27	21-Jan-27
Proc2040	T2 - Detail & Submit	15	15	22-Jan-27	11-Feb-27
Proc2050	T2 - Approve Submittal	15	15	12-Feb-27	04-Mar-27
Proc2060	T2 - Fabricate & Deliver	80	80	05-Mar-27	25-Jun-27
Timber 3		165	165	23-Nov-26	19-Jul-27
Proc3000	T3 -Poulate Beams & Columns	15	15	23-Nov-26	15-Dec-26
Proc3010	T3 - Populate DLT Plank	15	15	16-Dec-26	07-Jan-27
Proc3020	T3 - Connect Timber	15	15	08-Jan-27	28-Jan-27
Proc3030	T3 - Incorporate Penetrations	10	10	29-Jan-27	11-Feb-27
Proc3040	T3 - Detail & Submit	15	15	12-Feb-27	04-Mar-27
Proc3050	T3 - Approve Submittal	15	15	05-Mar-27	25-Mar-27
Proc3060	T3 - Fabricate & Deliver	80	80	26-Mar-27	19-Jul-27
Timber 4		165	165	16-Dec-26	09-Aug-27
Proc4000	T4 -Poulate Beams & Columns	15	15	16-Dec-26	07-Jan-27
Proc4010	T4 - Populate DLT Plank	15	15	08-Jan-27	28-Jan-27
Proc4020	T4 - Connect Timber	15	15	29-Jan-27	18-Feb-27
Proc4030	T4 - Incorporate Penetrations	10	10	19-Feb-27	04-Mar-27
Proc4040	T4 - Detail & Submit	15	15	05-Mar-27	25-Mar-27
Proc4050	T4 - Approve Submittal	15	15	26-Mar-27	15-Apr-27
Proc4060	T4 - Fabricate & Deliver	80	80	16-Apr-27	09-Aug-27
Timber 5		165	165	08-Jan-27	30-Aug-27
Proc5000	T5 -Poulate Beams & Columns	15	15	08-Jan-27	28-Jan-27
Proc5010	T5 - Populate DLT Plank	15	15	29-Jan-27	18-Feb-27
Proc5020	T5 - Connect Timber	15	15	19-Feb-27	11-Mar-27
Proc5030	T5 - Incorporate Penetrations	10	10	12-Mar-27	25-Mar-27
Proc5040	T5 - Detail & Submit	15	15	26-Mar-27	15-Apr-27
Proc5050	T5 - Approve Submittal	15	15	16-Apr-27	06-May-27
Proc5060	T5 - Fabricate & Deliver	80	80	07-May-27	30-Aug-27
Steel		170	170	12-Oct-26	11-Jun-27
Zone 1 - Main School Building - B		110	110	12-Oct-26	18-Mar-27
PROC11000	Z1 - Steel Modeling	30	30	12-Oct-26	20-Nov-26
PROC11010	Z1 - Steel Detailing / Fabrication Drawings	20	20	23-Nov-26	22-Dec-26
PROC11020	Z1 - Submit	20	20	23-Dec-26	21-Jan-27
PROC11030	Z1 - Scrub	10	10	22-Jan-27	04-Feb-27
PROC11040	Z1 - Fab	30	30	05-Feb-27	18-Mar-27
Zone 2 - Auditorium Building - A		110	110	23-Nov-26	29-Apr-27
PROC12000	Z2 - Steel Modeling	30	30	23-Nov-26	07-Jan-27
PROC12010	Z2 - Steel Detailing / Fabrication Drawings	20	20	08-Jan-27	04-Feb-27
PROC12020	Z2 - Submit	20	20	05-Feb-27	04-Mar-27

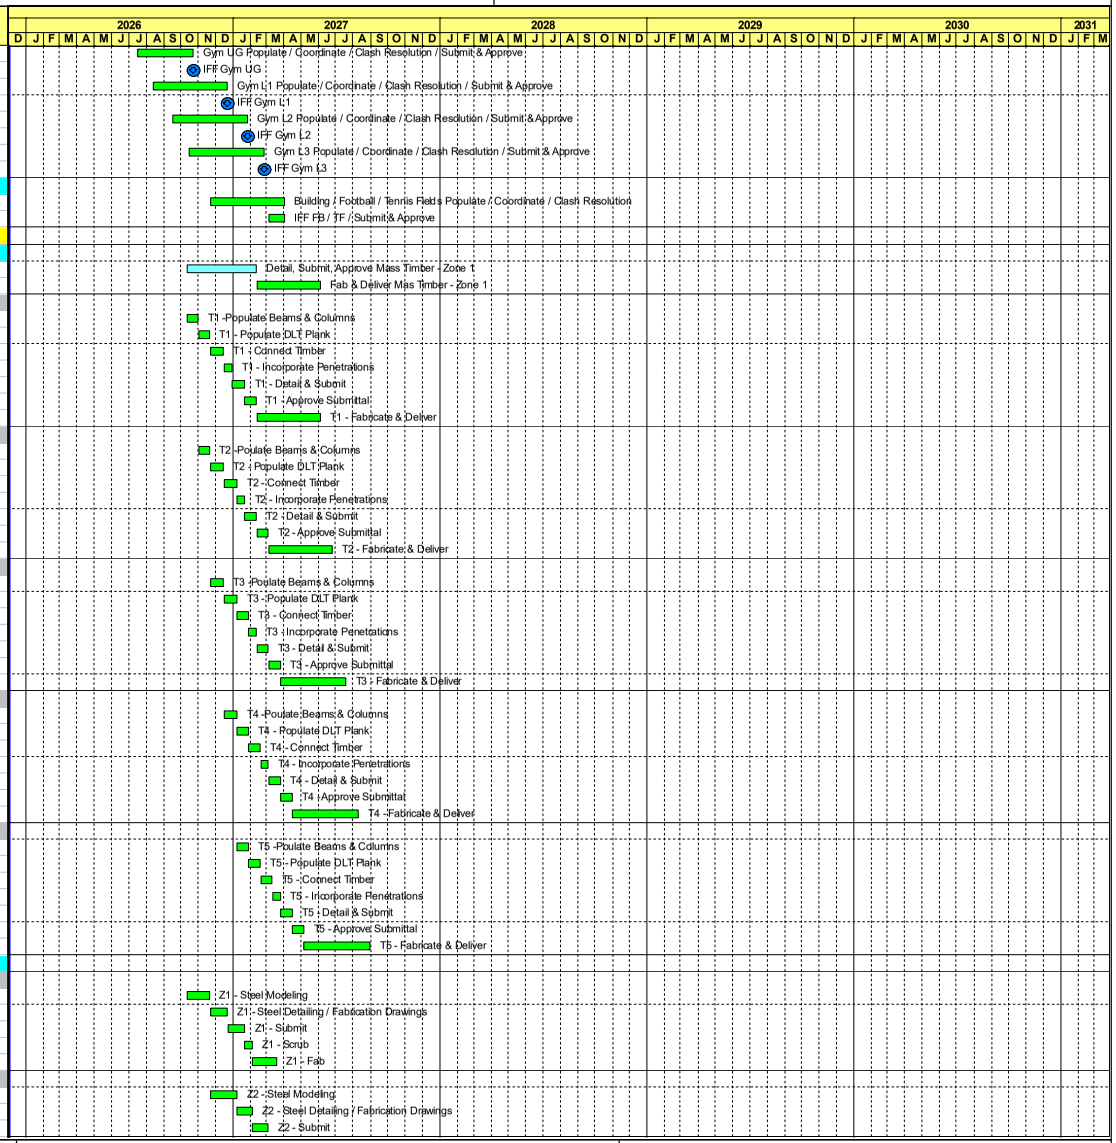


Remaining Level of Effort | Actual Work | Critical Remaining Work
Actual Level of Effort | Remaining Work | Meeting Milestone

Jefferson High School 1.6.26

data date :01-Dec-25 Page 4 of 19 TASK filter: <100%.


Activity ID	Activity Name	Orig Dur	Remaining Duration	Start	Finish
PROC12030	Z2 - Scrub	10	10	05-Mar-27	18-Mar-27
PROC12040	Z2 - Fab	30	30	19-Mar-27	29-Apr-27
Zone 3 - Gym Building - C		110	110	08-Jan-27	11-Jun-27
PROC13000	Z3 - Steel Modeling	30	30	08-Jan-27	18-Feb-27
PROC13010	Z3 - Steel Detailing / Fabrication Drawings	20	20	19-Feb-27	18-Mar-27
PROC13020	Z3 - Submit	20	20	19-Mar-27	15-Apr-27
PROC13030	Z3 - Scrub	10	10	16-Apr-27	29-Apr-27
PROC13040	Z3 - Fab	30	30	30-Apr-27	11-Jun-27
Construction		1252	1206	15-Aug-25 A	05-Sep-30
Cons10000	Start of Construction	0	0	23-Jun-26	
Cons10010	Construction Duration	1045	1045	02-Jun-26	17-Jul-30
HCC		1252	1206	15-Aug-25 A	05-Sep-30
Pacific Power		546	500	15-Aug-25 A	18-Nov-27
Pwr15000	Pacific Power System Impact Study	42	5	15-Aug-25 A	05-Dec-25
Pwr15010	Pacific Power Drafts Master Electric Service Agreement	60	60	08-Dec-25	05-Mar-26
Pwr15020	PPS Reviews & Signs MESA, Makes Upfront Payment	20	20	06-Mar-26	02-Apr-26
Pwr15030	Transformer Procurement	410	410	03-Apr-26	11-Nov-27
Pwr15032	Early Work Fields Temp Power Online / Transformers Delivered	0	0	10-Jul-26*	
Pwr15033	Building B Temp Power Source Online	0	0	04-Jan-27*	
Pwr15035	Killingsworth Underground & Pole Work Complete	0	0		15-Jan-27*
Pwr15040	Install Transformers & Power up PPS Switchgear	5	5	12-Nov-27	18-Nov-27
Phase 1		218	218	13-Apr-26	19-Feb-27
Fld10000	Softball & Baseball Fields Mobilization, Site Fencing, Temp MEP & Vac Truck U	15	15	02-Jun-26	22-Jun-26
Fld10010	Site Survey / Set Controls / Underground Modeling / Clash Detection	35	35	13-Apr-26	01-Jun-26
Softball Field		130	130	10-Jul-26	14-Jan-27
SBF10005	Site Demo, Prep & Strip Grade	10	10	10-Jul-26	23-Jul-26
SBF10010	Site Utilities, Underground, Civil / Stormwater	25	25	24-Jul-26	27-Aug-26
SBF10015	Rough Grade Site & Gravel Parking Lot, Install Loop Access Road	10	10	28-Aug-26	11-Sep-26
SBF10020	Site Concrete / CMU & Dugouts / Footings	20	20	14-Aug-26	11-Sep-26
SBF10025	Fine Grade / Light & Utility Poles / Scoreboard / Fencing Fabric & Backstop	20	20	14-Sep-26	09-Oct-26
SBF10030	Field Turf / Storage Shed	25	25	12-Oct-26	13-Nov-26
SBF10035	Stripes & Lines	10	10	02-Nov-26	13-Nov-26
SBF10040	Bleachers / MEP RI / Parking Lot Improvements	15	15	09-Nov-26	01-Dec-26
SBF10045	Area Landscape / Site Furnishings & MEP Trim Out / Irrigation	10	10	23-Nov-26	08-Dec-26
SBF10050	Architectural Accessories & Plantings	15	15	09-Dec-26	30-Dec-26
SBF10055	Punchlist & Cx	10	10	31-Dec-26	14-Jan-27
Baseball Field		160	160	06-Jul-26	19-Feb-27
BBF12000	Site Demo,Prep & Strip Grade	10	10	06-Jul-26	17-Jul-26
BBF12005	Site Utilities, Underground, Civil / Stormwater	35	35	20-Jul-26	04-Sep-26
BBF12007	Rough Grade & Install Temp Loop Access Road	10	10	08-Sep-26	21-Sep-26
BBF12015	Site Concrete & CMU & Dugouts / Footings	25	25	24-Aug-26	28-Sep-26
BBF12020	Fine Grade / Light & Utility Poles / Scoreboard / Fencing Fabric & Backstop	20	20	29-Sep-26	26-Oct-26
BBF12025	Field Turf / Storage Shed	35	35	27-Oct-26	16-Dec-26
BBF12030	Stripes & Lines	15	15	03-Dec-26	23-Dec-26
BBF12035	Bleachers & Backstops / MEP RI	30	30	10-Dec-26	22-Jan-27
BBF12040	Area Landscape / Site Furnishings & MEP Trim Out / Irrigation & Plantings	20	20	11-Jan-27	05-Feb-27
BBF12050	Punchlist & Cx	10	10	08-Feb-27	19-Feb-27
Fields Frontage Improvements		64	64	13-Jul-26	09-Oct-26
FI13000	Underground ROW Utilities Install	12	12	13-Jul-26*	28-Jul-26
FI13020	Remove & Replace Curb & SW @ Alberta South Side	15	15	22-Jul-26	11-Aug-26
FI13040	Remove & Replace Curb & SW @ Alberta North Side	15	15	05-Aug-26	25-Aug-26
FI13060	Remove & Replace Curb & SW @ Kirby	15	15	17-Aug-26	04-Sep-26
FI13080	Remove & Replace Curbs & SW @ Commercial	15	15	27-Aug-26	17-Sep-26
FI13100	Asphalt Paving @ Alberta	4	4	18-Sep-26	23-Sep-26
FI131120	Asphalt Paving @ Kirby	6	6	24-Sep-26	01-Oct-26
FI131130	Asphalt Paving @ Commercial	6	6	02-Oct-26	09-Oct-26
Phase 2		707	707	20-Nov-26	04-Sep-29
20000	Moblization, Temp Power& Demo	10	10	20-Nov-26	07-Dec-26
Building B - Main Education Building		498	498	07-Dec-26	17-Nov-28
Underground		79	79	07-Dec-26	29-Mar-27
30000	Mass Excavation / Structural Fill to BO Footing	45	45	07-Dec-26	09-Feb-27
30010	Underground Deep Utilities	30	30	29-Dec-26	09-Feb-27
Area 1 & 1A		25	25	21-Dec-26	26-Jan-27
30100	FRP Concrete Footings / Plynths / Walls	10	10	21-Dec-26	05-Jan-27
30110	Backfill from BO Footing to SOG	3	3	06-Jan-27	08-Jan-27

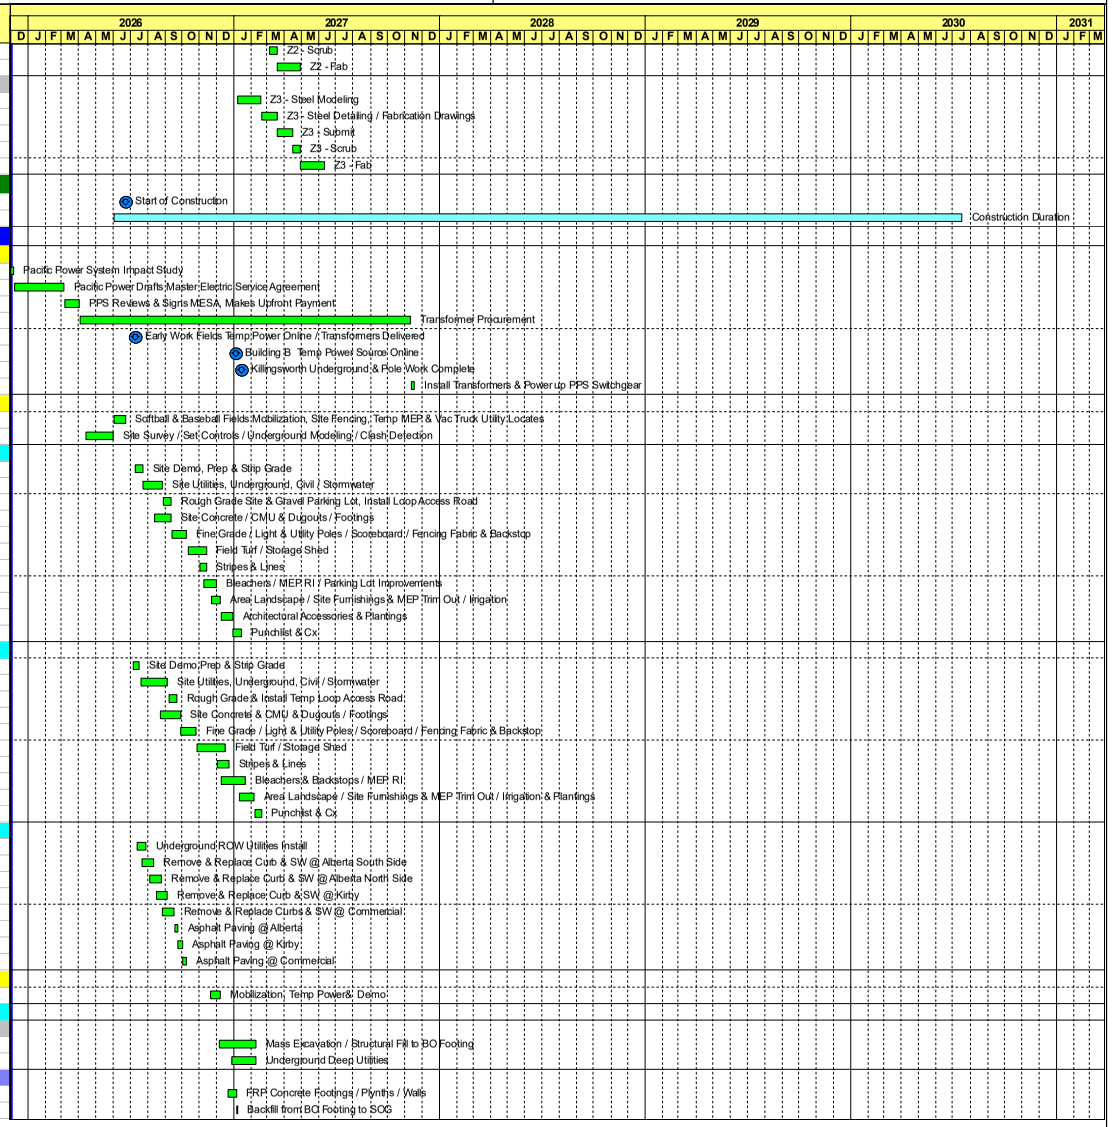

Remaining Level of Effort | Actual Work | Critical Remaining Work

Actual Level of Effort | Remaining Work | Meeting Milestone

Activity ID	Activity Name	Orig Dur	Remaining Duration	Start	Finish
30120	Underground Utility Install / Backfill & Fine Grade	12	12	11-Jan-27	26-Jan-27
Area 2		27	27	06-Jan-27	11-Feb-27
30200	FRP Concrete Footings / Plynths / Walls	12	12	06-Jan-27	21-Jan-27
30210	Backfill from BO Footing to SOG	3	3	22-Jan-27	26-Jan-27
30220	Underground Utility Install / Backfill & Fine Grade	12	12	27-Jan-27	11-Feb-27
Area 3		23	23	22-Jan-27	23-Feb-27
30300	FRP Concrete Footings / Plynths / Walls	10	10	22-Jan-27	04-Feb-27
30310	Backfill from BO Footing to SOG	3	3	05-Feb-27	09-Feb-27
30320	Underground Utility Install / Backfill & Fine Grade	10	10	10-Feb-27	23-Feb-27
Area 4		23	23	05-Feb-27	09-Mar-27
30400	FRP Concrete Footings / Plynths / Walls	10	10	05-Feb-27	18-Feb-27
30410	Backfill from BO Footing to SOG	3	3	19-Feb-27	23-Feb-27
30420	Underground Utility Install / Backfill & Fine Grade	10	10	24-Feb-27	09-Mar-27
Area 5		27	27	19-Feb-27	29-Mar-27
30500	FRP Concrete Footings / Plynths / Walls	12	12	19-Feb-27	08-Mar-27
30510	Backfill from BO Footing to SOG	3	3	09-Mar-27	11-Mar-27
30520	Underground Utility Install / Backfill & Fine Grade	12	12	12-Mar-27	29-Mar-27
Slab on Grade		58	58	27-Jan-27	16-Apr-27
Area 1 & 1A		14	14	27-Jan-27	15-Feb-27
31100	Vapor Barrier	2	2	27-Jan-27	28-Jan-27
31110	FRP SOG	12	12	29-Jan-27	15-Feb-27
Area 2		14	14	12-Feb-27	03-Mar-27
31200	Vapor Barrier	2	2	12-Feb-27	15-Feb-27
31210	FRP SOG	12	12	16-Feb-27	03-Mar-27
Area 3		14	14	24-Feb-27	15-Mar-27
31300	Vapor Barrier	2	2	24-Feb-27	25-Feb-27
31310	FRP SOG	12	12	26-Feb-27	15-Mar-27
Area 4		14	14	10-Mar-27	29-Mar-27
31400	Vapor Barrier	2	2	10-Mar-27	11-Mar-27
31410	FRP SOG	12	12	12-Mar-27	29-Mar-27
Area 5		14	14	30-Mar-27	16-Apr-27
31500	Vapor Barrier	2	2	30-Mar-27	31-Mar-27
31510	FRP SOG	12	12	01-Apr-27	16-Apr-27
Structure		149	149	12-Apr-27	09-Nov-27
Steel Zones 1A & 1B Floors 1-3		27	27	12-Apr-27	18-May-27
32010	Erect Columns & Beams	10	10	12-Apr-27	23-Apr-27
32020	Bolt / Weld / Plumb	5	5	26-Apr-27	30-Apr-27
32030	Edge Deck / Studs	5	5	03-May-27	07-May-27
32040	MEP Deck Rough-in	2	2	10-May-27	11-May-27
32050	FRP SOMD	5	5	12-May-27	18-May-27
32070	Set Brace Frames within Wood Zone 1	5	5	26-Apr-27	30-Apr-27
Mass Timber Zone 1 Floors 1-3		20	20	03-May-27	28-May-27
32060	Set Wood Columns & DLT Deck Floors 1-3	15	15	03-May-27	21-May-27
32080	Plumb & Complete Final Connections	5	5	24-May-27	28-May-27
Steel Zones 1A & 1B Floors 3-Roof		31	31	01-Jun-27	14-Jul-27
32100	Erect Columns & Beams	10	10	01-Jun-27	14-Jun-27
32110	Bolt / Weld / Plumb	5	5	15-Jun-27	21-Jun-27
32120	Edge Deck / Studs	5	5	22-Jun-27	28-Jun-27
32130	MEP Deck Rough-in	6	6	29-Jun-27	07-Jul-27
32140	FRP SOMD	5	5	08-Jul-27	14-Jul-27
32150	Set Brace Frames within Wood Zone 1	5	5	15-Jun-27	21-Jun-27
Mass Timber Zone 1 Floors 3-Roof		20	20	22-Jun-27	20-Jul-27
32160	Set Wood Columns & DLT Deck Floors 3-Roof	15	15	22-Jun-27	13-Jul-27
32170	Plumb & Complete Final Connections	5	5	14-Jul-27	20-Jul-27
Steel Zone 2 Floors 1-3		26	26	21-Jul-27	25-Aug-27
32200	Erect Columns & Beams	5	5	21-Jul-27	27-Jul-27
32210	Bolt / Weld / Plumb	5	5	28-Jul-27	03-Aug-27
32220	Edge Deck / Studs	5	5	04-Aug-27	10-Aug-27
32230	MEP Deck Rough-in	6	6	11-Aug-27	18-Aug-27
32240	FRP SOMD	5	5	19-Aug-27	25-Aug-27
32250	Set Brace Frames within Wood Zone 2	5	5	28-Jul-27	03-Aug-27
Mass Timber Zone 2 Floors 1-3		28	28	04-Aug-27	13-Sep-27
32260	Set Wood Columns & DLT Deck Floors 1-3	23	23	04-Aug-27	03-Sep-27
32270	Plumb & Complete Final Connections	5	5	03-Sep-27	13-Sep-27
Steel Zone 2 Floors 3-Roof		26	26	13-Sep-27	19-Oct-27
32300	Erect Columns & Beams	5	5	13-Sep-27	20-Sep-27

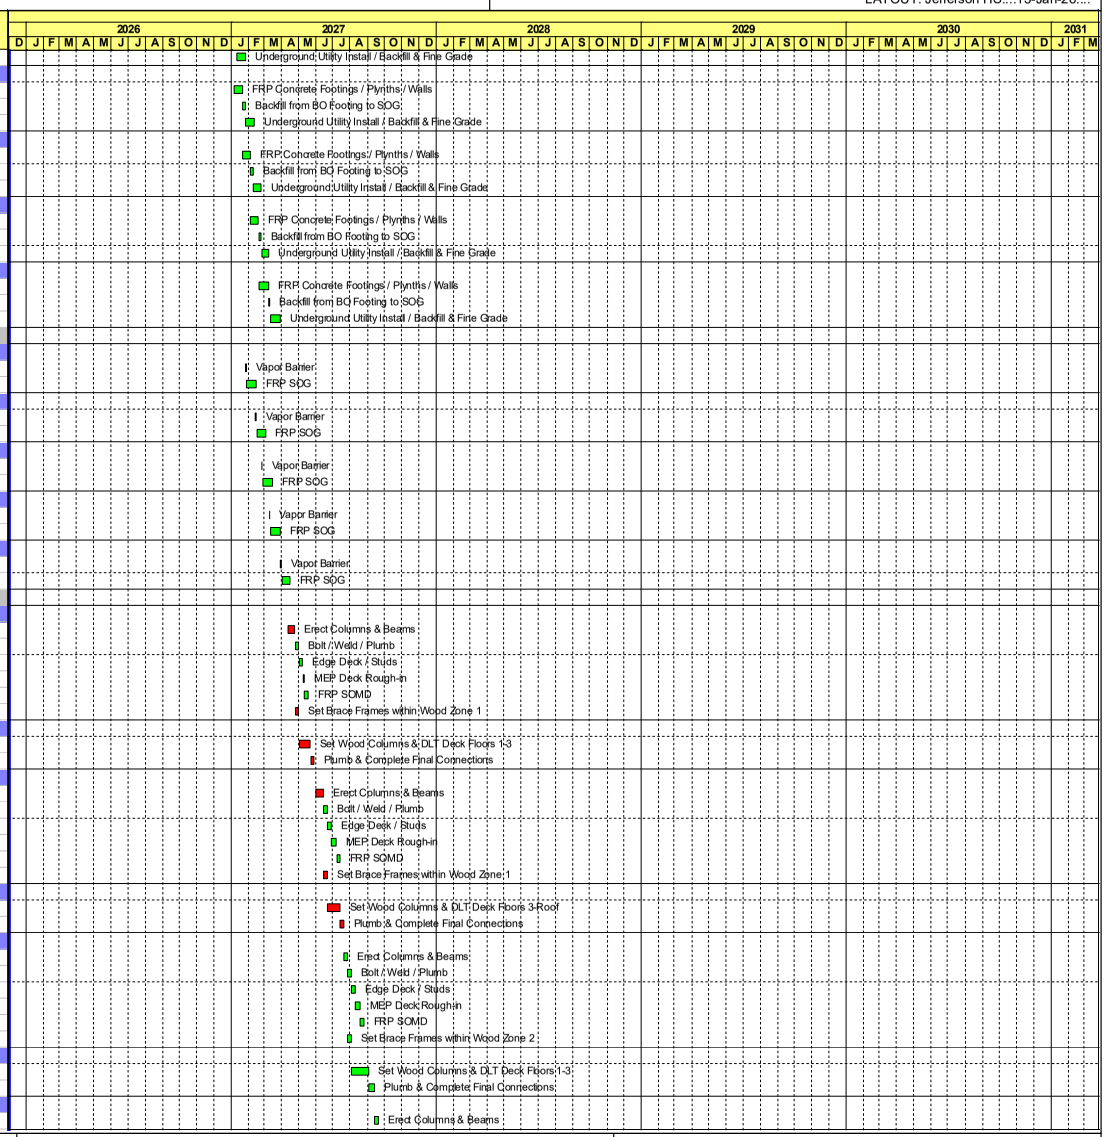

Remaining Level of Effort | Actual Work | Critical Remaining Work

Actual Level of Effort | Remaining Work | Meeting Milestone


Jefferson High School 1.6.26

data date :01-Dec-25 Page 6 of 19 TASK filter: <100%.

Jefferson High

LAYOUT: Jefferson HS....13-Jan-26....

Activity ID	Activity Name	Orig Dur	Remaining Duration	Start	Finish
32310	Bolt / Weld / Plumb	5	5	20-Sep-27	27-Sep-27
32320	Edge Deck / Studs	5	5	27-Sep-27	04-Oct-27
32330	MEP Deck Rough-in	6	6	04-Oct-27	12-Oct-27
32340	FRP SOMD	5	5	12-Oct-27	19-Oct-27
32350	Set Brace Frames within Wood Zone 2	5	5	20-Sep-27	27-Sep-27
Mass Timber Zone 2 Floor 3-Roof		31	31	27-Sep-27	09-Nov-27
32360	Set Wood Columns & DLT Deck Floors 1-3	26	26	27-Sep-27	02-Nov-27
32370	Plumb & Complete Final Connections	5	5	02-Nov-27	09-Nov-27
Steel Zone 3Roof Deck		11	11	27-Sep-27	12-Oct-27
32400	Erect Columns & Beams	3	3	27-Sep-27	30-Sep-27
32410	Bolt / Weld / Plumb	2	2	30-Sep-27	04-Oct-27
32420	Edge Deck / Studs	2	2	04-Oct-27	06-Oct-27
32430	MEP Deck Rough-in	1	1	06-Oct-27	07-Oct-27
32440	FRP SOMD	3	3	07-Oct-27	12-Oct-27
Mass Timber Zone 3 Floors 1-Roof		8	8	12-Oct-27	22-Oct-27
32460	Set Wood Columns & DLT Deck Floors 1-3	6	6	12-Oct-27	20-Oct-27
32470	Plumb & Complete Final Connections	2	2	20-Oct-27	22-Oct-27
Roof		184	184	21-Jul-27	10-Apr-28
RF33000	Roof Area 1 - Parapet Framing	5	5	21-Jul-27	27-Jul-27
RF33010	Roof Area 1 - Temp Roof	20	20	28-Jul-27	24-Aug-27
RF33020	Roof Area 1 - Roof	80	80	18-Aug-27	10-Dec-27
RF33030	Roof Area 2 - Parapet Framing	5	5	09-Nov-27	16-Nov-27
RF33040	Roof Area 2 - Temp Roof	20	20	16-Nov-27	16-Dec-27
RF33050	Roof Area 2 - Roof	80	80	09-Dec-27	03-Apr-28
RF33060	Roof Area 3 - Parapet Framing	5	5	16-Nov-27	23-Nov-27
RF33070	Roof Area 3 - Temp Roof	20	20	23-Nov-27	23-Dec-27
RF33080	Roof Area 3 - Roof	80	80	16-Dec-27	10-Apr-28
Facade		262	262	21-Jul-27	31-Jul-28
Fac34000	Facade 1 - Curb / Layout	7	7	11-Aug-27	19-Aug-27
Fac34010	Facade 1 - Exterior Panels	7	7	20-Aug-27	30-Aug-27
Fac34020	Facade 1 - WB Repair	7	7	31-Aug-27	09-Sep-27
Fac34030	Facade 1 - Install Windows	7	7	10-Sep-27	20-Sep-27
Fac34040	Facade 1 - "Z" Framing	14	14	21-Sep-27	08-Oct-27
Fac34050	Facade 1 - Metal Shrouds	14	14	11-Oct-27	28-Oct-27
Fac34060	Facade 1 - Insulation	14	14	29-Oct-27	17-Nov-27
Fac34070	Facade 1 - Hat Framing	14	14	18-Nov-27	09-Dec-27
Fac34080	Facade 1 - Metal Panel / Masonry	14	14	10-Dec-27	30-Dec-27
Fac34090	Facade 1 - Clean	5	5	03-Jan-28	07-Jan-28
Fac34095	Facade 1 - Pre-Punch & Quality Check	15	15	10-Jan-28	28-Jan-28
Fac34100	Mass Timber QC	15	15	21-Jul-27	10-Aug-27
Fac34110	Facade 2 - Curb / Layout	7	7	20-Aug-27	30-Aug-27
Fac34120	Facade 2 - Exterior Panels	7	7	31-Aug-27	09-Sep-27
Fac34130	Facade 2 - WB Repair	7	7	10-Sep-27	20-Sep-27
Fac34140	Facade 2 - Install Windows	7	7	21-Sep-27	29-Sep-27
Fac34150	Facade 2 - "Z" Framing	14	14	11-Oct-27	28-Oct-27
Fac34160	Facade 2 - Metal Shrouds	14	14	29-Oct-27	17-Nov-27
Fac34170	Facade 2 - Insulation	14	14	18-Nov-27	09-Dec-27
Fac34180	Facade 2 - Hat Framing	14	14	10-Dec-27	30-Dec-27
Fac34190	Facade 2 - Metal Panel / Masonry	14	14	03-Jan-28	20-Jan-28
Fac34200	Facade 2 - Clean	5	5	21-Jan-28	27-Jan-28
Fac34205	Facade 2 - Pre-Punch & Quality Check	15	15	28-Jan-28	17-Feb-28
Fac34210	Facade 3 - Curb / Layout	7	7	23-Dec-27	05-Jan-28
Fac34220	Facade 3 - Exterior Panels	7	7	05-Jan-28	14-Jan-28
Fac34230	Facade 3 - WB Repair	7	7	14-Jan-28	25-Jan-28
Fac34240	Facade 3 - Install Windows	7	7	25-Jan-28	03-Feb-28
Fac34250	Facade 3 - "Z" Framing	14	14	03-Feb-28	23-Feb-28
Fac34260	Facade 3 - Metal Shrouds	14	14	23-Feb-28	14-Mar-28
Fac34270	Facade 3 - Insulation	14	14	14-Mar-28	03-Apr-28
Fac34280	Facade 3 - Hat Framing	14	14	03-Apr-28	21-Apr-28
Fac34290	Facade 3 - Metal Panel / Masonry	14	14	21-Apr-28	11-May-28
Fac34300	Facade 3 - Clean	5	5	11-May-28	18-May-28
Fac34305	Facade 3 - Pre-Punch & Quality Check	15	15	18-May-28	09-Jun-28
Fac34310	Facade 4 - Curb / Layout	7	7	05-Jan-28	14-Jan-28
Fac34320	Facade 4 - Exterior Panels	7	7	14-Jan-28	25-Jan-28
Fac34330	Facade 4 - WB Repair	7	7	25-Jan-28	03-Feb-28
Fac34340	Facade 4 - Install Windows	7	7	03-Feb-28	14-Feb-28

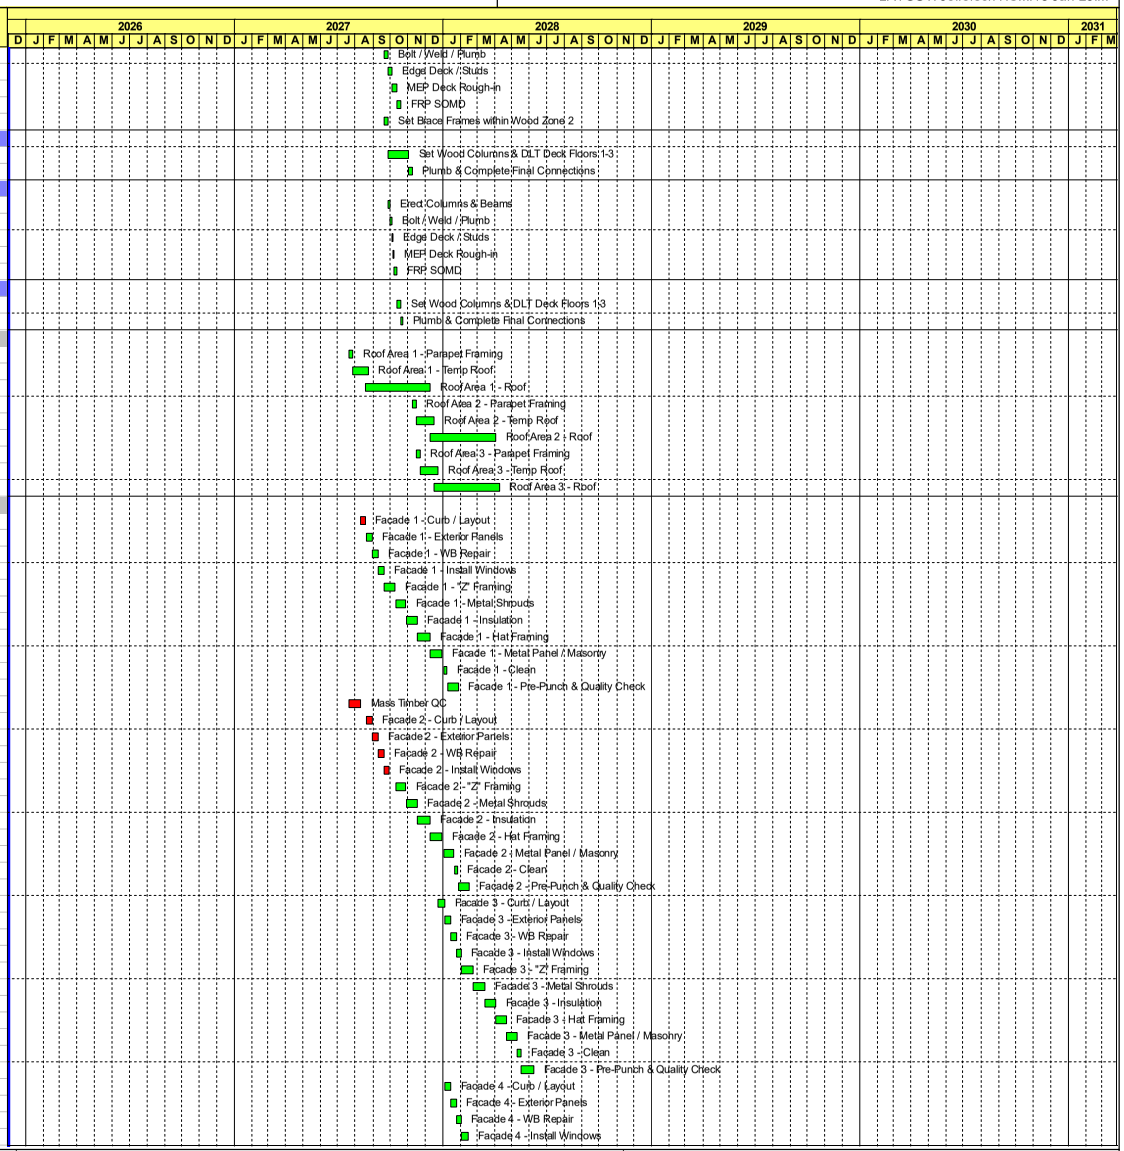

Remaining Level of Effort | Actual Work | Critical Remaining Work
Actual Level of Effort | Remaining Work | Meeting Milestone


Jefferson High School 1.6.26

data date :01-Dec-25 Page 7 of 19 TASK filter: <100%.

Jefferson High

LAYOUT: Jefferson HS....13-Jan-26....

Activity ID	Activity Name	Orig Dur	Remaining Duration	Start	Finish
Fac34350	Facade 4 - "Z" Framing	14	14	14-Feb-28	03-Mar-28
Fac34360	Facade 4 - Metal Shrouds	14	14	03-Mar-28	23-Mar-28
Fac34370	Facade 4 - Insulation	14	14	23-Mar-28	12-Apr-28
Fac34380	Facade 4 - Hat Framing	14	14	12-Apr-28	02-May-28
Fac34390	Facade 4 - Metal Panel / Masonry	14	14	02-May-28	22-May-28
Fac34400	Facade 4 - Clean	5	5	22-May-28	30-May-28
Fac34405	Facade 4 - Pre-Punch & Quality Check	15	15	30-May-28	20-Jun-28
Fac34410	Facade 5 - Curb / Layout	7	7	14-Jan-28	25-Jan-28
Fac34420	Facade 5 - Exterior Panels	7	7	25-Jan-28	03-Feb-28
Fac34430	Facade 5 - WB Repair	7	7	03-Feb-28	14-Feb-28
Fac34440	Facade 5 - Install Windows	7	7	14-Feb-28	23-Feb-28
Fac34450	Facade 5 - "Z" Framing	14	14	03-Mar-28	23-Mar-28
Fac34460	Facade 5 - Metal Shrouds	14	14	23-Mar-28	12-Apr-28
Fac34470	Facade 5 - Insulation	14	14	12-Apr-28	02-May-28
Fac34480	Facade 5 - Hat Framing	14	14	02-May-28	22-May-28
Fac34490	Facade 5 - Metal Panel / Masonry	14	14	22-May-28	12-Jun-28
Fac34500	Facade 5 - Clean	5	5	12-Jun-28	19-Jun-28
Fac34505	Facade 5 - Pre-Punch & Quality Check	15	15	19-Jun-28	11-Jul-28
Fac34510	Facade 6 - Curb / Layout	7	7	25-Jan-28	03-Feb-28
Fac34520	Facade 6 - Exterior Panels	7	7	03-Feb-28	14-Feb-28
Fac34530	Facade 6 - WB Repair	7	7	14-Feb-28	23-Feb-28
Fac34540	Facade 6 - Install Windows	7	7	23-Feb-28	03-Mar-28
Fac34550	Facade 6 - "Z" Framing	14	14	23-Mar-28	12-Apr-28
Fac34560	Facade 6 - Metal Shrouds	14	14	12-Apr-28	02-May-28
Fac34570	Facade 6 - Insulation	14	14	02-May-28	22-May-28
Fac34580	Facade 6 - Hat Framing	14	14	22-May-28	12-Jun-28
Fac34590	Facade 6 - Metal Panel / Masonry	14	14	12-Jun-28	30-Jun-28
Fac34600	Facade 6 - Clean	5	5	30-Jun-28	10-Jul-28
Fac34605	Facade 6 - Pre-Punch & Quality Check	15	15	10-Jul-28	31-Jul-28
Interior Buildout		290	290	30-Sep-27	17-Nov-28
Level 1		238	238	30-Sep-27	06-Sep-28
Area A - Staff & Child Care		200	200	30-Sep-27	13-Jul-28
B10000	L1A - Shaft Duct & Pipe	10	10	30-Sep-27	13-Oct-27
B10010	L1A - Priority Walls	7	7	14-Oct-27	22-Oct-27
B10020	L1A - OH RI Prior to Framing	7	7	25-Oct-27	02-Nov-27
B10030	L1A - Framing	7	7	03-Nov-27	11-Nov-27
B10040	L1A - Wall Rough-in	7	7	12-Nov-27	22-Nov-27
B10050	L1A - Top Rock	7	7	23-Nov-27	03-Dec-27
B10060	L1A - OH RI High (Fire Protection, Classroom Elec Rough-in)	7	7	06-Dec-27	14-Dec-27
B10070	L1A - OH RI High (Plumbing, Core Elec RI)	7	7	06-Dec-27	14-Dec-27
B10080	L1A - OH RI Mid (Hydronic, Refer, Gas, Elec-Corridor, Plmbg Insul)	7	7	15-Dec-27	23-Dec-27
B10090	L1A - OH RI Low (Duct, Elec FA, Lighting Cont., LV, Hyd Insul, FA, LC)	7	7	27-Dec-27	05-Jan-28
B10100	L1A - Soffits / HL	5	5	06-Jan-28	12-Jan-28
B10110	L1A - Pickup Work	6	6	13-Jan-28	20-Jan-28
B10120	L1A - Cover & Stock	3	3	21-Jan-28	25-Jan-28
B10130	L1A - Drywall & Insulation	7	7	26-Jan-28	03-Feb-28
B10140	L1A - MT Finish Treatment	7	7	04-Feb-28	14-Feb-28
B10150	L1A - Taping	7	7	15-Feb-28	23-Feb-28
B10160	L1A - Paint	7	7	24-Feb-28	03-Mar-28
B10170	L1A - Resinous Flooring	5	5	06-Mar-28	10-Mar-28
B10180	L1A - Pull LV Wire	7	7	06-Mar-28	14-Mar-28
B10190	L1A - Bathroom Tile	5	5	15-Mar-28	21-Mar-28
B10200	L1A - T-Bar Device Tile	7	7	15-Mar-28	23-Mar-28
B10210	L1A - Ceiling Trim MEP	7	7	24-Mar-28	03-Apr-28
B10220	L1A - Casework	7	7	24-Mar-28	03-Apr-28
B10230	L1A - Flooring	7	7	04-Apr-28	12-Apr-28
B10240	L1A - MEP Fixtures & Trim	7	7	13-Apr-28	21-Apr-28
B10250	L1A - Doors / Hardware	5	5	13-Apr-28	19-Apr-28
B10260	L1A - ACT	7	7	24-Apr-28	02-May-28
B10270	L1A - Specialties	20	20	03-May-28	31-May-28
B10280	L1A - Specialy MEP Trim	5	5	01-Jun-28	07-Jun-28
B10290	L1A - Final Clean	5	5	08-Jun-28	14-Jun-28
B10300	L1A - Cx Tile	5	5	15-Jun-28	21-Jun-28
B10310	L1A - Pre-Punch	15	15	22-Jun-28	13-Jul-28
Area S - Servery & Bathrooms		200	200	14-Oct-27	27-Jul-28
B11000	L1S - Shaft Duct & Pipe	10	10	14-Oct-27	27-Oct-27

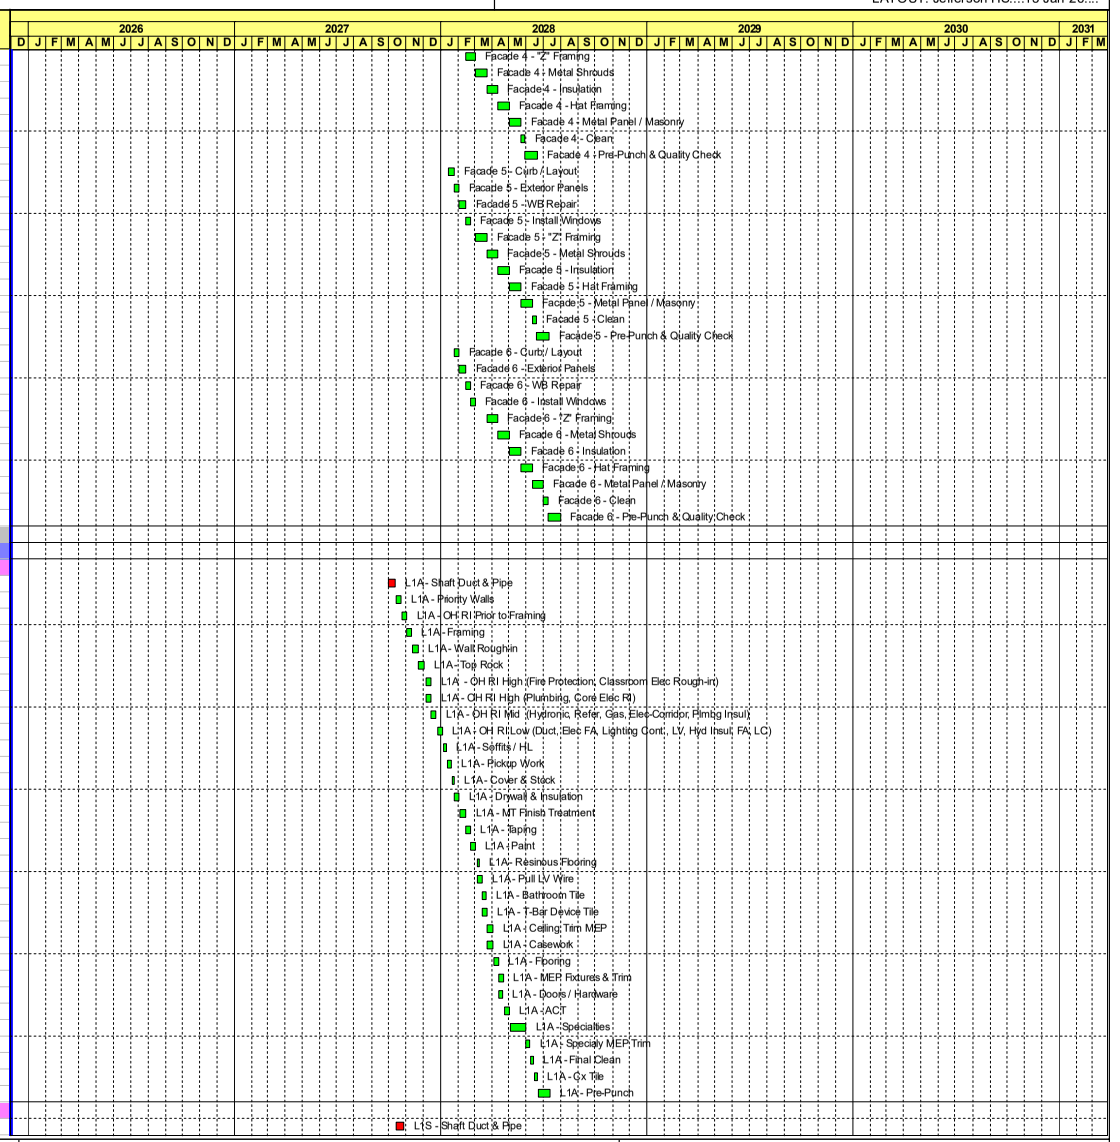


Remaining Level of Effort | Actual Work | Critical Remaining Work

Actual Level of Effort | Remaining Work | Meeting Milestone

Jefferson High School 1.6.26

data date :01-Dec-25 Page 8 of 19 TASK filter: <100%.

Activity ID	Activity Name	Orig Dur	Remaining Duration	Start	Finish
B11010	L1S - Priority Walls	7	7	28-Oct-27	05-Nov-27
B11020	L1S - OH Rl Prior to Framing	7	7	08-Nov-27	16-Nov-27
B11030	L1S - Framing	7	7	17-Nov-27	29-Nov-27
B11040	L1S - Wall Rough-in	7	7	30-Nov-27	08-Dec-27
B11050	L1S - Top Rock	7	7	09-Dec-27	17-Dec-27
B11060	L1S - OH Rl High (Fire Protection, Classroom Elec Rough-in)	7	7	20-Dec-27	29-Dec-27
B11070	L1S - OH Rl High (Plumbing, Core Elec Rl)	7	7	20-Dec-27	29-Dec-27
B11080	L1S - OH Rl Mid (Hydronic, Refer, Gas, Elec-Corridor, Plmbg Insul)	7	7	30-Dec-27	10-Jan-28
B11090	L1S - OH Rl Low (Duct, Elec FA, Lighting Cont., LV, Hyd Insul, FA, LC)	7	7	11-Jan-28	19-Jan-28
B11100	L1S - Soffits / HL	5	5	20-Jan-28	26-Jan-28
B11110	L1S - Pickup Work	6	6	27-Jan-28	03-Feb-28
B11120	L1S - Cover & Stock	3	3	04-Feb-28	08-Feb-28
B11130	L1S - Drywall & Insulation	7	7	09-Feb-28	17-Feb-28
B11140	L1S - MT Finish Treatment	7	7	18-Feb-28	28-Feb-28
B11150	L1S - Taping	7	7	29-Feb-28	08-Mar-28
B11160	L1S - Paint	7	7	09-Mar-28	17-Mar-28
B11170	L1S - Resinous Flooring	5	5	20-Mar-28	24-Mar-28
B11180	L1S - Pull LV Wire	7	7	20-Mar-28	28-Mar-28
B11190	L1S - Bathroom Tile	5	5	29-Mar-28	04-Apr-28
B11200	L1S - T-Bar Device Tile	7	7	29-Mar-28	06-Apr-28
B11210	L1S - Ceiling Trim MEP	7	7	07-Apr-28	17-Apr-28
B11220	L1S - Casework	7	7	07-Apr-28	17-Apr-28
B11230	L1S - Flooring	7	7	18-Apr-28	26-Apr-28
B11240	L1S - MEP Fixtures & Trim	7	7	27-Apr-28	05-May-28
B11250	L1S - Doors / Hardware	5	5	27-Apr-28	03-May-28
B11260	L1S - ACT	7	7	08-May-28	16-May-28
B11270	L1S - Specialties	20	20	17-May-28	14-Jun-28
B11280	L1S - Specialy MEP Trim	5	5	15-Jun-28	21-Jun-28
B11290	L1S - Final Clean	5	5	22-Jun-28	28-Jun-28
B11300	L1S - Cx Tile	5	5	29-Jun-28	06-Jul-28
B11305	L1S - Pre-Punch	15	15	07-Jul-28	27-Jul-28
Area B - Main Entry & Mechanical		200	200	28-Oct-27	10-Aug-28
B12000	L1B - Shaft Duct & Pipe	10	10	28-Oct-27	10-Nov-27
B12010	L1B - Set & Connect AHU 501	5	5	11-Nov-27	17-Nov-27
B12020	L1B - Priority Walls	7	7	11-Nov-27	19-Nov-27
B12030	L1B - OH Rl Prior to Framing	7	7	22-Nov-27	02-Dec-27
B12040	L1B - Framing	7	7	03-Dec-27	13-Dec-27
B12050	L1B - Wall Rough-in	7	7	14-Dec-27	22-Dec-27
B12060	L1B - Top Rock	7	7	23-Dec-27	04-Jan-28
B12070	L1B - OH Rl High (Fire Protection, Classroom Elec Rough-in)	7	7	05-Jan-28	13-Jan-28
B12080	L1B - OH Rl High (Plumbing, Core Elec Rl)	7	7	05-Jan-28	13-Jan-28
B12090	L1B - OH Rl Mid (Hydronic, Refer, Gas, Elec-Corridor, Plmbg Insul)	7	7	14-Jan-28	24-Jan-28
B12100	L1B - OH Rl Low (Duct, Elec FA, Lighting Cont., LV, Hyd Insul, FA, LC)	7	7	25-Jan-28	02-Feb-28
B12110	L1B - Soffits / HL	5	5	03-Feb-28	09-Feb-28
B12120	L1B - Pickup Work	6	6	10-Feb-28	17-Feb-28
B12130	L1B - Cover & Stock	3	3	18-Feb-28	22-Feb-28
B12140	L1B - Drywall & Insulation	7	7	23-Feb-28	02-Mar-28
B12150	L1B - MT Finish Treatment	7	7	03-Mar-28	13-Mar-28
B12160	L1B - Taping	7	7	14-Mar-28	22-Mar-28
B12170	L1B - Paint	7	7	23-Mar-28	31-Mar-28
B12180	L1B - Resinous Flooring	5	5	03-Apr-28	07-Apr-28
B12190	L1B - Pull LV Wire	7	7	03-Apr-28	11-Apr-28
B12200	L1B - Bathroom Tile	5	5	12-Apr-28	18-Apr-28
B12210	L1B - T-Bar Device Tile	7	7	12-Apr-28	20-Apr-28
B12220	L1B - Ceiling Trim MEP	7	7	21-Apr-28	01-May-28
B12230	L1B - Casework	7	7	21-Apr-28	01-May-28
B12240	L1B - Flooring	7	7	02-May-28	10-May-28
B12250	L1B - MEP Fixtures & Trim	7	7	11-May-28	19-May-28
B12260	L1B - Doors / Hardware	5	5	11-May-28	17-May-28
B12270	L1B - ACT	7	7	22-May-28	31-May-28
B12280	L1B - Specialties	20	20	01-Jun-28	28-Jun-28
B12290	L1B - Specialy MEP Trim	5	5	29-Jun-28	06-Jul-28
B12300	L1B - Final Clean	5	5	07-Jul-28	13-Jul-28
B12310	L1B - Cx Tile	5	5	14-Jul-28	20-Jul-28
B12315	L1B - Pre-Punch	15	15	21-Jul-28	10-Aug-28
Area C - Commons		208	208	11-Nov-27	06-Sep-28

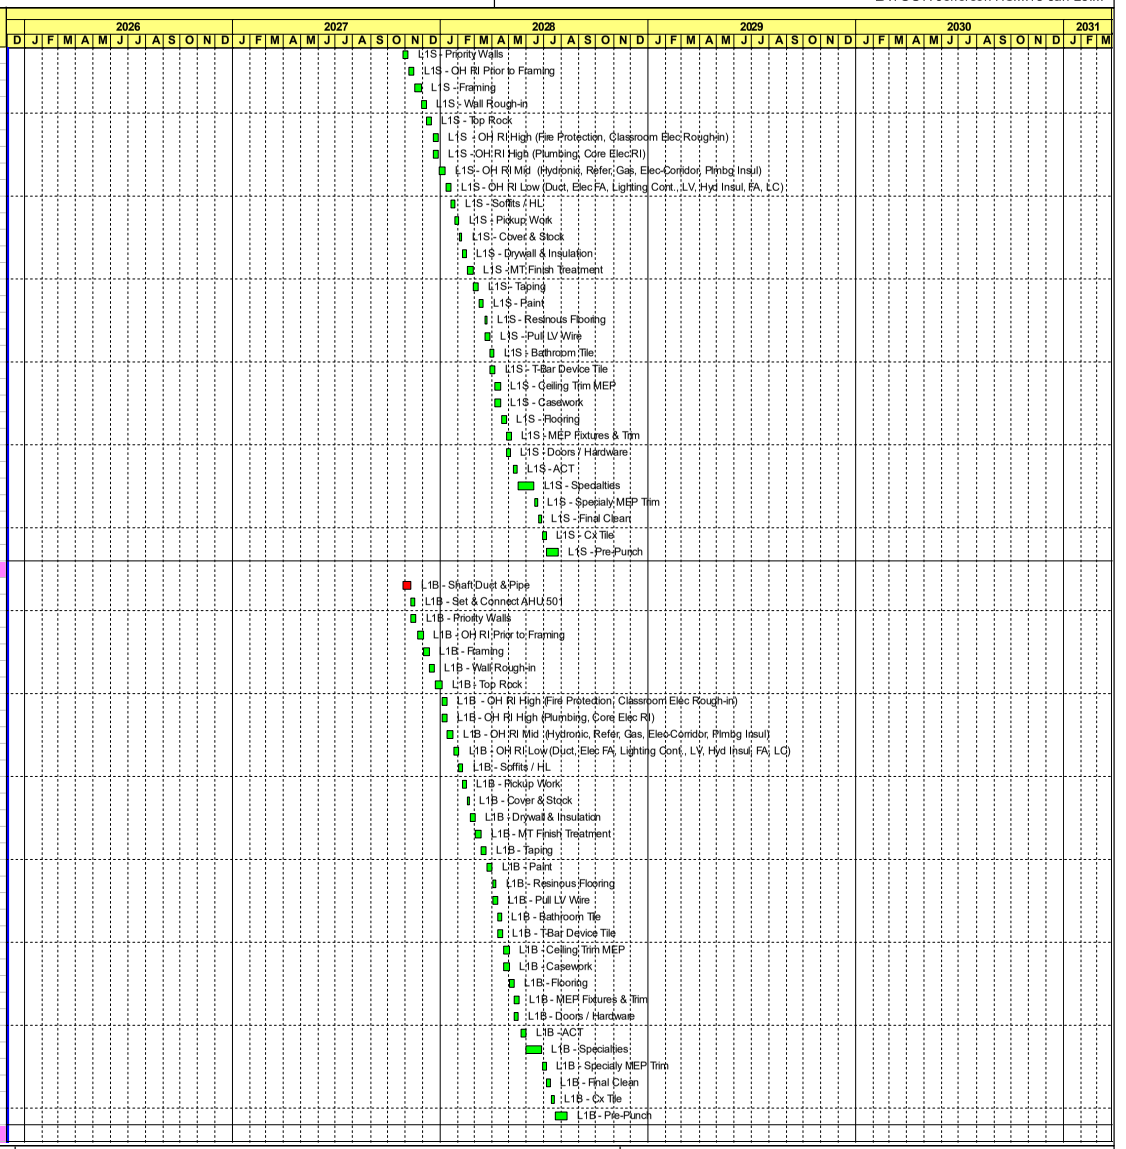


Remaining Level of Effort
Actual Work
Critical Remaining Work
Actual Level of Effort
Remaining Work
Meeting Milestone

Jefferson High

LAYOUT: Jefferson HS....13-Jan-26....

Activity ID	Activity Name	Orig Dur	Remaining Duration	Start	Finish
B13000	L1C - Shaft Duct & Pipe	10	10	11-Nov-27	24-Nov-27
B13010	L1C - Priority Walls	7	7	29-Nov-27	07-Dec-27
B13020	L1C - OH RI Prior to Framing	7	7	08-Dec-27	16-Dec-27
B13030	L1C - Framing	7	7	17-Dec-27	28-Dec-27
B13040	L1C - Wall Rough-in	7	7	29-Dec-27	07-Jan-28
B13050	L1C - Top Rock	7	7	10-Jan-28	18-Jan-28
B13060	L1C - OH RI High (Fire Protection, Classroom Elec Rough-in)	7	7	19-Jan-28	27-Jan-28
B13070	L1C - OH RI High (Plumbing, Core Elec RI)	7	7	19-Jan-28	27-Jan-28
B13080	L1C - OH RI Mid (Hydronic, Refer, Gas, Elec-Corridor, Plmbg Insul)	7	7	28-Jan-28	07-Feb-28
B13090	L1C - OH RI Low (Duct, Elec FA, Lighting Cont., LV, Hyd Insul, FA, LC)	7	7	08-Feb-28	16-Feb-28
B13100	L1C - Soffits / HL	5	5	17-Feb-28	23-Feb-28
B13110	L1C - Pickup Work	6	6	24-Feb-28	02-Mar-28
B13120	L1C - Cover & Stock	3	3	03-Mar-28	07-Mar-28
B13130	L1C - Drywall & Insulation	7	7	08-Mar-28	16-Mar-28
B13140	L1C - MT Finish Treatment	7	7	17-Mar-28	27-Mar-28
B13150	L1C - Taping	7	7	28-Mar-28	05-Apr-28
B13160	L1C - Paint	7	7	06-Apr-28	14-Apr-28
B13170	L1C - Resinous Flooring	5	5	17-Apr-28	21-Apr-28
B13180	L1C - Pull LV Wire	7	7	17-Apr-28	25-Apr-28
B13190	L1C - Bathroom Tile	5	5	26-Apr-28	02-May-28
B13200	L1C - T-Bar Device Tile	7	7	26-Apr-28	04-May-28
B13210	L1C - Ceiling Trim MEP	7	7	05-May-28	15-May-28
B13220	L1C - Casework	7	7	05-May-28	15-May-28
B13230	L1C - Flooring	15	15	16-May-28	06-Jun-28
B13240	L1C - MEP Fixtures & Trim	7	7	07-Jun-28	15-Jun-28
B13250	L1C - Doors / Hardware	5	5	07-Jun-28	13-Jun-28
B13260	L1C - ACT	7	7	16-Jun-28	26-Jun-28
B13270	L1C - Specialties	20	20	27-Jun-28	25-Jul-28
B13280	L1C - Specialy MEP Trim	5	5	26-Jul-28	01-Aug-28
B13290	L1C - Final Clean	5	5	02-Aug-28	08-Aug-28
B13300	L1C - Cx Tile	5	5	09-Aug-28	15-Aug-28
B13305	L1C - Pre-Punch	15	15	16-Aug-28	06-Sep-28
Level 2		210	210	29-Nov-27	22-Sep-28
Area GC - General Classrooms		203	203	29-Nov-27	13-Sep-28
B20000	L2GC - Shaft Duct & Pipe	10	10	29-Nov-27	10-Dec-27
B20010	L2GC - Priority Walls	7	7	13-Dec-27	21-Dec-27
B20020	L2GC - OH RI Prior to Framing	7	7	22-Dec-27	03-Jan-28
B20030	L2GC - Framing	7	7	04-Jan-28	12-Jan-28
B20040	L2GC - Wall Rough-in	7	7	13-Jan-28	21-Jan-28
B20050	L2GC - Top Rock	7	7	24-Jan-28	01-Feb-28
B20060	L2GC - OH RI High (Fire Protection, Classroom Elec Rough-in)	7	7	02-Feb-28	10-Feb-28
B20070	L2GC - OH RI High (Plumbing, Core Elec RI)	7	7	02-Feb-28	10-Feb-28
B20080	L2GC - OH RI Mid (Hydronic, Refer, Gas, Elec-Corridor, Plmbg Insul)	7	7	11-Feb-28	21-Feb-28
B20090	L2GC - OH RI Low (Duct, Elec FA, Lighting Cont., LV, Hyd Insul, FA, LC)	7	7	22-Feb-28	01-Mar-28
B20100	L2GC - Soffits / HL	5	5	02-Mar-28	08-Mar-28
B20110	L2GC - Pickup Work	6	6	09-Mar-28	16-Mar-28
B20120	L2GC - Cover & Stock	3	3	17-Mar-28	21-Mar-28
B20130	L2GC - Drywall & Insulation	7	7	22-Mar-28	30-Mar-28
B20140	L2GC - MT Finish Treatment	7	7	31-Mar-28	10-Apr-28
B20150	L2GC - Gypcrete	7	7	31-Mar-28	10-Apr-28
B20160	L2GC - Taping	7	7	11-Apr-28	19-Apr-28
B20170	L2GC - Paint	7	7	20-Apr-28	28-Apr-28
B20180	L2GC - Resinous Flooring	5	5	01-May-28	05-May-28
B20190	L2GC - Pull LV Wire	7	7	01-May-28	09-May-28
B20200	L2GC - Bathroom Tile	5	5	10-May-28	16-May-28
B20210	L2GC - T-Bar Device Tile	7	7	10-May-28	18-May-28
B20220	L2GC - Ceiling Trim MEP	7	7	19-May-28	30-May-28
B20230	L2GC - Casework	7	7	19-May-28	30-May-28
B20240	L2GC - Flooring	7	7	31-May-28	08-Jun-28
B20250	L2GC - MEP Fixtures & Trim	7	7	09-Jun-28	19-Jun-28
B20260	L2GC - Doors / Hardware	5	5	09-Jun-28	15-Jun-28
B20270	L2GC - ACT	7	7	20-Jun-28	28-Jun-28
B20280	L2GC - Specialties	20	20	29-Jun-28	27-Jul-28
B20290	L2GC - Specialy MEP Trim	5	5	28-Jul-28	03-Aug-28
B20300	L2GC - Final Clean	5	5	04-Aug-28	10-Aug-28
B20310	L2GC - Cx Tile	5	5	16-Aug-28	22-Aug-28

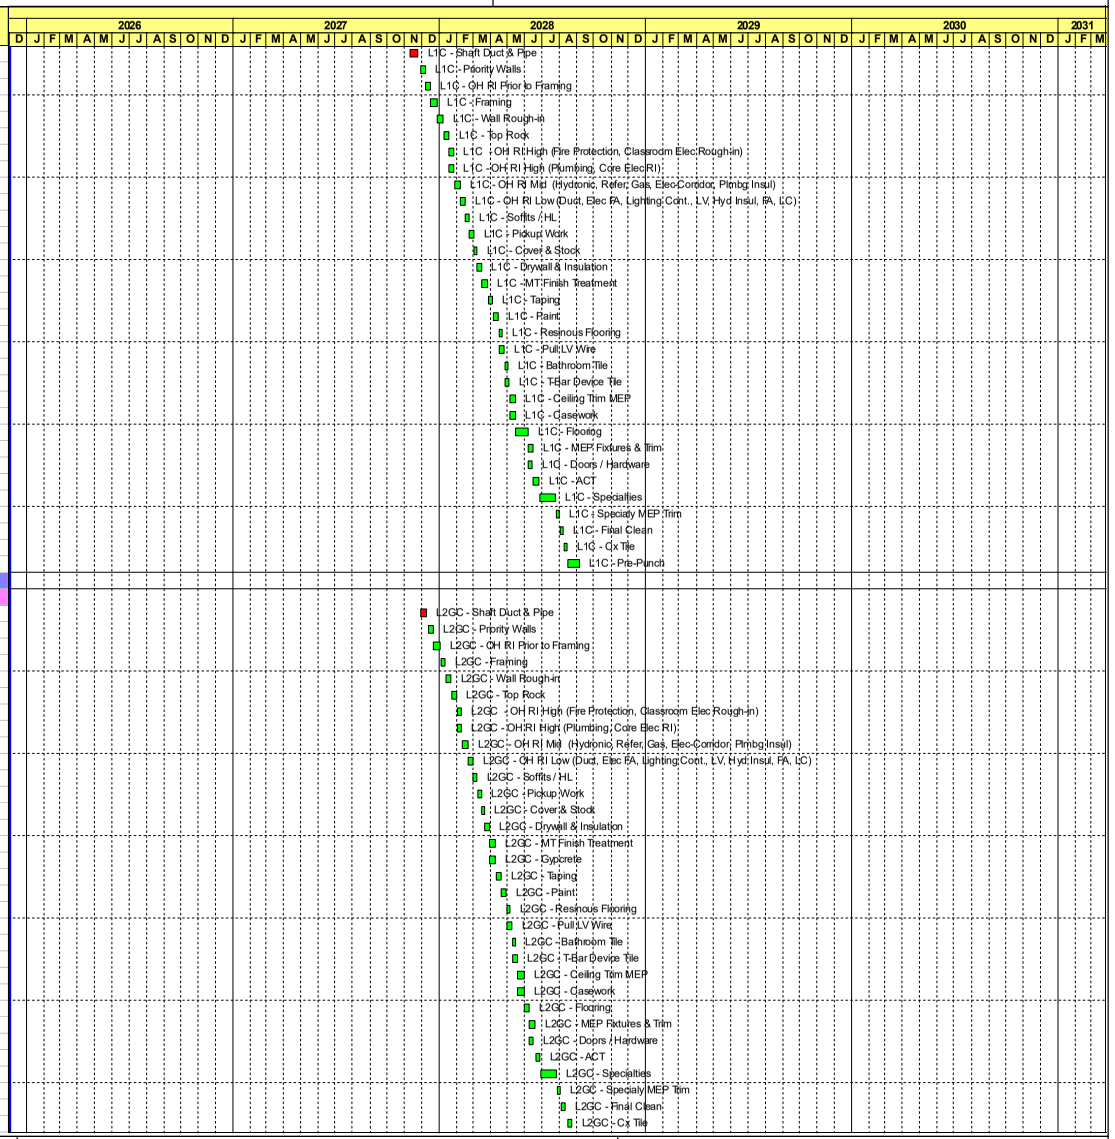

Remaining Level of Effort | Actual Work | Critical Remaining Work

Actual Level of Effort | Remaining Work | Meeting Milestone


Jefferson High School 1.6.26

data date :01-Dec-25 Page 10 of 19 TASK filter: <100%.

Jefferson High

LAYOUT: Jefferson HS....13-Jan-26....

Activity ID	Activity Name	Orig Dur	Remaining Duration	Start	Finish
B20315	L2GC - Pre-Punch	15	15	23-Aug-28	13-Sep-28
Area B - General Classrooms & Suppor		200	200	13-Dec-27	22-Sep-28
B21000	L2B - Shaft Duct & Pipe	10	10	13-Dec-27	27-Dec-27
B21010	L2B - Priority Walls	7	7	28-Dec-27	06-Jan-28
B21020	L2B - OH RI Prior to Framing	7	7	07-Jan-28	17-Jan-28
B21030	L2B - Framing	7	7	18-Jan-28	26-Jan-28
B21040	L2B - Wall Rough-in	7	7	27-Jan-28	04-Feb-28
B21050	L2B - Top Rock	7	7	07-Feb-28	15-Feb-28
B21060	L2B - OH RI High (Fire Protection, Classroom Elec Rough-in)	7	7	16-Feb-28	24-Feb-28
B21070	L2B - OH RI High (Plumbing, Core Elec RI)	7	7	16-Feb-28	24-Feb-28
B21080	L2B - OH RI Mid (Hydronic, Refer, Gas, Elec-Corridor, Plmbg Insul)	7	7	25-Feb-28	06-Mar-28
B21090	L2B - OH RI Low (Duct, Elec FA, Lighting Cont., LV, Hyd Insul, FA, LC)	7	7	07-Mar-28	15-Mar-28
B21100	L2B - Soffits / HL	5	5	16-Mar-28	22-Mar-28
B21110	L2B - Pickup Work	6	6	23-Mar-28	30-Mar-28
B21120	L2B - Cover & Stock	3	3	31-Mar-28	04-Apr-28
B21130	L2B - Drywall & Insulation	7	7	05-Apr-28	13-Apr-28
B21140	L2B - MT Finish Treatment	7	7	14-Apr-28	24-Apr-28
B21150	L2B - Gypcrete	7	7	14-Apr-28	24-Apr-28
B21160	L2B - Taping	7	7	25-Apr-28	03-May-28
B21170	L2B - Paint	7	7	04-May-28	12-May-28
B21180	L2B - Resinous Flooring	5	5	15-May-28	19-May-28
B21190	L2B - Pull LV Wire	7	7	15-May-28	23-May-28
B21200	L2B - Bathroom Tile	5	5	24-May-28	31-May-28
B21210	L2B - T-Bar Device Tile	7	7	24-May-28	02-Jun-28
B21220	L2B - Ceiling Trim MEP	7	7	05-Jun-28	13-Jun-28
B21230	L2B - Casework	7	7	05-Jun-28	13-Jun-28
B21240	L2B - Flooring	7	7	14-Jun-28	22-Jun-28
B21250	L2B - MEP Fixtures & Trim	7	7	23-Jun-28	03-Jul-28
B21260	L2B - Doors / Hardware	5	5	23-Jun-28	29-Jun-28
B21270	L2B - ACT	7	7	05-Jul-28	13-Jul-28
B21280	L2B - Specialties	20	20	14-Jul-28	10-Aug-28
B21290	L2B - Specialy MEP Trim	5	5	11-Aug-28	17-Aug-28
B21300	L2B - Final Clean	5	5	18-Aug-28	24-Aug-28
B21310	L2B - Cx Tile	5	5	25-Aug-28	31-Aug-28
B21315	L2B - Pre-Punch	15	15	01-Sep-28	22-Sep-28
Level 3		210	210	28-Dec-27	20-Oct-28
Area GC - General Classrooms		200	200	28-Dec-27	06-Oct-28
B30000	L3GC - Shaft Duct & Pipe	10	10	28-Dec-27	11-Jan-28
B30010	L3GC - Priority Walls	7	7	12-Jan-28	20-Jan-28
B30020	L3GC - OH RI Prior to Framing	7	7	21-Jan-28	31-Jan-28
B30030	L3GC - Framing	7	7	01-Feb-28	09-Feb-28
B30040	L3GC - Wall Rough-in	7	7	10-Feb-28	18-Feb-28
B30050	L3GC - Top Rock	7	7	21-Feb-28	29-Feb-28
B30060	L3GC - OH RI High (Fire Protection, Classroom Elec Rough-in)	7	7	01-Mar-28	09-Mar-28
B30070	L3GC - OH RI High (Plumbing, Core Elec RI)	7	7	01-Mar-28	09-Mar-28
B30080	L3GC - OH RI Mid (Hydronic, Refer, Gas, Elec-Corridor, Plmbg Insul)	7	7	10-Mar-28	20-Mar-28
B30090	L3GC - OH RI Low (Duct, Elec FA, Lighting Cont., LV, Hyd Insul, FA, LC)	7	7	21-Mar-28	29-Mar-28
B30100	L3GC - Soffits / HL	5	5	30-Mar-28	05-Apr-28
B30110	L3GC - Pickup Work	6	6	06-Apr-28	13-Apr-28
B30120	L3GC - Cover & Stock	3	3	14-Apr-28	18-Apr-28
B30130	L3GC - Drywall & Insulation	7	7	19-Apr-28	27-Apr-28
B30140	L3GC - MT Finish Treatment	7	7	28-Apr-28	08-May-28
B30150	L3GC - Gypcrete	7	7	28-Apr-28	08-May-28
B30160	L3GC - Taping	7	7	09-May-28	17-May-28
B30170	L3GC - Paint	7	7	18-May-28	26-May-28
B30180	L3GC - Resinous Flooring	5	5	30-May-28	05-Jun-28
B30190	L3GC - Pull LV Wire	7	7	30-May-28	07-Jun-28
B30200	L3GC - Bathroom Tile	5	5	08-Jun-28	14-Jun-28
B30210	L3GC - T-Bar Device Tile	7	7	08-Jun-28	16-Jun-28
B30220	L3GC - Ceiling Trim MEP	7	7	19-Jun-28	27-Jun-28
B30230	L3GC - Casework	7	7	19-Jun-28	27-Jun-28
B30240	L3GC - Flooring	7	7	28-Jun-28	07-Jul-28
B30250	L3GC - MEP Fixtures & Trim	7	7	10-Jul-28	18-Jul-28
B30260	L3GC - Doors / Hardware	5	5	10-Jul-28	14-Jul-28
B30270	L3GC - ACT	7	7	19-Jul-28	27-Jul-28
B30280	L3GC - Specialties	20	20	28-Jul-28	24-Aug-28

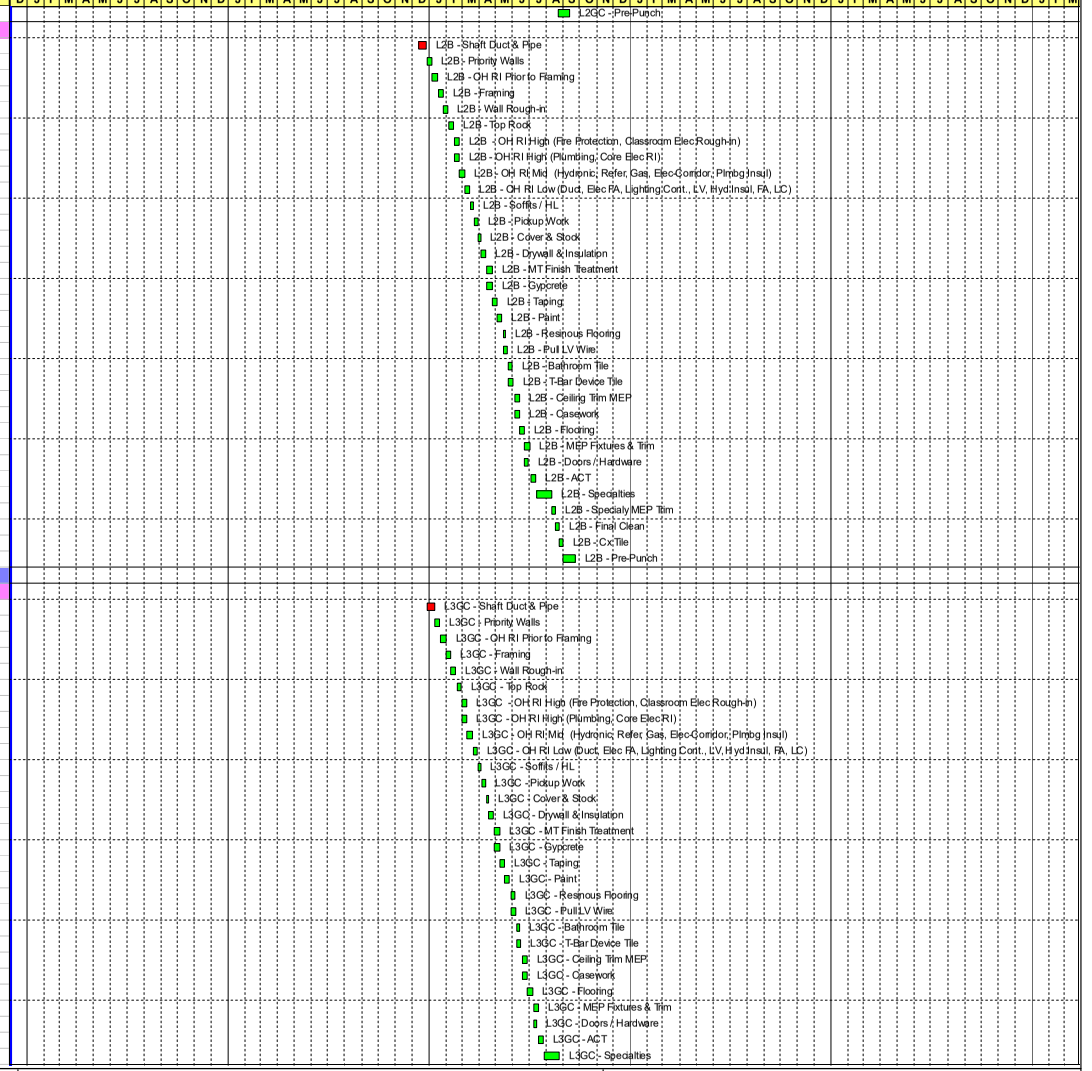


Remaining Level of Effort | Actual Work | Critical Remaining Work
Actual Level of Effort | Remaining Work | Meeting Milestone


Jefferson High School 1.6.26

data date :01-Dec-25 Page 11 of 19 TASK filter: <100%.

Activity ID	Activity Name	Orig Dur	Remaining Duration	Start	Finish
B30290	L3GC - Specialty MEP Trim	5	5	25-Aug-28	31-Aug-28
B30300	L3GC - Final Clean	5	5	01-Sep-28	08-Sep-28
B30310	L3GC - Cx Tile	5	5	11-Sep-28	15-Sep-28
B30315	L3GC - Pre-Punch	15	15	18-Sep-28	06-Oct-28
Area SC - Science Classrooms		200	200	12-Jan-28	20-Oct-28
B31000	L3SC - Shaft Duct & Pipe	10	10	12-Jan-28	25-Jan-28
B31010	L3SC - Priority Walls	7	7	26-Jan-28	03-Feb-28
B31020	L3SC - OH RI Prior to Framing	7	7	04-Feb-28	14-Feb-28
B31030	L3SC - Framing	7	7	15-Feb-28	23-Feb-28
B31040	L3SC - Wall Rough-in	7	7	24-Feb-28	03-Mar-28
B31050	L3SC - Top Rock	7	7	06-Mar-28	14-Mar-28
B31060	L3SC - OH RI High (Fire Protection, Classroom Elec Rough-in)	7	7	15-Mar-28	23-Mar-28
B31070	L3SC - OH RI High (Plumbing, Core Elec RI)	7	7	15-Mar-28	23-Mar-28
B31080	L3SC - OH RI Mid (Hydronic, Refer, Gas, Elec-Corridor, Plmbg Insul)	7	7	24-Mar-28	03-Apr-28
B31090	L3SC - OH RI Low (Duct, Elec FA, Lighting Cont., LV, Hyd Insul, FA, LC)	7	7	04-Apr-28	12-Apr-28
B31100	L3SC - Soffits / HL	5	5	13-Apr-28	19-Apr-28
B31110	L3SC - Pickup Work	6	6	20-Apr-28	27-Apr-28
B31120	L3SC - Cover & Stock	3	3	28-Apr-28	02-May-28
B31130	L3SC - Drywall & Insulation	7	7	03-May-28	11-May-28
B31140	L3SC - MT Finish Treatment	7	7	12-May-28	22-May-28
B31150	L3SC - Gyprete	7	7	12-May-28	22-May-28
B31160	L3SC - Taping	7	7	23-May-28	01-Jun-28
B31170	L3SC - Paint	7	7	02-Jun-28	12-Jun-28
B31180	L3SC - Resinous Flooring	5	5	13-Jun-28	19-Jun-28
B31190	L3SC - Pull LV Wire	7	7	13-Jun-28	21-Jun-28
B31200	L3SC - Bathroom Tile	5	5	22-Jun-28	28-Jun-28
B31210	L3SC - T-Bar Device Tile	7	7	22-Jun-28	30-Jun-28
B31220	L3SC - Ceiling Trim MEP	7	7	03-Jul-28	12-Jul-28
B31230	L3SC - Casework	7	7	03-Jul-28	12-Jul-28
B31240	L3SC - Flooring	7	7	13-Jul-28	21-Jul-28
B31250	L3SC - MEP Fixtures & Trim	7	7	24-Jul-28	01-Aug-28
B31260	L3SC - Doors / Hardware	5	5	24-Jul-28	28-Jul-28
B31270	L3SC - ACT	7	7	02-Aug-28	10-Aug-28
B31280	L3SC - Specialties	20	20	11-Aug-28	08-Sep-28
B31290	L3SC - Specialy MEP Trim	5	5	11-Sep-28	15-Sep-28
B31300	L3SC - Final Clean	5	5	18-Sep-28	22-Sep-28
B31310	L3SC - Cx Tile	5	5	25-Sep-28	29-Sep-28
B31315	L3SC - Pre-Punch	15	15	02-Oct-28	20-Oct-28
Level 4		210	210	26-Jan-28	17-Nov-28
Area GC - General Classrooms		200	200	26-Jan-28	03-Nov-28
B40000	L4GC - Shaft Duct & Pipe	10	10	26-Jan-28	08-Feb-28
B40010	L4GC - Priority Walls	7	7	09-Feb-28	17-Feb-28
B40020	L4GC - OH RI Prior to Framing	7	7	18-Feb-28	28-Feb-28
B40030	L4GC - Framing	7	7	29-Feb-28	08-Mar-28
B40040	L4GC - Wall Rough-in	7	7	09-Mar-28	17-Mar-28
B40050	L4GC - Top Rock	7	7	20-Mar-28	28-Mar-28
B40060	L4GC - OH RI High (Fire Protection, Classroom Elec Rough-in)	7	7	29-Mar-28	06-Apr-28
B40070	L4GC - OH RI High (Plumbing, Core Elec RI)	7	7	29-Mar-28	06-Apr-28
B40080	L4GC - OH RI Mid (Hydronic, Refer, Gas, Elec-Corridor, Plmbg Insul)	7	7	07-Apr-28	17-Apr-28
B40090	L4GC - OH RI Low (Duct, Elec FA, Lighting Cont., LV, Hyd Insul, FA, LC)	7	7	18-Apr-28	26-Apr-28
B40100	L4GC - Soffits / HL	5	5	27-Apr-28	03-May-28
B40110	L4GC - Pickup Work	6	6	04-May-28	11-May-28
B40120	L4GC - Cover & Stock	3	3	12-May-28	16-May-28
B40130	L4GC - Drywall & Insulation	7	7	17-May-28	25-May-28
B40140	L4GC - MT Finish Treatment	7	7	26-May-28	06-Jun-28
B40150	L4GC - Gyprete	7	7	26-May-28	06-Jun-28
B40160	L4GC - Taping	7	7	07-Jun-28	15-Jun-28
B40170	L4GC - Paint	7	7	16-Jun-28	26-Jun-28
B40180	L4GC - Resinous Flooring	5	5	27-Jun-28	03-Jul-28
B40190	L4GC - Pull LV Wire	7	7	27-Jun-28	06-Jul-28
B40200	L4GC - Bathroom Tile	5	5	07-Jul-28	13-Jul-28
B40210	L4GC - T-Bar Device Tile	7	7	07-Jul-28	17-Jul-28
B40220	L4GC - Ceiling Trim MEP	7	7	18-Jul-28	26-Jul-28
B40230	L4GC - Casework	7	7	18-Jul-28	26-Jul-28
B40240	L4GC - Flooring	7	7	27-Jul-28	04-Aug-28
B40250	L4GC - MEP Fixtures & Trim	7	7	07-Aug-28	15-Aug-28

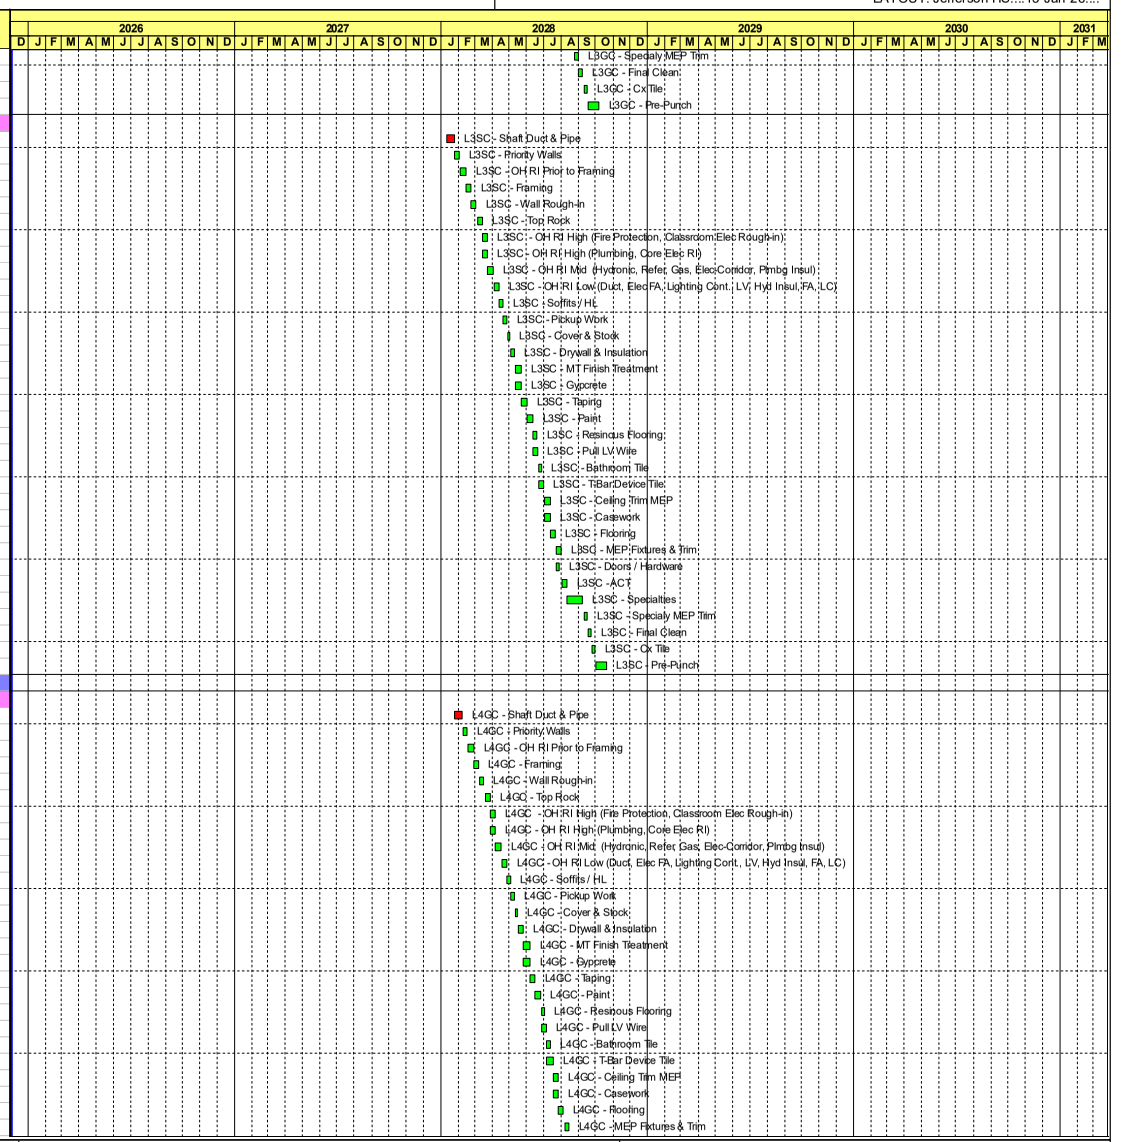

Activity ID	Activity Name	Orig Dur	Remaining Duration	Start	Finish
B40260	L4GC - Doors / Hardware	5	5	07-Aug-28	11-Aug-28
B40270	L4GC - ACT	7	7	16-Aug-28	24-Aug-28
B40280	L4GC - Specialties	20	20	25-Aug-28	22-Sep-28
B40290	L4GC - Specialy MEP Trim	5	5	25-Sep-28	29-Sep-28
B40300	L4GC - Final Clean	5	5	02-Oct-28	06-Oct-28
B40310	L4GC - Cx Tile	5	5	09-Oct-28	13-Oct-28
B40315	L4GC - Pre-Punch	15	15	16-Oct-28	03-Nov-28
Area SC - Science Classrooms		200	200	09-Feb-28	17-Nov-28
B41000	L4SC - Shaft Duct & Pipe	10	10	09-Feb-28	22-Feb-28
B41010	L4SC - Priority Walls	7	7	23-Feb-28	02-Mar-28
B41020	L4SC - OH RI Prior to Framing	7	7	03-Mar-28	13-Mar-28
B41030	L4SC - Framing	7	7	14-Mar-28	22-Mar-28
B41040	L4SC - Wall Rough-in	7	7	23-Mar-28	31-Mar-28
B41050	L4SC - Top Rock	7	7	03-Apr-28	11-Apr-28
B41060	L4SC - OH RI High (Fire Protection, Classroom Elec Rough-in)	7	7	12-Apr-28	20-Apr-28
B41070	L4SC - OH RI High (Plumbing, Core Elec RI)	7	7	12-Apr-28	20-Apr-28
B41080	L4SC - OH RI Mid (Hydronic, Refer, Gas, Elec-Corridor, Plmbg Insul)	7	7	21-Apr-28	01-May-28
B41090	L4SC - OH RI Low (Duct, Elec FA, Lighting Cont., LV, Hyd Insul, FA, LC)	7	7	02-May-28	10-May-28
B41100	L4SC - Soffits / HL	5	5	11-May-28	17-May-28
B41110	L4SC - Pickup Work	6	6	18-May-28	25-May-28
B41120	L4SC - Cover & Stock	3	3	26-May-28	31-May-28
B41130	L4SC - Drywall & Insulation	7	7	01-Jun-28	09-Jun-28
B41140	L4SC - MT Finish Treatment	7	7	12-Jun-28	20-Jun-28
B41150	L4SC - Gypcrete	7	7	12-Jun-28	20-Jun-28
B41160	L4SC - Taping	7	7	21-Jun-28	29-Jun-28
B41170	L4SC - Paint	7	7	30-Jun-28	11-Jul-28
B41180	L4SC - Resinous Flooring	5	5	12-Jul-28	18-Jul-28
B41190	L4SC - Pull LV Wire	7	7	12-Jul-28	20-Jul-28
B41200	L4SC - Bathroom Tile	5	5	21-Jul-28	27-Jul-28
B41210	L4SC - T-Bar Device Tile	7	7	21-Jul-28	31-Jul-28
B41220	L4SC - Ceiling Trim MEP	7	7	01-Aug-28	09-Aug-28
B41230	L4SC - Casework	7	7	01-Aug-28	09-Aug-28
B41240	L4SC - Flooring	7	7	10-Aug-28	18-Aug-28
B41250	L4SC - MEP Fixtures & Trim	7	7	21-Aug-28	29-Aug-28
B41260	L4SC - Doors / Hardware	5	5	21-Aug-28	25-Aug-28
B41270	L4SC - ACT	7	7	30-Aug-28	08-Sep-28
B41280	L4SC - Specialties	20	20	11-Sep-28	06-Oct-28
B41290	L4SC - Specialy MEP Trim	5	5	09-Oct-28	13-Oct-28
B41300	L4SC - Final Clean	5	5	16-Oct-28	20-Oct-28
B41310	L4SC - Cx Tile	5	5	23-Oct-28	27-Oct-28
B41315	L4SC - Pre-Punch	15	15	30-Oct-28	17-Nov-28
Building A- Auditorium		431	431	10-Feb-27	18-Oct-28
Underground		73	73	10-Feb-27	21-May-27
40000	Mass Excavation / Structural Fill to BO Footing	46	46	10-Feb-27	14-Apr-27
40010	Underground Deep Utilities	20	20	10-Mar-27	06-Apr-27
Area 1		23	23	24-Feb-27	26-Mar-27
40100	FRP Concrete Footings / Plynths / Walls	10	10	24-Feb-27	09-Mar-27
40110	Backfill from BO Footing to SOG	3	3	10-Mar-27	12-Mar-27
40120	Underground Utility Install / Backfill & Fine Grade	10	10	15-Mar-27	26-Mar-27
Area 2		23	23	10-Mar-27	09-Apr-27
40200	FRP Concrete Footings / Plynths / Walls	10	10	10-Mar-27	23-Mar-27
40210	Backfill from BO Footing to SOG	3	3	24-Mar-27	26-Mar-27
40220	Underground Utility Install / Backfill & Fine Grade	10	10	29-Mar-27	09-Apr-27
Area 3		23	23	24-Mar-27	23-Apr-27
40300	FRP Concrete Footings / Plynths / Walls	10	10	24-Mar-27	06-Apr-27
40310	Backfill from BO Footing to SOG	3	3	07-Apr-27	09-Apr-27
40320	Underground Utility Install / Backfill & Fine Grade	10	10	12-Apr-27	23-Apr-27
Area 4		23	23	07-Apr-27	07-May-27
40400	FRP Concrete Footings / Plynths / Walls	10	10	07-Apr-27	20-Apr-27
40410	Backfill from BO Footing to SOG	3	3	21-Apr-27	23-Apr-27
40420	Underground Utility Install / Backfill & Fine Grade	10	10	26-Apr-27	07-May-27
Area 5		23	23	21-Apr-27	21-May-27
40500	FRP Concrete Footings / Plynths / Walls	10	10	21-Apr-27	04-May-27
40510	Backfill from BO Footing to SOG	3	3	05-May-27	07-May-27
40520	Underground Utility Install / Backfill & Fine Grade	10	10	10-May-27	21-May-27
Slab on Grade		62	62	29-Mar-27	23-Jun-27

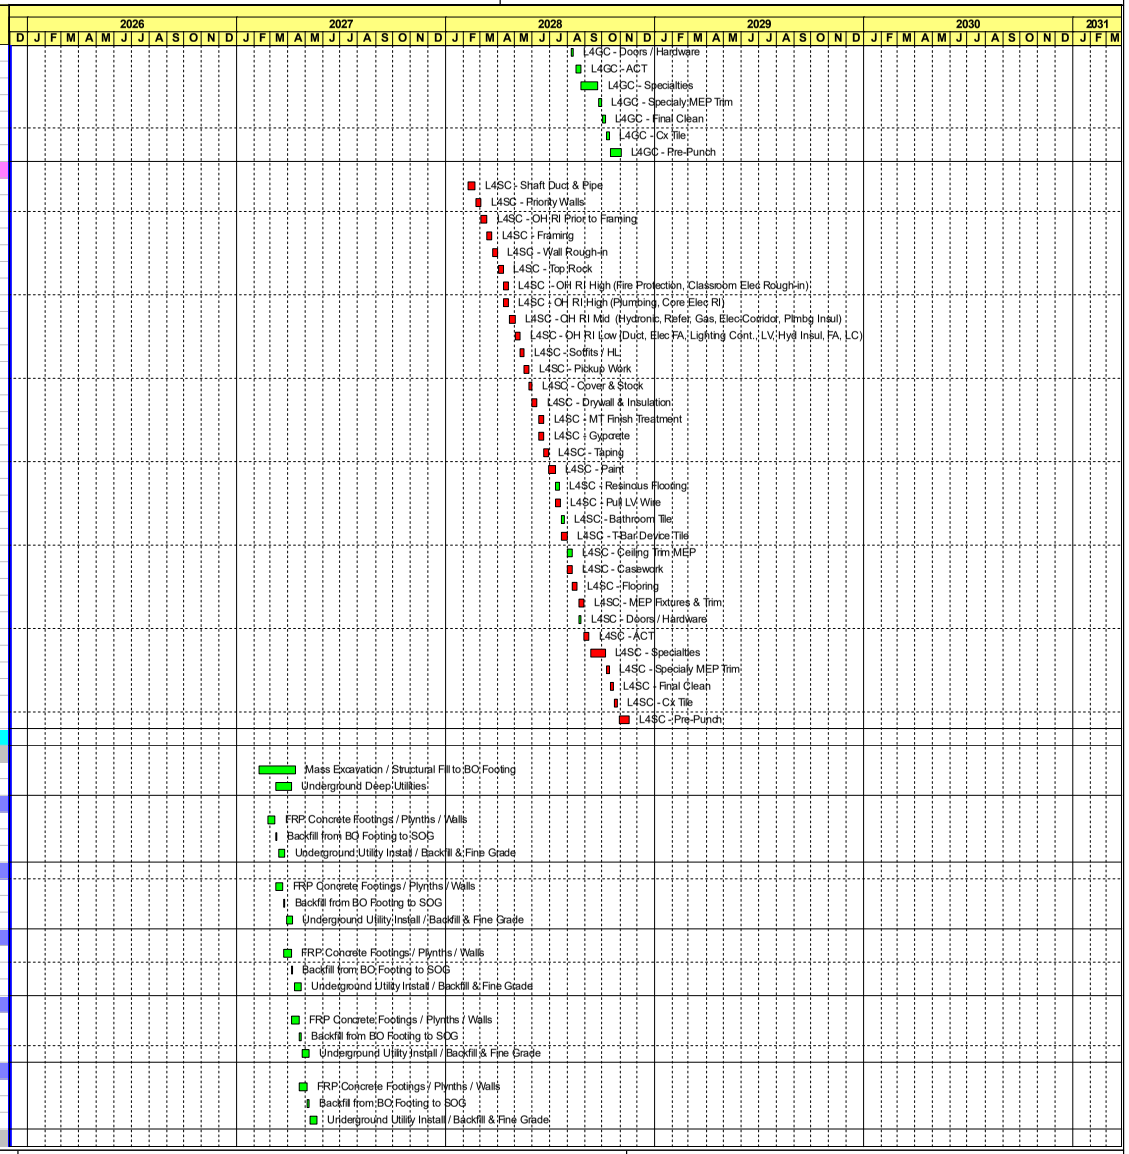

Remaining Level of Effort | Actual Work | Critical Remaining Work

Actual Level of Effort | Remaining Work | Meeting Milestone

PROCEDEO 40

Jefferson High

LAYOUT: Jefferson HS....13-Jan-26....

Activity ID	Activity Name	Orig Dur	Remaining Duration	Start	Finish
Area 1		14	14	29-Mar-27	15-Apr-27
41000	Vapor Barrier	2	2	29-Mar-27	30-Mar-27
41010	FRP SOG	12	12	31-Mar-27	15-Apr-27
Area 2		14	14	12-Apr-27	29-Apr-27
41100	Vapor Barrier	2	2	12-Apr-27	13-Apr-27
41110	FRP SOG	12	12	14-Apr-27	29-Apr-27
Area 3		14	14	26-Apr-27	13-May-27
41200	Vapor Barrier	2	2	26-Apr-27	27-Apr-27
41210	FRP SOG	12	12	28-Apr-27	13-May-27
Area 4		14	14	10-May-27	27-May-27
41300	Vapor Barrier	2	2	10-May-27	11-May-27
41310	FRP SOG	12	12	12-May-27	27-May-27
Area 5		22	22	24-May-27	23-Jun-27
41400	Vapor Barrier	2	2	24-May-27	25-May-27
41410	FRP SOG	20	20	26-May-27	23-Jun-27
Structure		80	80	30-Apr-27	23-Aug-27
42010	Erect L2 & Roof	35	35	30-Apr-27	18-Jun-27
42020	Bolt / Weld / Deck / Level 2 & Roof	30	30	21-Jun-27	02-Aug-27
42030	Layout & Install MEP RI & Sleeves - L2 - Area 1	3	3	28-Jun-27	30-Jun-27
42040	Layout & Install MEP RI & Sleeves - L2 - Area 2	3	3	01-Jul-27	06-Jul-27
42050	Layout & Install MEP RI & Sleeves - L2 - Area 3	3	3	07-Jul-27	09-Jul-27
42060	Layout & Install MEP RI & Sleeves - L2 - Area 4	3	3	12-Jul-27	14-Jul-27
42070	Layout & Install MEP RI & Sleeves - L2 - Area 5	3	3	15-Jul-27	19-Jul-27
42100	FRP L2 SOMD - Area 1	4	4	01-Jul-27	07-Jul-27
42110	FRP L2 SOMD - Area 2	4	4	07-Jul-27	12-Jul-27
42120	FRP L2 SOMD - Area 3	4	4	12-Jul-27	15-Jul-27
42130	FRP L2 SOMD - Area 4	4	4	15-Jul-27	20-Jul-27
42140	FRP L2 SOMD - Area 5	4	4	20-Jul-27	23-Jul-27
42200	Layout & Install MEP RI & Sleeves - Roof - Area 1	4	4	02-Aug-27	05-Aug-27
42210	Layout & Install MEP RI & Sleeves - Roof - Area 2	4	4	06-Aug-27	11-Aug-27
42220	Layout & Install MEP RI & Sleeves - Roof - Area 3	4	4	12-Aug-27	17-Aug-27
42300	FRP Roof SOMD - Area 1	4	4	06-Aug-27	11-Aug-27
42310	FRP Roof SOMD - Area 2	4	4	12-Aug-27	17-Aug-27
42320	FRP Roof SOMD - Area 3	4	4	18-Aug-27	23-Aug-27
Roof		105	105	18-Aug-27	18-Jan-28
RF43000	Roof Area 4 - Parapet Framing	5	5	18-Aug-27	24-Aug-27
RF43010	Roof Area 4 - Temp Roof	20	20	25-Aug-27	22-Sep-27
RF43020	Roof Area 4 - Roof	80	80	16-Sep-27	11-Jan-28
RF43030	Roof Area 5 - Parapet Framing	5	5	25-Aug-27	31-Aug-27
RF43040	Roof Area 5 - Temp Roof	20	20	01-Sep-27	29-Sep-27
RF43050	Roof Area 5 - Roof	80	80	23-Sep-27	18-Jan-28
Facade		152	152	12-Aug-27	17-Mar-28
Fac44000	Facade 7 - Curb / Layout	7	7	12-Aug-27	20-Aug-27
Fac44010	Facade 7 - Exterior Panels	7	7	23-Aug-27	31-Aug-27
Fac44020	Facade 7 - WB Repair	7	7	01-Sep-27	10-Sep-27
Fac44030	Facade 7 - Install Windows	7	7	13-Sep-27	21-Sep-27
Fac44040	Facade 7 - "Z" Framing	14	14	22-Sep-27	11-Oct-27
Fac44050	Facade 7 - Metal Shrouds	14	14	12-Oct-27	29-Oct-27
Fac44060	Facade 7 - Insulation	14	14	01-Nov-27	18-Nov-27
Fac44070	Facade 7 - Hat Framing	14	14	19-Nov-27	10-Dec-27
Fac44080	Facade 7 - Metal Panel / Masonry	20	20	13-Dec-27	11-Jan-28
Fac44090	Facade 7 - Clean	5	5	12-Jan-28	18-Jan-28
Fac44095	Facade 7 - Pre-Punch & Quality Check	15	15	19-Jan-28	08-Feb-28
Fac44100	Facade 8 - Curb / Layout	7	7	23-Aug-27	31-Aug-27
Fac44110	Facade 8 - Exterior Panels	7	7	01-Sep-27	10-Sep-27
Fac44120	Facade 8 - WB Repair	7	7	13-Sep-27	21-Sep-27
Fac44130	Facade 8 - Install Windows	7	7	22-Sep-27	30-Sep-27
Fac44140	Facade 8 - "Z" Framing	14	14	12-Oct-27	29-Oct-27
Fac44150	Facade 8 - Metal Shrouds	14	14	01-Nov-27	18-Nov-27
Fac44160	Facade 8 - Insulation	14	14	19-Nov-27	10-Dec-27
Fac44170	Facade 8 - Hat Framing	14	14	13-Dec-27	03-Jan-28
Fac44180	Facade 8 - Metal Panel / Masonry	20	20	04-Jan-28	31-Jan-28
Fac44190	Facade 8 - Clean	5	5	01-Feb-28	07-Feb-28
Fac44195	Facade 8 - Pre-Punch & Quality Check	15	15	08-Feb-28	28-Feb-28
Fac44200	Facade 9 - Curb / Layout	7	7	01-Sep-27	10-Sep-27
Fac44210	Facade 9 - Exterior Panels	7	7	13-Sep-27	21-Sep-27



Remaining Level of Effort | Actual Work | Critical Remaining Work
Actual Level of Effort | Remaining Work | Meeting Milestone


Jefferson High School 1.6.26

data date :01-Dec-25 Page 14 of 19 TASK filter: <100%.

Jefferson High

LAYOUT: Jefferson HS....13-Jan-26....

Activity ID	Activity Name	Orig Dur	Remaining Duration	Start	Finish
Fac44220	Facade 9 - WB Repair	7	7	22-Sep-27	30-Sep-27
Fac44230	Facade 9 - Install Windows	7	7	01-Oct-27	11-Oct-27
Fac44240	Facade 9 - "Z" Framing	14	14	01-Nov-27	18-Nov-27
Fac44250	Facade 9 - Metal Shrouds	14	14	19-Nov-27	10-Dec-27
Fac44260	Facade 9 - Insulation	14	14	13-Dec-27	03-Jan-28
Fac44270	Facade 9 - Hat Framing	14	14	04-Jan-28	21-Jan-28
Fac44280	Facade 9 - Metal Panel / Masonry	20	20	24-Jan-28	18-Feb-28
Fac44290	Facade 9 - Clean	5	5	21-Feb-28	25-Feb-28
Fac44295	Facade 9 - Pre-Punch & Quality Check	15	15	28-Feb-28	17-Mar-28
Interior Buildout		260	260	12-Oct-27	18-Oct-28
Level 1		260	260	12-Oct-27	18-Oct-28
Area TA - Theater Auxiliary		200	200	12-Oct-27	25-Jul-28
A10000	L1TA - Shaft Duct & Pipe	10	10	12-Oct-27	25-Oct-27
A10010	L1TA - Priority Walls	7	7	26-Oct-27	03-Nov-27
A10020	L1TA - OH RI Prior to Framing	7	7	04-Nov-27	12-Nov-27
A10030	L1TA - Framing	7	7	15-Nov-27	23-Nov-27
A10040	L1TA - Wall Rough-in	7	7	24-Nov-27	06-Dec-27
A10050	L1TA - Top Rock	7	7	07-Dec-27	15-Dec-27
A10060	L1TA - OH RI High (Fire Protection, Classroom Elec Rough-in)	7	7	16-Dec-27	27-Dec-27
A10070	L1TA - OH RI High (Plumbing, Core Elec RI)	7	7	16-Dec-27	27-Dec-27
A10080	L1TA - OH RI Mid (Hydronic, Refer, Gas, Elec-Corridor, Plmbg Insul)	7	7	28-Dec-27	06-Jan-28
A10090	L1TA - OH RI Low (Duct, Elec FA, Lighting Cont., LV, Hyd Insul, FA, LC)	7	7	07-Jan-28	17-Jan-28
A10100	L1TA - Soffits / HL	5	5	18-Jan-28	24-Jan-28
A10110	L1TA - Pickup Work	6	6	25-Jan-28	01-Feb-28
A10120	L1TA - Cover & Stock	3	3	02-Feb-28	04-Feb-28
A10130	L1TA - Drywall & Insulation	7	7	07-Feb-28	15-Feb-28
A10140	L1TA - MT Finish Treatment	7	7	16-Feb-28	24-Feb-28
A10150	L1TA - Taping	7	7	25-Feb-28	06-Mar-28
A10160	L1TA - Paint	7	7	07-Mar-28	15-Mar-28
A10170	L1TA - Resinous Flooring	5	5	16-Mar-28	22-Mar-28
A10180	L1TA - Pull LV Wire	7	7	16-Mar-28	24-Mar-28
A10190	L1TA - Bathroom Tile	5	5	27-Mar-28	31-Mar-28
A10200	L1TA - T-Bar Device Tile	7	7	27-Mar-28	04-Apr-28
A10210	L1TA - Ceiling Trim MEP	7	7	05-Apr-28	13-Apr-28
A10220	L1TA - Casework	7	7	05-Apr-28	13-Apr-28
A10230	L1TA - Flooring	7	7	14-Apr-28	24-Apr-28
A10240	L1TA - MEP Fixtures & Trim	7	7	25-Apr-28	03-May-28
A10250	L1TA - Doors / Hardware	5	5	25-Apr-28	01-May-28
A10260	L1TA - ACT	7	7	04-May-28	12-May-28
A10270	L1TA - Specialties	20	20	15-May-28	12-Jun-28
A10280	L1TA - Specialy MEP Trim	5	5	13-Jun-28	19-Jun-28
A10290	L1TA - Final Clean	5	5	20-Jun-28	26-Jun-28
A10300	L1TA - Cx Tile	5	5	27-Jun-28	03-Jul-28
A10305	L1TA - Pre-Punch	15	15	05-Jul-28	25-Jul-28
Theater		250	250	26-Oct-27	18-Oct-28
A11000	Aud - Rough In / Framing & Interior Finishes	250	250	26-Oct-27	18-Oct-28
Level 2		200	200	26-Oct-27	08-Aug-28
Area TA - Theater Auxiliary		200	200	26-Oct-27	08-Aug-28
A20000	L1TA - Shaft Duct & Pipe	10	10	26-Oct-27	08-Nov-27
A20010	L1TA - Priority Walls	7	7	09-Nov-27	17-Nov-27
A20020	L1TA - OH RI Prior to Framing	7	7	18-Nov-27	30-Nov-27
A20030	L1TA - Framing	7	7	01-Dec-27	09-Dec-27
A20040	L1TA - Wall Rough-in	7	7	10-Dec-27	20-Dec-27
A20050	L1TA - Top Rock	7	7	21-Dec-27	30-Dec-27
A20060	L1TA - OH RI High (Fire Protection, Classroom Elec Rough-in)	7	7	03-Jan-28	11-Jan-28
A20070	L1TA - OH RI High (Plumbing, Core Elec RI)	7	7	03-Jan-28	11-Jan-28
A20080	L1TA - OH RI Mid (Hydronic, Refer, Gas, Elec-Corridor, Plmbg Insul)	7	7	12-Jan-28	20-Jan-28
A20090	L1TA - OH RI Low (Duct, Elec FA, Lighting Cont., LV, Hyd Insul, FA, LC)	7	7	21-Jan-28	31-Jan-28
A20100	L1TA - Soffits / HL	5	5	01-Feb-28	07-Feb-28
A20110	L1TA - Pickup Work	6	6	08-Feb-28	15-Feb-28
A20120	L1TA - Cover & Stock	3	3	16-Feb-28	18-Feb-28
A20130	L1TA - Drywall & Insulation	7	7	21-Feb-28	29-Feb-28
A20140	L1TA - MT Finish Treatment	7	7	01-Mar-28	09-Mar-28
A20150	L1TA - Taping	7	7	10-Mar-28	20-Mar-28
A20160	L1TA - Paint	7	7	21-Mar-28	29-Mar-28
A20170	L1TA - Resinous Flooring	5	5	30-Mar-28	05-Apr-28

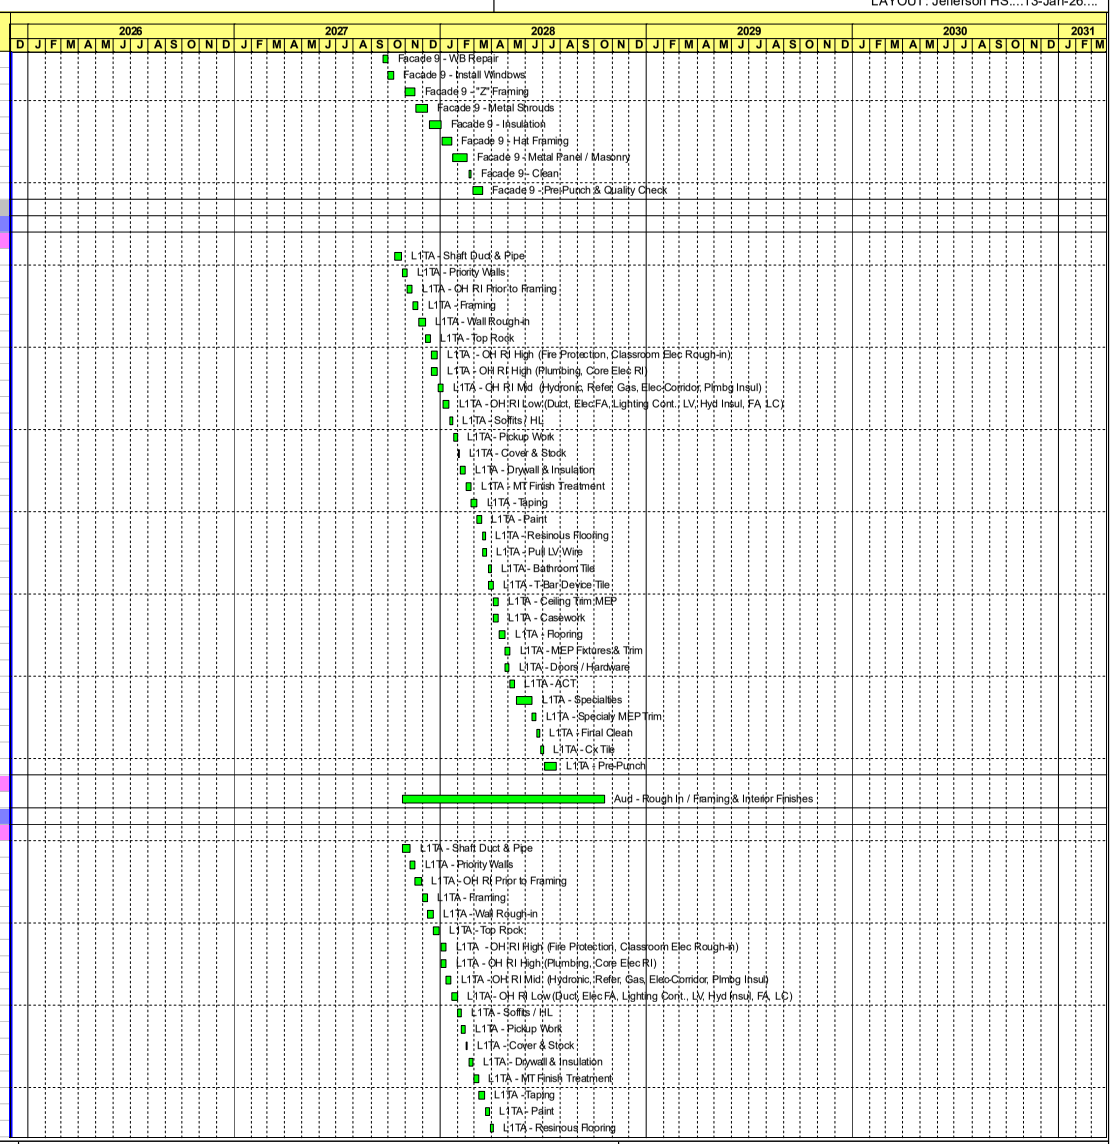


Remaining Level of Effort | Actual Work | Critical Remaining Work
Actual Level of Effort | Remaining Work | Meeting Milestone

Jefferson High School 1.6.26

data date :01-Dec-25 Page 15 of 19 TASK filter: <100%.


Activity ID	Activity Name	Orig Dur	Remaining Duration	Start	Finish
A20180	L1TA - Pull LV Wire	7	7	30-Mar-28	07-Apr-28
A20190	L1TA - Bathroom Tile	5	5	10-Apr-28	14-Apr-28
A20200	L1TA - T-Bar Device Tile	7	7	10-Apr-28	18-Apr-28
A20210	L1TA - Ceiling Trim MEP	7	7	19-Apr-28	27-Apr-28
A20220	L1TA - Casework	7	7	19-Apr-28	27-Apr-28
A20230	L1TA - Flooring	7	7	28-Apr-28	08-May-28
A20240	L1TA - MEP Fixtures & Trim	7	7	09-May-28	17-May-28
A20250	L1TA - Doors / Hardware	5	5	09-May-28	15-May-28
A20260	L1TA - ACT	7	7	18-May-28	26-May-28
A20270	L1TA - Specialties	20	20	30-May-28	26-Jun-28
A20280	L1TA - Specialy MEP Trim	5	5	27-Jun-28	03-Jul-28
A20290	L1TA - Final Clean	5	5	05-Jul-28	11-Jul-28
A20300	L1TA - Cx Tile	5	5	12-Jul-28	18-Jul-28
A20305	L1TA - Pre-Punch	15	15	19-Jul-28	08-Aug-28
Building C - Gym		482	482	10-Feb-27	03-Jan-29
Underground		60	60	10-Feb-27	04-May-27
50000	Mass Excavation / Structural Fill to BO Footing	27	27	10-Feb-27	18-Mar-27
50010	Underground Deep Utilities	25	25	24-Feb-27	30-Mar-27
Area 1		18	18	24-Feb-27	19-Mar-27
50100	FRP Concrete Footings / Plynths / Walls	8	8	24-Feb-27	05-Mar-27
50110	Backfill from BO Footing to SOG	2	2	08-Mar-27	09-Mar-27
50120	Underground Utility Install / Backfill & Fine Grade	8	8	10-Mar-27	19-Mar-27
Area 2		18	18	08-Mar-27	31-Mar-27
50200	FRP Concrete Footings / Plynths / Walls	8	8	08-Mar-27	17-Mar-27
50210	Backfill from BO Footing to SOG	2	2	18-Mar-27	19-Mar-27
50220	Underground Utility Install / Backfill & Fine Grade	8	8	22-Mar-27	31-Mar-27
Area 3		18	18	18-Mar-27	12-Apr-27
50300	FRP Concrete Footings / Plynths / Walls	8	8	18-Mar-27	29-Mar-27
50310	Backfill from BO Footing to SOG	2	2	30-Mar-27	31-Mar-27
50320	Underground Utility Install / Backfill & Fine Grade	8	8	01-Apr-27	12-Apr-27
Area 4		18	18	30-Mar-27	22-Apr-27
50400	FRP Concrete Footings / Plynths / Walls	8	8	30-Mar-27	08-Apr-27
50410	Backfill from BO Footing to SOG	2	2	09-Apr-27	12-Apr-27
50420	Underground Utility Install / Backfill & Fine Grade	8	8	13-Apr-27	22-Apr-27
Area 5		18	18	09-Apr-27	04-May-27
50500	FRP Concrete Footings / Plynths / Walls	8	8	09-Apr-27	20-Apr-27
50510	Backfill from BO Footing to SOG	2	2	21-Apr-27	22-Apr-27
50520	Underground Utility Install / Backfill & Fine Grade	8	8	23-Apr-27	04-May-27
Slab on Grade		196	196	22-Mar-27	28-Dec-27
Area 1		12	12	22-Mar-27	06-Apr-27
51100	Vapor Barrier	2	2	22-Mar-27	23-Mar-27
51110	FRP SOG	10	10	24-Mar-27	06-Apr-27
Area 2		12	12	01-Apr-27	16-Apr-27
51200	Vapor Barrier	2	2	01-Apr-27	02-Apr-27
51210	FRP SOG	10	10	05-Apr-27	16-Apr-27
Area 3		14	14	13-Apr-27	30-Apr-27
51300	Vapor Barrier	2	2	13-Apr-27	14-Apr-27
51310	FRP SOG	12	12	15-Apr-27	30-Apr-27
Area 4		18	18	22-Oct-27	17-Nov-27
51400	Vapor Barrier	6	6	22-Oct-27	01-Nov-27
51410	FRP SOG	12	12	01-Nov-27	17-Nov-27
Area 5		26	26	17-Nov-27	28-Dec-27
51500	Vapor Barrier	6	6	17-Nov-27	29-Nov-27
51510	FRP SOG	20	20	29-Nov-27	28-Dec-27
Structure		194	194	26-Apr-27	31-Jan-28
52010	Build CMU Walls & Brace	60	60	26-Apr-27	20-Jul-27
52100	Erect L2 & Roof	20	20	19-Jul-27	13-Aug-27
52110	Bolt / Weld / Deck / Level 2 & Roof	18	18	16-Aug-27	09-Sep-27
52120	Layout & Install MEP RI & Sleeves - L2 / Mezz - Area 1	3	3	23-Aug-27	25-Aug-27
52130	Layout & Install MEP RI & Sleeves - L2 / Mezz - Area 2	3	3	26-Aug-27	30-Aug-27
52140	Layout & Install MEP RI & Sleeves - L2 / Mezz - Area 3	3	3	31-Aug-27	02-Sep-27
52150	Layout & Install MEP RI & Sleeves - L2 / Mezz - Area 4	3	3	03-Sep-27	08-Sep-27
52160	Layout & Install MEP RI & Sleeves - L2 / Mezz - Area 5	3	3	09-Sep-27	13-Sep-27
52170	FRP L2 / Mezz SOMD - Area 1	2	2	26-Aug-27	27-Aug-27
52180	FRP L2 / Mezz SOMD - Area 2	2	2	31-Aug-27	01-Sep-27
52190	FRP L2 / Mezz SOMD - Area 3	2	2	03-Sep-27	07-Sep-27

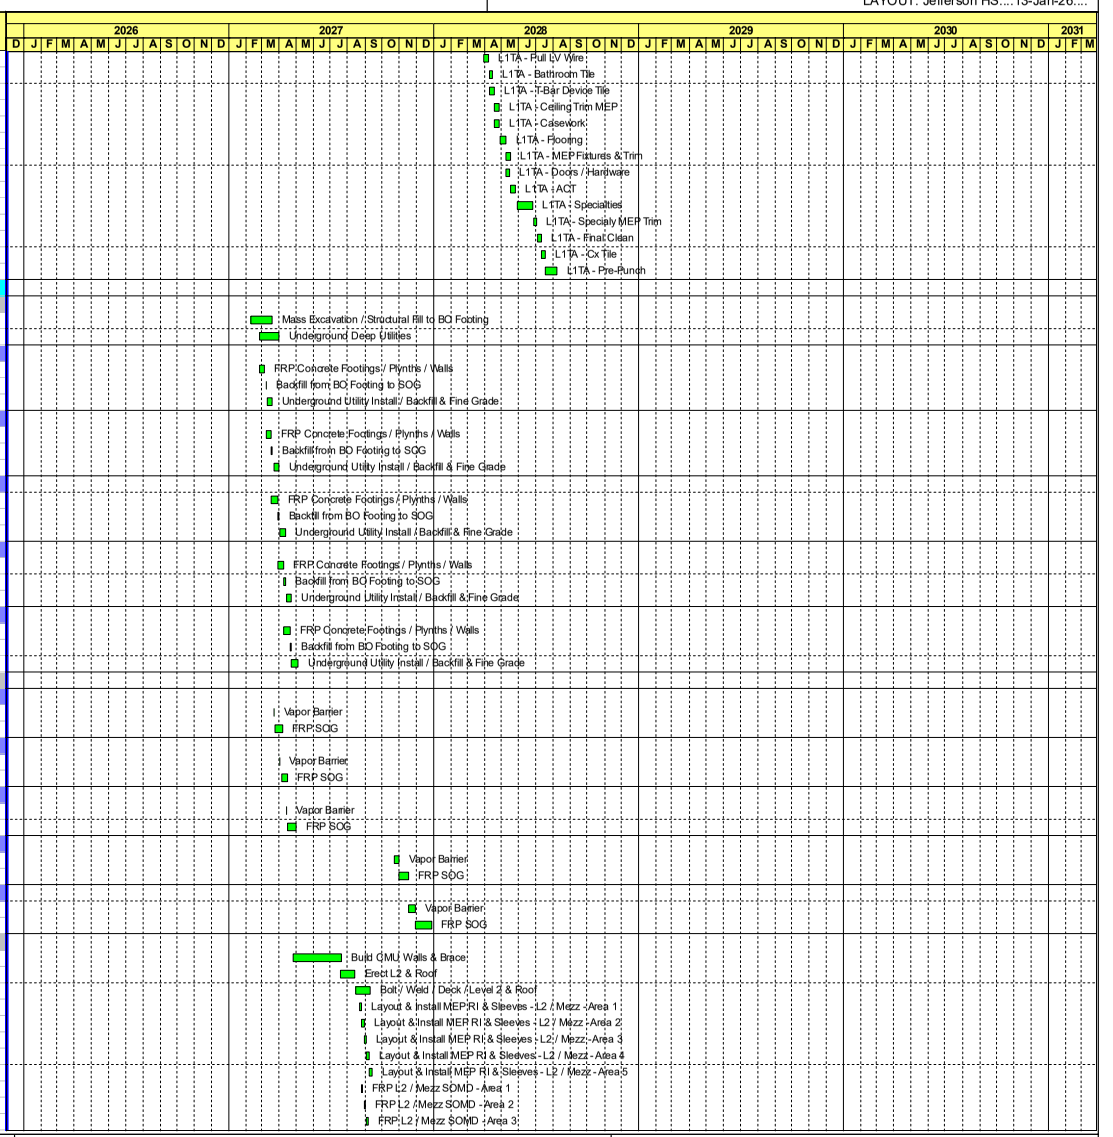

Remaining Level of Effort | Actual Work | Critical Remaining Work

Actual Level of Effort | Remaining Work | Meeting Milestone

Activity ID	Activity Name	Orig Dur	Remaining Duration	Start	Finish
52200	FRP L2 / Mezz SOMD - Area 4	2	2	09-Sep-27	10-Sep-27
52210	FRP L2 / Mezz SOMD - Area 5	2	2	14-Sep-27	15-Sep-27
52220	Layout & Install MEP RI & Sleeves - Roof - Area 1	2	2	10-Sep-27	13-Sep-27
52230	Layout & Install MEP RI & Sleeves - Roof - Area 2	2	2	14-Sep-27	15-Sep-27
52240	Layout & Install MEP RI & Sleeves - Roof - Area 3	2	2	16-Sep-27	17-Sep-27
52250	FRP Roof SOMD -Area 1	3	3	14-Sep-27	16-Sep-27
52260	FRP Roof SOMD -Area 2	3	3	16-Sep-27	20-Sep-27
52270	FRP Roof SOMD -Area 3	3	3	20-Sep-27	22-Sep-27
Staging Area		67	67	22-Oct-27	31-Jan-28
52280	Demob Tower Crane 2	5	5	22-Oct-27	29-Oct-27
52290	Prep & Pour SOG	10	10	29-Oct-27	12-Nov-27
52300	Build CMU Walls (East)	20	20	09-Nov-27	09-Dec-27
52310	Set Steel Trusses	10	10	09-Dec-27	23-Dec-27
52320	Set Wood Trusses	10	10	23-Dec-27	10-Jan-28
52330	Set Wood DLT Roof Deck	15	15	10-Jan-28	31-Jan-28
Roof		161	161	23-Sep-27	10-May-28
RF53000	Roof Area 6 - Parapet Framing	5	5	23-Sep-27	29-Sep-27
RF53010	Roof Area 6 - Temp Roof	20	20	30-Sep-27	27-Oct-27
RF53020	Roof Area 6 - Roofing	40	40	21-Oct-27	17-Dec-27
RF53030	Roof Area 7 - Parapet Framing	5	5	31-Jan-28	07-Feb-28
RF53040	Roof Area 7 - Temp Roof	20	20	07-Feb-28	06-Mar-28
RF53050	Roof Area 7 - Roofing	40	40	28-Feb-28	24-Apr-28
RF53055	PV Panels	12	12	24-Apr-28	10-May-28
Facade		145	145	31-Jan-28	23-Aug-28
Fac54000	Facade 10 - Curb / Layout	7	7	31-Jan-28	09-Feb-28
Fac54010	Facade 10 - Exterior Panels	7	7	09-Feb-28	18-Feb-28
Fac54020	Facade 10 - WB Repair	7	7	18-Feb-28	29-Feb-28
Fac54030	Facade 10 - Install Windows	7	7	29-Feb-28	09-Mar-28
Fac54040	Facade 10 - "Z" Framing	14	14	09-Mar-28	29-Mar-28
Fac54050	Facade 10 - Metal Shrouds	14	14	29-Mar-28	18-Apr-28
Fac54060	Facade 10 - Insulation	14	14	18-Apr-28	08-May-28
Fac54070	Facade 10 - Hat Framing	14	14	08-May-28	26-May-28
Fac54080	Facade 10 - Metal Panel / Masonry	20	20	26-May-28	26-Jun-28
Fac54090	Facade 10 - Clean	5	5	26-Jun-28	03-Jul-28
Fac54095	Facade 10 - Pre-Punch & Quality Check	15	15	03-Jul-28	25-Jul-28
Fac54100	Facade 11 - Curb / Layout	7	7	09-Feb-28	18-Feb-28
Fac54110	Facade 11 - Exterior Panels	7	7	18-Feb-28	29-Feb-28
Fac54120	Facade 11 - WB Repair	7	7	29-Feb-28	09-Mar-28
Fac54130	Facade 11 - Install Windows	7	7	09-Mar-28	20-Mar-28
Fac54140	Facade 11 - "Z" Framing	14	14	20-Mar-28	07-Apr-28
Fac54150	Facade 11 - Metal Shrouds	14	14	07-Apr-28	27-Apr-28
Fac54160	Facade 11 - Insulation	14	14	27-Apr-28	17-May-28
Fac54170	Facade 11 - Hat Framing	14	14	17-May-28	07-Jun-28
Fac54180	Facade 11 - Metal Panel / Masonry	20	20	07-Jun-28	06-Jul-28
Fac54190	Facade 11 - Clean	5	5	06-Jul-28	13-Jul-28
Fac54195	Facade 11 - Pre-Punch & Quality Check	15	15	13-Jul-28	03-Aug-28
Fac54200	Facade 12 - Curb / Layout	7	7	18-Feb-28	29-Feb-28
Fac54210	Facade 12 - Exterior Panels	7	7	29-Feb-28	09-Mar-28
Fac54220	Facade 12 - WB Repair	7	7	09-Mar-28	20-Mar-28
Fac54230	Facade 12 - Install Windows	7	7	20-Mar-28	29-Mar-28
Fac54240	Facade 12 - "Z" Framing	14	14	07-Apr-28	27-Apr-28
Fac54250	Facade 12 - Metal Shrouds	14	14	27-Apr-28	17-May-28
Fac54260	Facade 12 - Insulation	14	14	17-May-28	07-Jun-28
Fac54270	Facade 12 - Hat Framing	14	14	07-Jun-28	27-Jun-28
Fac54280	Facade 12 - Metal Panel / Masonry	20	20	27-Jun-28	26-Jul-28
Fac54290	Facade 12 - Clean	5	5	26-Jul-28	02-Aug-28
Fac54295	Facade 12 - Pre-Punch & Quality Check	15	15	02-Aug-28	23-Aug-28
Interior Buildout		324	324	23-Sep-27	03-Jan-29
Level 1 / Level 1 Mezzanine		324	324	23-Sep-27	03-Jan-29
Area GA - Gym Auxiliary & Main Electrical / Lockers		200	200	23-Sep-27	06-Jul-28
C10000	L1GA - Shaft Duct & Pipe	7	7	23-Sep-27	01-Oct-27
C10010	L1GA - Priority Walls	7	7	04-Oct-27	12-Oct-27
C10020	L1GA - OH RI Prior to Framing	7	7	13-Oct-27	21-Oct-27
C10030	L1GA - Framing	7	7	22-Oct-27	01-Nov-27
C10040	L1GA - Wall Rough-in	7	7	02-Nov-27	10-Nov-27
C10050	L1GA - Top Rock	7	7	11-Nov-27	19-Nov-27

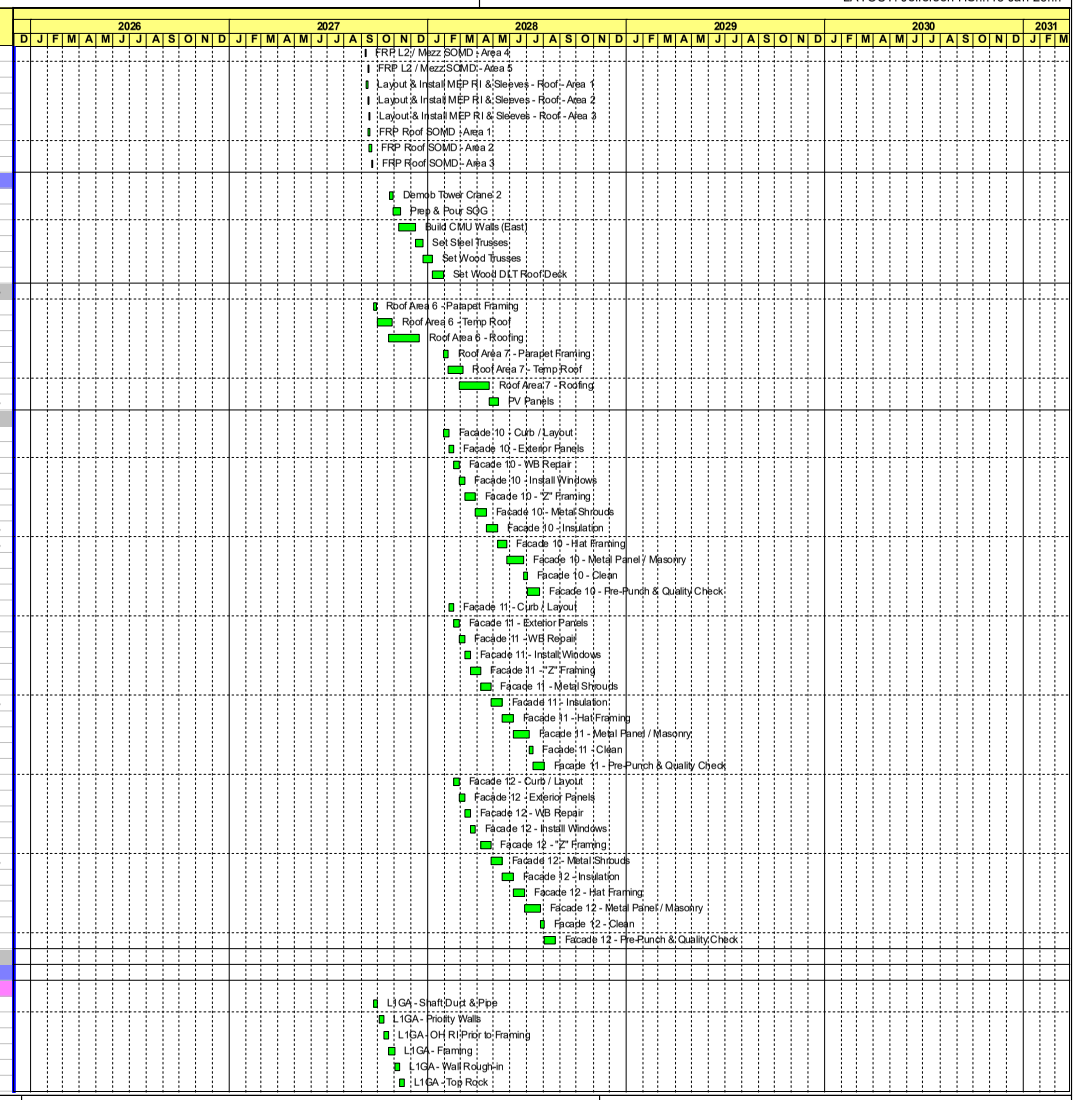


Remaining Level of Effort | Actual Work | Critical Remaining Work

Actual Level of Effort | Remaining Work | Meeting Milestone

Jefferson High

LAYOUT: Jefferson HS....13-Jan-26....

Activity ID	Activity Name	Orig Dur	Remaining Duration	Start	Finish
C10060	L1GA - OH RI High (Fire Protection, Classroom Elec Rough-in)	7	7	22-Nov-27	02-Dec-27
C10070	L1GA - OH RI High (Plumbing, Core Elec RI)	7	7	22-Nov-27	02-Dec-27
C10080	L1GA - OH RI Mid (Hydronic, Refer, Gas, Elec-Corridor, Plmbg Insul)	7	7	03-Dec-27	13-Dec-27
C10090	L1GA - OH RI Low (Duct, Elec FA, Lighting Cont., LV, Hyd Insul, FA, LW)	7	7	14-Dec-27	22-Dec-27
C10100	L1GA - Soffits / HL	5	5	23-Dec-27	30-Dec-27
C10110	L1GA - Pickup Work	6	6	03-Jan-28	10-Jan-28
C10120	L1GA - Cover & Stock	3	3	11-Jan-28	13-Jan-28
C10130	L1GA - Drywall & Insulation	7	7	14-Jan-28	24-Jan-28
C10140	L1GA- MT Finish Treatment	7	7	25-Jan-28	02-Feb-28
C10150	L1GA - Taping	7	7	03-Feb-28	11-Feb-28
C10160	L1GA - Paint	7	7	14-Feb-28	22-Feb-28
C10170	L1GA - Resinous Flooring	5	5	23-Feb-28	29-Feb-28
C10180	L1GA - Pull LV Wire	7	7	23-Feb-28	02-Mar-28
C10190	L1GA - Bathroom Tile	5	5	03-Mar-28	09-Mar-28
C10200	L1GA - T-Bar Device Tile	7	7	03-Mar-28	13-Mar-28
C10210	L1GA - Ceiling Trim MEP	7	7	14-Mar-28	22-Mar-28
C10220	L1GA - Casework	7	7	14-Mar-28	22-Mar-28
C10230	L1GA - Flooring	10	10	23-Mar-28	05-Apr-28
C10240	L1GA - MEP Fixtures & Trim	7	7	06-Apr-28	14-Apr-28
C10250	L1GA - Doors / Hardware	5	5	06-Apr-28	12-Apr-28
C10260	L1GA - ACT	7	7	17-Apr-28	25-Apr-28
C10270	L1GA - Specialties	20	20	26-Apr-28	23-May-28
C10280	L1GA - Specialy MEP Trim	5	5	24-May-28	31-May-28
C10290	L1GA - Final Clean	5	5	01-Jun-28	07-Jun-28
C10300	L1GA - Cx Tile	5	5	08-Jun-28	14-Jun-28
C10305	L1GA - Pre-Punch	15	15	15-Jun-28	06-Jul-28
Area G - Gym		240	240	24-Jan-28	03-Jan-29
C11000	Gym - Rough In / Framing & Interior Finishes	240	240	24-Jan-28	03-Jan-29
Level 2		230	230	04-Oct-27	28-Aug-28
Area GA - Auxiliary Gym & Weights		230	230	04-Oct-27	28-Aug-28
C20000	L2GA - Shaft Duct & Pipe	7	7	04-Oct-27	12-Oct-27
C20010	L2GA - Priority Walls	7	7	13-Oct-27	21-Oct-27
C20020	L2GA - OH RI Prior to Framing	7	7	22-Oct-27	01-Nov-27
C20030	L2GA - Framing	7	7	02-Nov-27	10-Nov-27
C20040	L2GA - Wall Rough-in	7	7	11-Nov-27	19-Nov-27
C20050	L2GA - Top Rock	7	7	22-Nov-27	02-Dec-27
C20060	L2GA - OH RI High (Fire Protection, Classroom Elec Rough-in)	7	7	03-Dec-27	13-Dec-27
C20070	L2GA - OH RI High (Plumbing, Core Elec RI)	7	7	03-Dec-27	13-Dec-27
C20080	L2GA - OH RI Mid (Hydronic, Refer, Gas, Elec-Corridor, Plmbg Insul)	7	7	14-Dec-27	22-Dec-27
C20090	L2GA - OH RI Low (Duct, Elec FA, Lighting Cont., LV, Hyd Insul, FA, LW)	7	7	23-Dec-27	04-Jan-28
C20100	L2GA - Soffits / HL	5	5	05-Jan-28	11-Jan-28
C20110	L2GA - Pickup Work	6	6	12-Jan-28	19-Jan-28
C20120	L2GA - Cover & Stock	3	3	20-Jan-28	24-Jan-28
C20130	L2GA - Drywall & Insulation	7	7	25-Jan-28	02-Feb-28
C20140	L2GA- MT Finish Treatment	7	7	03-Feb-28	11-Feb-28
C20150	L2GA - Taping	7	7	14-Feb-28	22-Feb-28
C20160	L2GA - Paint	7	7	23-Feb-28	02-Mar-28
C20170	L2GA - Resinous Flooring	5	5	03-Mar-28	09-Mar-28
C20180	L2GA - Pull LV Wire	7	7	03-Mar-28	13-Mar-28
C20190	L2GA - Bathroom Tile	5	5	14-Mar-28	20-Mar-28
C20200	L2GA - T-Bar Device Tile	7	7	14-Mar-28	22-Mar-28
C20210	L2GA - Ceiling Trim MEP	7	7	23-Mar-28	31-Mar-28
C20220	L2GA - Casework	7	7	23-Mar-28	31-Mar-28
C20230	L2GA - Flooring	20	20	03-Apr-28	28-Apr-28
C20240	L2GA - MEP Fixtures & Trim	7	7	01-May-28	09-May-28
C20250	L2GA - Doors / Hardware	5	5	01-May-28	05-May-28
C20260	L2GA - ACT	7	7	10-May-28	18-May-28
C20270	L2GA - Specialties	40	40	19-May-28	17-Jul-28
C20280	L2GA - Specialy MEP Trim	5	5	18-Jul-28	24-Jul-28
C20290	L2GA - Final Clean	5	5	25-Jul-28	31-Jul-28
C20300	L2GA - Cx Tile	5	5	01-Aug-28	07-Aug-28
C20305	L2GA - Pre-Punch	15	15	08-Aug-28	28-Aug-28
Sidewalks / Landscaping		195	195	09-Feb-28	10-Nov-28
60000	Site Work / Right of Way Improvements - Kirby	50	50	09-Feb-28	18-Apr-28
60010	Site Work / Right of Way Improvements - Killingsworth	25	25	29-Feb-28	03-Apr-28
60020	Site Work / Right of Way Improvements - Commercial	25	25	23-Aug-28	28-Sep-28

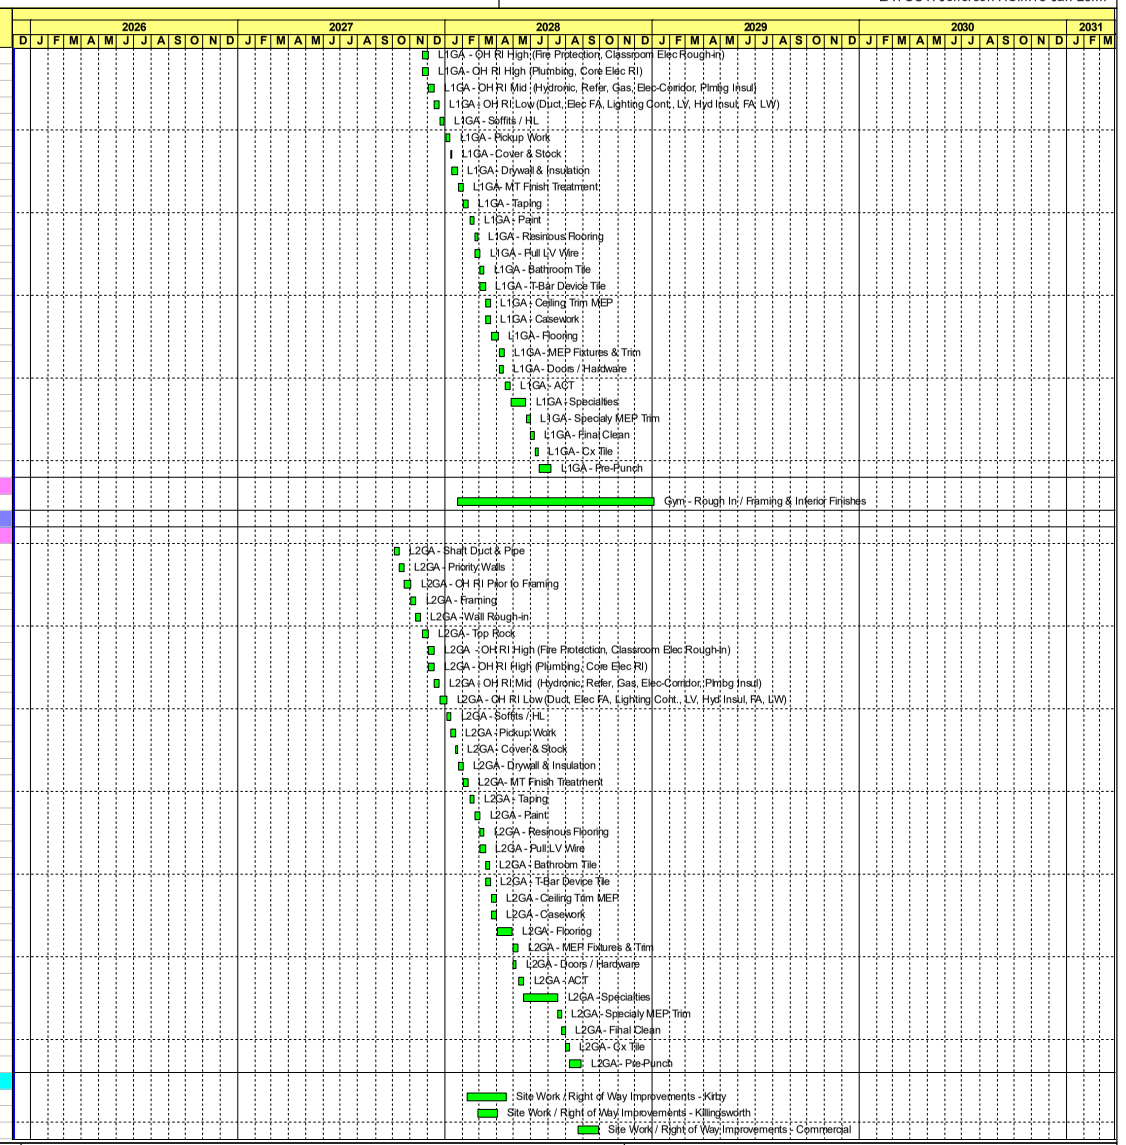


Remaining Level of Effort | Actual Work | Critical Remaining Work

Actual Level of Effort | Remaining Work | Meeting Milestone

Jefferson High School 1.6.26

data date :01-Dec-25 Page 18 of 19 TASK filter: <100%.


Activity ID	Activity Name	Orig Dur	Remaining Duration	Start	Finish
60030	Site Work / Right of Way Improvements - South Courtyard	50	50	01-Sep-28	10-Nov-28
Commissioning		119	119	09-Aug-28	29-Jan-29
90002	Building B MEP Start-up / Balancing / Commissioning	50	50	15-Nov-28	29-Jan-29
90012	Building A MEP Start-up / Balancing / Commissioning	50	50	09-Aug-28	18-Oct-28
90014	Building C MEP Start-up / Balancing / Commissioning	50	50	02-Nov-28	17-Jan-29
Closeout		153	153	30-Jan-29	04-Sep-29
90000	Weather Contingency	20	20	30-Jan-29	26-Feb-29
90010	New Building Punch	50	50	27-Feb-29	07-May-29
90015	TCO	0	0		07-May-29
90020	Otis / FF&E Install & Move-in (Aug 15 2029)	70	70	08-May-29	15-Aug-29*
90030	Contingency	13	13	16-Aug-29	04-Sep-29
Phase 3		265	265	15-Aug-29	05-Sep-30
099000	Existing Building Vacated	0	0		15-Aug-29
100000	Current Building Demolition / Abatement	105	105	16-Aug-29	18-Jan-30
100010	Build Football Field / Tennis Courts	150	150	11-Dec-29	17-Jul-30
100020	Site Works	45	45	08-Apr-30	10-Jun-30
100030	Punch, Commissioning & Closeout	35	35	18-Jul-30	05-Sep-30*
Hoisting		342	342	21-Dec-26	24-Apr-28
100040	Manlift Duration	115	115	12-Apr-27	22-Sep-27
100050	Tower Crane Duration	342	342	21-Dec-26	24-Apr-28

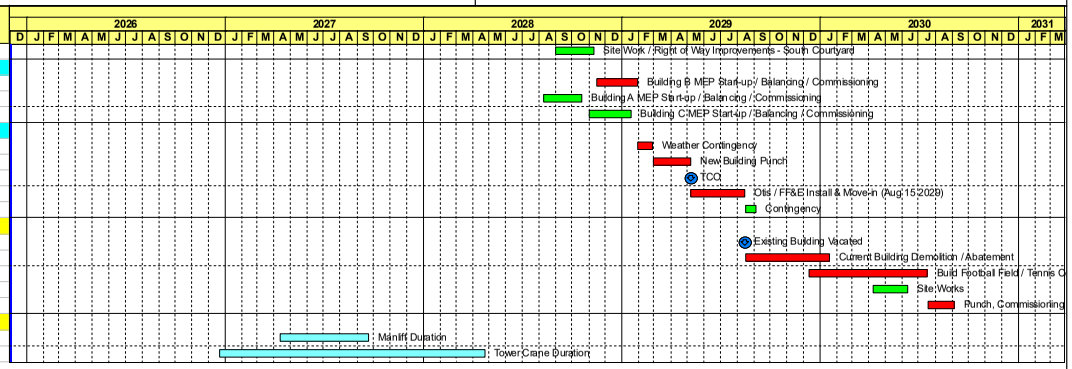

Jefferson High-1

LAYOUT: Jefferson HS Delay L3 L4....13-Jan-26....

Activity ID	Activity Name	Orig Dur	Remaining Duration	Start	Finish
Owner Milestones		724	724	08-May-26	15-Mar-29
MS0900	PPS Ground Breaking Ceremony	0	0	08-May-26*	
MS1000	Baseball / Softball Season Completion	0	0		01-Jun-26*
MS1010	Last Day of School 2026	0	0		12-Jun-26*
MS1020	First Day of Spring Practice Softball / Baseball	0	0	01-Mar-27*	
MS1030	Last Day of Basketball Practice / Early Gym Demo	0	0		15-Mar-29*
MS1040	Last Day of Football Practice	0	0		13-Nov-26*
PRECONSTRUCTION		731	658	19-Mar-25 A	05-Jul-28
Deign & Permitting from Bora		417	344	19-Mar-25 A	09-Apr-27
Design		331	258	01-Sep-25 A	08-Dec-26
Fields		114	41	01-Sep-25 A	30-Jan-26
D1200	JHS Early Fields Construction Documents	110	41	01-Sep-25 A	30-Jan-26
D1230	JHS Early Fields 100% CD Set	0	0		30-Jan-26*
New School Building		268	258	27-Oct-25 A	08-Dec-26
D1500	JHS Design Development	110	87	27-Oct-25 A	06-Apr-26
D1510	JHS DD Pricing Set (Structural/ Arch Gridlock)	0	0		30-Jan-26
D1520	JHS DD Cost Estimate	35	35	02-Feb-26	20-Mar-26
D1530	JHS DD Estimate Set Owner Review	10	10	02-Feb-26	13-Feb-26
D1540	JHS DD Estimate Set Owner Page Turns	10	10	16-Feb-26	27-Feb-26
D1550	JHS DD DPA (Design Phase Approval)	5	5	23-Mar-26	27-Mar-26
D1560	JHS QC Review	40	40	30-Jan-26	26-Mar-26
D1570	JHS Construction Documents	161	161	07-Apr-26	20-Nov-26
D1580	JHS 50% CD Set (100% CD Foundation to Grade Structural)	0	0	17-Jul-26	
D1590	Design Deliverable 1 (AR) Fire Protection Head Placement For DLT Pen. Coor	0	0	17-Jul-26	
D1600	Design Deliverable 2 (AR) Light Layout For DLT Pen. Coord.	0	0	17-Jul-26	
D1610	Design Deliverable 3 (AR) Shaft Rollout For DLT Pen. Coord.	0	0	17-Jul-26	
D1620	Structural Frame 100% CD Connected Structural Model LOD 300	0	0	12-Oct-26*	
D1630	JHS 50% CD Set Owner Review	10	10	17-Jul-26	30-Jul-26
D1640	JHS 50% CD Set Owner Page Turn	10	10	31-Jul-26	13-Aug-26
D1645	JHS 75% MEP Design / Equipment Selection	0	0	01-Oct-26*	
D1650	JHS 100% CD Set	0	0		20-Nov-26
D1660	JHS PPS 100% CD Set Owner Review	10	10	23-Nov-26	08-Dec-26
Permit		390	344	19-Mar-25 A	09-Apr-27
PER0900	JHS MPG Submit 25% DD Documents for Review	0	0	01-Dec-25	
PER0910	JHS MPG Submit 100% DD Documents for Review	0	0	07-Apr-26	
PER0930	JHS Public Works Permit / Right of Way Scope	260	126	19-Mar-25 A	01-Jun-26
PER0940	JHS Land Use - Type III CU	100	77	06-Oct-25 A	23-Mar-26
PER0950	JHS Land Use - Historic Review	60	60	21-Jan-26*	14-Apr-26
PER1000	JHS Permit Set A: Early Fields	88	88	02-Mar-26*	02-Jul-26
PER1020	JHS Permit Set B: Foundation to Grade	87	87	03-Aug-26*	04-Dec-26
PER1040	JHS Permit Set C: Building Permit	85	85	10-Dec-26	09-Apr-27
HCC		658	658	01-Dec-25	05-Jul-28
Contracts & Buyout		417	417	01-Dec-25	23-Jul-27
BO60000	Sub Bids, Normalization & EWA Preparation (Early Fields)	45	45	01-Dec-25	05-Feb-26
BO60010	Early Work Amendment Execution (Early Fields)	20	20	06-Feb-26	05-Mar-26
BO60020	Phase 1 - Execute Critical Subcontracts (Early Fields)	20	20	06-Mar-26	02-Apr-26
BO60030	Athletic Field Specialties Long Lead Time	60	60	03-Apr-26	26-Jun-26
BO60040	MEPF Trade Partner RFP, Bids & PPS Amendment	56	56	23-Jan-26*	10-Apr-26
BO60050	PPS Amendment for MEPF Trade Partner District Approval	20	20	13-Apr-26	08-May-26
BO60060	Mass Timber RFP Bids & PPS Amendment	45	45	12-Jan-26*	13-Mar-26
BO60062	Mass Exc / UG Utilities / Foundations RFP Bids & Early Work Amendment	30	30	17-Jul-26	27-Aug-26
BO60064	EWA Mass Exc / UG Utilities / Foundations District Approval	20	20	28-Aug-26	25-Sep-26
BO60070	Early Work Amendment for Mass Timber District Approval	20	20	16-Mar-26	10-Apr-26
BO60080	Sub Bids, Normalization & Budget Preparation (Balance of Work)	70	70	17-Jul-26	23-Oct-26
BO60090	Phase 2 Early Work Amendment Execution District Appoval	20	20	26-Oct-26	20-Nov-26
BO60100	Balance of Work - Execute Critical Subcontracts & Start Submittals	20	20	23-Nov-26	22-Dec-26
BO60110	Steel Fab & Erect Sub Bids, Normalization Early Work Amendment	20	20	17-Jul-26	13-Aug-26
BO60120	Structural Steel Mill Order, Fab & Erect Early Work Amendment Execution by D	20	20	14-Aug-26	11-Sep-26
BO60130	Prepare & Release Mill Order	10	10	14-Sep-26	25-Sep-26
BO60140	Roll & Ship Steel to Fabricator	75	75	28-Sep-26	15-Jan-27
BO60150	Misc Iron / Stairs Procurement	90	90	18-Mar-27	23-Jul-27
BO60170	Full GMP Amendment Negotiation & Execution	95	95	26-Oct-26	11-Mar-27
BO60180	Early Start of Phase 2 Work	0	0	23-Dec-26	
BO60190	Balance of Work - Execute All Remaining Subcontractors	30	30	12-Mar-27	22-Apr-27
Trade Partner Selection for Precon Assist & Procurement		460	460	11-May-26	02-Mar-28

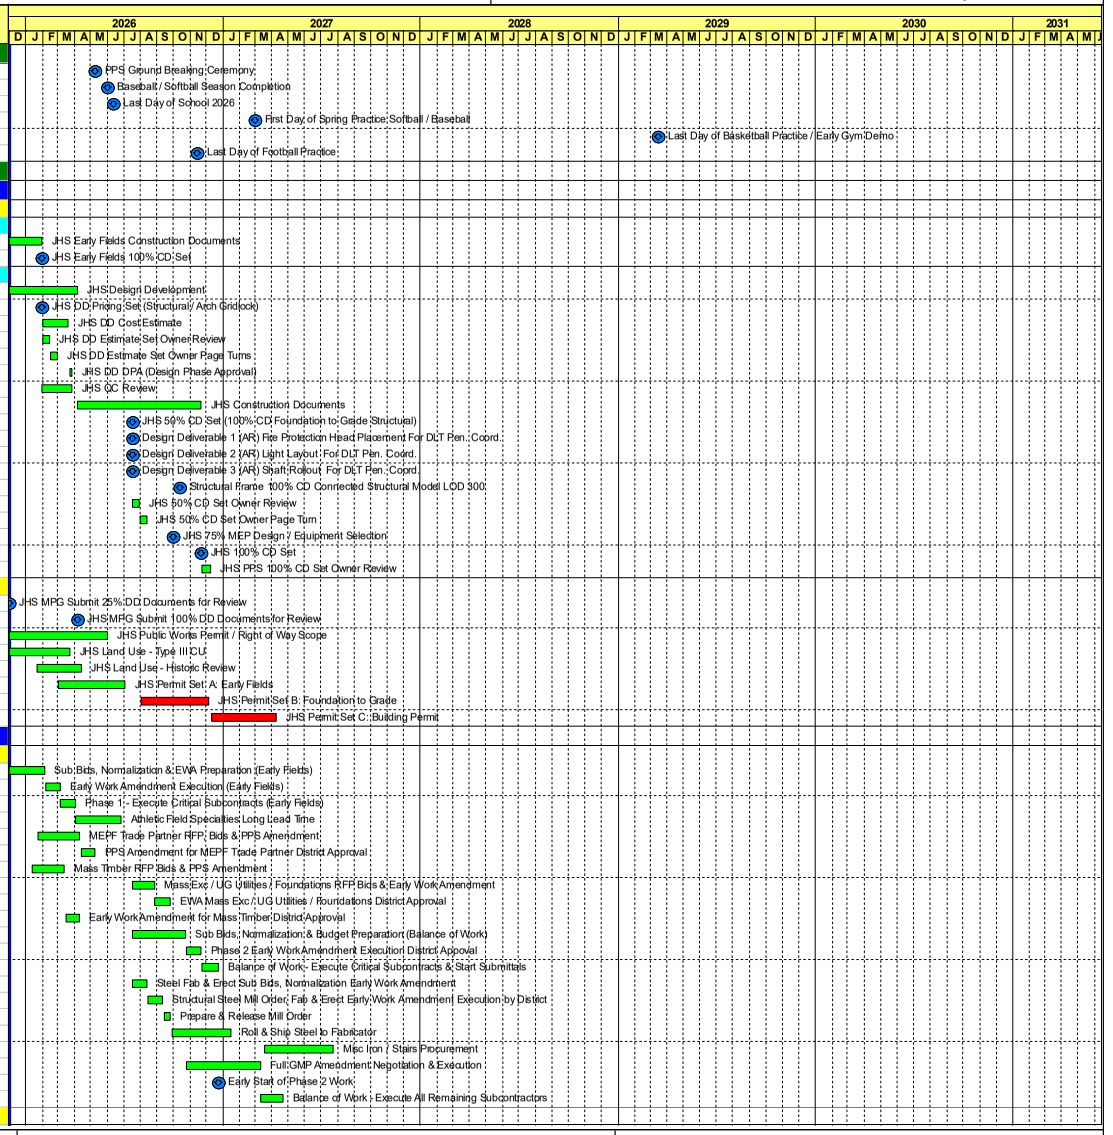


Remaining Level of Effort | Actual Work | Critical Remaining Work
Actual Level of Effort | Remaining Work | Meeting Milestone

Jefferson High School 1.6.26 - Delay L3 L4

data date :01-Dec-25 Page 1 of 19 TASK filter: <100%.

Activity ID	Activity Name	Orig Dur	Remaining Duration	Start	Finish
Mass Timber		190	190	11-May-26	09-Feb-27
TPS1200	Trade Partner Selection Complete - Mass Timber	0	0	11-May-26	
TPS1210	BIM Coordination for Timber	190	190	11-May-26	09-Feb-27
TPS1220	Select & Source Materials	100	100	11-May-26	30-Sep-26
Electrical		460	460	11-May-26	02-Mar-28
TPS1300	Trade Partner Selection Complete - Electrical	0	0	11-May-26	
TPS1310	Trade Partner Budgeting / VE & Early BIM Efforts & Temp Power Install	156	156	11-May-26	21-Dec-26
TPS1320	Electrical Switchgear & Emergency Generator Long Lead Equipment	323	323	23-Nov-26	02-Mar-28
TPS1330	Misc. Electrical & Data Submittals / Procurement	150	150	23-Dec-26	26-Jul-27
TPS1340	Misc Security & AV Submittals / Procurement	150	150	23-Dec-26	26-Jul-27
Mechanical / Plumbing		309	309	11-May-26	28-Jul-27
TPS1400	Trade Partner Selection Complete - Mechanical / Plumbing	0	0	11-May-26	
TPS1410	Trade Partner Budgeting / VE & Early BIM Efforts & Temp Water Install	156	156	11-May-26	21-Dec-26
TPS1420	Major MEP Equipment Long Lead Equipment Submittals / Procurement	172	172	23-Nov-26	28-Jul-27
Fire Protection		442	442	11-May-26	07-Feb-28
TPS1600	Trade Partner Selection Complete- Fire Protection	0	0	11-May-26	
TPS1602	Trade Partner Budgeting / VE & Early BIM Efforts	156	156	11-May-26	21-Dec-26
TPS1610	Fire Pump Long Lead Submittals / Procurement	100	100	23-Nov-26	15-Apr-27
TPS1620	Fire Protection DFS Submittals / Approval	145	145	16-Apr-27	09-Nov-27
TPS1630	Fire Protection Submitals / Procurement	60	60	10-Nov-27	07-Feb-28
Structural Steel Detailing		216	216	11-May-26	17-Mar-27
TPS1700	Structural Steel Detailer Selection Complete	0	0	11-May-26	
TPS1710	Structural Steel Detailing BIM Efforts	156	156	11-May-26	21-Dec-26
TPS1720	Misc Iron / Stairs Detailing & Submittals	60	60	22-Dec-26	17-Mar-27
General Material Procurement		593	593	06-Mar-26	05-Jul-28
Early Fields Phase 1 Work		85	85	06-Mar-26	06-Jul-26
019000	Underground Utilities / Plumbing - Submittals / Procurement	60	60	03-Apr-26	26-Jun-26
019010	Rebar / Concrete - Submittals / Procurement	60	60	03-Apr-26	26-Jun-26
019020	Field Turf Products & Electrical / Data - Submittals / Procurement	65	65	06-Mar-26	05-Jun-26
019030	Site Furnishings - Submittals / Procurement	65	65	03-Apr-26	06-Jul-26
019040	Site Landscaping - Submittals / Procurement	65	65	03-Apr-26	06-Jul-26
019050	Curbs & Sidewalk & ROW - Submittals / Procurement	60	60	03-Apr-26	26-Jun-26
019060	Early Field Procurement Complete	0	0		06-Jul-26
JHS Main Building Phase 2 Work		450	450	28-Sep-26	05-Jul-28
019750	Early MEP Underground - Submittals / Procurement	45	45	28-Sep-26	01-Dec-26
019800	Gymnasium & Theatrical Specialties - Submittals / Procurement	120	120	23-Apr-27	12-Oct-27
020200	PV Panels - Submittals / Procurement	305	305	23-Apr-27	05-Jul-28
020300	Site Civil - Submittals / Procurement	60	60	28-Sep-26	22-Dec-26
020700	Foundation Reinforcing - Submittals / Procurement	65	65	28-Sep-26	30-Dec-26
020900	Utility Materials, Catch Basins & Vaults - Submittals / Procurement	43	43	28-Sep-26	25-Nov-26
021100	Underslab Plumbing - Procurement	45	45	23-Nov-26	28-Jan-27
021300	Underslab Electrical - Procurement	45	45	23-Nov-26	28-Jan-27
021700	Plumbing Fixtures, Tubs & Showers - Submittals / Procurement	127	127	23-Apr-27	21-Oct-27
021900	Finishes - Submittals / Procurement	130	130	23-Apr-27	26-Oct-27
022200	Elevator Rails, Platform & Equipment - Submittals / Procurement	85	85	23-Dec-26	22-Apr-27
022400	Elevator Cab Packages - Submittals / Procurement	127	127	23-Dec-26	22-Jun-27
022800	Glazing Systems - Submittals / Procurement	246	246	23-Dec-26	10-Dec-27
024165	Temp Roof - Submittals / Procurement	60	60	23-Dec-26	18-Mar-27
024170	Roofing - Submittals / Procurement	87	87	23-Dec-26	26-Apr-27
024190	Exterior Skin System - Submittals / Design / DFS Approval / Procurement	175	175	23-Dec-26	30-Aug-27
BIM Coordination		354	354	01-Dec-25	23-Apr-27
Early Fields		55	55	25-Mar-26	10-Jun-26
D1130	Survey Coordination	55	55	25-Mar-26	10-Jun-26
D1140	Civil Modeling	21	21	08-Apr-26	06-May-26
D1150	Civil Coordination	24	24	07-May-26	10-Jun-26
D1160	IFF Underground	0	0		10-Jun-26
Timber 1		70	70	17-Jul-26	23-Oct-26
BIM1000	T1 - Populate Model	15	15	17-Jul-26	06-Aug-26
BIM1010	T1 - Initial Space Coordination with MEP	15	15	07-Aug-26	27-Aug-26
BIM1020	T1 - Initial Clash Detection	15	15	28-Aug-26	18-Sep-26
BIM1030	T1 - Penetration Coordination	10	10	21-Sep-26	02-Oct-26
BIM1040	T1 - Issue Penetration Drawings Clashes Resolved	5	5	05-Oct-26	09-Oct-26
BIM1050	T1 - Structural Penetration Coordination & Approval	10	10	12-Oct-26	23-Oct-26
Timber 2		70	70	07-Aug-26	13-Nov-26
BIM2000	T2 - Populate Model	15	15	07-Aug-26	27-Aug-26
BIM2010	T2 - Initial Space Coordination with MEP	15	15	28-Aug-26	18-Sep-26

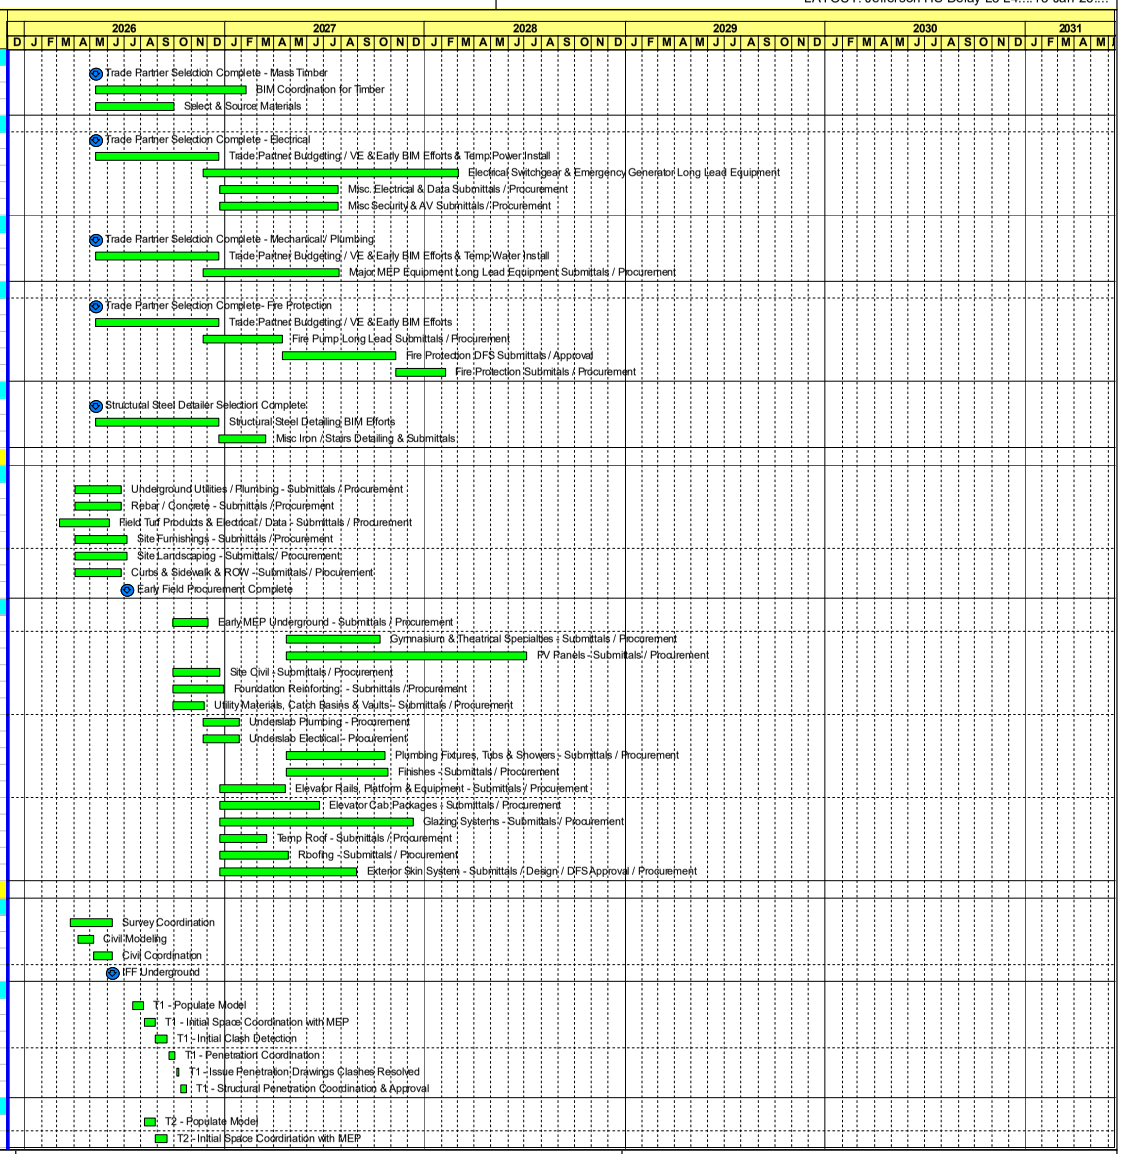


Remaining Level of Effort | Actual Work | Critical Remaining Work

Actual Level of Effort | Remaining Work | Meeting Milestone

Jefferson High School 1.6.26 - Delay L3 L4

Activity ID	Activity Name	Orig Dur	Remaining Duration	Start	Finish
BIM2020	T2 - Initial Clash Detection	15	15	21-Sep-26	09-Oct-26
BIM2030	T2 - Penetration Coordination	10	10	12-Oct-26	23-Oct-26
BIM2040	T2 - Issue Penetration Drawings Clashes Resolved	5	5	26-Oct-26	30-Oct-26
BIM2050	T2 - Structural Penetration Coordination & Approval	10	10	02-Nov-26	13-Nov-26
Timber 3		70	70	28-Aug-26	08-Dec-26
BIM3000	T3 - Populate Model	15	15	28-Aug-26	18-Sep-26
BIM3010	T3 - Initial Space Coordination with MEP	15	15	21-Sep-26	09-Oct-26
BIM3020	T3 - Initial Clash Detection	15	15	12-Oct-26	30-Oct-26
BIM3030	T3 - Penetration Coordination	10	10	02-Nov-26	13-Nov-26
BIM3040	T3 - Issue Penetration Drawings Clashes Resolved	5	5	16-Nov-26	20-Nov-26
BIM3050	T3 - Structural Penetration Coordination & Approval	10	10	23-Nov-26	08-Dec-26
Timber 4		70	70	21-Sep-26	30-Dec-26
BIM4000	T4 - Populate Model	15	15	21-Sep-26	09-Oct-26
BIM4010	T4 - Initial Space Coordination with MEP	15	15	12-Oct-26	30-Oct-26
BIM4020	T4 - Initial Clash Detection	15	15	02-Nov-26	20-Nov-26
BIM4030	T4 - Penetration Coordination	10	10	23-Nov-26	08-Dec-26
BIM4040	T4 - Issue Penetration Drawings Clashes Resolved	5	5	09-Dec-26	15-Dec-26
BIM4050	T4 - Structural Penetration Coordination & Approval	10	10	16-Dec-26	30-Dec-26
Timber 5		70	70	12-Oct-26	21-Jan-27
BIM5000	T5 - Populate Model	15	15	12-Oct-26	30-Oct-26
BIM5010	T5 - Initial Space Coordination with MEP	15	15	02-Nov-26	20-Nov-26
BIM5020	T5 - Initial Clash Detection	15	15	23-Nov-26	15-Dec-26
BIM5030	T5 - Penetration Coordination	10	10	16-Dec-26	30-Dec-26
BIM5040	T5 - Issue Penetration Drawings Clashes Resolved	5	5	31-Dec-26	07-Jan-27
BIM5050	T5 - Structural Penetration Coordination & Approval	10	10	08-Jan-27	21-Jan-27
Architectural Routing (AR) @ MEP Timber Elements		248	248	01-Dec-25	20-Nov-26
BIM6000	T1 AR Populate / Coordinate	90	90	17-Jul-26	20-Nov-26
BIM6010	T1 IFF AR	0	0		20-Nov-26
BIM6020	T2 AR Populate / Coordinate	90	90	01-Dec-25	09-Apr-26
BIM6030	T2 IFF AR	0	0		09-Apr-26
BIM6040	T3 AR Populate / Coordinate	90	90	01-Dec-25	09-Apr-26
BIM6050	T3 IFF AR	0	0		09-Apr-26
BIM6060	T4 AR Populate / Coordinate	90	90	01-Dec-25	09-Apr-26
BIM6070	T4 IFF AR	0	0		09-Apr-26
BIM6080	T5 AR Populate / Coordinate	90	90	01-Dec-25	09-Apr-26
BIM6090	T5 IFF AR	0	0		09-Apr-26
DLT		60	60	09-Dec-26	04-Mar-27
BIM7000	MEP Connection Coordination / Architectural Ceiling Layout	60	60	09-Dec-26	04-Mar-27
Auditorium (A)		154	154	17-Jul-26	24-Feb-27
BIM8000	Aud UG Populate / Coordinate / Clash Resolution / Submit & Approve	70	70	17-Jul-26	23-Oct-26
BIM8010	IFF Aud UG	0	0		23-Oct-26
BIM8020	Aud L1 Populate / Coordinate / Clash Resolution / Submit & Approve	90	90	14-Aug-26	22-Dec-26
BIM8030	IFF Aud L1	0	0		22-Dec-26
BIM8040	Aud L2 Populate / Coordinate / Clash Resolution / Submit & Approve	90	90	17-Sep-26	26-Jan-27
BIM8050	IFF Aud L2	0	0		26-Jan-27
BIM8060	Aud L3 Populate / Coordinate / Clash Resolution / Submit & Approve	90	90	16-Oct-26	24-Feb-27
BIM8070	IFF Aud L3	0	0		24-Feb-27
Main Building (B)		196	196	17-Jul-26	23-Apr-27
BIM9000	MB UG Populate / Coordinate / Clash Resolution / Submit & Approve	90	90	17-Jul-26	20-Nov-26
BIM9010	IFF MB UG	0	0		20-Nov-26
BIM9020	MB L1 Populate / Coordinate / Clash Resolution / Submit & Approve	90	90	14-Aug-26	22-Dec-26
BIM9030	IFF MB L1	0	0		22-Dec-26
BIM9040	MB L2 Populate / Coordinate / Clash Resolution / Submit & Approve	90	90	17-Sep-26	26-Jan-27
BIM9050	IFF MB L2	0	0		26-Jan-27
BIM9060	MB L3 Populate / Coordinate / Clash Resolution / Submit & Approve	90	90	16-Oct-26	24-Feb-27
BIM9070	IFF MB L3	0	0		24-Feb-27
BIM9080	MB L4 Populate / Coordinate / Clash Resolution / Submit & Approve	90	90	16-Nov-26	25-Mar-27
BIM9090	IFF MB L4	0	0		25-Mar-27
BIM9100	MB L5 Populate / Coordinate / Clash Resolution / Submit & Approve	90	90	17-Dec-26	23-Apr-27
BIM9110	IFF MB L5	0	0		23-Apr-27
Gym (C)		154	154	17-Jul-26	24-Feb-27
BIM10000	Gym UG Populate / Coordinate / Clash Resolution / Submit & Approve	70	70	17-Jul-26	23-Oct-26
BIM10010	IFF Gym UG	0	0		23-Oct-26
BIM10020	Gym L1 Populate / Coordinate / Clash Resolution / Submit & Approve	90	90	14-Aug-26	22-Dec-26
BIM10030	IFF Gym L1	0	0		22-Dec-26
BIM10040	Gym L2 Populate / Coordinate / Clash Resolution / Submit & Approve	90	90	17-Sep-26	26-Jan-27

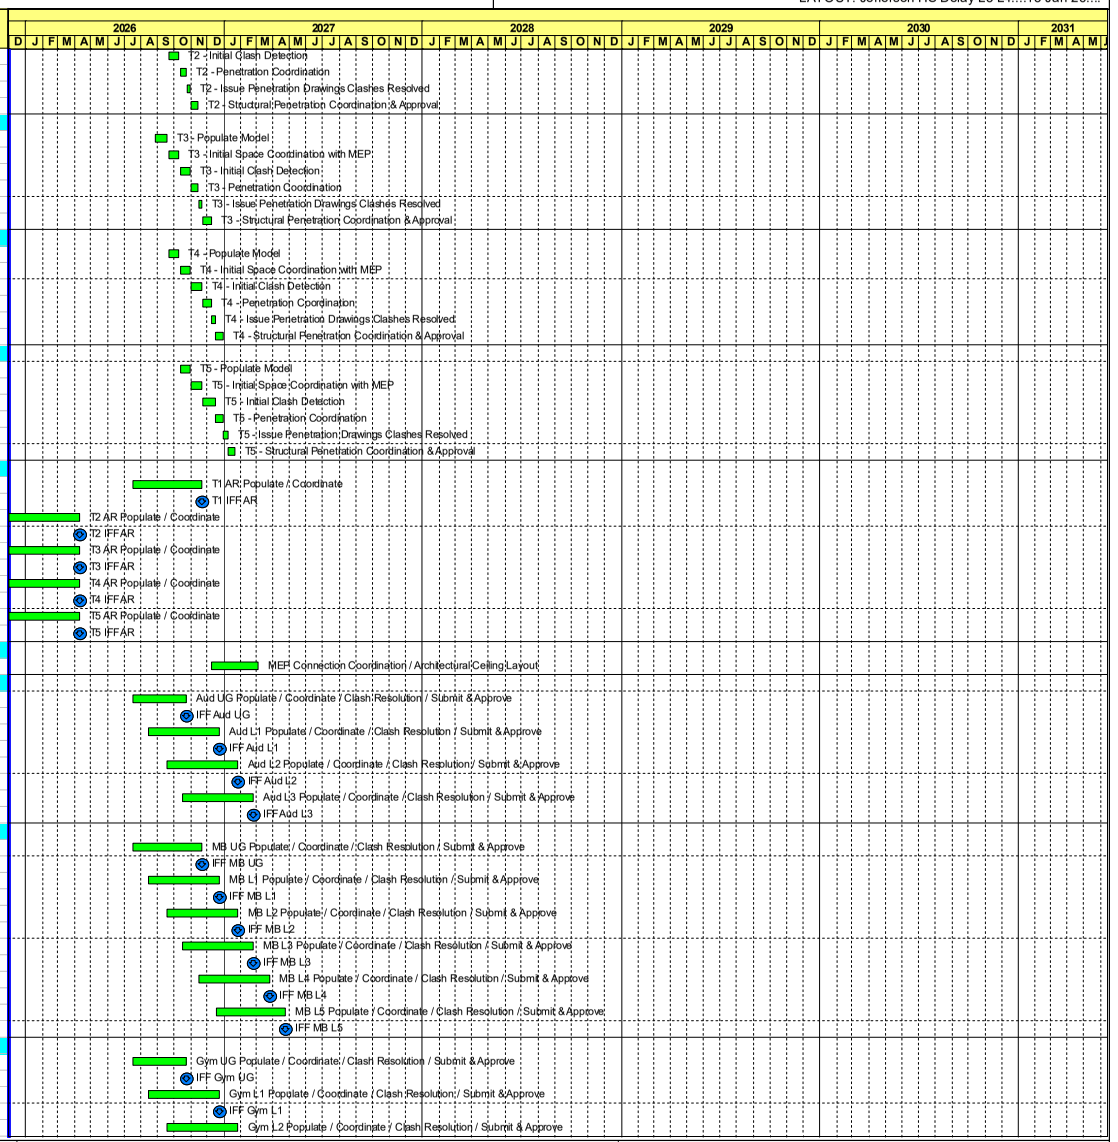


Remaining Level of Effort | Actual Work | Critical Remaining Work

Actual Level of Effort | Remaining Work | Meeting Milestone


Jefferson High School 1.6.26 - Delay L3 L4

Activity ID	Activity Name	Orig Dur	Remaining Duration	Start	Finish
BIM10050	IFF Gym L2	0	0		26-Jan-27
BIM10060	Gym L3 Populate / Coordinate / Clash Resolution / Submit & Approve	90	90	16-Oct-26	24-Feb-27
BIM10070	IFF Gym L3	0	0		24-Feb-27
Phase 3		90	90	23-Nov-26	01-Apr-27
BIM11000	Building / Football / Tennis Fields Populate / Coordinate / Clash Resolution	90	90	23-Nov-26	01-Apr-27
BIM11010	IFF FB / TF / Submit & Approve	20	20	05-Mar-27	01-Apr-27
PROCUREMENT		225	225	12-Oct-26	30-Aug-27
Mass Timber		225	225	12-Oct-26	30-Aug-27
Proc9000	Detail, Submit, Approve Mass Timber - Zone 1	85	85	12-Oct-26	11-Feb-27
Proc9010	Fab & Deliver Mas Timber - Zone 1	80	80	12-Feb-27	04-Jun-27
Timber 1		165	165	12-Oct-26	04-Jun-27
Proc1000	T1 -Populate Beams & Columns	15	15	12-Oct-26	30-Oct-26
Proc1010	T1 - Populate DLT Plank	15	15	02-Nov-26	20-Nov-26
Proc1020	T1 - Connect Timber	15	15	23-Nov-26	15-Dec-26
Proc1030	T1 - Incorporate Penetrations	10	10	16-Dec-26	30-Dec-26
Proc1040	T1 - Detail & Submit	15	15	31-Dec-26	21-Jan-27
Proc1050	T1 - Approve Submittal	15	15	22-Jan-27	11-Feb-27
Proc1060	T1 - Fabricate & Deliver	80	80	12-Feb-27	04-Jun-27
Timber 2		165	165	02-Nov-26	25-Jun-27
Proc2000	T2 -Poulate Beams & Columns	15	15	02-Nov-26	20-Nov-26
Proc2010	T2 - Populate DLT Plank	15	15	23-Nov-26	15-Dec-26
Proc2020	T2 - Connect Timber	15	15	16-Dec-26	07-Jan-27
Proc2030	T2 - Incorporate Penetrations	10	10	08-Jan-27	21-Jan-27
Proc2040	T2 - Detail & Submit	15	15	22-Jan-27	11-Feb-27
Proc2050	T2 - Approve Submittal	15	15	12-Feb-27	04-Mar-27
Proc2060	T2 - Fabricate & Deliver	80	80	05-Mar-27	25-Jun-27
Timber 3		165	165	23-Nov-26	19-Jul-27
Proc3000	T3 -Poulate Beams & Columns	15	15	23-Nov-26	15-Dec-26
Proc3010	T3 - Populate DLT Plank	15	15	16-Dec-26	07-Jan-27
Proc3020	T3 - Connect Timber	15	15	08-Jan-27	28-Jan-27
Proc3030	T3 - Incorporate Penetrations	10	10	29-Jan-27	11-Feb-27
Proc3040	T3 - Detail & Submit	15	15	12-Feb-27	04-Mar-27
Proc3050	T3 - Approve Submittal	15	15	05-Mar-27	25-Mar-27
Proc3060	T3 - Fabricate & Deliver	80	80	26-Mar-27	19-Jul-27
Timber 4		165	165	16-Dec-26	09-Aug-27
Proc4000	T4 -Poulate Beams & Columns	15	15	16-Dec-26	07-Jan-27
Proc4010	T4 - Populate DLT Plank	15	15	08-Jan-27	28-Jan-27
Proc4020	T4 - Connect Timber	15	15	29-Jan-27	18-Feb-27
Proc4030	T4 - Incorporate Penetrations	10	10	19-Feb-27	04-Mar-27
Proc4040	T4 - Detail & Submit	15	15	05-Mar-27	25-Mar-27
Proc4050	T4 - Approve Submittal	15	15	26-Mar-27	15-Apr-27
Proc4060	T4 - Fabricate & Deliver	80	80	16-Apr-27	09-Aug-27
Timber 5		165	165	08-Jan-27	30-Aug-27
Proc5000	T5 -Poulate Beams & Columns	15	15	08-Jan-27	28-Jan-27
Proc5010	T5 - Populate DLT Plank	15	15	29-Jan-27	18-Feb-27
Proc5020	T5 - Connect Timber	15	15	19-Feb-27	11-Mar-27
Proc5030	T5 - Incorporate Penetrations	10	10	12-Mar-27	25-Mar-27
Proc5040	T5 - Detail & Submit	15	15	26-Mar-27	15-Apr-27
Proc5050	T5 - Approve Submittal	15	15	16-Apr-27	06-May-27
Proc5060	T5 - Fabricate & Deliver	80	80	07-May-27	30-Aug-27
Steel		170	170	12-Oct-26	11-Jun-27
Zone 1 - Main School Building - B		110	110	12-Oct-26	18-Mar-27
PROC11000	Z1 - Steel Modeling	30	30	12-Oct-26	20-Nov-26
PROC11010	Z1 - Steel Detailing / Fabrication Drawings	20	20	23-Nov-26	22-Dec-26
PROC11020	Z1 - Submit	20	20	23-Dec-26	21-Jan-27
PROC11030	Z1 - Scrub	10	10	22-Jan-27	04-Feb-27
PROC11040	Z1 - Fab	30	30	05-Feb-27	18-Mar-27
Zone 2 - Auditorium Building - A		110	110	23-Nov-26	29-Apr-27
PROC12000	Z2 - Steel Modeling	30	30	23-Nov-26	07-Jan-27
PROC12010	Z2 - Steel Detailing / Fabrication Drawings	20	20	08-Jan-27	04-Feb-27
PROC12020	Z2 - Submit	20	20	05-Feb-27	04-Mar-27
PROC12030	Z2 - Scrub	10	10	05-Mar-27	18-Mar-27
PROC12040	Z2 - Fab	30	30	19-Mar-27	29-Apr-27
Zone 3 - Gym Building - C		110	110	08-Jan-27	11-Jun-27
PROC13000	Z3 - Steel Modeling	30	30	08-Jan-27	18-Feb-27
PROC13010	Z3 - Steel Detailing / Fabrication Drawings	20	20	19-Feb-27	18-Mar-27

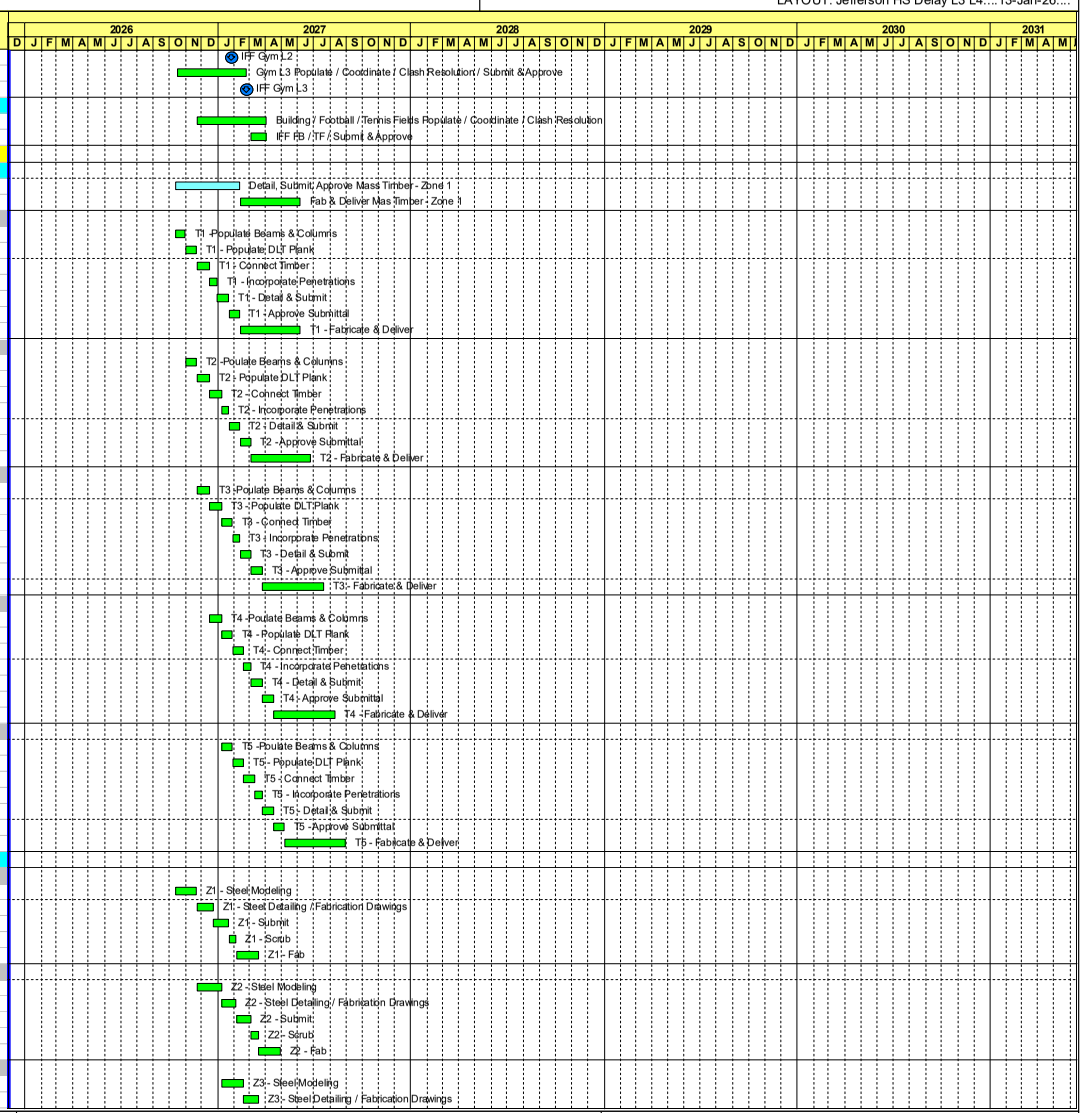

PROCEDEO 50

Activity ID	Activity Name	Orig Dur	Remaining Duration	Start	Finish
PROC13020	Z3 - Submit	20	20	19-Mar-27	15-Apr-27
PROC13030	Z3 - Scrub	10	10	16-Apr-27	29-Apr-27
PROC13040	Z3 - Fab	30	30	30-Apr-27	11-Jun-27
Construction		1308	1262	15-Aug-25 A	22-Nov-30
Cons10000	Start of Construction	0	0	23-Jun-26	
Cons10010	Construction Duration	1016	1016	02-Jun-26	04-Jun-30
HCC		1308	1262	15-Aug-25 A	22-Nov-30
Pacific Power		546	500	15-Aug-25 A	18-Nov-27
Pwr15000	Pacific Power System Impact Study	42	5	15-Aug-25 A	05-Dec-25
Pwr15010	Pacific Power Drafts Master Electric Service Agreement	60	60	08-Dec-25	05-Mar-26
Pwr15020	PPS Reviews & Signs MESA, Makes Upfront Payment	20	20	06-Mar-26	02-Apr-26
Pwr15030	Transformer Procurement	410	410	03-Apr-26	11-Nov-27
Pwr15032	Early Work Fields Temp Power Online / Transformers Delivered	0	0	10-Jul-26*	
Pwr15033	Building B Temp Power Source Online	0	0	04-Jan-27*	
Pwr15035	Killingsworth Underground & Pole Work Complete	0	0		15-Jan-27*
Pwr15040	Install Transformers & Power up PPS Switchgear	5	5	12-Nov-27	18-Nov-27
Phase 1		218	218	13-Apr-26	19-Feb-27
Fld10000	Softball & Baseball Fields Mobilization, Site Fencing, Temp MEP & Vac Truck U	15	15	02-Jun-26	22-Jun-26
Fld10010	Site Survey / Set Controls / Underground Modeling / Clash Detection	35	35	13-Apr-26	01-Jun-26
Softball Field		130	130	10-Jul-26	14-Jan-27
SBF10005	Site Demo, Prep & Strip Grade	10	10	10-Jul-26	23-Jul-26
SBF10010	Site Utilities, Underground, Civil / Stormwater	25	25	24-Jul-26	27-Aug-26
SBF10015	Rough Grade Site & Gravel Parking Lot, Install Loop Access Road	10	10	28-Aug-26	11-Sep-26
SBF10020	Site Concrete / CMU & Dugouts / Footings	20	20	14-Aug-26	11-Sep-26
SBF10025	Fine Grade / Light & Utility Poles / Scoreboard / Fencing Fabric & Backstop	20	20	14-Sep-26	09-Oct-26
SBF10030	Field Turf / Storage Shed	25	25	12-Oct-26	13-Nov-26
SBF10035	Stripes & Lines	10	10	02-Nov-26	13-Nov-26
SBF10040	Bleachers / MEP RI / Parking Lot Improvements	15	15	09-Nov-26	01-Dec-26
SBF10045	Area Landscape / Site Furnishings & MEP Trim Out / Irrigation	10	10	23-Nov-26	08-Dec-26
SBF10050	Architectural Accessories & Plantings	15	15	09-Dec-26	30-Dec-26
SBF10055	Punchlist & Cx	10	10	31-Dec-26	14-Jan-27
Baseball Field		160	160	06-Jul-26	19-Feb-27
BBF12000	Site Demo,Prep & Strip Grade	10	10	06-Jul-26	17-Jul-26
BBF12005	Site Utilities, Underground, Civil / Stormwater	35	35	20-Jul-26	04-Sep-26
BBF12007	Rough Grade & Install Temp Loop Access Road	10	10	08-Sep-26	21-Sep-26
BBF12015	Site Concrete & CMU & Dugouts / Footings	25	25	24-Aug-26	28-Sep-26
BBF12020	Fine Grade / Light & Utility Poles / Scoreboard / Fencing Fabric & Backstop	20	20	29-Sep-26	26-Oct-26
BBF12025	Field Turf / Storage Shed	35	35	27-Oct-26	16-Dec-26
BBF12030	Stripes & Lines	15	15	03-Dec-26	23-Dec-26
BBF12035	Bleachers & Backstops / MEP RI	30	30	10-Dec-26	22-Jan-27
BBF12040	Area Landscape / Site Furnishings & MEP Trim Out / Irrigation & Plantings	20	20	11-Jan-27	05-Feb-27
BBF12050	Punchlist & Cx	10	10	08-Feb-27	19-Feb-27
Fields Frontage Improvements		64	64	13-Jul-26	09-Oct-26
FI13000	Underground ROW Utilities Install	12	12	13-Jul-26*	28-Jul-26
FI13020	Remove & Replace Curb & SW @ Alberta South Side	15	15	22-Jul-26	11-Aug-26
FI13040	Remove & Replace Curb & SW @ Alberta North Side	15	15	05-Aug-26	25-Aug-26
FI13060	Remove & Replace Curb & SW @ Kirby	15	15	17-Aug-26	04-Sep-26
FI13080	Remove & Replace Curbs & SW @ Commercial	15	15	27-Aug-26	17-Sep-26
FI13100	Asphalt Paving @ Alberta	4	4	18-Sep-26	23-Sep-26
FI131120	Asphalt Paving @ Kirby	6	6	24-Sep-26	01-Oct-26
FI131130	Asphalt Paving @ Commercial	6	6	02-Oct-26	09-Oct-26
Phase 2		1015	1015	20-Nov-26	22-Nov-30
20000	Mobilization, Temp Power& Demo	10	10	20-Nov-26	07-Dec-26
Building B - Main Education Building		886	886	07-Dec-26	04-Jun-30
Underground		79	79	07-Dec-26	29-Mar-27
30000	Mass Excavation / Structural Fill to BO Footing	45	45	07-Dec-26	09-Feb-27
30010	Underground Deep Utilities	30	30	29-Dec-26	09-Feb-27
Area 1 & 1A		25	25	21-Dec-26	26-Jan-27
30100	FRP Concrete Footings / Plynths / Walls	10	10	21-Dec-26	05-Jan-27
30110	Backfill from BO Footing to SOG	3	3	06-Jan-27	08-Jan-27
30120	Underground Utility Install / Backfill & Fine Grade	12	12	11-Jan-27	26-Jan-27
Area 2		27	27	06-Jan-27	11-Feb-27
30200	FRP Concrete Footings / Plynths / Walls	12	12	06-Jan-27	21-Jan-27
30210	Backfill from BO Footing to SOG	3	3	22-Jan-27	26-Jan-27
30220	Underground Utility Install / Backfill & Fine Grade	12	12	27-Jan-27	11-Feb-27

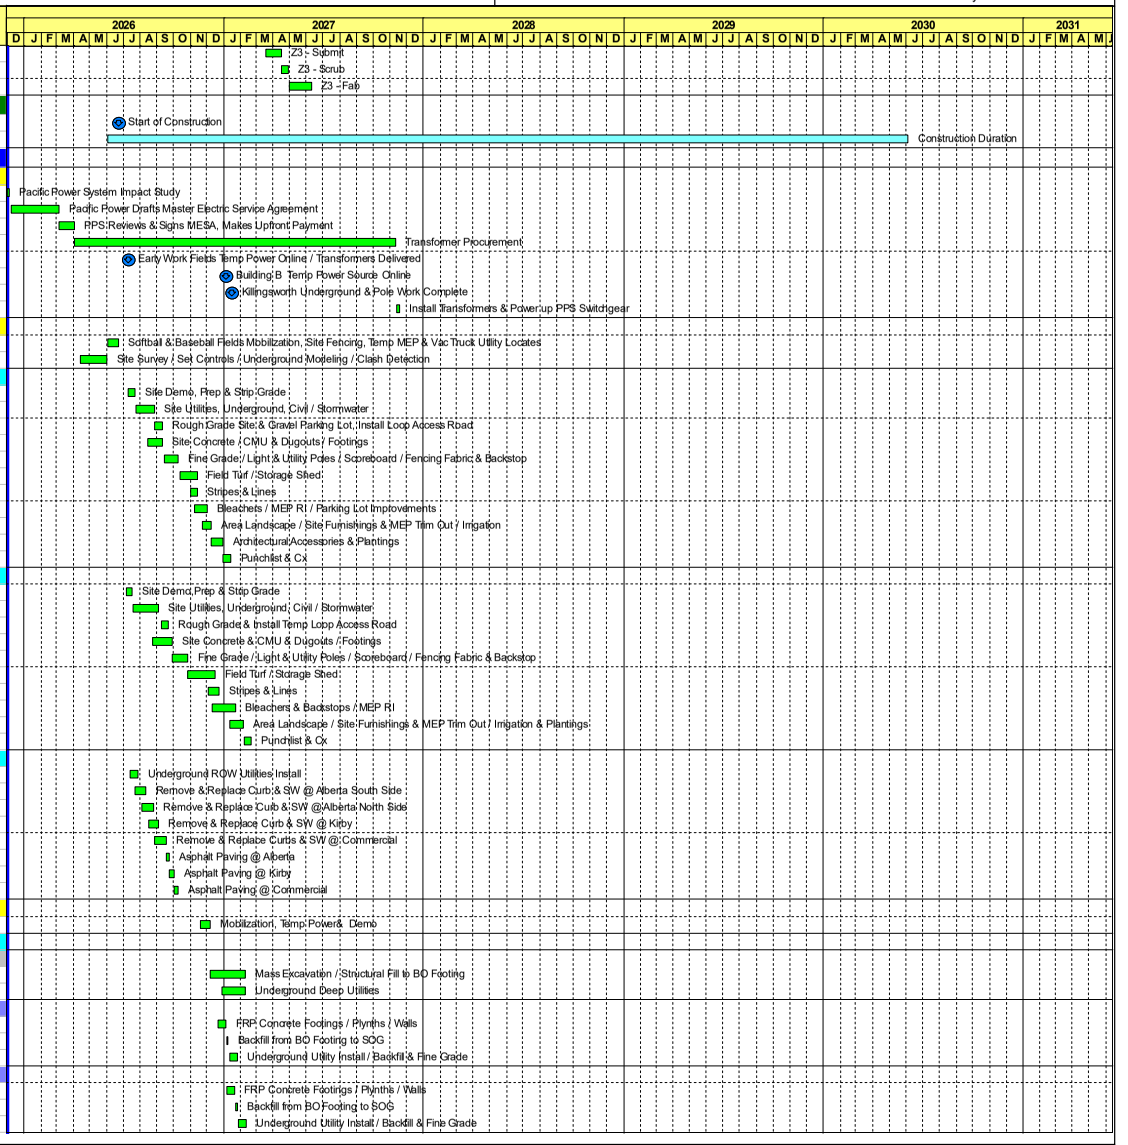


Remaining Level of Effort | Actual Work | Critical Remaining Work

Actual Level of Effort | Remaining Work | Meeting Milestone

Jefferson High School 1.6.26 - Delay L3 L4

Activity ID	Activity Name	Orig Dur	Remaining Duration	Start	Finish
Area 3		23	23	22-Jan-27	23-Feb-27
30300	FRP Concrete Footings / Plynths / Walls	10	10	22-Jan-27	04-Feb-27
30310	Backfill from BO Footing to SOG	3	3	05-Feb-27	09-Feb-27
30320	Underground Utility Install / Backfill & Fine Grade	10	10	10-Feb-27	23-Feb-27
Area 4		23	23	05-Feb-27	09-Mar-27
30400	FRP Concrete Footings / Plynths / Walls	10	10	05-Feb-27	18-Feb-27
30410	Backfill from BO Footing to SOG	3	3	19-Feb-27	23-Feb-27
30420	Underground Utility Install / Backfill & Fine Grade	10	10	24-Feb-27	09-Mar-27
Area 5		27	27	19-Feb-27	29-Mar-27
30500	FRP Concrete Footings / Plynths / Walls	12	12	19-Feb-27	08-Mar-27
30510	Backfill from BO Footing to SOG	3	3	09-Mar-27	11-Mar-27
30520	Underground Utility Install / Backfill & Fine Grade	12	12	12-Mar-27	29-Mar-27
Slab on Grade		58	58	27-Jan-27	16-Apr-27
Area 1 & 1A		14	14	27-Jan-27	15-Feb-27
31100	Vapor Barrier	2	2	27-Jan-27	28-Jan-27
31110	FRP SOG	12	12	29-Jan-27	15-Feb-27
Area 2		14	14	12-Feb-27	03-Mar-27
31200	Vapor Barrier	2	2	12-Feb-27	15-Feb-27
31210	FRP SOG	12	12	16-Feb-27	03-Mar-27
Area 3		14	14	24-Feb-27	15-Mar-27
31300	Vapor Barrier	2	2	24-Feb-27	25-Feb-27
31310	FRP SOG	12	12	26-Feb-27	15-Mar-27
Area 4		14	14	10-Mar-27	29-Mar-27
31400	Vapor Barrier	2	2	10-Mar-27	11-Mar-27
31410	FRP SOG	12	12	12-Mar-27	29-Mar-27
Area 5		14	14	30-Mar-27	16-Apr-27
31500	Vapor Barrier	2	2	30-Mar-27	31-Mar-27
31510	FRP SOG	12	12	01-Apr-27	16-Apr-27
Structure		149	149	12-Apr-27	09-Nov-27
Steel Zones 1A & 1B Floors 1-3		27	27	12-Apr-27	18-May-27
32010	Erect Columns & Beams	10	10	12-Apr-27	23-Apr-27
32020	Bolt / Weld / Plumb	5	5	26-Apr-27	30-Apr-27
32030	Edge Deck / Studs	5	5	03-May-27	07-May-27
32040	MEP Deck Rough-in	2	2	10-May-27	11-May-27
32050	FRP SOMD	5	5	12-May-27	18-May-27
32070	Set Brace Frames within Wood Zone 1	5	5	26-Apr-27	30-Apr-27
Mass Timber Zone 1 Floors 1-3		20	20	03-May-27	28-May-27
32060	Set Wood Columns & DLT Deck Floors 1-3	15	15	03-May-27	21-May-27
32080	Plumb & Complete Final Connections	5	5	24-May-27	28-May-27
Steel Zones 1A & 1B Floors 3-Roof		31	31	01-Jun-27	14-Jul-27
32100	Erect Columns & Beams	10	10	01-Jun-27	14-Jun-27
32110	Bolt / Weld / Plumb	5	5	15-Jun-27	21-Jun-27
32120	Edge Deck / Studs	5	5	22-Jun-27	28-Jun-27
32130	MEP Deck Rough-in	6	6	29-Jun-27	07-Jul-27
32140	FRP SOMD	5	5	08-Jul-27	14-Jul-27
32150	Set Brace Frames within Wood Zone 1	5	5	15-Jun-27	21-Jun-27
Mass Timber Zone 1 Floors 3-Roof		20	20	22-Jun-27	20-Jul-27
32160	Set Wood Columns & DLT Deck Floors 3-Roof	15	15	22-Jun-27	13-Jul-27
32170	Plumb & Complete Final Connections	5	5	14-Jul-27	20-Jul-27
Steel Zone 2 Floors 1-3		26	26	21-Jul-27	25-Aug-27
32200	Erect Columns & Beams	5	5	21-Jul-27	27-Jul-27
32210	Bolt / Weld / Plumb	5	5	28-Jul-27	03-Aug-27
32220	Edge Deck / Studs	5	5	04-Aug-27	10-Aug-27
32230	MEP Deck Rough-in	6	6	11-Aug-27	18-Aug-27
32240	FRP SOMD	5	5	19-Aug-27	25-Aug-27
32250	Set Brace Frames within Wood Zone 2	5	5	28-Jul-27	03-Aug-27
Mass Timber Zone 2 Floors 1-3		31	31	04-Aug-27	16-Sep-27
32260	Set Wood Columns & DLT Deck Floors 1-3	26	26	04-Aug-27	09-Sep-27
32270	Plumb & Complete Final Connections	5	5	10-Sep-27	16-Sep-27
Steel Zone 2 Floors 3-Roof		26	26	17-Sep-27	22-Oct-27
32300	Erect Columns & Beams	5	5	17-Sep-27	23-Sep-27
32310	Bolt / Weld / Plumb	5	5	24-Sep-27	30-Sep-27
32320	Edge Deck / Studs	5	5	01-Oct-27	07-Oct-27
32330	MEP Deck Rough-in	6	6	08-Oct-27	15-Oct-27
32340	FRP SOMD	5	5	18-Oct-27	22-Oct-27
32350	Set Brace Frames within Wood Zone 2	5	5	24-Sep-27	30-Sep-27

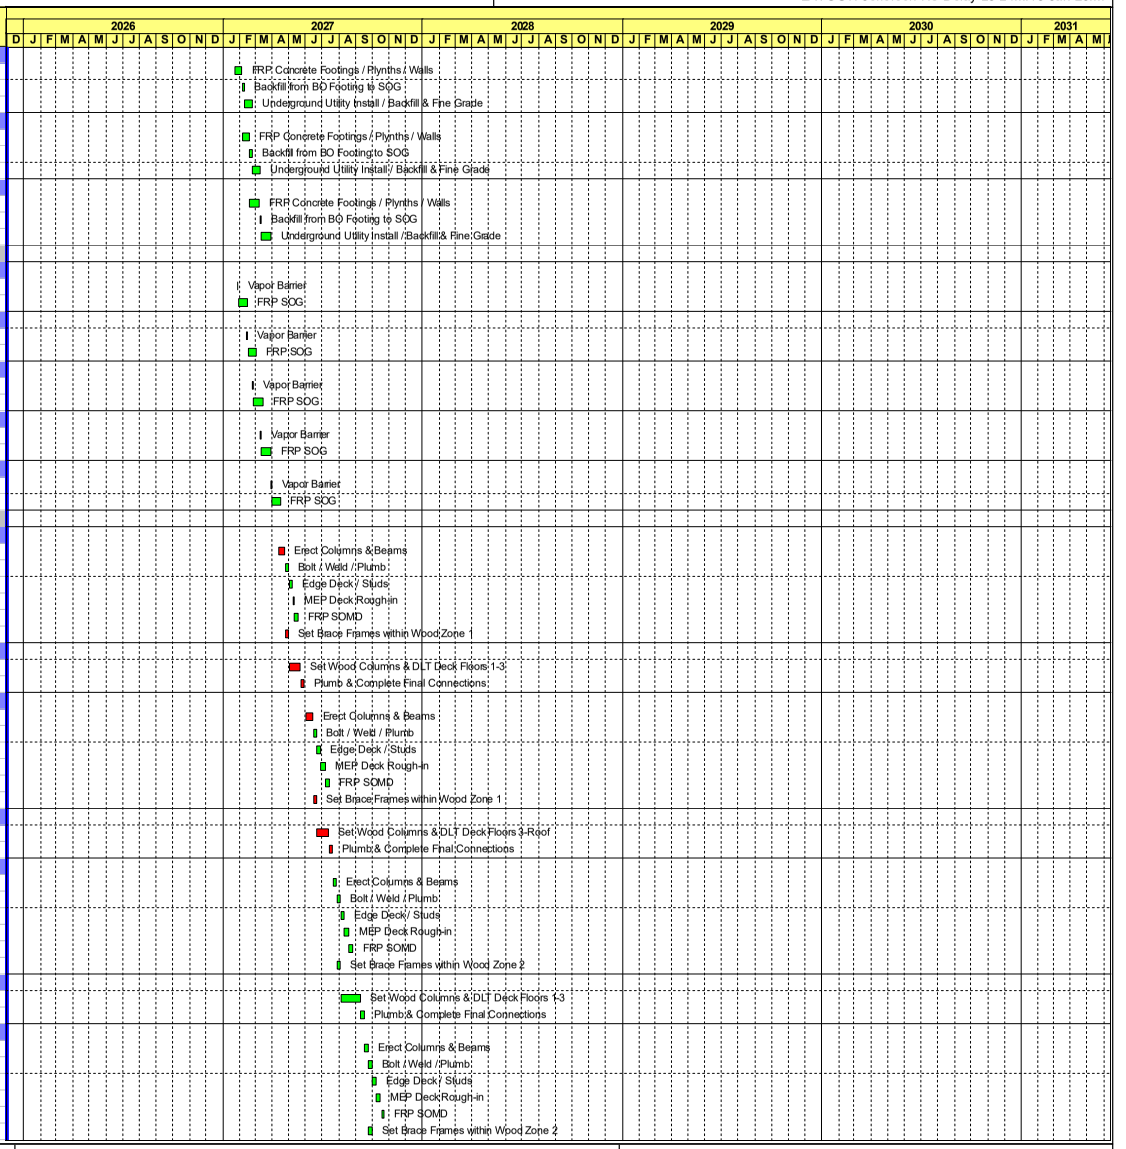


Remaining Level of Effort | Actual Work | Critical Remaining Work
Actual Level of Effort | Remaining Work | Meeting Milestone

Jefferson High School 1.6.26 - Delay L3 L4

Jefferson High-1

LAYOUT: Jefferson HS Delay L3 L4....13-Jan-26....

Activity ID	Activity Name	Orig Dur	Remaining Duration	Start	Finish
Mass Timber Zone 2 Floor 3-Roof		28	28	01-Oct-27	09-Nov-27
32360	Set Wood Columns & DLT Deck Floors 1-3	23	23	01-Oct-27	02-Nov-27
32370	Plumb & Complete Final Connections	5	5	02-Nov-27	09-Nov-27
Steel Zone 3Roof Deck		11	11	01-Oct-27	15-Oct-27
32400	Erect Columns & Beams	3	3	01-Oct-27	05-Oct-27
32410	Bolt / Weld / Plumb	2	2	06-Oct-27	07-Oct-27
32420	Edge Deck / Studs	2	2	08-Oct-27	11-Oct-27
32430	MEP Deck Rough-in	1	1	12-Oct-27	12-Oct-27
32440	FRP SOMD	3	3	13-Oct-27	15-Oct-27
Mass Timber Zone 3 Floors 1-Roof		8	8	18-Oct-27	27-Oct-27
32460	Set Wood Columns & DLT Deck Floors 1-3	6	6	18-Oct-27	25-Oct-27
32470	Plumb & Complete Final Connections	2	2	26-Oct-27	27-Oct-27
Roof		184	184	21-Jul-27	10-Apr-28
RF33000	Roof Area 1 - Parapet Framing	5	5	21-Jul-27	27-Jul-27
RF33010	Roof Area 1 - Temp Roof	20	20	28-Jul-27	24-Aug-27
RF33020	Roof Area 1 - Roof	80	80	18-Aug-27	10-Dec-27
RF33030	Roof Area 2 - Parapet Framing	5	5	09-Nov-27	16-Nov-27
RF33040	Roof Area 2 - Temp Roof	20	20	16-Nov-27	16-Dec-27
RF33050	Roof Area 2 - Roof	80	80	09-Dec-27	03-Apr-28
RF33060	Roof Area 3 - Parapet Framing	5	5	16-Nov-27	23-Nov-27
RF33070	Roof Area 3 - Temp Roof	20	20	23-Nov-27	23-Dec-27
RF33080	Roof Area 3 - Roof	80	80	16-Dec-27	10-Apr-28
Facade		262	262	21-Jul-27	31-Jul-28
Fac34000	Facade 1 - Curb / Layout	7	7	11-Aug-27	19-Aug-27
Fac34010	Facade 1 - Exterior Panels	7	7	20-Aug-27	30-Aug-27
Fac34020	Facade 1 - WB Repair	7	7	31-Aug-27	09-Sep-27
Fac34030	Facade 1 - Install Windows	7	7	10-Sep-27	20-Sep-27
Fac34040	Facade 1 - "Z" Framing	14	14	21-Sep-27	08-Oct-27
Fac34050	Facade 1 - Metal Shrouds	14	14	11-Oct-27	28-Oct-27
Fac34060	Facade 1 - Insulation	14	14	29-Oct-27	17-Nov-27
Fac34070	Facade 1 - Hat Framing	14	14	18-Nov-27	09-Dec-27
Fac34080	Facade 1 - Metal Panel / Masonry	14	14	10-Dec-27	30-Dec-27
Fac34090	Facade 1 - Clean	5	5	03-Jan-28	07-Jan-28
Fac34095	Facade 1 - Pre-Punch & Quality Check	15	15	10-Jan-28	28-Jan-28
Fac34100	Mass Timber QC	15	15	21-Jul-27	10-Aug-27
Fac34110	Facade 2 - Curb / Layout	7	7	20-Aug-27	30-Aug-27
Fac34120	Facade 2 - Exterior Panels	7	7	31-Aug-27	09-Sep-27
Fac34130	Facade 2 - WB Repair	7	7	10-Sep-27	20-Sep-27
Fac34140	Facade 2 - Install Windows	7	7	21-Sep-27	29-Sep-27
Fac34150	Facade 2 - "Z" Framing	14	14	11-Oct-27	28-Oct-27
Fac34160	Facade 2 - Metal Shrouds	14	14	29-Oct-27	17-Nov-27
Fac34170	Facade 2 - Insulation	14	14	18-Nov-27	09-Dec-27
Fac34180	Facade 2 - Hat Framing	14	14	10-Dec-27	30-Dec-27
Fac34190	Facade 2 - Metal Panel / Masonry	14	14	03-Jan-28	20-Jan-28
Fac34200	Facade 2 - Clean	5	5	21-Jan-28	27-Jan-28
Fac34205	Facade 2 - Pre-Punch & Quality Check	15	15	28-Jan-28	17-Feb-28
Fac34210	Facade 3 - Curb / Layout	7	7	23-Dec-27	05-Jan-28
Fac34220	Facade 3 - Exterior Panels	7	7	05-Jan-28	14-Jan-28
Fac34230	Facade 3 - WB Repair	7	7	14-Jan-28	25-Jan-28
Fac34240	Facade 3 - Install Windows	7	7	25-Jan-28	03-Feb-28
Fac34250	Facade 3 - "Z" Framing	14	14	03-Feb-28	23-Feb-28
Fac34260	Facade 3 - Metal Shrouds	14	14	23-Feb-28	14-Mar-28
Fac34270	Facade 3 - Insulation	14	14	14-Mar-28	03-Apr-28
Fac34280	Facade 3 - Hat Framing	14	14	03-Apr-28	21-Apr-28
Fac34290	Facade 3 - Metal Panel / Masonry	14	14	21-Apr-28	11-May-28
Fac34300	Facade 3 - Clean	5	5	11-May-28	18-May-28
Fac34305	Facade 3 - Pre-Punch & Quality Check	15	15	18-May-28	09-Jun-28
Fac34310	Facade 4 - Curb / Layout	7	7	05-Jan-28	14-Jan-28
Fac34320	Facade 4 - Exterior Panels	7	7	14-Jan-28	25-Jan-28
Fac34330	Facade 4 - WB Repair	7	7	25-Jan-28	03-Feb-28
Fac34340	Facade 4 - Install Windows	7	7	03-Feb-28	14-Feb-28
Fac34350	Facade 4 - "Z" Framing	14	14	14-Feb-28	03-Mar-28
Fac34360	Facade 4 - Metal Shrouds	14	14	03-Mar-28	23-Mar-28
Fac34370	Facade 4 - Insulation	14	14	23-Mar-28	12-Apr-28
Fac34380	Facade 4 - Hat Framing	14	14	12-Apr-28	02-May-28
Fac34390	Facade 4 - Metal Panel / Masonry	14	14	02-May-28	22-May-28

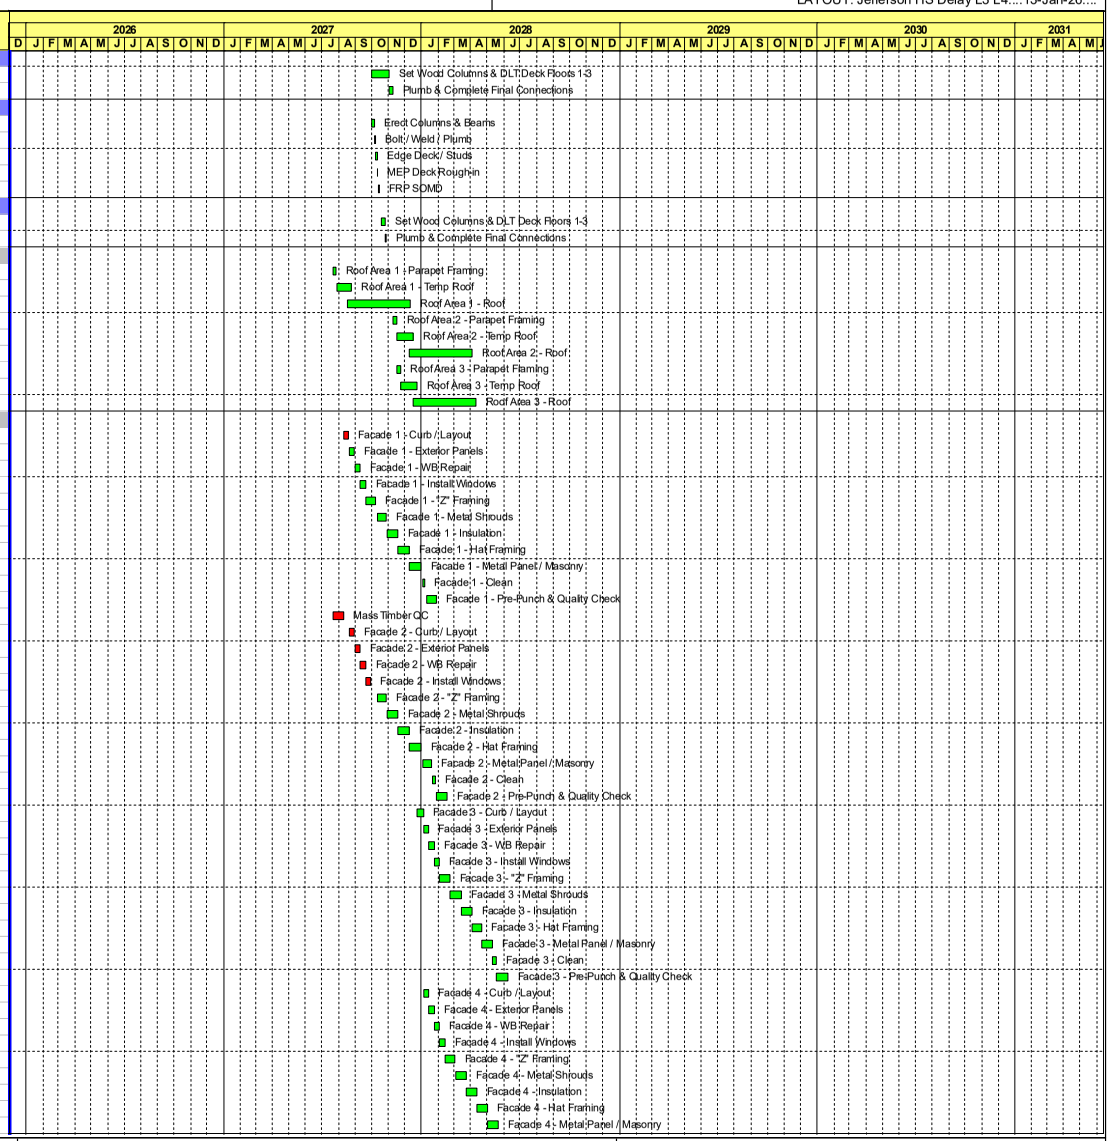

Remaining Level of Effort | Actual Work | Critical Remaining Work
Actual Level of Effort | Remaining Work | Meeting Milestone


Jefferson High School 1.6.26 - Delay L3 L4

data date :01-Dec-25 Page 7 of 19 TASK filter: <100%.

Jefferson High-1

LAYOUT: Jefferson HS Delay L3 L4....13-Jan-26....

Activity ID	Activity Name	Orig Dur	Remaining Duration	Start	Finish
Fac34400	Facade 4 - Clean	5	5	22-May-28	30-May-28
Fac34405	Facade 4 - Pre-Punch & Quality Check	15	15	30-May-28	20-Jun-28
Fac34410	Facade 5 - Curb / Layout	7	7	14-Jan-28	25-Jan-28
Fac34420	Facade 5 - Exterior Panels	7	7	25-Jan-28	03-Feb-28
Fac34430	Facade 5 - WB Repair	7	7	03-Feb-28	14-Feb-28
Fac34440	Facade 5 - Install Windows	7	7	14-Feb-28	23-Feb-28
Fac34450	Facade 5 - "Z" Framing	14	14	03-Mar-28	23-Mar-28
Fac34460	Facade 5 - Metal Shrouds	14	14	23-Mar-28	12-Apr-28
Fac34470	Facade 5 - Insulation	14	14	12-Apr-28	02-May-28
Fac34480	Facade 5 - Hat Framing	14	14	02-May-28	22-May-28
Fac34490	Facade 5 - Metal Panel / Masonry	14	14	22-May-28	12-Jun-28
Fac34500	Facade 5 - Clean	5	5	12-Jun-28	19-Jun-28
Fac34505	Facade 5 - Pre-Punch & Quality Check	15	15	19-Jun-28	11-Jul-28
Fac34510	Facade 6 - Curb / Layout	7	7	25-Jan-28	03-Feb-28
Fac34520	Facade 6 - Exterior Panels	7	7	03-Feb-28	14-Feb-28
Fac34530	Facade 6 - WB Repair	7	7	14-Feb-28	23-Feb-28
Fac34540	Facade 6 - Install Windows	7	7	23-Feb-28	03-Mar-28
Fac34550	Facade 6 - "Z" Framing	14	14	23-Mar-28	12-Apr-28
Fac34560	Facade 6 - Metal Shrouds	14	14	12-Apr-28	02-May-28
Fac34570	Facade 6 - Insulation	14	14	02-May-28	22-May-28
Fac34580	Facade 6 - Hat Framing	14	14	22-May-28	12-Jun-28
Fac34590	Facade 6 - Metal Panel / Masonry	14	14	12-Jun-28	30-Jun-28
Fac34600	Facade 6 - Clean	5	5	30-Jun-28	10-Jul-28
Fac34605	Facade 6 - Pre-Punch & Quality Check	15	15	10-Jul-28	31-Jul-28
Interior Buildout		678	678	30-Sep-27	04-Jun-30
Level 1		238	238	30-Sep-27	06-Sep-28
Area A - Staff & Child Care		200	200	30-Sep-27	13-Jul-28
B10000	L1A- Shaft Duct & Pipe	10	10	30-Sep-27	13-Oct-27
B10010	L1A- Priority Walls	7	7	14-Oct-27	22-Oct-27
B10020	L1A- OH RI Prior to Framing	7	7	25-Oct-27	02-Nov-27
B10030	L1A- Framing	7	7	03-Nov-27	11-Nov-27
B10040	L1A- Wall Rough-in	7	7	12-Nov-27	22-Nov-27
B10050	L1A- Top Rock	7	7	23-Nov-27	03-Dec-27
B10060	L1A - OH RI High (Fire Protection, Classroom Elec Rough-in)	7	7	06-Dec-27	14-Dec-27
B10070	L1A- OH RI High (Plumbing, Core Elec RI)	7	7	06-Dec-27	14-Dec-27
B10080	L1A- OH RI Mid (Hydronic, Refer, Gas, Elec-Corridor, Plmbg Insul)	7	7	15-Dec-27	23-Dec-27
B10090	L1A- OH RI Low (Duct, Elec FA, Lighting Cont., LV, Hyd Insul, FA, LC)	7	7	27-Dec-27	05-Jan-28
B10100	L1A- Soffits / HL	5	5	06-Jan-28	12-Jan-28
B10110	L1A- Pickup Work	6	6	13-Jan-28	20-Jan-28
B10120	L1A- Cover & Stock	3	3	21-Jan-28	25-Jan-28
B10130	L1A- Drywall & Insulation	7	7	26-Jan-28	03-Feb-28
B10140	L1A- MT Finish Treatment	7	7	04-Feb-28	14-Feb-28
B10150	L1A- Taping	7	7	15-Feb-28	23-Feb-28
B10160	L1A- Paint	7	7	24-Feb-28	03-Mar-28
B10170	L1A- Resinous Flooring	5	5	06-Mar-28	10-Mar-28
B10180	L1A- Pull LV Wire	7	7	06-Mar-28	14-Mar-28
B10190	L1A- Bathroom Tile	5	5	15-Mar-28	21-Mar-28
B10200	L1A- T-Bar Device Tile	7	7	15-Mar-28	23-Mar-28
B10210	L1A- Ceiling Trim MEP	7	7	24-Mar-28	03-Apr-28
B10220	L1A- Casework	7	7	24-Mar-28	03-Apr-28
B10230	L1A- Flooring	7	7	04-Apr-28	12-Apr-28
B10240	L1A- MEP Fixtures & Trim	7	7	13-Apr-28	21-Apr-28
B10250	L1A- Doors / Hardware	5	5	13-Apr-28	19-Apr-28
B10260	L1A- ACT	7	7	24-Apr-28	02-May-28
B10270	L1A- Specialties	20	20	03-May-28	31-May-28
B10280	L1A- Specialy MEP Trim	5	5	01-Jun-28	07-Jun-28
B10290	L1A- Final Clean	5	5	08-Jun-28	14-Jun-28
B10300	L1A- Cx Tile	5	5	15-Jun-28	21-Jun-28
B10310	L1A- Pre-Punch	15	15	22-Jun-28	13-Jul-28
Area S - Servery & Bathrooms		200	200	14-Oct-27	27-Jul-28
B11000	L1S - Shaft Duct & Pipe	10	10	14-Oct-27	27-Oct-27
B11010	L1S - Priority Walls	7	7	28-Oct-27	05-Nov-27
B11020	L1S - OH RI Prior to Framing	7	7	08-Nov-27	16-Nov-27
B11030	L1S - Framing	7	7	17-Nov-27	29-Nov-27
B11040	L1S - Wall Rough-in	7	7	30-Nov-27	08-Dec-27
B11050	L1S - Top Rock	7	7	09-Dec-27	17-Dec-27

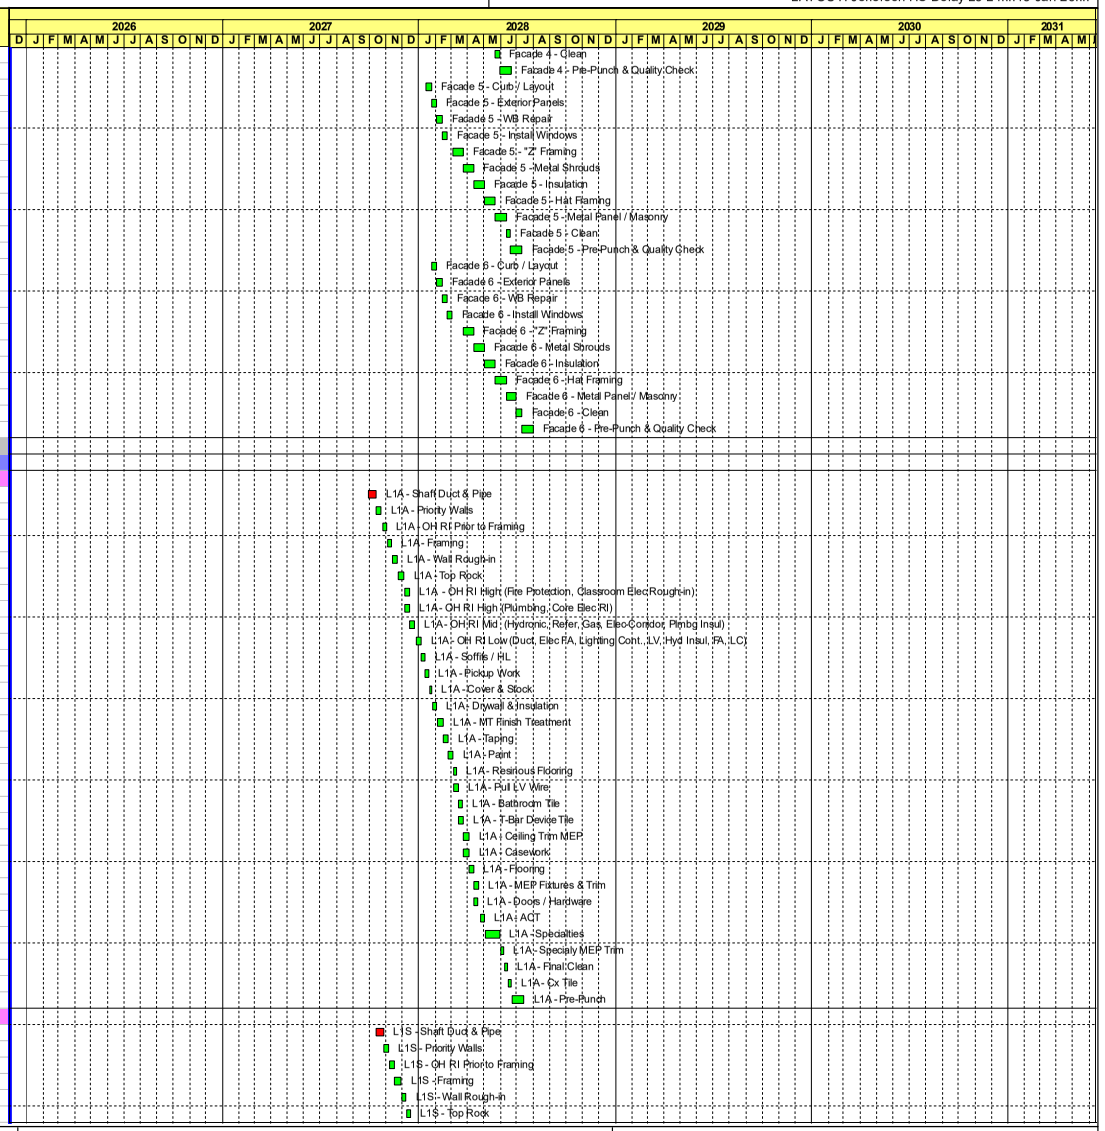


Remaining Level of Effort | Actual Work | Critical Remaining Work | Actual Level of Effort | Remaining Work | Meeting Milestone

Jefferson High School 1.6.26 - Delay L3 L4

data date :01-Dec-25 Page 8 of 19 TASK filter: <100%.

Activity ID	Activity Name	Orig Dur	Remaining Duration	Start	Finish
B11060	L1S - OH RI High (Fire Protection, Classroom Elec Rough-in)	7	7	20-Dec-27	29-Dec-27
B11070	L1S - OH RI High (Plumbing, Core Elec RI)	7	7	20-Dec-27	29-Dec-27
B11080	L1S - OH RI Mid (Hydronic, Refer, Gas, Elec-Corridor, Plmbg Insul)	7	7	30-Dec-27	10-Jan-28
B11090	L1S - OH RI Low (Duct, Elec FA, Lighting Cont., LV, Hyd Insul, FA, LC)	7	7	11-Jan-28	19-Jan-28
B11100	L1S - Soffits / HL	5	5	20-Jan-28	26-Jan-28
B11110	L1S - Pickup Work	6	6	27-Jan-28	03-Feb-28
B11120	L1S - Cover & Stock	3	3	04-Feb-28	08-Feb-28
B11130	L1S - Drywall & Insulation	7	7	09-Feb-28	17-Feb-28
B11140	L1S - MT Finish Treatment	7	7	18-Feb-28	28-Feb-28
B11150	L1S - Taping	7	7	29-Feb-28	08-Mar-28
B11160	L1S - Paint	7	7	09-Mar-28	17-Mar-28
B11170	L1S - Resinous Flooring	5	5	20-Mar-28	24-Mar-28
B11180	L1S - Pull LV Wire	7	7	20-Mar-28	28-Mar-28
B11190	L1S - Bathroom Tile	5	5	29-Mar-28	04-Apr-28
B11200	L1S - TBar Device Tile	7	7	29-Mar-28	06-Apr-28
B11210	L1S - Ceiling Trim MEP	7	7	07-Apr-28	17-Apr-28
B11220	L1S - Casework	7	7	07-Apr-28	17-Apr-28
B11230	L1S - Flooring	7	7	18-Apr-28	26-Apr-28
B11240	L1S - MEP Fixtures & Trim	7	7	27-Apr-28	05-May-28
B11250	L1S - Doors / Hardware	5	5	27-Apr-28	03-May-28
B11260	L1S - ACT	7	7	08-May-28	16-May-28
B11270	L1S - Specialties	20	20	17-May-28	14-Jun-28
B11280	L1S - Specialy MEP Trim	5	5	15-Jun-28	21-Jun-28
B11290	L1S - Final Clean	5	5	22-Jun-28	28-Jun-28
B11300	L1S - Cx Tile	5	5	29-Jun-28	06-Jul-28
B11305	L1S - Pre-Punch	15	15	07-Jul-28	27-Jul-28
Area B - Main Entry & Mechanical		200	200	28-Oct-27	10-Aug-28
B12000	L1B - Shaft Duct & Pipe	10	10	28-Oct-27	10-Nov-27
B12010	L1B - Set & Connect AHU 501	5	5	11-Nov-27	17-Nov-27
B12020	L1B - Priority Walls	7	7	11-Nov-27	19-Nov-27
B12030	L1B - OH RI Prior to Framing	7	7	22-Nov-27	02-Dec-27
B12040	L1B - Framing	7	7	03-Dec-27	13-Dec-27
B12050	L1B - Wall Rough-in	7	7	14-Dec-27	22-Dec-27
B12060	L1B - Top Rock	7	7	23-Dec-27	04-Jan-28
B12070	L1B - OH RI High (Fire Protection, Classroom Elec Rough-in)	7	7	05-Jan-28	13-Jan-28
B12080	L1B - OH RI High (Plumbing, Core Elec RI)	7	7	05-Jan-28	13-Jan-28
B12090	L1B - OH RI Mid (Hydronic, Refer, Gas, Elec-Corridor, Plmbg Insul)	7	7	14-Jan-28	24-Jan-28
B12100	L1B - OH RI Low (Duct, Elec FA, Lighting Cont., LV, Hyd Insul, FA, LC)	7	7	25-Jan-28	02-Feb-28
B12110	L1B - Soffits / HL	5	5	03-Feb-28	09-Feb-28
B12120	L1B - Pickup Work	6	6	10-Feb-28	17-Feb-28
B12130	L1B - Cover & Stock	3	3	18-Feb-28	22-Feb-28
B12140	L1B - Drywall & Insulation	7	7	23-Feb-28	02-Mar-28
B12150	L1B - MT Finish Treatment	7	7	03-Mar-28	13-Mar-28
B12160	L1B - Taping	7	7	14-Mar-28	22-Mar-28
B12170	L1B - Paint	7	7	23-Mar-28	31-Mar-28
B12180	L1B - Resinous Flooring	5	5	03-Apr-28	07-Apr-28
B12190	L1B - Pull LV Wire	7	7	03-Apr-28	11-Apr-28
B12200	L1B - Bathroom Tile	5	5	12-Apr-28	18-Apr-28
B12210	L1B - TBar Device Tile	7	7	12-Apr-28	20-Apr-28
B12220	L1B - Ceiling Trim MEP	7	7	21-Apr-28	01-May-28
B12230	L1B - Casework	7	7	21-Apr-28	01-May-28
B12240	L1B - Flooring	7	7	02-May-28	10-May-28
B12250	L1B - MEP Fixtures & Trim	7	7	11-May-28	19-May-28
B12260	L1B - Doors / Hardware	5	5	11-May-28	17-May-28
B12270	L1B - ACT	7	7	22-May-28	31-May-28
B12280	L1B - Specialties	20	20	01-Jun-28	28-Jun-28
B12290	L1B - Specialy MEP Trim	5	5	29-Jun-28	06-Jul-28
B12300	L1B - Final Clean	5	5	07-Jul-28	13-Jul-28
B12310	L1B - Cx Tile	5	5	14-Jul-28	20-Jul-28
B12315	L1B - Pre-Punch	15	15	21-Jul-28	10-Aug-28
Area C - Commons		208	208	11-Nov-27	06-Sep-28
B13000	L1C - Shaft Duct & Pipe	10	10	11-Nov-27	24-Nov-27
B13010	L1C - Priority Walls	7	7	29-Nov-27	07-Dec-27
B13020	L1C - OH RI Prior to Framing	7	7	08-Dec-27	16-Dec-27
B13030	L1C - Framing	7	7	17-Dec-27	28-Dec-27
B13040	L1C - Wall Rough-in	7	7	29-Dec-27	07-Jan-28

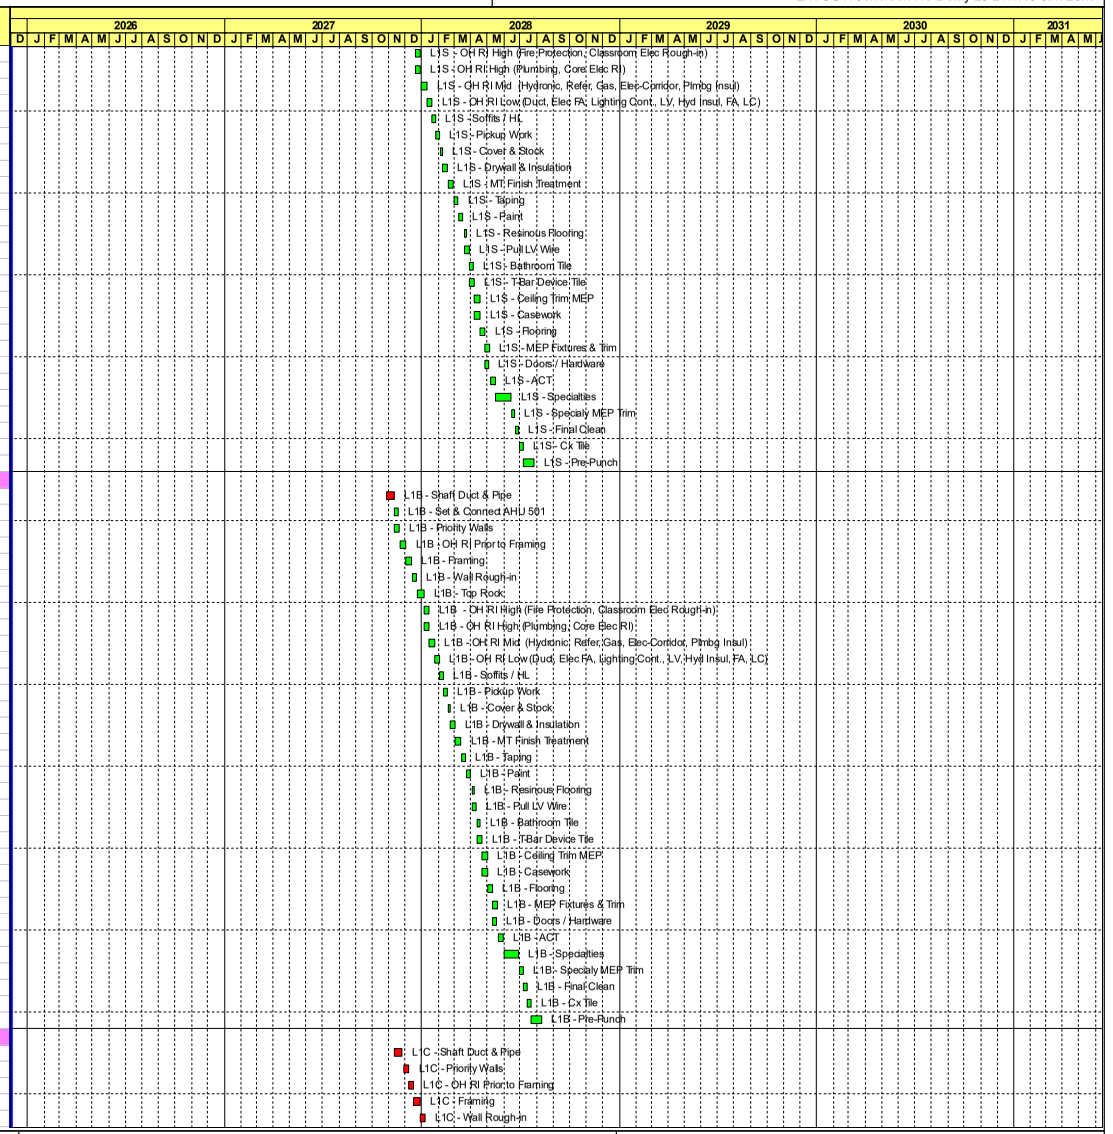

Remaining Level of Effort | Actual Work | Critical Remaining Work

Actual Level of Effort | Remaining Work | Meeting Milestone


Jefferson High School 1.6.26 - Delay L3 L4

data date :01-Dec-25 Page 9 of 19 TASK filter: <100%.

Activity ID	Activity Name	Orig Dur	Remaining Duration	Start	Finish
B13050	L1C - Top Rock	7	7	10-Jan-28	18-Jan-28
B13060	L1C - OH RI High (Fire Protection, Classroom Elec Rough-in)	7	7	19-Jan-28	27-Jan-28
B13070	L1C - OH RI High (Plumbing, Core Elec RI)	7	7	19-Jan-28	27-Jan-28
B13080	L1C - OH RI Mid (Hydronic, Refer, Gas, Elec-Corridor, Plmbg Insul)	7	7	28-Jan-28	07-Feb-28
B13090	L1C - OH RI Low (Duct, Elec FA, Lighting Cont., LV, Hyd Insul, FA, LC)	7	7	08-Feb-28	16-Feb-28
B13100	L1C - Soffits / HL	5	5	17-Feb-28	23-Feb-28
B13110	L1C - Pickup Work	6	6	24-Feb-28	02-Mar-28
B13120	L1C - Cover & Stock	3	3	03-Mar-28	07-Mar-28
B13130	L1C - Drywall & Insulation	7	7	08-Mar-28	16-Mar-28
B13140	L1C - MT Finish Treatment	7	7	17-Mar-28	27-Mar-28
B13150	L1C - Taping	7	7	28-Mar-28	05-Apr-28
B13160	L1C - Paint	7	7	06-Apr-28	14-Apr-28
B13170	L1C - Resinous Flooring	5	5	17-Apr-28	21-Apr-28
B13180	L1C - Pull LV Wire	7	7	17-Apr-28	25-Apr-28
B13190	L1C - Bathroom Tile	5	5	26-Apr-28	02-May-28
B13200	L1C - T-Bar Device Tile	7	7	26-Apr-28	04-May-28
B13210	L1C - Ceiling Trim MEP	7	7	05-May-28	15-May-28
B13220	L1C - Casework	7	7	05-May-28	15-May-28
B13230	L1C - Flooring	15	15	16-May-28	06-Jun-28
B13240	L1C - MEP Fixtures & Trim	7	7	07-Jun-28	15-Jun-28
B13250	L1C - Doors / Hardware	5	5	07-Jun-28	13-Jun-28
B13260	L1C - ACT	7	7	16-Jun-28	26-Jun-28
B13270	L1C - Specialties	20	20	27-Jun-28	25-Jul-28
B13280	L1C - Specialy MEP Trim	5	5	26-Jul-28	01-Aug-28
B13290	L1C - Final Clean	5	5	02-Aug-28	08-Aug-28
B13300	L1C - Cx Tile	5	5	09-Aug-28	15-Aug-28
B13305	L1C - Pre-Punch	15	15	16-Aug-28	06-Sep-28
Level 2		218	218	29-Nov-27	04-Oct-28
Area GC - General Classrooms		208	208	29-Nov-27	20-Sep-28
B20000	L2GC - Shaft Duct & Pipe	10	10	29-Nov-27	10-Dec-27
B20010	L2GC - Priority Walls	7	7	13-Dec-27	21-Dec-27
B20020	L2GC - OH RI Prior to Framing	7	7	22-Dec-27	03-Jan-28
B20030	L2GC - Framing	7	7	04-Jan-28	12-Jan-28
B20040	L2GC - Wall Rough-in	7	7	13-Jan-28	21-Jan-28
B20050	L2GC - Top Rock	7	7	24-Jan-28	01-Feb-28
B20060	L2GC - OH RI High (Fire Protection, Classroom Elec Rough-in)	7	7	02-Feb-28	10-Feb-28
B20070	L2GC - OH RI High (Plumbing, Core Elec RI)	7	7	02-Feb-28	10-Feb-28
B20080	L2GC - OH RI Mid (Hydronic, Refer, Gas, Elec-Corridor, Plmbg Insul)	7	7	11-Feb-28	21-Feb-28
B20090	L2GC - OH RI Low (Duct, Elec FA, Lighting Cont., LV, Hyd Insul, FA, LC)	7	7	22-Feb-28	01-Mar-28
B20100	L2GC - Soffits / HL	5	5	02-Mar-28	08-Mar-28
B20110	L2GC - Pickup Work	6	6	09-Mar-28	16-Mar-28
B20120	L2GC - Cover & Stock	3	3	17-Mar-28	21-Mar-28
B20130	L2GC - Drywall & Insulation	7	7	22-Mar-28	30-Mar-28
B20140	L2GC - MT Finish Treatment	7	7	31-Mar-28	10-Apr-28
B20150	L2GC - Gypcrete	7	7	31-Mar-28	10-Apr-28
B20160	L2GC - Taping	7	7	11-Apr-28	19-Apr-28
B20170	L2GC - Paint	7	7	20-Apr-28	28-Apr-28
B20180	L2GC - Resinous Flooring	5	5	01-May-28	05-May-28
B20190	L2GC - Pull LV Wire	7	7	01-May-28	09-May-28
B20200	L2GC - Bathroom Tile	5	5	10-May-28	16-May-28
B20210	L2GC - T-Bar Device Tile	7	7	10-May-28	18-May-28
B20220	L2GC - Ceiling Trim MEP	7	7	19-May-28	30-May-28
B20230	L2GC - Casework	7	7	19-May-28	30-May-28
B20240	L2GC - Flooring	7	7	31-May-28	08-Jun-28
B20250	L2GC - MEP Fixtures & Trim	7	7	09-Jun-28	19-Jun-28
B20260	L2GC - Doors / Hardware	5	5	09-Jun-28	15-Jun-28
B20270	L2GC - ACT	7	7	20-Jun-28	28-Jun-28
B20280	L2GC - Specialties	20	20	29-Jun-28	27-Jul-28
B20290	L2GC - Specialy MEP Trim	5	5	28-Jul-28	03-Aug-28
B20300	L2GC - Final Clean	5	5	04-Aug-28	10-Aug-28
B20310	L2GC - Cx Tile	5	5	16-Aug-28	22-Aug-28
B20315	L2GC - Pre-Punch	15	15	30-Aug-28	20-Sep-28
Area B - General Classrooms & Suppor		208	208	13-Dec-27	04-Oct-28
B21000	L2B - Shaft Duct & Pipe	10	10	13-Dec-27	27-Dec-27
B21010	L2B - Priority Walls	7	7	28-Dec-27	06-Jan-28
B21020	L2B - OH RI Prior to Framing	7	7	07-Jan-28	17-Jan-28




Activity ID	Activity Name	Orig Dur	Remaining Duration	Start	Finish
B21030	L2B - Framing	7	7	18-Jan-28	26-Jan-28
B21040	L2B - Wall Rough-in	7	7	27-Jan-28	04-Feb-28
B21050	L2B - Top Rock	7	7	07-Feb-28	15-Feb-28
B21060	L2B - OH RI High (Fire Protection, Classroom Elec Rough-in)	7	7	16-Feb-28	24-Feb-28
B21070	L2B - OH RI High (Plumbing, Core Elec RI)	7	7	16-Feb-28	24-Feb-28
B21080	L2B - OH RI Mid (Hydronic, Refer, Gas, Elec-Corridor, Plmbg Insul)	7	7	25-Feb-28	06-Mar-28
B21090	L2B - OH RI Low (Duct, Elec FA, Lighting Cont., LV, Hyd Insul, FA, LC)	7	7	07-Mar-28	15-Mar-28
B21100	L2B - Soffits / HL	5	5	16-Mar-28	22-Mar-28
B21110	L2B - Pickup Work	6	6	23-Mar-28	30-Mar-28
B21120	L2B - Cover & Stock	3	3	31-Mar-28	04-Apr-28
B21130	L2B - Drywall & Insulation	7	7	05-Apr-28	13-Apr-28
B21140	L2B - MT Finish Treatment	7	7	14-Apr-28	24-Apr-28
B21150	L2B - Gypcrete	7	7	14-Apr-28	24-Apr-28
B21160	L2B - Taping	7	7	25-Apr-28	03-May-28
B21170	L2B - Paint	7	7	04-May-28	12-May-28
B21180	L2B - Resinous Flooring	5	5	15-May-28	19-May-28
B21190	L2B - Pull LV Wire	7	7	15-May-28	23-May-28
B21200	L2B - Bathroom Tile	5	5	24-May-28	31-May-28
B21210	L2B - T-Bar Device Tile	7	7	24-May-28	02-Jun-28
B21220	L2B - Ceiling Trim MEP	7	7	05-Jun-28	13-Jun-28
B21230	L2B - Casework	7	7	05-Jun-28	13-Jun-28
B21240	L2B - Flooring	7	7	14-Jun-28	22-Jun-28
B21250	L2B - MEP Fixtures & Trim	7	7	23-Jun-28	03-Jul-28
B21260	L2B - Doors / Hardware	5	5	23-Jun-28	29-Jun-28
B21270	L2B - ACT	7	7	05-Jul-28	13-Jul-28
B21280	L2B - Specialties	20	20	14-Jul-28	10-Aug-28
B21290	L2B - Specialy MEP Trim	5	5	11-Aug-28	17-Aug-28
B21300	L2B - Final Clean	5	5	18-Aug-28	24-Aug-28
B21310	L2B - Cx Tile	5	5	25-Aug-28	31-Aug-28
B21315	L2B - Pre-Punch	15	15	14-Sep-28	04-Oct-28
Level 3		210	210	06-Jul-29	06-May-30
Area GC - General Classrooms		200	200	06-Jul-29	22-Apr-30
B30000	L3GC - Shaft Duct & Pipe	10	10	06-Jul-29	19-Jul-29
B30010	L3GC - Priority Walls	7	7	20-Jul-29	30-Jul-29
B30020	L3GC - OH RI Prior to Framing	7	7	31-Jul-29	08-Aug-29
B30030	L3GC - Framing	7	7	09-Aug-29	17-Aug-29
B30040	L3GC - Wall Rough-in	7	7	20-Aug-29	28-Aug-29
B30050	L3GC - Top Rock	7	7	29-Aug-29	07-Sep-29
B30060	L3GC - OH RI High (Fire Protection, Classroom Elec Rough-in)	7	7	10-Sep-29	18-Sep-29
B30070	L3GC - OH RI High (Plumbing, Core Elec RI)	7	7	10-Sep-29	18-Sep-29
B30080	L3GC - OH RI Mid (Hydronic, Refer, Gas, Elec-Corridor, Plmbg Insul)	7	7	19-Sep-29	27-Sep-29
B30090	L3GC - OH RI Low (Duct, Elec FA, Lighting Cont., LV, Hyd Insul, FA, LC)	7	7	28-Sep-29	08-Oct-29
B30100	L3GC - Soffits / HL	5	5	09-Oct-29	15-Oct-29
B30110	L3GC - Pickup Work	6	6	16-Oct-29	23-Oct-29
B30120	L3GC - Cover & Stock	3	3	24-Oct-29	26-Oct-29
B30130	L3GC - Drywall & Insulation	7	7	29-Oct-29	06-Nov-29
B30140	L3GC - MT Finish Treatment	7	7	07-Nov-29	15-Nov-29
B30150	L3GC - Gypcrete	7	7	07-Nov-29	15-Nov-29
B30160	L3GC - Taping	7	7	16-Nov-29	28-Nov-29
B30170	L3GC - Paint	7	7	29-Nov-29	07-Dec-29
B30180	L3GC - Resinous Flooring	5	5	10-Dec-29	14-Dec-29
B30190	L3GC - Pull LV Wire	7	7	10-Dec-29	18-Dec-29
B30200	L3GC - Bathroom Tile	5	5	19-Dec-29	27-Dec-29
B30210	L3GC - T-Bar Device Tile	7	7	19-Dec-29	02-Jan-30
B30220	L3GC - Ceiling Trim MEP	7	7	03-Jan-30	11-Jan-30
B30230	L3GC - Casework	7	7	03-Jan-30	11-Jan-30
B30240	L3GC - Flooring	7	7	14-Jan-30	22-Jan-30
B30250	L3GC - MEP Fixtures & Trim	7	7	23-Jan-30	31-Jan-30
B30260	L3GC - Doors / Hardware	5	5	23-Jan-30	29-Jan-30
B30270	L3GC - ACT	7	7	01-Feb-30	11-Feb-30
B30280	L3GC - Specialties	20	20	12-Feb-30	11-Mar-30
B30290	L3GC - Specialy MEP Trim	5	5	12-Mar-30	18-Mar-30
B30300	L3GC - Final Clean	5	5	19-Mar-30	25-Mar-30
B30310	L3GC - Cx Tile	5	5	26-Mar-30	01-Apr-30
B30315	L3GC - Pre-Punch	15	15	02-Apr-30	22-Apr-30
Area SC - Science Classrooms		200	200	20-Jul-29	06-May-30

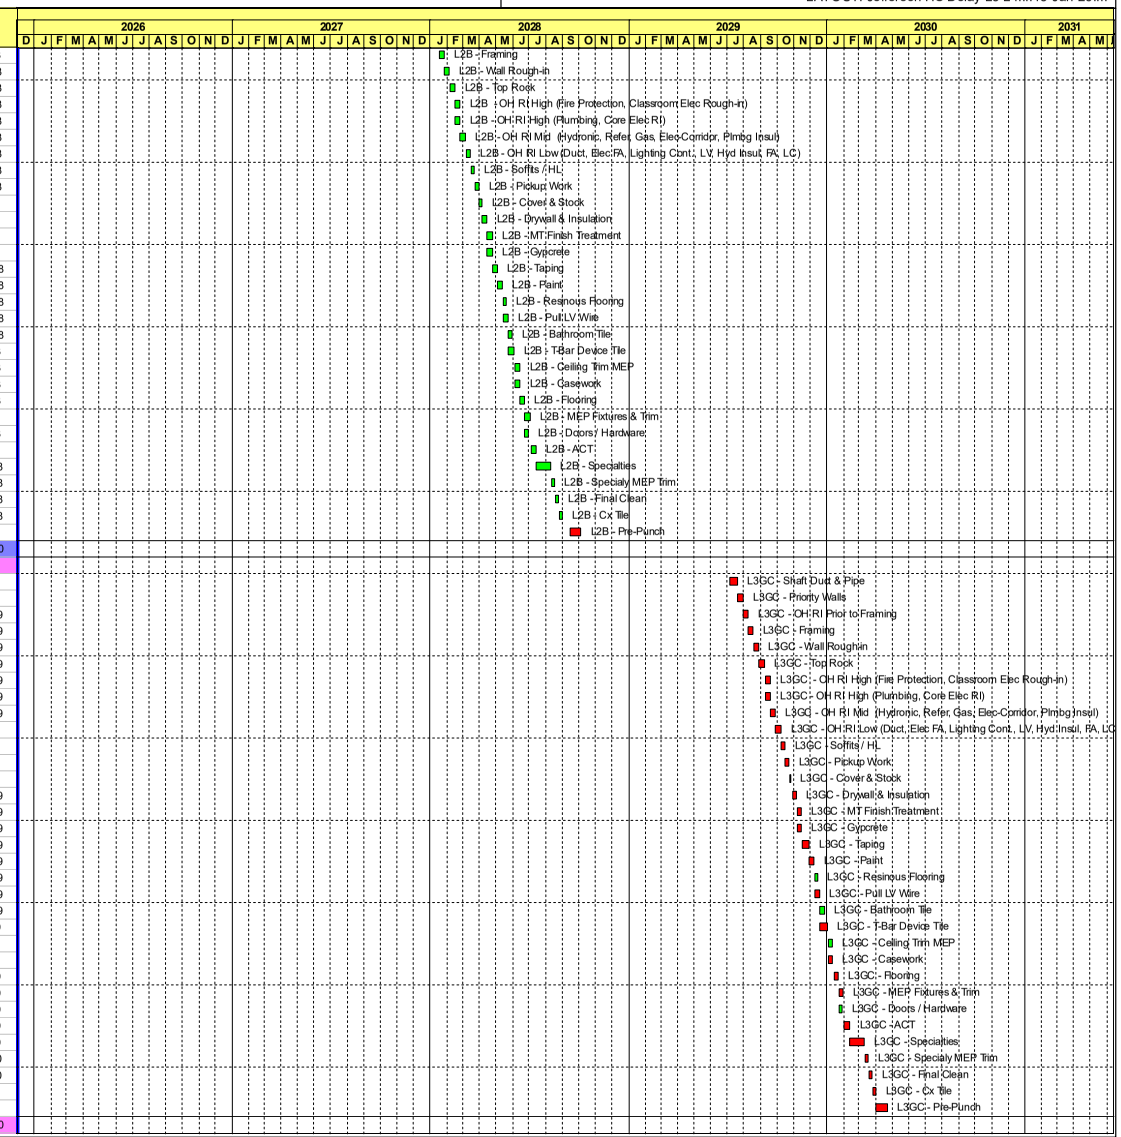

Remaining Level of Effort | Actual Work | Critical Remaining Work

Actual Level of Effort | Remaining Work | Meeting Milestone

Activity ID	Activity Name	Orig Dur	Remaining Duration	Start	Finish
B31000	L3SC - Shaft Duct & Pipe	10	10	20-Jul-29	02-Aug-29
B31010	L3SC - Priority Walls	7	7	03-Aug-29	13-Aug-29
B31020	L3SC - OH RI Prior to Framing	7	7	14-Aug-29	22-Aug-29
B31030	L3SC - Framing	7	7	23-Aug-29	31-Aug-29
B31040	L3SC - Wall Rough-in	7	7	04-Sep-29	12-Sep-29
B31050	L3SC - Top Rock	7	7	13-Sep-29	21-Sep-29
B31060	L3SC - OH RI High (Fire Protection, Classroom Elec Rough-in)	7	7	24-Sep-29	02-Oct-29
B31070	L3SC - OH RI High (Plumbing, Core Elec RI)	7	7	24-Sep-29	02-Oct-29
B31080	L3SC - OH RI Mid (Hydronic, Refer, Gas, Elec-Corridor, Plmbg Insul)	7	7	03-Oct-29	11-Oct-29
B31090	L3SC - OH RI Low (Duct, Elec FA, Lighting Cont., LV, Hyd Insul, FA, LC)	7	7	12-Oct-29	22-Oct-29
B31100	L3SC - Soffits / HL	5	5	23-Oct-29	29-Oct-29
B31110	L3SC - Pickup Work	6	6	30-Oct-29	06-Nov-29
B31120	L3SC - Cover & Stock	3	3	07-Nov-29	09-Nov-29
B31130	L3SC - Drywall & Insulation	7	7	12-Nov-29	20-Nov-29
B31140	L3SC - MT Finish Treatment	7	7	21-Nov-29	03-Dec-29
B31150	L3SC - Gypcrete	7	7	21-Nov-29	03-Dec-29
B31160	L3SC - Taping	7	7	04-Dec-29	12-Dec-29
B31170	L3SC - Paint	7	7	13-Dec-29	21-Dec-29
B31180	L3SC - Resinous Flooring	5	5	26-Dec-29	03-Jan-30
B31190	L3SC - Pull LV Wire	7	7	26-Dec-29	07-Jan-30
B31200	L3SC - Bathroom Tile	5	5	08-Jan-30	14-Jan-30
B31210	L3SC - T-Bar Device Tile	7	7	08-Jan-30	16-Jan-30
B31220	L3SC - Ceiling Trim MEP	7	7	17-Jan-30	25-Jan-30
B31230	L3SC - Casework	7	7	17-Jan-30	25-Jan-30
B31240	L3SC - Flooring	7	7	28-Jan-30	05-Feb-30
B31250	L3SC - MEP Fixtures & Trim	7	7	06-Feb-30	14-Feb-30
B31260	L3SC - Doors / Hardware	5	5	06-Feb-30	12-Feb-30
B31270	L3SC -ACT	7	7	15-Feb-30	25-Feb-30
B31280	L3SC - Specialties	20	20	26-Feb-30	25-Mar-30
B31290	L3SC - Specialy MEP Trim	5	5	26-Mar-30	01-Apr-30
B31300	L3SC - Final Clean	5	5	02-Apr-30	08-Apr-30
B31310	L3SC - Cx Tile	5	5	09-Apr-30	15-Apr-30
B31315	L3SC - Pre-Punch	15	15	16-Apr-30	06-May-30
Level 4		210	210	03-Aug-29	04-Jun-30
Area GC - General Classrooms		200	200	03-Aug-29	20-May-30
B40000	L4GC - Shaft Duct & Pipe	10	10	03-Aug-29	16-Aug-29
B40010	L4GC - Priority Walls	7	7	17-Aug-29	27-Aug-29
B40020	L4GC - OH RI Prior to Framing	7	7	28-Aug-29	06-Sep-29
B40030	L4GC - Framing	7	7	07-Sep-29	17-Sep-29
B40040	L4GC - Wall Rough-in	7	7	18-Sep-29	26-Sep-29
B40050	L4GC - Top Rock	7	7	27-Sep-29	05-Oct-29
B40060	L4GC - OH RI High (Fire Protection, Classroom Elec Rough-in)	7	7	08-Oct-29	16-Oct-29
B40070	L4GC - OH RI High (Plumbing, Core Elec RI)	7	7	08-Oct-29	16-Oct-29
B40080	L4GC - OH RI Mid (Hydronic, Refer, Gas, Elec-Corridor, Plmbg Insul)	7	7	17-Oct-29	25-Oct-29
B40090	L4GC - OH RI Low (Duct, Elec FA, Lighting Cont., LV, Hyd Insul, FA, LC)	7	7	26-Oct-29	05-Nov-29
B40100	L4GC - Soffits / HL	5	5	06-Nov-29	12-Nov-29
B40110	L4GC - Pickup Work	6	6	13-Nov-29	20-Nov-29
B40120	L4GC - Cover & Stock	3	3	21-Nov-29	27-Nov-29
B40130	L4GC - Drywall & Insulation	7	7	28-Nov-29	06-Dec-29
B40140	L4GC - MT Finish Treatment	7	7	07-Dec-29	17-Dec-29
B40150	L4GC - Gypcrete	7	7	07-Dec-29	17-Dec-29
B40160	L4GC - Taping	7	7	18-Dec-29	28-Dec-29
B40170	L4GC - Paint	7	7	02-Jan-30	10-Jan-30
B40180	L4GC - Resinous Flooring	5	5	11-Jan-30	17-Jan-30
B40190	L4GC - Pull LV Wire	7	7	11-Jan-30	21-Jan-30
B40200	L4GC - Bathroom Tile	5	5	22-Jan-30	28-Jan-30
B40210	L4GC - T-Bar Device Tile	7	7	22-Jan-30	30-Jan-30
B40220	L4GC - Ceiling Trim MEP	7	7	31-Jan-30	08-Feb-30
B40230	L4GC - Casework	7	7	31-Jan-30	08-Feb-30
B40240	L4GC - Flooring	7	7	11-Feb-30	19-Feb-30
B40250	L4GC - MEP Fixtures & Trim	7	7	20-Feb-30	28-Feb-30
B40260	L4GC - Doors / Hardware	5	5	20-Feb-30	26-Feb-30
B40270	L4GC - ACT	7	7	01-Mar-30	11-Mar-30
B40280	L4GC - Specialties	20	20	12-Mar-30	08-Apr-30
B40290	L4GC - Specialy MEP Trim	5	5	09-Apr-30	15-Apr-30
B40300	L4GC - Final Clean	5	5	16-Apr-30	22-Apr-30

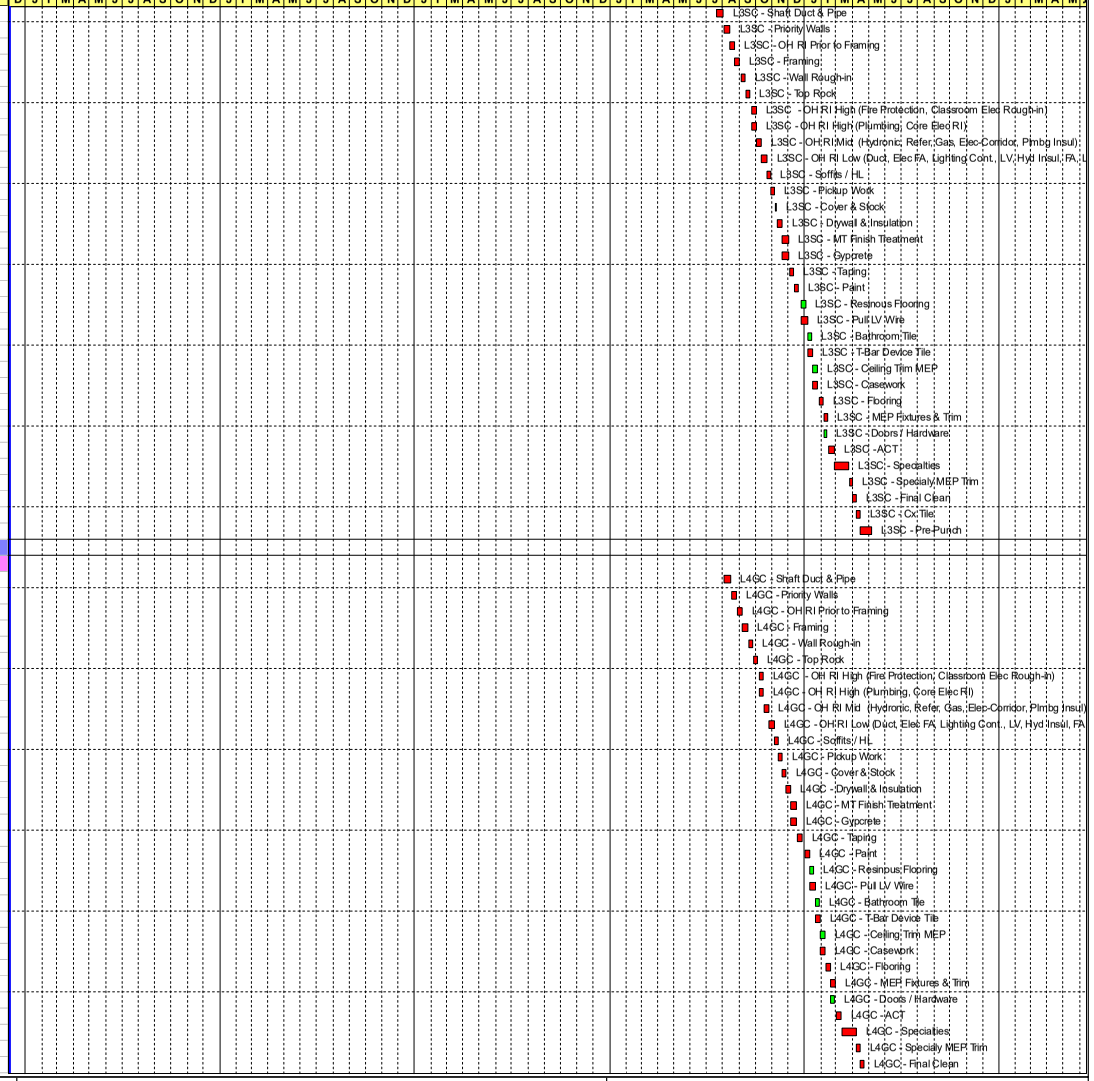


Remaining Level of Effort | Actual Work | Critical Remaining Work
Actual Level of Effort | Remaining Work | Meeting Milestone

Jefferson High School 1.6.26 - Delay L3 L4

data date :01-Dec-25 Page 12 of 19 TASK filter: <100%.


Activity ID	Activity Name	Orig Dur	Remaining Duration	Start	Finish
B40310	L4GC - Cx Tile	5	5	23-Apr-30	29-Apr-30
B40315	L4GC - Pre-Punch	15	15	30-Apr-30	20-May-30
Area SC - Science Classrooms		200	200	17-Aug-29	04-Jun-30
B41000	L4SC - Shaft Duct & Pipe	10	10	17-Aug-29	30-Aug-29
B41010	L4SC - Priority Walls	7	7	31-Aug-29	11-Sep-29
B41020	L4SC - OH RI Prior to Framing	7	7	12-Sep-29	20-Sep-29
B41030	L4SC - Framing	7	7	21-Sep-29	01-Oct-29
B41040	L4SC - Wall Rough-in	7	7	02-Oct-29	10-Oct-29
B41050	L4SC - Top Rock	7	7	11-Oct-29	19-Oct-29
B41060	L4SC - OH RI High (Fire Protection, Classroom Elec Rough-in)	7	7	22-Oct-29	30-Oct-29
B41070	L4SC - OH RI High (Plumbing, Core Elec RI)	7	7	22-Oct-29	30-Oct-29
B41080	L4SC - OH RI Mid (Hydronic, Refer, Gas, Elec-Corridor, Plmbg Insul)	7	7	31-Oct-29	08-Nov-29
B41090	L4SC - OH RI Low (Duct, Elec FA, Lighting Cont., LV, Hyd Insul, FA, LC)	7	7	09-Nov-29	19-Nov-29
B41100	L4SC - Soffits / HL	5	5	20-Nov-29	28-Nov-29
B41110	L4SC - Pickup Work	6	6	29-Nov-29	06-Dec-29
B41120	L4SC - Cover & Stock	3	3	07-Dec-29	11-Dec-29
B41130	L4SC - Drywall & Insulation	7	7	12-Dec-29	20-Dec-29
B41140	L4SC - MT Finish Treatment	7	7	21-Dec-29	04-Jan-30
B41150	L4SC - Gyprete	7	7	21-Dec-29	04-Jan-30
B41160	L4SC - Taping	7	7	07-Jan-30	15-Jan-30
B41170	L4SC - Paint	7	7	16-Jan-30	24-Jan-30
B41180	L4SC - Resihous Flooring	5	5	25-Jan-30	31-Jan-30
B41190	L4SC - Pull LV Wire	7	7	25-Jan-30	04-Feb-30
B41200	L4SC - Bathroom Tile	5	5	05-Feb-30	11-Feb-30
B41210	L4SC - T-Bar Device Tile	7	7	05-Feb-30	13-Feb-30
B41220	L4SC - Ceiling Trim MEP	7	7	14-Feb-30	22-Feb-30
B41230	L4SC - Casework	7	7	14-Feb-30	22-Feb-30
B41240	L4SC - Flooring	7	7	25-Feb-30	05-Mar-30
B41250	L4SC - MEP Fixtures & Trim	7	7	06-Mar-30	14-Mar-30
B41260	L4SC - Doors / Hardware	5	5	06-Mar-30	12-Mar-30
B41270	L4SC - ACT	7	7	15-Mar-30	25-Mar-30
B41280	L4SC - Specialties	20	20	26-Mar-30	22-Apr-30
B41290	L4SC - Specialy MEP Trim	5	5	23-Apr-30	29-Apr-30
B41300	L4SC - Final Clean	5	5	30-Apr-30	06-May-30
B41310	L4SC - Cx Tile	5	5	07-May-30	13-May-30
B41315	L4SC - Pre-Punch	15	15	14-May-30	04-Jun-30
Building A - Auditorium		432	432	10-Feb-27	19-Oct-28
Underground		73	73	10-Feb-27	21-May-27
40000	Mass Excavation / Structural Fill to BO Footing	46	46	10-Feb-27	14-Apr-27
40010	Underground Deep Utilities	20	20	10-Mar-27	06-Apr-27
Area 1		23	23	24-Feb-27	26-Mar-27
40100	FRP Concrete Footings / Plynths / Walls	10	10	24-Feb-27	09-Mar-27
40110	Backfill from BO Footing to SOG	3	3	10-Mar-27	12-Mar-27
40120	Underground Utility Install / Backfill & Fine Grade	10	10	15-Mar-27	26-Mar-27
Area 2		23	23	10-Mar-27	09-Apr-27
40200	FRP Concrete Footings / Plynths / Walls	10	10	10-Mar-27	23-Mar-27
40210	Backfill from BO Footing to SOG	3	3	24-Mar-27	26-Mar-27
40220	Underground Utility Install / Backfill & Fine Grade	10	10	29-Mar-27	09-Apr-27
Area 3		23	23	24-Mar-27	23-Apr-27
40300	FRP Concrete Footings / Plynths / Walls	10	10	24-Mar-27	06-Apr-27
40310	Backfill from BO Footing to SOG	3	3	07-Apr-27	09-Apr-27
40320	Underground Utility Install / Backfill & Fine Grade	10	10	12-Apr-27	23-Apr-27
Area 4		23	23	07-Apr-27	07-May-27
40400	FRP Concrete Footings / Plynths / Walls	10	10	07-Apr-27	20-Apr-27
40410	Backfill from BO Footing to SOG	3	3	21-Apr-27	23-Apr-27
40420	Underground Utility Install / Backfill & Fine Grade	10	10	26-Apr-27	07-May-27
Area 5		23	23	21-Apr-27	21-May-27
40500	FRP Concrete Footings / Plynths / Walls	10	10	21-Apr-27	04-May-27
40510	Backfill from BO Footing to SOG	3	3	05-May-27	07-May-27
40520	Underground Utility Install / Backfill & Fine Grade	10	10	10-May-27	21-May-27
Slab on Grade		62	62	29-Mar-27	23-Jun-27
Area 1		14	14	29-Mar-27	15-Apr-27
41000	Vapor Barrier	2	2	29-Mar-27	30-Mar-27
41010	FRP SOG	12	12	31-Mar-27	15-Apr-27
Area 2		14	14	12-Apr-27	29-Apr-27
41100	Vapor Barrier	2	2	12-Apr-27	13-Apr-27

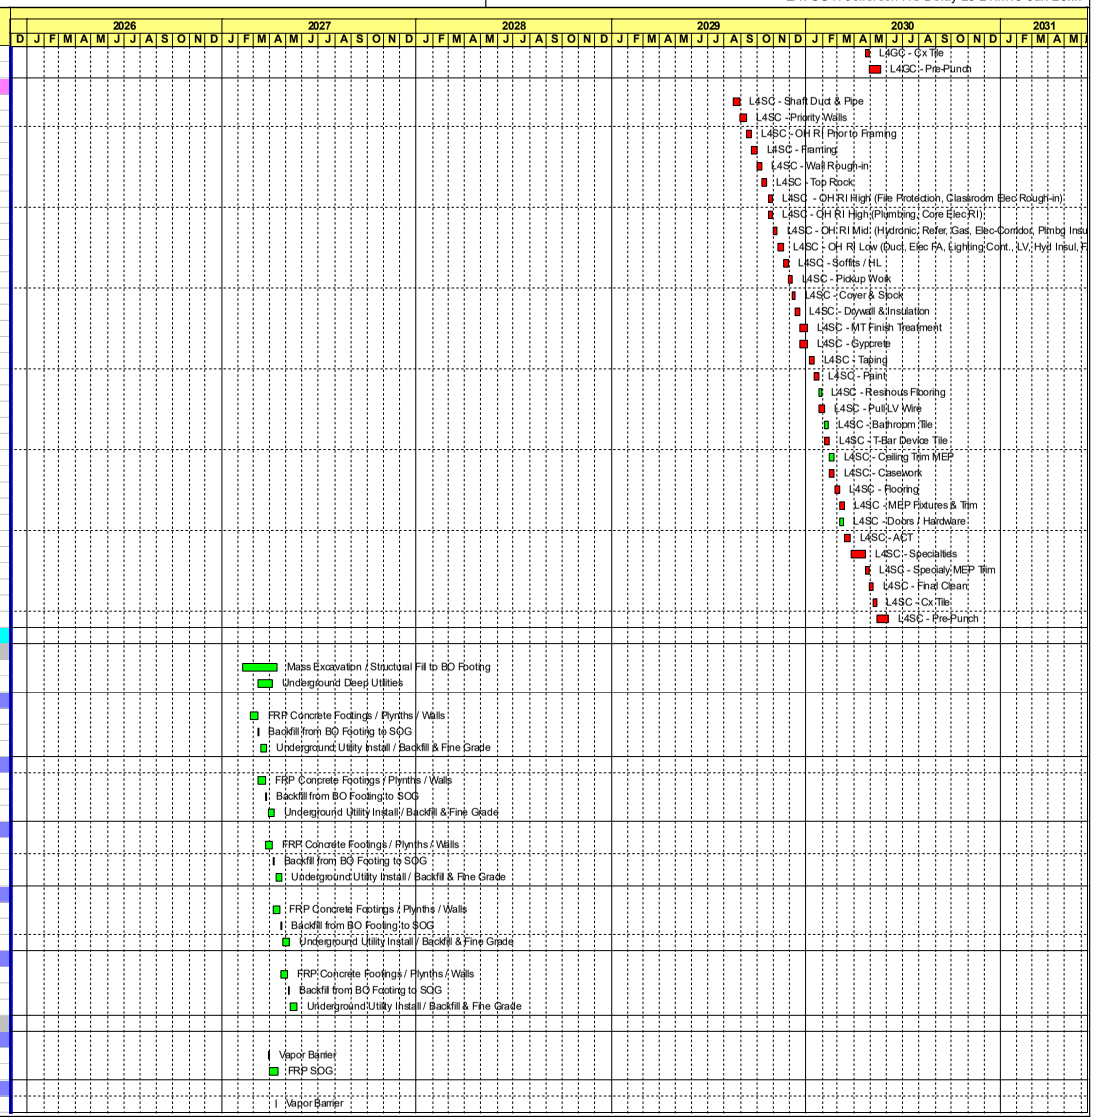

Jefferson High-1

LAYOUT: Jefferson HS Delay L3 L4....13-Jan-26....

Activity ID	Activity Name	Orig Dur	Remaining Duration	Start	Finish
41110	FRP SOG	12	12	14-Apr-27	29-Apr-27
Area 3		14	14	26-Apr-27	13-May-27
41200	Vapor Barrier	2	2	26-Apr-27	27-Apr-27
41210	FRP SOG	12	12	28-Apr-27	13-May-27
Area 4		14	14	10-May-27	27-May-27
41300	Vapor Barrier	2	2	10-May-27	11-May-27
41310	FRP SOG	12	12	12-May-27	27-May-27
Area 5		22	22	24-May-27	23-Jun-27
41400	Vapor Barrier	2	2	24-May-27	25-May-27
41410	FRP SOG	20	20	26-May-27	23-Jun-27
Structure		81	81	30-Apr-27	24-Aug-27
42010	Erect L2 & Roof	35	35	30-Apr-27	18-Jun-27
42020	Bolt / Weld / Deck / Level 2 & Roof	30	30	21-Jun-27	02-Aug-27
42030	Layout & Install MEP RI & Sleeves - L2 - Area 1	3	3	28-Jun-27	30-Jun-27
42040	Layout & Install MEP RI & Sleeves - L2 - Area 2	3	3	01-Jul-27	06-Jul-27
42050	Layout & Install MEP RI & Sleeves - L2 - Area 3	3	3	07-Jul-27	09-Jul-27
42060	Layout & Install MEP RI & Sleeves - L2 - Area 4	3	3	12-Jul-27	14-Jul-27
42070	Layout & Install MEP RI & Sleeves - L2 - Area 5	3	3	15-Jul-27	19-Jul-27
42100	FRP L2 SOMD - Area 1	4	4	01-Jul-27	07-Jul-27
42110	FRP L2 SOMD - Area 2	4	4	07-Jul-27	12-Jul-27
42120	FRP L2 SOMD - Area 3	4	4	12-Jul-27	15-Jul-27
42130	FRP L2 SOMD - Area 4	4	4	15-Jul-27	20-Jul-27
42140	FRP L2 SOMD - Area 5	4	4	20-Jul-27	23-Jul-27
42200	Layout & Install MEP RI & Sleeves - Roof - Area 1	4	4	03-Aug-27	06-Aug-27
42210	Layout & Install MEP RI & Sleeves - Roof - Area 2	4	4	09-Aug-27	12-Aug-27
42220	Layout & Install MEP RI & Sleeves - Roof - Area 3	4	4	13-Aug-27	18-Aug-27
42300	FRP Roof SOMD - Area 1	4	4	09-Aug-27	12-Aug-27
42310	FRP Roof SOMD - Area 2	4	4	12-Aug-27	17-Aug-27
42320	FRP Roof SOMD - Area 3	4	4	19-Aug-27	24-Aug-27
Roof		105	105	18-Aug-27	18-Jan-28
RF43000	Roof Area 4 - Parapet Framing	5	5	18-Aug-27	24-Aug-27
RF43010	Roof Area 4 - Temp Roof	20	20	25-Aug-27	22-Sep-27
RF43020	Roof Area 4 - Roof	80	80	16-Sep-27	11-Jan-28
RF43030	Roof Area 5 - Parapet Framing	5	5	25-Aug-27	31-Aug-27
RF43040	Roof Area 5 - Temp Roof	20	20	01-Sep-27	29-Sep-27
RF43050	Roof Area 5 - Roof	80	80	23-Sep-27	18-Jan-28
Facade		152	152	13-Aug-27	20-Mar-28
Faot4000	Facade 7 - Curb / Layout	7	7	13-Aug-27	23-Aug-27
Faot4010	Facade 7 - Exterior Panels	7	7	24-Aug-27	01-Sep-27
Faot4020	Facade 7 - WB Repair	7	7	02-Sep-27	13-Sep-27
Faot4030	Facade 7 - Install Windows	7	7	14-Sep-27	22-Sep-27
Faot4040	Facade 7 - "Z" Framing	14	14	23-Sep-27	12-Oct-27
Faot4050	Facade 7 - Metal Shrouds	14	14	13-Oct-27	01-Nov-27
Faot4060	Facade 7 - Insulation	14	14	02-Nov-27	19-Nov-27
Faot4070	Facade 7 - Hat Framing	14	14	22-Nov-27	13-Dec-27
Faot4080	Facade 7 - Metal Panel / Masonry	20	20	14-Dec-27	12-Jan-28
Faot4090	Facade 7 - Clean	5	5	13-Jan-28	19-Jan-28
Faot4095	Facade 7 - Pre-Punch & Quality Check	15	15	20-Jan-28	09-Feb-28
Faot4100	Facade 8 - Curb / Layout	7	7	24-Aug-27	01-Sep-27
Faot4110	Facade 8 - Exterior Panels	7	7	02-Sep-27	13-Sep-27
Faot4120	Facade 8 - WB Repair	7	7	14-Sep-27	22-Sep-27
Faot4130	Facade 8 - Install Windows	7	7	23-Sep-27	01-Oct-27
Faot4140	Facade 8 - "Z" Framing	14	14	13-Oct-27	01-Nov-27
Faot4150	Facade 8 - Metal Shrouds	14	14	02-Nov-27	19-Nov-27
Faot4160	Facade 8 - Insulation	14	14	22-Nov-27	13-Dec-27
Faot4170	Facade 8 - Hat Framing	14	14	14-Dec-27	04-Jan-28
Faot4180	Facade 8 - Metal Panel / Masonry	20	20	05-Jan-28	01-Feb-28
Faot4190	Facade 8 - Clean	5	5	02-Feb-28	08-Feb-28
Faot4195	Facade 8 - Pre-Punch & Quality Check	15	15	09-Feb-28	29-Feb-28
Faot4200	Facade 9 - Curb / Layout	7	7	02-Sep-27	13-Sep-27
Faot4210	Facade 9 - Exterior Panels	7	7	14-Sep-27	22-Sep-27
Faot4220	Facade 9 - WB Repair	7	7	23-Sep-27	01-Oct-27
Faot4230	Facade 9 - Install Windows	7	7	04-Oct-27	12-Oct-27
Faot4240	Facade 9 - "Z" Framing	14	14	02-Nov-27	19-Nov-27
Faot4250	Facade 9 - Metal Shrouds	14	14	22-Nov-27	13-Dec-27
Faot4260	Facade 9 - Insulation	14	14	14-Dec-27	04-Jan-28

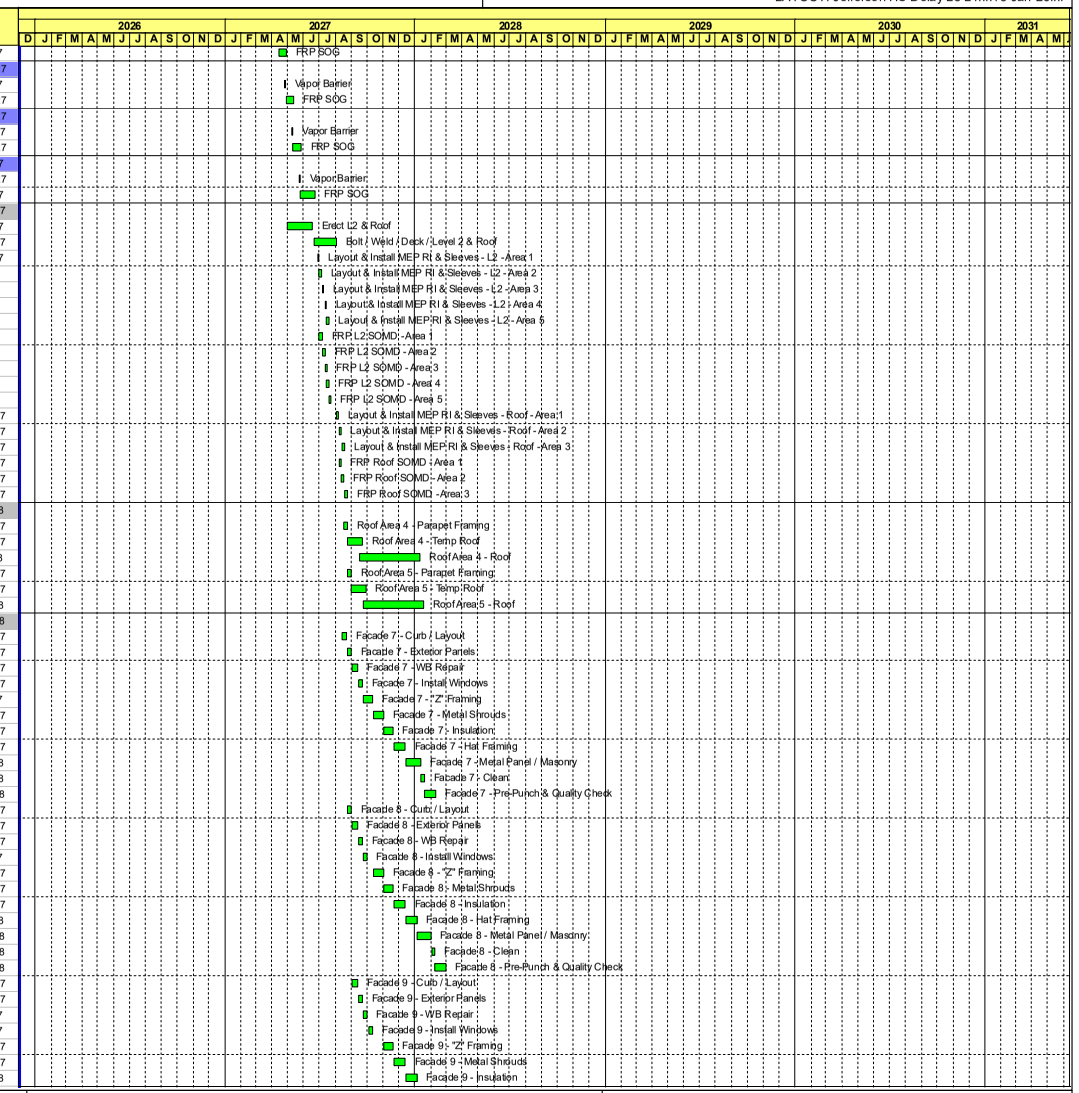

Remaining Level of Effort | Actual Work | Critical Remaining Work

Actual Level of Effort | Remaining Work | Meeting Milestone


Jefferson High School 1.6.26 - Delay L3 L4

data date :01-Dec-25 Page 14 of 19 TASK filter: <100%.

Jefferson High-1

LAYOUT: Jefferson HS Delay L3 L4....13-Jan-26....

Activity ID	Activity Name	Orig Dur	Remaining Duration	Start	Finish
Fac44270	Facade 9 - Hat Framing	14	14	05-Jan-28	24-Jan-28
Fac44280	Facade 9 - Metal Panel / Masonry	20	20	25-Jan-28	21-Feb-28
Fac44290	Facade 9 - Clean	5	5	22-Feb-28	28-Feb-28
Fac44295	Facade 9 - Pre-Punch & Quality Check	15	15	29-Feb-28	20-Mar-28
Interior Buildout		260	260	13-Oct-27	19-Oct-28
Level 1		260	260	13-Oct-27	19-Oct-28
Area TA - Theater Auxiliary		200	200	13-Oct-27	26-Jul-28
A10000	L1TA - Shaft Duct & Pipe	10	10	13-Oct-27	26-Oct-27
A10010	L1TA - Priority Walls	7	7	27-Oct-27	04-Nov-27
A10020	L1TA - OH RI Prior to Framing	7	7	05-Nov-27	15-Nov-27
A10030	L1TA - Framing	7	7	16-Nov-27	24-Nov-27
A10040	L1TA - Wall Rough-in	7	7	29-Nov-27	07-Dec-27
A10050	L1TA - Top Rock	7	7	08-Dec-27	16-Dec-27
A10060	L1TA - OH RI High (Fire Protection, Classroom Elec Rough-in)	7	7	17-Dec-27	28-Dec-27
A10070	L1TA - OH RI High (Plumbing, Core Elec RI)	7	7	17-Dec-27	28-Dec-27
A10080	L1TA - OH RI Mid (Hydronic, Refer, Gas, Elec-Corridor, Plmbg Insul)	7	7	29-Dec-27	07-Jan-28
A10090	L1TA - OH RI Low (Duct, Elec FA, Lighting Cont., LV, Hyd Insul, FA LC)	7	7	10-Jan-28	18-Jan-28
A10100	L1TA - Soffits / HL	5	5	19-Jan-28	25-Jan-28
A10110	L1TA - Pickup Work	6	6	26-Jan-28	02-Feb-28
A10120	L1TA - Cover & Stock	3	3	03-Feb-28	07-Feb-28
A10130	L1TA - Drywall & Insulation	7	7	08-Feb-28	16-Feb-28
A10140	L1TA - MT Finish Treatment	7	7	17-Feb-28	25-Feb-28
A10150	L1TA - Taping	7	7	28-Feb-28	07-Mar-28
A10160	L1TA - Paint	7	7	08-Mar-28	16-Mar-28
A10170	L1TA - Resinous Flooring	5	5	17-Mar-28	23-Mar-28
A10180	L1TA - Pull LV Wire	7	7	17-Mar-28	27-Mar-28
A10190	L1TA - Bathroom Tile	5	5	28-Mar-28	03-Apr-28
A10200	L1TA - T-Bar Device Tile	7	7	28-Mar-28	05-Apr-28
A10210	L1TA - Ceiling Trim MEP	7	7	06-Apr-28	14-Apr-28
A10220	L1TA - Casework	7	7	06-Apr-28	14-Apr-28
A10230	L1TA - Flooring	7	7	17-Apr-28	25-Apr-28
A10240	L1TA - MEP Fixtures & Trim	7	7	26-Apr-28	04-May-28
A10250	L1TA - Doors / Hardware	5	5	26-Apr-28	02-May-28
A10260	L1TA - ACT	7	7	05-May-28	15-May-28
A10270	L1TA - Specialties	20	20	16-May-28	13-Jun-28
A10280	L1TA - Specialy MEP Trim	5	5	14-Jun-28	20-Jun-28
A10290	L1TA - Final Clean	5	5	21-Jun-28	27-Jun-28
A10300	L1TA - Cx Tile	5	5	28-Jun-28	05-Jul-28
A10305	L1TA - Pre-Punch	15	15	06-Jul-28	26-Jul-28
Theater		250	250	27-Oct-27	19-Oct-28
A11000	Aud - Rough In / Framing & Interior Finishes	250	250	27-Oct-27	19-Oct-28
Level 2		200	200	27-Oct-27	09-Aug-28
Area TA - Theater Auxiliary		200	200	27-Oct-27	09-Aug-28
A20000	L1TA - Shaft Duct & Pipe	10	10	27-Oct-27	09-Nov-27
A20010	L1TA - Priority Walls	7	7	10-Nov-27	18-Nov-27
A20020	L1TA - OH RI Prior to Framing	7	7	19-Nov-27	01-Dec-27
A20030	L1TA - Framing	7	7	02-Dec-27	10-Dec-27
A20040	L1TA - Wall Rough-in	7	7	13-Dec-27	21-Dec-27
A20050	L1TA - Top Rock	7	7	22-Dec-27	03-Jan-28
A20060	L1TA - OH RI High (Fire Protection, Classroom Elec Rough-in)	7	7	04-Jan-28	12-Jan-28
A20070	L1TA - OH RI High (Plumbing, Core Elec RI)	7	7	04-Jan-28	12-Jan-28
A20080	L1TA - OH RI Mid (Hydronic, Refer, Gas, Elec-Corridor, Plmbg Insul)	7	7	13-Jan-28	21-Jan-28
A20090	L1TA - OH RI Low (Duct, Elec FA, Lighting Cont., LV, Hyd Insul, FA LC)	7	7	24-Jan-28	01-Feb-28
A20100	L1TA - Soffits / HL	5	5	02-Feb-28	08-Feb-28
A20110	L1TA - Pickup Work	6	6	09-Feb-28	16-Feb-28
A20120	L1TA - Cover & Stock	3	3	17-Feb-28	21-Feb-28
A20130	L1TA - Drywall & Insulation	7	7	22-Feb-28	01-Mar-28
A20140	L1TA - MT Finish Treatment	7	7	02-Mar-28	10-Mar-28
A20150	L1TA - Taping	7	7	13-Mar-28	21-Mar-28
A20160	L1TA - Paint	7	7	22-Mar-28	30-Mar-28
A20170	L1TA - Resinous Flooring	5	5	31-Mar-28	06-Apr-28
A20180	L1TA - Pull LV Wire	7	7	31-Mar-28	10-Apr-28
A20190	L1TA - Bathroom Tile	5	5	11-Apr-28	17-Apr-28
A20200	L1TA - T-Bar Device Tile	7	7	11-Apr-28	19-Apr-28
A20210	L1TA - Ceiling Trim MEP	7	7	20-Apr-28	28-Apr-28
A20220	L1TA - Casework	7	7	20-Apr-28	28-Apr-28

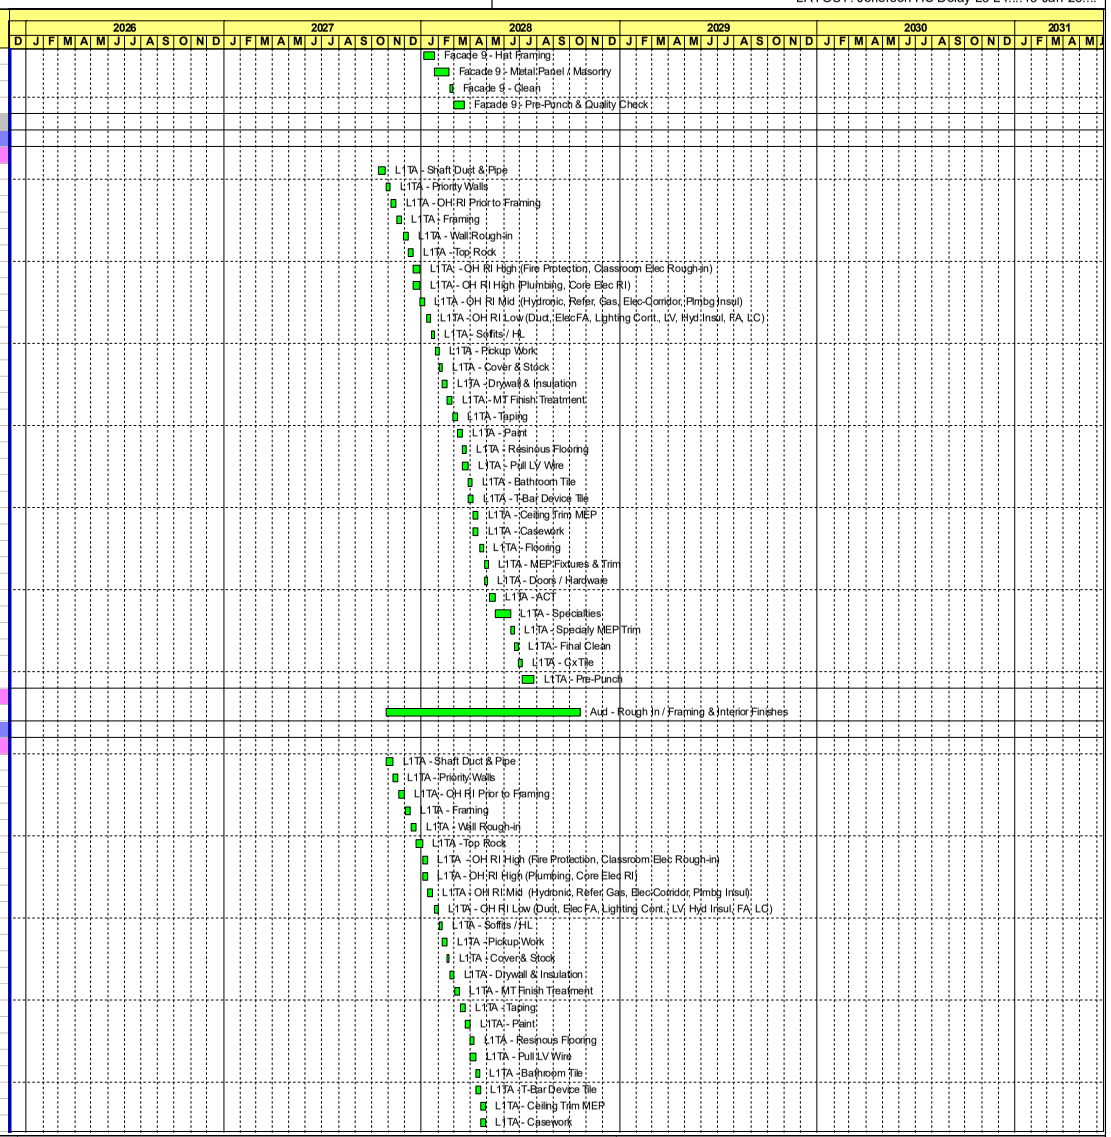

Remaining Level of Effort | Actual Work | Critical Remaining Work
Actual Level of Effort | Remaining Work | Meeting Milestone


Jefferson High School 1.6.26 - Delay L3 L4

data date :01-Dec-25 Page 15 of 19 TASK filter: <100%.

Jefferson High-1

LAYOUT: Jefferson HS Delay L3 L4....13-Jan-26....

Activity ID	Activity Name	Orig Dur	Remaining Duration	Start	Finish
A20230	L1TA - Flooring	7	7	01-May-28	09-May-28
A20240	L1TA - MEP Fixtures & Trim	7	7	10-May-28	18-May-28
A20250	L1TA - Doors / Hardware	5	5	10-May-28	16-May-28
A20260	L1TA - ACT	7	7	19-May-28	30-May-28
A20270	L1TA - Specialties	20	20	31-May-28	27-Jun-28
A20280	L1TA - Specialy MEP Trim	5	5	28-Jun-28	05-Jul-28
A20290	L1TA - Final Clean	5	5	06-Jul-28	12-Jul-28
A20300	L1TA - Cx Tile	5	5	13-Jul-28	19-Jul-28
A20305	L1TA - Pre-Punch	15	15	20-Jul-28	09-Aug-28
Building C - Gym		485	485	10-Feb-27	08-Jan-29
Underground		60	60	10-Feb-27	04-May-27
50000	Mass Excavation / Structural Fill to BO Footing	27	27	10-Feb-27	18-Mar-27
50010	Underground Deep Utilities	25	25	24-Feb-27	30-Mar-27
Area 1		18	18	24-Feb-27	19-Mar-27
50100	FRP Concrete Footings / Plynths / Walls	8	8	24-Feb-27	05-Mar-27
50110	Backfill from BO Footing to SOG	2	2	08-Mar-27	09-Mar-27
50120	Underground Utility Install / Backfill & Fine Grade	8	8	10-Mar-27	19-Mar-27
Area 2		18	18	08-Mar-27	31-Mar-27
50200	FRP Concrete Footings / Plynths / Walls	8	8	08-Mar-27	17-Mar-27
50210	Backfill from BO Footing to SOG	2	2	18-Mar-27	19-Mar-27
50220	Underground Utility Install / Backfill & Fine Grade	8	8	22-Mar-27	31-Mar-27
Area 3		18	18	18-Mar-27	12-Apr-27
50300	FRP Concrete Footings / Plynths / Walls	8	8	18-Mar-27	29-Mar-27
50310	Backfill from BO Footing to SOG	2	2	30-Mar-27	31-Mar-27
50320	Underground Utility Install / Backfill & Fine Grade	8	8	01-Apr-27	12-Apr-27
Area 4		18	18	30-Mar-27	22-Apr-27
50400	FRP Concrete Footings / Plynths / Walls	8	8	30-Mar-27	08-Apr-27
50410	Backfill from BO Footing to SOG	2	2	09-Apr-27	12-Apr-27
50420	Underground Utility Install / Backfill & Fine Grade	8	8	13-Apr-27	22-Apr-27
Area 5		18	18	09-Apr-27	04-May-27
50500	FRP Concrete Footings / Plynths / Walls	8	8	09-Apr-27	20-Apr-27
50510	Backfill from BO Footing to SOG	2	2	21-Apr-27	22-Apr-27
50520	Underground Utility Install / Backfill & Fine Grade	8	8	23-Apr-27	04-May-27
Slab on Grade		199	199	22-Mar-27	03-Jan-28
Area 1		12	12	22-Mar-27	06-Apr-27
51100	Vapor Barrier	2	2	22-Mar-27	23-Mar-27
51110	FRP SOG	10	10	24-Mar-27	06-Apr-27
Area 2		12	12	01-Apr-27	16-Apr-27
51200	Vapor Barrier	2	2	01-Apr-27	02-Apr-27
51210	FRP SOG	10	10	05-Apr-27	16-Apr-27
Area 3		14	14	13-Apr-27	30-Apr-27
51300	Vapor Barrier	2	2	13-Apr-27	14-Apr-27
51310	FRP SOG	12	12	15-Apr-27	30-Apr-27
Area 4		18	18	28-Oct-27	22-Nov-27
51400	Vapor Barrier	6	6	28-Oct-27	04-Nov-27
51410	FRP SOG	12	12	05-Nov-27	22-Nov-27
Area 5		26	26	23-Nov-27	03-Jan-28
51500	Vapor Barrier	6	6	23-Nov-27	02-Dec-27
51510	FRP SOG	20	20	03-Dec-27	03-Jan-28
Structure		197	197	26-Apr-27	03-Feb-28
52010	Build CMU Walls & Brace	60	60	26-Apr-27	20-Jul-27
52100	Erect L2 & Roof	20	20	19-Jul-27	13-Aug-27
52110	Bolt / Weld / Deck / Level 2 & Roof	18	18	16-Aug-27	09-Sep-27
52120	Layout & Install MEP RI & Sleeves - L2 / Mezz - Area 1	3	3	23-Aug-27	25-Aug-27
52130	Layout & Install MEP RI & Sleeves - L2 / Mezz - Area 2	3	3	26-Aug-27	30-Aug-27
52140	Layout & Install MEP RI & Sleeves - L2 / Mezz - Area 3	3	3	31-Aug-27	02-Sep-27
52150	Layout & Install MEP RI & Sleeves - L2 / Mezz - Area 4	3	3	03-Sep-27	08-Sep-27
52160	Layout & Install MEP RI & Sleeves - L2 / Mezz - Area 5	3	3	09-Sep-27	13-Sep-27
52170	FRP L2 / Mezz SOMD - Area 1	2	2	26-Aug-27	27-Aug-27
52180	FRP L2 / Mezz SOMD - Area 2	2	2	31-Aug-27	01-Sep-27
52190	FRP L2 / Mezz SOMD - Area 3	2	2	03-Sep-27	07-Sep-27
52200	FRP L2 / Mezz SOMD - Area 4	2	2	09-Sep-27	10-Sep-27
52210	FRP L2 / Mezz SOMD - Area 5	2	2	14-Sep-27	15-Sep-27
52220	Layout & Install MEP RI & Sleeves - Roof - Area 1	2	2	10-Sep-27	13-Sep-27
52230	Layout & Install MEP RI & Sleeves - Roof - Area 2	2	2	14-Sep-27	15-Sep-27
52240	Layout & Install MEP RI & Sleeves - Roof - Area 3	2	2	16-Sep-27	17-Sep-27

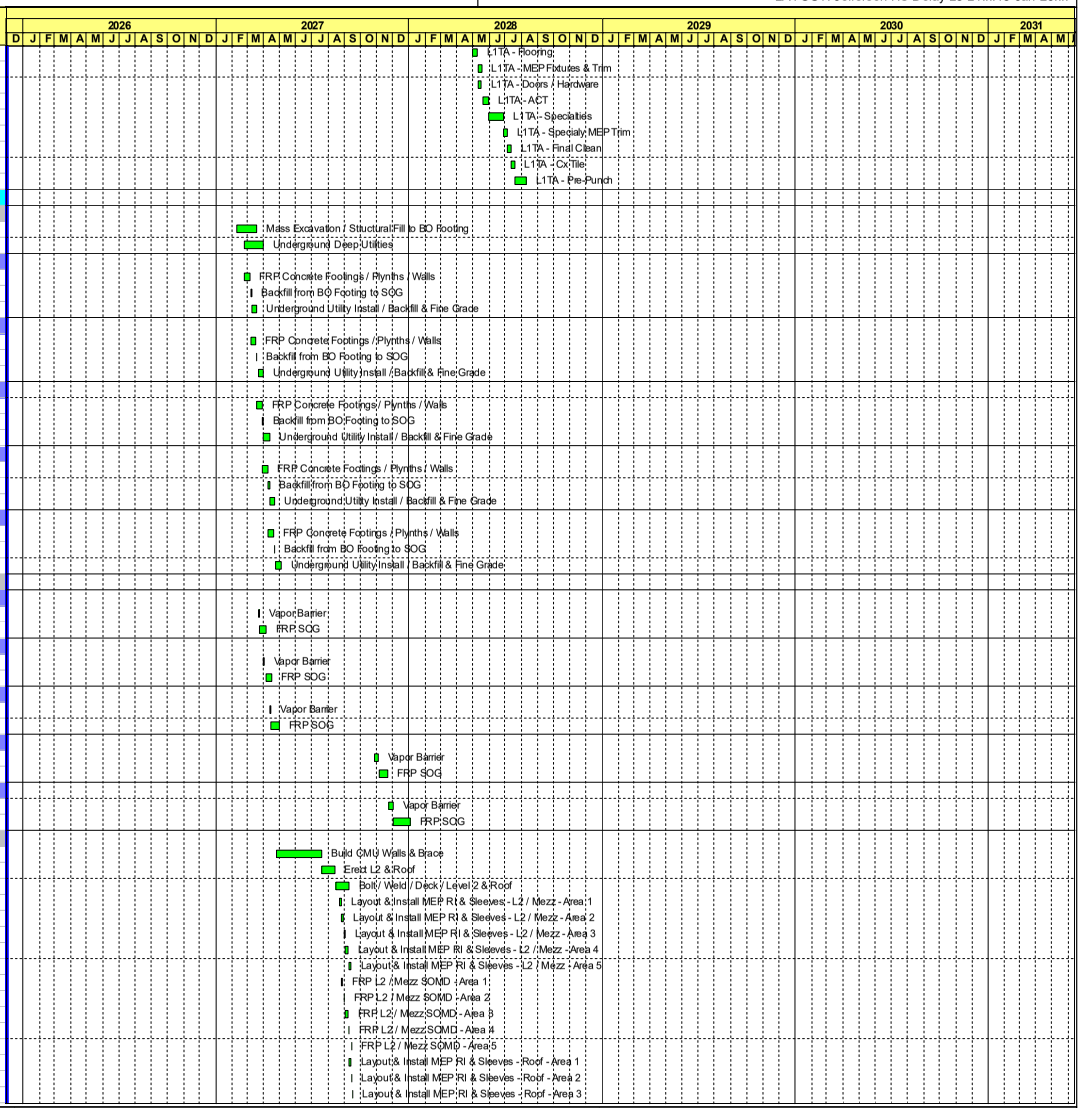


Remaining Level of Effort | Actual Work | Critical Remaining Work
Actual Level of Effort | Remaining Work | Meeting Milestone

Jefferson High School 1.6.26 - Delay L3 L4

data date :01-Dec-25 Page 16 of 19 TASK filter: <100%.

Activity ID	Activity Name	Orig Dur	Remaining Duration	Start	Finish
52250	FRP Roof SOMD - Area 1	3	3	14-Sep-27	16-Sep-27
52260	FRP Roof SOMD - Area 2	3	3	16-Sep-27	20-Sep-27
52270	FRP Roof SOMD - Area 3	3	3	20-Sep-27	22-Sep-27
Staging Area		67	67	28-Oct-27	03-Feb-28
52280	Demob Tower Crane 2	5	5	28-Oct-27	03-Nov-27
52290	Prep & Pour SOG	10	10	04-Nov-27	17-Nov-27
52300	Build CMU Walls (East)	20	20	15-Nov-27	14-Dec-27
52310	Set Steel Trusses	10	10	15-Dec-27	29-Dec-27
52320	Set Wood Trusses	10	10	30-Dec-27	13-Jan-28
52330	Set Wood DLT Roof Deck	15	15	14-Jan-28	03-Feb-28
Roof		164	164	23-Sep-27	15-May-28
RF53000	Roof Area 6 - Parapet Framing	5	5	23-Sep-27	29-Sep-27
RF53010	Roof Area 6 - Temp Roof	20	20	30-Sep-27	27-Oct-27
RF53020	Roof Area 6 - Roofing	40	40	21-Oct-27	17-Dec-27
RF53030	Roof Area 7 - Parapet Framing	5	5	04-Feb-28	10-Feb-28
RF53040	Roof Area 7 - Temp Roof	20	20	11-Feb-28	09-Mar-28
RF53050	Roof Area 7 - Roofing	40	40	03-Mar-28	27-Apr-28
RF53055	PV Panels	12	12	28-Apr-28	15-May-28
Facade		145	145	04-Feb-28	28-Aug-28
Fac54000	Facade 10 - Curb / Layout	7	7	04-Feb-28	14-Feb-28
Fac54010	Facade 10 - Exterior Panels	7	7	15-Feb-28	23-Feb-28
Fac54020	Facade 10 - WB Repair	7	7	24-Feb-28	03-Mar-28
Fac54030	Facade 10 - Install Windows	7	7	06-Mar-28	14-Mar-28
Fac54040	Facade 10 - "Z" Framing	14	14	15-Mar-28	03-Apr-28
Fac54050	Facade 10 - Metal Shrouds	14	14	04-Apr-28	21-Apr-28
Fac54060	Facade 10 - Insulation	14	14	24-Apr-28	11-May-28
Fac54070	Facade 10 - Hat Framing	14	14	12-May-28	01-Jun-28
Fac54080	Facade 10 - Metal Panel / Masonry	20	20	02-Jun-28	29-Jun-28
Fac54090	Facade 10 - Clean	5	5	30-Jun-28	07-Jul-28
Fac54095	Facade 10 - Pre-Punch & Quality Check	15	15	10-Jul-28	28-Jul-28
Fac54100	Facade 11 - Curb / Layout	7	7	15-Feb-28	23-Feb-28
Fac54110	Facade 11 - Exterior Panels	7	7	24-Feb-28	03-Mar-28
Fac54120	Facade 11 - WB Repair	7	7	06-Mar-28	14-Mar-28
Fac54130	Facade 11 - Install Windows	7	7	15-Mar-28	23-Mar-28
Fac54140	Facade 11 - "Z" Framing	14	14	24-Mar-28	12-Apr-28
Fac54150	Facade 11 - Metal Shrouds	14	14	13-Apr-28	02-May-28
Fac54160	Facade 11 - Insulation	14	14	03-May-28	22-May-28
Fac54170	Facade 11 - Hat Framing	14	14	23-May-28	12-Jun-28
Fac54180	Facade 11 - Metal Panel / Masonry	20	20	13-Jun-28	11-Jul-28
Fac54190	Facade 11 - Clean	5	5	12-Jul-28	18-Jul-28
Fac54195	Facade 11 - Pre-Punch & Quality Check	15	15	19-Jul-28	08-Aug-28
Fac54200	Facade 12 - Curb / Layout	7	7	24-Feb-28	03-Mar-28
Fac54210	Facade 12 - Exterior Panels	7	7	06-Mar-28	14-Mar-28
Fac54220	Facade 12 - WB Repair	7	7	15-Mar-28	23-Mar-28
Fac54230	Facade 12 - Install Windows	7	7	24-Mar-28	03-Apr-28
Fac54240	Facade 12 - "Z" Framing	14	14	13-Apr-28	02-May-28
Fac54250	Facade 12 - Metal Shrouds	14	14	03-May-28	22-May-28
Fac54260	Facade 12 - Insulation	14	14	23-May-28	12-Jun-28
Fac54270	Facade 12 - Hat Framing	14	14	13-Jun-28	30-Jun-28
Fac54280	Facade 12 - Metal Panel / Masonry	20	20	03-Jul-28	31-Jul-28
Fac54290	Facade 12 - Clean	5	5	01-Aug-28	07-Aug-28
Fac54295	Facade 12 - Pre-Punch & Quality Check	15	15	08-Aug-28	28-Aug-28
Interior Buildout		327	327	23-Sep-27	08-Jan-29
Level 1 / Level 1 Mezzanine		327	327	23-Sep-27	08-Jan-29
Area GA - GymAuxiliary & Main Electrical / Lockers		200	200	23-Sep-27	06-Jul-28
C10000	L1GA - Shaft Duct & Pipe	7	7	23-Sep-27	01-Oct-27
C10010	L1GA - Priority Walls	7	7	04-Oct-27	12-Oct-27
C10020	L1GA - OH RI Prior to Framing	7	7	13-Oct-27	21-Oct-27
C10030	L1GA - Framing	7	7	22-Oct-27	01-Nov-27
C10040	L1GA - Wall Rough-in	7	7	02-Nov-27	10-Nov-27
C10050	L1GA - Top Rock	7	7	11-Nov-27	19-Nov-27
C10060	L1GA - OH RI High (Fire Protection, Classroom Elec Rough-in)	7	7	22-Nov-27	02-Dec-27
C10070	L1GA - OH RI High (Plumbing, Core Elec RI)	7	7	22-Nov-27	02-Dec-27
C10080	L1GA - OH RI Mid (Hydronic, Refer, Gas, Elec-Corridor, Plmbg Insul)	7	7	03-Dec-27	13-Dec-27
C10090	L1GA - OH RI Low (Duct, Elec FA, Lighting Cont., LV, Hyd Insul, FA, LW)	7	7	14-Dec-27	22-Dec-27
C10100	L1GA - Soffits / HL	5	5	23-Dec-27	30-Dec-27

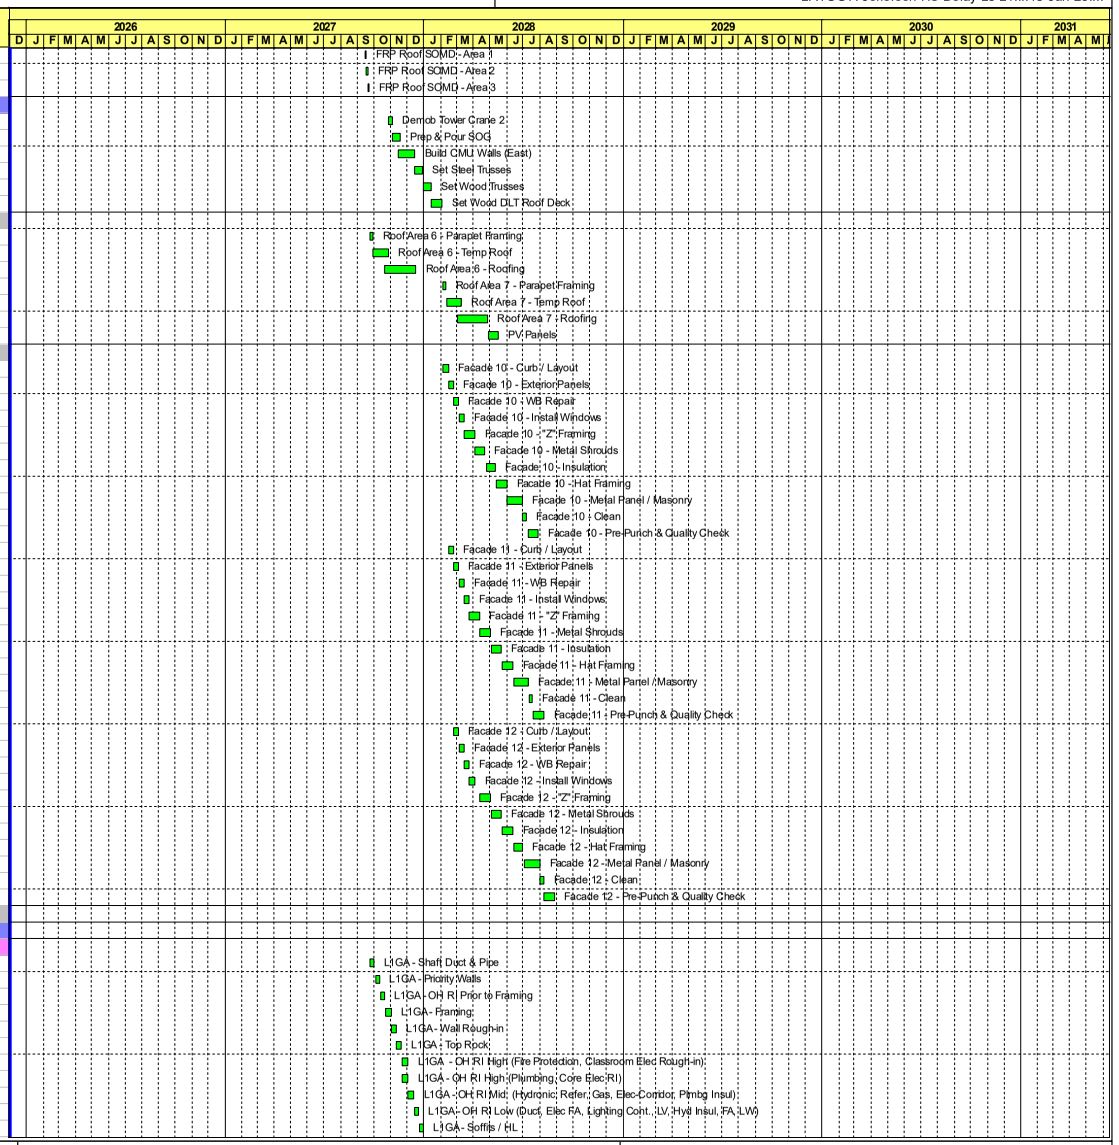

Remaining Level of Effort | Actual Work | Critical Remaining Work
Actual Level of Effort | Remaining Work | Meeting Milestone


Jefferson High School 1.6.26 - Delay L3 L4

data date :01-Dec-25 Page 17 of 19 TASK filter: <100%.

Jefferson High-1

LAYOUT: Jefferson HS Delay L3 L4....13-Jan-26....

Activity ID	Activity Name	Orig Dur	Remaining Duration	Start	Finish
C10110	L1GA - Pickup Work	6	6	03-Jan-28	10-Jan-28
C10120	L1GA - Cover & Stock	3	3	11-Jan-28	13-Jan-28
C10130	L1GA - Drywall & Insulation	7	7	14-Jan-28	24-Jan-28
C10140	L1GA- MT Finish Treatment	7	7	25-Jan-28	02-Feb-28
C10150	L1GA - Taping	7	7	03-Feb-28	11-Feb-28
C10160	L1GA - Paint	7	7	14-Feb-28	22-Feb-28
C10170	L1GA - Resinous Flooring	5	5	23-Feb-28	29-Feb-28
C10180	L1GA - Pull LV Wire	7	7	23-Feb-28	02-Mar-28
C10190	L1GA - Bathroom Tile	5	5	03-Mar-28	09-Mar-28
C10200	L1GA - T-Bar Device Tile	7	7	03-Mar-28	13-Mar-28
C10210	L1GA - Ceiling Trim MEP	7	7	14-Mar-28	22-Mar-28
C10220	L1GA - Casework	7	7	14-Mar-28	22-Mar-28
C10230	L1GA - Flooring	10	10	23-Mar-28	05-Apr-28
C10240	L1GA - MEP Fixtures & Trim	7	7	06-Apr-28	14-Apr-28
C10250	L1GA - Doors / Hardware	5	5	06-Apr-28	12-Apr-28
C10260	L1GA - ACT	7	7	17-Apr-28	25-Apr-28
C10270	L1GA - Specialties	20	20	26-Apr-28	23-May-28
C10280	L1GA - Specialy MEP Trim	5	5	24-May-28	31-May-28
C10290	L1GA - Final Clean	5	5	01-Jun-28	07-Jun-28
C10300	L1GA - Cx Tile	5	5	08-Jun-28	14-Jun-28
C10305	L1GA - Pre-Punch	15	15	15-Jun-28	06-Jul-28
Area G - Gym		240	240	28-Jan-28	08-Jan-29
C11000	Gym - Rough In / Framing & Interior Finishes	240	240	28-Jan-28	08-Jan-29
Level 2		230	230	04-Oct-27	28-Aug-28
Area GA - Auxiliary Gym & Weights		230	230	04-Oct-27	28-Aug-28
C20000	L2GA - Shaft Duct & Pipe	7	7	04-Oct-27	12-Oct-27
C20010	L2GA - Priority Walls	7	7	13-Oct-27	21-Oct-27
C20020	L2GA - OH RI Prior to Framing	7	7	22-Oct-27	01-Nov-27
C20030	L2GA - Framing	7	7	02-Nov-27	10-Nov-27
C20040	L2GA - Wall Rough-in	7	7	11-Nov-27	19-Nov-27
C20050	L2GA - Top Rock	7	7	22-Nov-27	02-Dec-27
C20060	L2GA - OH RI High (Fire Protection, Classroom Elec Rough-in)	7	7	03-Dec-27	13-Dec-27
C20070	L2GA - OH RI High (Plumbing, Core Elec RI)	7	7	03-Dec-27	13-Dec-27
C20080	L2GA - OH RI Mid (Hydronic, Refer, Gas, Elec-Corridor, Plmbg Insul)	7	7	14-Dec-27	22-Dec-27
C20090	L2GA - OH RI Low (Duct, Elec FA, Lighting Cont., LV, Hyd Insul, FA, LW)	7	7	23-Dec-27	04-Jan-28
C20100	L2GA - Soffits / HL	5	5	05-Jan-28	11-Jan-28
C20110	L2GA - Pickup Work	6	6	12-Jan-28	19-Jan-28
C20120	L2GA - Cover & Stock	3	3	20-Jan-28	24-Jan-28
C20130	L2GA - Drywall & Insulation	7	7	25-Jan-28	02-Feb-28
C20140	L2GA- MT Finish Treatment	7	7	03-Feb-28	11-Feb-28
C20150	L2GA - Taping	7	7	14-Feb-28	22-Feb-28
C20160	L2GA - Paint	7	7	23-Feb-28	02-Mar-28
C20170	L2GA - Resinous Flooring	5	5	03-Mar-28	09-Mar-28
C20180	L2GA - Pull LV Wire	7	7	03-Mar-28	13-Mar-28
C20190	L2GA - Bathroom Tile	5	5	14-Mar-28	20-Mar-28
C20200	L2GA - T-Bar Device Tile	7	7	14-Mar-28	22-Mar-28
C20210	L2GA - Ceiling Trim MEP	7	7	23-Mar-28	31-Mar-28
C20220	L2GA - Casework	7	7	23-Mar-28	31-Mar-28
C20230	L2GA - Flooring	20	20	03-Apr-28	28-Apr-28
C20240	L2GA - MEP Fixtures & Trim	7	7	01-May-28	09-May-28
C20250	L2GA - Doors / Hardware	5	5	01-May-28	05-May-28
C20260	L2GA - ACT	7	7	10-May-28	18-May-28
C20270	L2GA - Specialties	40	40	19-May-28	17-Jul-28
C20280	L2GA - Specialy MEP Trim	5	5	18-Jul-28	24-Jul-28
C20290	L2GA - Final Clean	5	5	25-Jul-28	31-Jul-28
C20300	L2GA - Cx Tile	5	5	01-Aug-28	07-Aug-28
C20305	L2GA - Pre-Punch	15	15	08-Aug-28	28-Aug-28
Sidewalks / Landscaping		194	194	10-Feb-28	10-Nov-28
60000	Site Work / Right of Way Improvements - Kirby	50	50	10-Feb-28	19-Apr-28
60010	Site Work / Right of Way Improvements - Killingsworth	25	25	01-Mar-28	04-Apr-28
60020	Site Work / Right of Way Improvements - Commercial	25	25	29-Aug-28	03-Oct-28
60030	Site Work / Right of Way Improvements - South Courtyard	50	50	01-Sep-28	10-Nov-28
Commissioning		187	187	23-Mar-28	15-Dec-28
90002	Building B MEP Start-up / Balancing / Commissioning	50	50	05-Oct-28	15-Dec-28
90012	Building A MEP Start-up / Balancing / Commissioning	50	50	10-Aug-28	19-Oct-28
90014	Building C MEP Start-up / Balancing / Commissioning	50	50	23-Mar-28	01-Jun-28

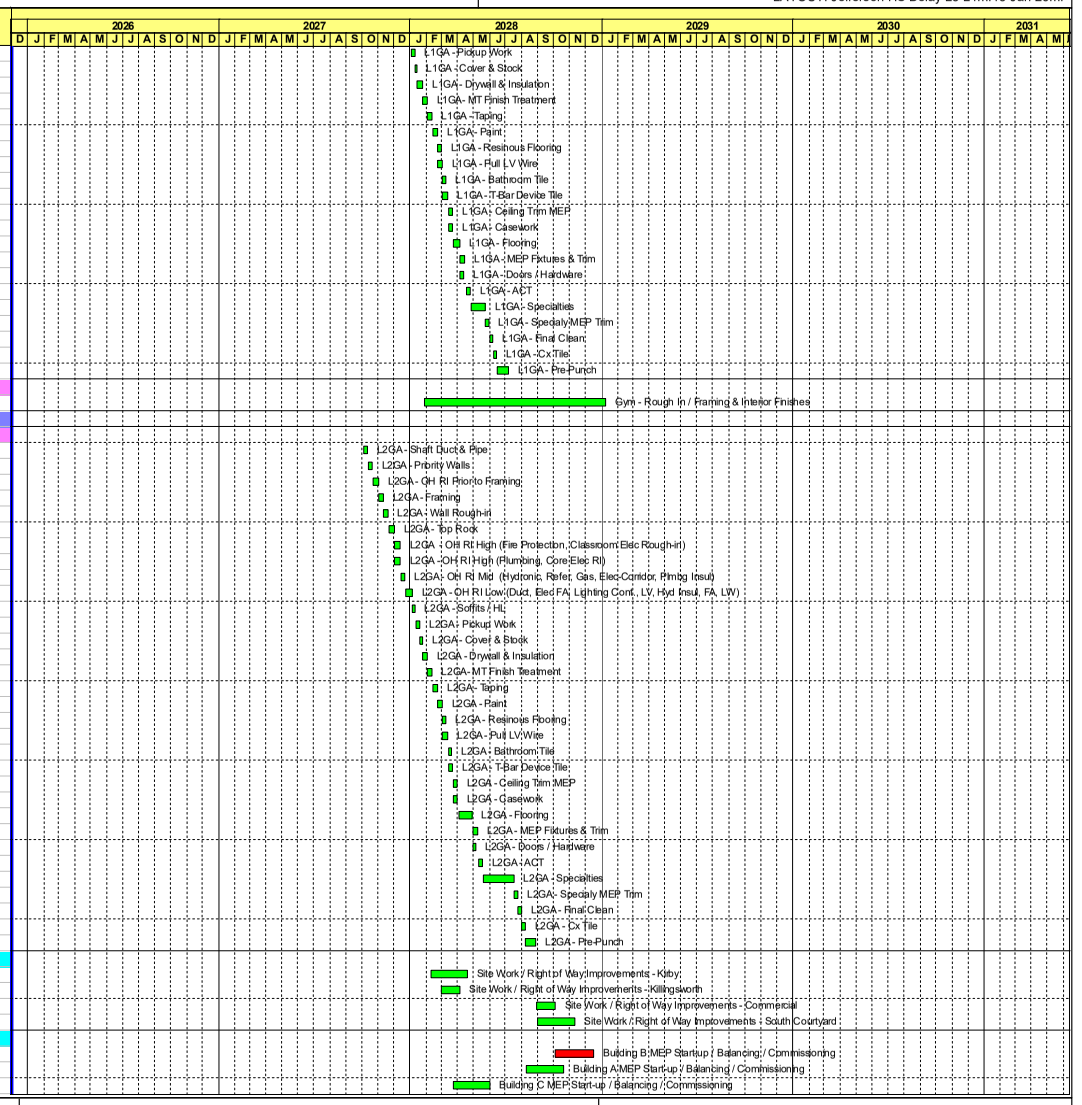

Remaining Level of Effort | Actual Work | Critical Remaining Work
Actual Level of Effort | Remaining Work | Meeting Milestone


Jefferson High School 1.6.26 - Delay L3 L4

data date :01-Dec-25 Page 18 of 19 TASK filter: <100%.

Jefferson High-1

LAYOUT: Jefferson HS Delay L3 L4....13-Jan-26....

Activity ID	Activity Name	Orig Dur	Remaining Duration	Start	Finish
Closeout		490	490	18-Dec-28	22-Nov-30
90000	Weather Contingency	20	20	18-Dec-28	16-Jan-29
90010	New Building Punch & Fire Life Safety FA Testing	50	50	17-Jan-29	27-Mar-29
90015	TCO Buildings A & B	0	0		27-Mar-29
90017	TCO Building C	0	0		08-Jan-29
90020	Otis / FF&E Install & Move-in	70	70	28-Mar-29	05-Jul-29*
90025	Teaching Ready / Start of Classes	0	0	06-Jul-29	
90030	Contingency	13	13	06-Jul-29	24-Jul-29
91000	L3 & L4 Punch & Life Safety FA Testing	50	50	05-Jun-30	15-Aug-30
91020	L3 & L4 FF&E Install & Move-in	70	70	16-Aug-30	22-Nov-30
Phase 3		265	265	05-Jul-29	25-Jul-30
099000	Existing Building Vacated	0	0		05-Jul-29
100000	Current Building Demolition / Abatement	105	105	06-Jul-29	04-Dec-29
100010	Build Football Field / Tennis Courts	150	150	29-Oct-29	04-Jun-30
100020	Site Works	45	45	26-Feb-30	29-Apr-30
100030	Punch, Commissioning & Closeout	35	35	05-Jun-30	25-Jul-30*
Hoisting		345	345	21-Dec-26	27-Apr-28
100040	Manlift Duration	115	115	12-Apr-27	22-Sep-27
100050	Tower Crane Duration	345	345	21-Dec-26	27-Apr-28

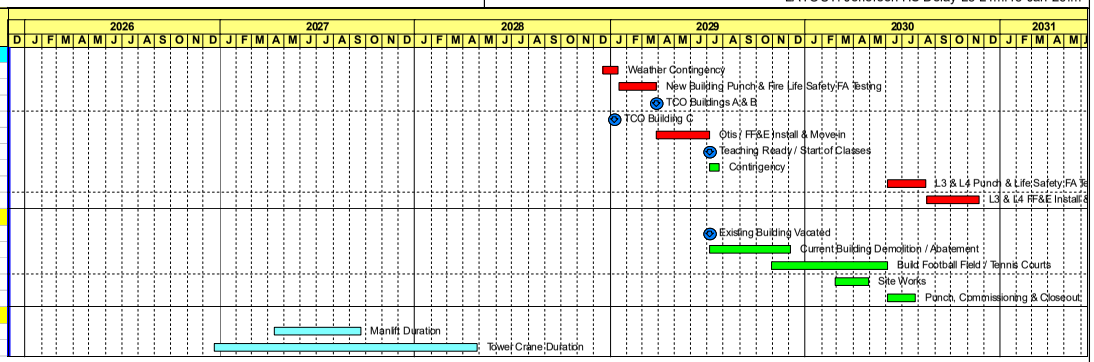

Remaining Level of Effort | Actual Work | Critical Remaining Work
Actual Level of Effort | Remaining Work | Meeting Milestone

Jefferson High School 1.6.26 - Delay L3 L4

data date :01-Dec-25 Page 19 of 19 TASK filter: <100%.

Jefferson High School – Value of Construction Use of Softball Field

Use Option 1 – Craft Worker Parking

ROM net value (potential for savings) is $317,557 as detailed below.

- We figure that for roughly 2 years the jobsite headcount will be high enough that we can't park in the surrounding neighborhood.
- There are about 250 parking days per year assuming Monday-Friday work. 500 parking days for 2 years.
- Average headcount in that time of 200 craft workers.
- Figure a fair value for one parking stall for one day is $8.
- Parking value over life of project = 500 x 200 x $8 = $800,000
- Deduct the cost escalation on the softball field work if the softball field is built at the same time as the football field in late 2029. $137,000
- Deduct cost of importing and removing temporary rock on softball field $3.82/SF x 90,430 SF = $345,443
- Net value to the District if used for parking is $800,000 - $137,000 - $345,443 = $317,557

Use Option 2 – Laydown Yard


Below is a summary of the attached feedback from local Subcontractors. ROM net value (potential for savings) is $306,565 as detailed below.

Structural Concrete


  - HSI - $100,000
- Precast & Masonry
  - J&S - $15,000
- Steel
  - Columbia Steel - 10/29 From Kale Park in email. Kale later recommended adding $100/truck in phone call: $550 per 25,000 lb truck (12.5 tons). JHS has 1,682 tons in Matt's estimate. (1,682 / 12.5) x $550 = $74,008.
- Mass Timber
  - StructureCraft - $30,000 for offsite local staging of trucks to accommodate the "float" in trailer supply chain described in the attached email.
- Glazing
  - Dallas Glass - $20,000
- Framing and Gyp Board

    - IES - $100,000
- Fire Suppression
    - Basic - $0
    - Patriot - 10/29: Chuck Rabitoy called and he says they only deliver a week or so material, directly into the building, so no cost premium.
- Plumbing & HVAC
    - HydroTemp - $350,000
    - JH Kelly - $0
- Electrical
    - CCE - $100,000
    - OEG - $0
- Subtotal of Subcontractor input = $789,008
- Deduct the cost escalation on the softball field work if the softball field is built at the same time as the football field in late 2029. $137,000
- Deduct cost of importing and removing temporary rock on softball field $3.82/SF x 90,430 SF = $345,443
- Net value to the District if used for parking is $789,008 - $137,000 - $345,443 = $306,565

2025 JHS Design and Construction Schedule

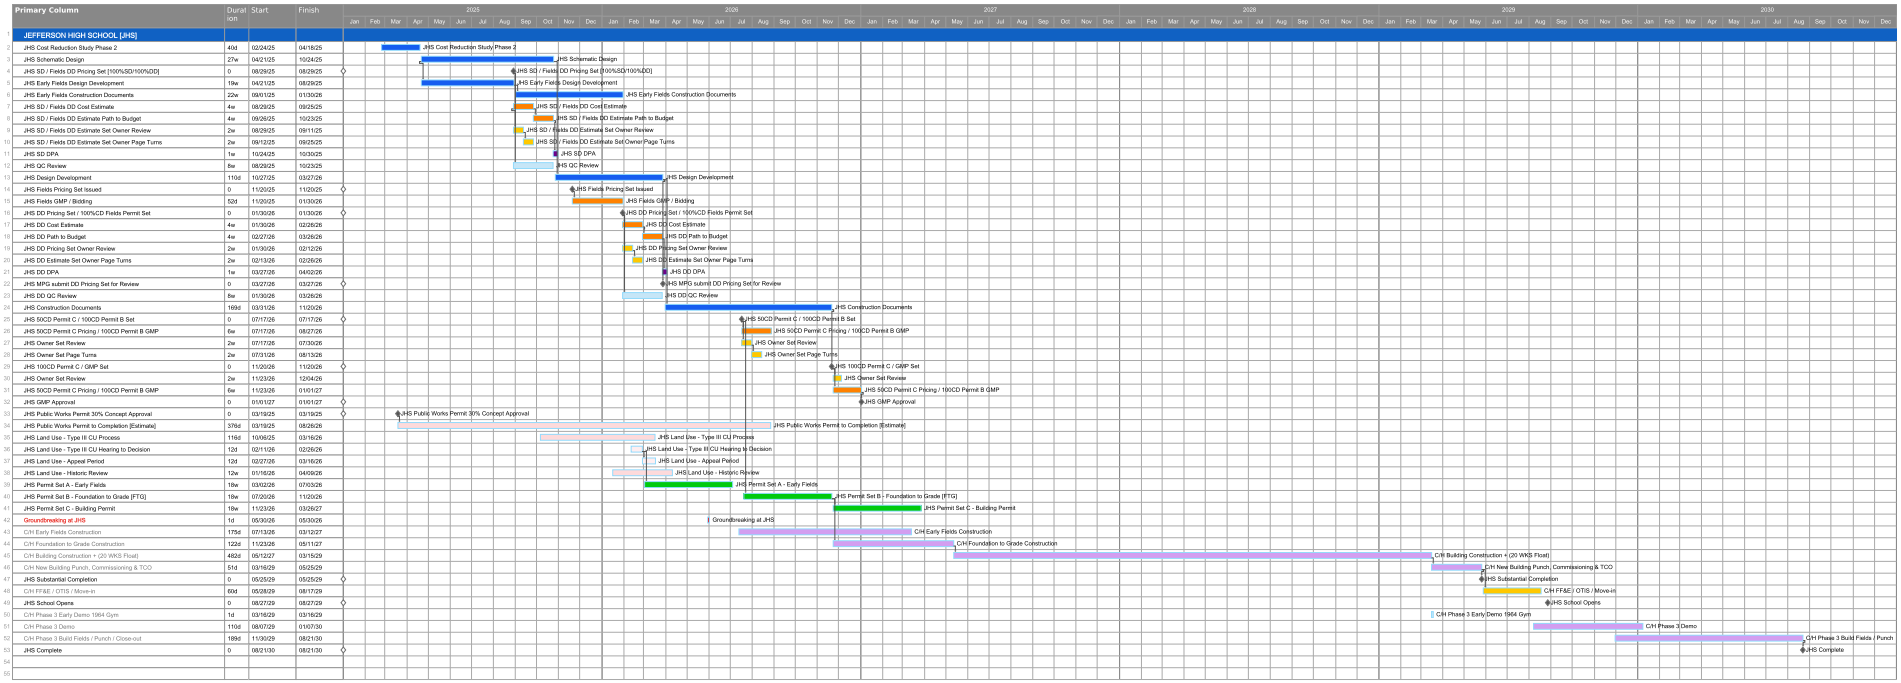


	Primary Column	Duration	Start	Finish
1	JEFFERSON HIGH SCHOOL [JHS]			
2	JHS Cost Reduction Study Phase 2	40d	02/24/25	04/18/25
3	JHS Schematic Design	27w	04/21/25	10/24/25
4	JHS SD / Fields DD Pricing Set [100%SD/100%DD]	0	08/29/25	08/29/25
5	JHS Early Fields Design Development	19w	04/21/25	08/29/25
6	JHS Early Fields Construction Documents	22w	09/01/25	01/30/26
7	JHS SD / Fields DD Cost Estimate	4w	08/29/25	09/25/25
8	JHS SD / Fields DD Estimate Path to Budget	4w	09/26/25	10/23/25
9	JHS SD / Fields DD Estimate Set Owner Review	2w	08/29/25	09/11/25
10	JHS SD / Fields DD Estimate Set Owner Page Turns	2w	09/12/25	09/25/25
11	JHS SD DPA	1w	10/24/25	10/30/25
12	JHS QC Review	8w	08/29/25	10/23/25
13	JHS Design Development	110d	10/27/25	03/27/26
14	JHS Fields Pricing Set Issued	0	11/20/25	11/20/25
15	JHS Fields GMP / Bidding	52d	11/20/25	01/30/26
16	JHS DD Pricing Set / 100%CD Fields Permit Set	0	01/30/26	01/30/26
17	JHS DD Cost Estimate	4w	01/30/26	02/26/26
18	JHS DD Path to Budget	4w	02/27/26	03/26/26
19	JHS DD Pricing Set Owner Review	2w	01/30/26	02/12/26
20	JHS DD Estimate Set Owner Page Turns	2w	02/13/26	02/26/26
21	JHS DD DPA	1w	03/27/26	04/02/26
22	JHS MPG submit DD Pricing Set for Review	0	03/27/26	03/27/26
23	JHS DD QC Review	8w	01/30/26	03/26/26
24	JHS Construction Documents	169d	03/31/26	11/20/26
25	JHS 50CD Permit C / 100CD Permit B Set	0	07/17/26	07/17/26
26	JHS 50CD Permit C Pricing / 100CD Permit B GMP	6w	07/17/26	08/27/26
27	JHS Owner Set Review	2w	07/17/26	07/30/26
28	JHS Owner Set Page Turns	2w	07/31/26	08/13/26
29	JHS 100CD Permit C / GMP Set	0	11/20/26	11/20/26
30	JHS Owner Set Review	2w	11/23/26	12/04/26
31	JHS 50CD Permit C Pricing / 100CD Permit B GMP	6w	11/23/26	01/01/27
32	JHS GMP Approval	0	01/01/27	01/01/27
33	JHS Public Works Permit 30% Concept Approval	0	03/19/25	03/19/25
34	JHS Public Works Permit to Completion [Estimate]	376d	03/19/25	08/26/26
35	JHS Land Use - Type III CU Process	116d	10/06/25	03/16/26
36	JHS Land Use - Type III CU Hearing to Decision	12d	02/11/26	02/26/26
37	JHS Land Use - Appeal Period	12d	02/27/26	03/16/26
38	JHS Land Use - Historic Review	12w	01/16/26	04/09/26
39	JHS Permit Set A - Early Fields	18w	07/03/26	07/03/26
40	JHS Permit Set B - Foundation to Grade [FTG]	18w	07/20/26	11/20/26
41	JHS Permit Set C - Building Permit	18w	11/23/26	03/26/27
42	Groundbreaking at JHS	1d	05/30/26	05/30/26
43	C/H Early Fields Construction	175d	07/13/26	03/12/27
44	C/H Foundation to Grade Construction	122d	11/23/26	05/11/27
45	C/H Building Construction + (20 WKS Float)	462d	05/12/27	03/15/29
46	C/H New Building Punch, Commissioning & TCO	51d	03/16/29	05/25/29
47	JHS Substantial Completion	0	05/25/29	05/25/29
48	C/H FF&E / OTIS / Move-in	60d	05/28/29	08/17/29
49	JHS School Opens	0	08/27/29	08/27/29
50	C/H Phase 3 Early Demo 1964 Gym	1d	03/16/29	03/16/29
51	C/H Phase 3 Demo	110d	08/07/29	01/07/30
52	C/H Phase 3 Build Fields / Punch / Close-out	189d	11/30/29	08/21/30
53	JHS Complete	0	08/21/30	08/21/30
54				
55				



BORA

JHS | 30087

Updated January 09, 2026

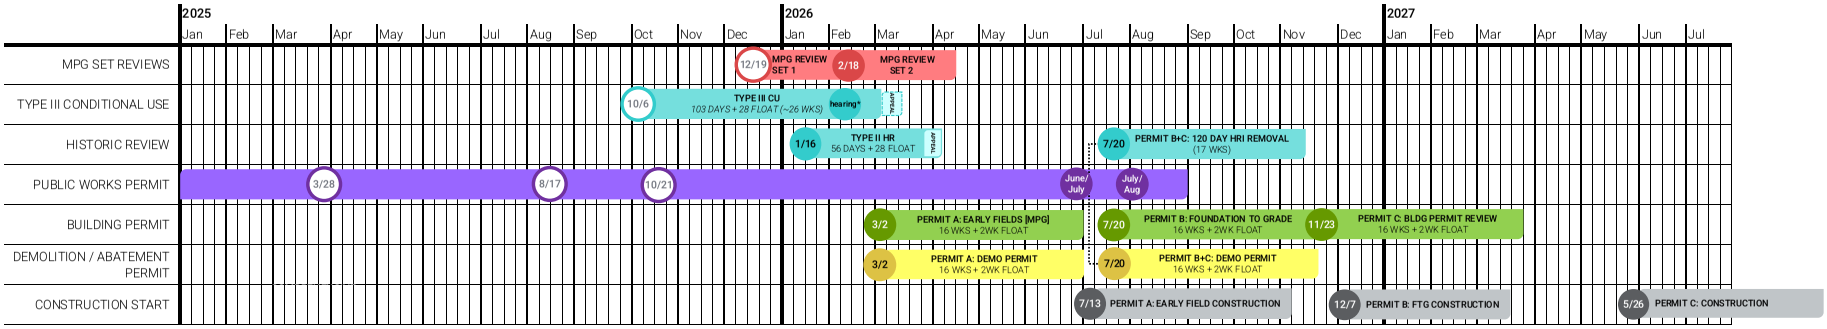

MPG SET REVIEWS

12/19/2025	MPG Review Set 1 Permit A 50%CD
02/18/2026	MPG Review Set 2 Permit BC 100%DD

CONDITIONAL USE + HISTORIC RESOURCE PERMIT

10/06/2025	Type III Conditional Use Submittal
01/16/2026	Type II Historic Review Submittal
02/26/2026	Type III Conditional Use Completion*
04/09/2026	Type II Historic Review Completion
07/20/2026	HRI Removal Waiting Period Start

PUBLIC WORKS PERMIT

03/28/2025	30% PWP Concept Approval
08/17/2025	60% PWP Concept Submittal
10/21/2025	60% PWP Hearing
~June / July 2026	Public Works Permit Final Submittal
~July / August 2027	Public Works Permit Release

CONSTRUCTION PERMIT

03/02/2026	Permit A Submitted Early Fields
07/07/2026	Permit A Issued Early Fields
07/20/2026	Permit B Submitted Foundation to Grade
11/20/2026	Permit B Issued Foundation to Grade
11/23/2026	Permit C Submitted School + Remaining Work
03/26/2027	Permit C Issued School + Remaining Work

DEMOLITION PERMIT

03/02/2026	Permit A Demo Permit Submitted
07/07/2026	Demo Permit Issued Permit A Scope
07/20/2026	Demo Permit Submitted Permit B+C Scope
11/20/2026	Demo Permit Issued Permit B+C Scope

CONSTRUCTION START

07/13/2026	Permit A Early Field Construction Begins
12/07/2026	Permit B Foundation to Grade Construction Begins
05/26/2027	Permit C Remaining Construction Begins

* based on 2/11/26 hearing date, does not include appeal period.

	2025 100% SD JHS - 1,700 students at 85% Utilization with Adjustments									
	Total SF	/ SF/TS	= TS	* Util	*	Students Per Classroom Range		= Student - low	Student - high	
General Classroom		950	40	85%	*	20	30	680	1,020	*(39) general classrooms + (1) ELL*
Science		1,500	11	85%	*	20	30	187	281	*(11) science labs*
Specialized Instruction		*varies*	11	75%		20	30	165	248	*(5) VAPA + (6) CTE*
Dance		2,000	2	85%	**	20	30	34	51	*(2) dance studios*
PE/Athletics		*varies*	4	75%	***	20	30	60	90	*(1) main gym, (1) Aux gym, (1) mat, (1) weights*
Special Education		*varies*	5	70%		15	24	53	84	*(2) int skills + (3) LRC*
Small Instructional		*varies*	4	0%		15	20	-	-	*(4) sm instruction*
Total			**77**					**1,179**	**1,773**	


* Supported with 5 Teacher Planning / Collaboration Rooms


** Added Dance Studios with 85% Utilization

*** Increased utilization to 75% to support Aux Gym and Mat Room use for Dance




DO NOT THROW
SOLIDS IN SINK
EMERGENCY E
IMPACT
CORNING

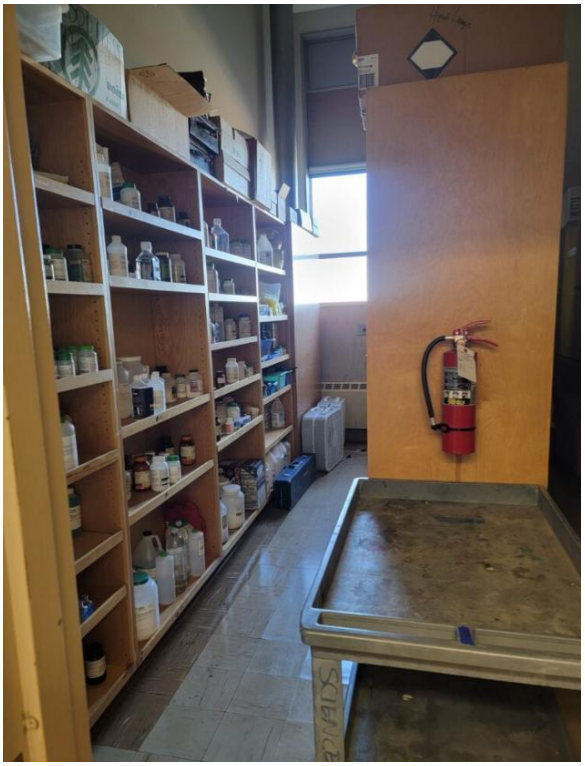

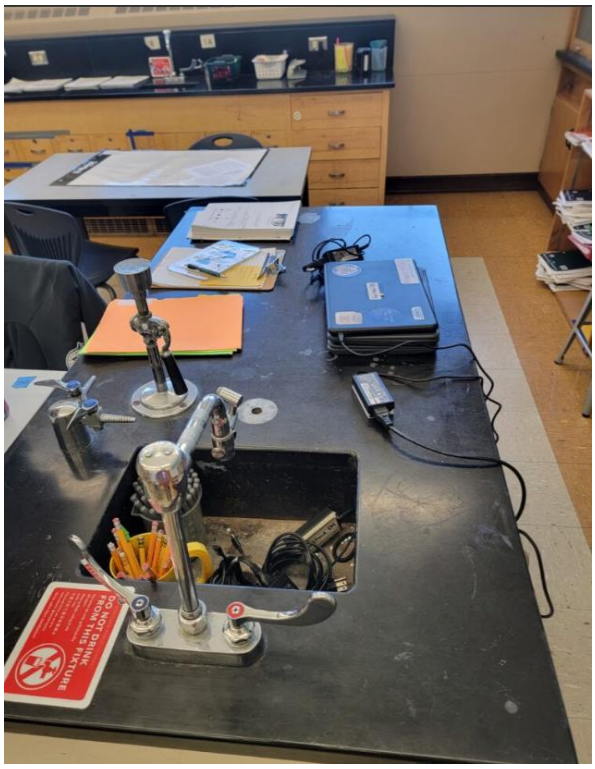
DO NOT DRINK
FROM THIS FIXTURE

Jefferson H.S.

Section List by Course and Term

For Term: Semester 1

Year: 2025-2026
Report: MST403

Term	Beg	End	Section ID		Staff Name	Room Name	Credit	Max	Total	Open
Course ID:	**0416CA1**			Course Title:	**Carpentry/Construct: Intro**					
S1	1	1	0416CA1-1		Teacher, Default Jeffersor	D-04	0.500	30	0	30
	3	3	0416CA1-2		Teacher, Default Jeffersor	D-04	0.500	30	0	30
							Course Total:	**60**	**0**	**60**
Course ID:	**0416CB1**			Course Title:	**Carpentry/Construct: Interm**					
S1	1	1	0416CB1-1		Teacher, Default Jeffersor	D-04	0.500	30	0	30
	3	3	0416CB1-2		Teacher, Default Jeffersor	D-04	0.500	30	0	30
							Course Total:	**60**	**0**	**60**
Course ID:	**0416CC1**			Course Title:	**Carpentry/Construct: Adv**					
S1	1	1	0416CC1-1		Teacher, Default Jeffersor	D-04	0.500	30	0	30
	3	3	0416CC1-2		Teacher, Default Jeffersor	D-04	0.500	30	0	30
							Course Total:	**60**	**0**	**60**
Course ID:	**0803VS**			Course Title:	**Virtual Scholars Online Course**					
S1	1	1	0803VS-SL01-1		Lynch, Shannon	B-38	0.000	40	1	39
	3	3	0803VS-NL03		Lipton, Nico A.	D-15	0.000	10	9	1
	4	4	0803VS-1		Lipton, Nico A.	D-15	0.000	10	12	-2
	5	5	0803VS-NL05		Lipton, Nico A.	D-15	0.000	10	3	7
	6	6	0803VS-2		Lipton, Nico A.	D-15	0.000	10	14	-4
	7	7	0803VS-NL07		Lipton, Nico A.	D-15	0.000	10	9	1
	8	8	0803VS-3		Lipton, Nico A.	D-15	0.000	10	9	1
							Course Total:	**100**	**57**	**43**
Course ID:	**08211**			Course Title:	**Teacher Aide**					
S1	7	7	08211-CW07		Wellington, Cory R.	C-23	0.500	40	1	39
							Course Total:	**40**	**1**	**39**

Jefferson H.S.

Section List by Course and Term

For Term: Semester 1

Year: 2025-2026
Report: MST403

Term	Beg	End	Section ID	Staff Name	Room Name	Credit	Max	Total	Open
Course ID: **08212**			Course Title: **Teacher Aide**						
S1	1	1	08212-SL01-1	Lynch, Shannon	B-38	0.500	40	1	39
	1	1	08212-LS01	Smith, Lauren R.	B-09	0.500	40	1	39
	1	1	08212-LR01	Rindfusz, Laura L.	B-27	0.500	40	2	38
	1	1	08212-AD01	Deland, Anthony	D-31	0.500	40	2	38
	2	2	08212-LR02-1	Rindfusz, Laura L.	B-27	0.500	40	2	38
	3	3	08212-LR03	Rindfusz, Laura L.	B-27	0.500	40	1	39
	3	3	08212-RB03	Lynch, Shannon	B-38	0.500	40	1	39
	3	3	08212-MM03	Lynch, Shannon	B-38	0.500	40	0	40
	3	3	08212-PF03-1	Fretel, Pamela	C-29	0.500	40	0	40
	3	3	08212-AS03-1	Schroth, Andrew	D-27		40	0	40
	4	4	08212-RN04	Lynch, Shannon	B-38	0.500	40	1	39
	4	4	08212-LR04-1	Rindfusz, Laura L.	B-27	0.500	40	1	39
	5	5	08212-LR05	Rindfusz, Laura L.	B-27	0.500	40	2	38
	5	5	08212-KW05	Waltner, Kyoko W.	C-32	0.500	40	1	39
	5	5	08212-AD05	Deland, Anthony	D-31	0.500	40	0	40
	5	5	08212-LM05	Morlock, Leigh	LIB	0.500	40	1	39
	6	6	08212-PF06	Fretel, Pamela	C-29	0.500	40	1	39
	6	6	08212-SG06-1	Gonzales, Steve R.	Dance	0.500	40	0	40
	6	6	08212-SL06	Lynch, Shannon	B-38	0.500	40	0	40
	6	6	08212-LR06	Rindfusz, Laura L.	B-27	0.500	40	1	39
	6	6	08212-RT06	Thompson, Raeann S.	D-12	0.500	40	1	39
	6	6	08212-JB06	Ballman, Joseph R.	C-03	0.500	40	0	40
	6	6	08212-JR06	Rutherford, Jacqueline	B-33	0.500	40	0	40
	7	7	08212-JJ07	Johnson, Jaydra	C-28	0.500	40	0	40
	7	7	08212-DIR07	Islam Roberts, Dejha	B-04	0.500	40	1	39
	7	7	08212-DHW07	Holden-Williams, Demetria	DUNG	0.500	40	1	39
	7	7	08212-DC07-1	Coffey, Daniel J.	B-21	0.500	40	2	38
	8	8	08212-DHW08	Holden-Williams, Demetria	DUNG	0.500	40	1	39
	8	8	08212-AH08	Hargrave, Amy L.	C-22	0.500	40	1	39
	8	8	08212-NB08	Brown, Niyah M.	B-04	0.500	40	1	39
	8	8	08212-MM08	Lynch, Shannon	B-38	0.500	40	3	37
	8	8	08212-OL08	Altieri, Olive D.	D-09	0.500	40	1	39
						Course Total:	**1280**	**30**	**1250**
Course ID: **08321**			Course Title: **9th Grade Success**						
S1	4	4	08321-3	Thompson, Raeann S.	D-12	0.500	33	26	7
	7	7	08321-4	Thompson, Raeann S.	D-12	0.500	33	18	15
	7	7	08321-1	Shelton, Wendy A.	C-10	0.500	33	19	14
	8	8	08321-2	Shelton, Wendy A.	C-10	0.500	33	32	1
						Course Total:	**132**	**95**	**37**
Course ID: **0841LG1**			Course Title: **Student Leadership/Government**						
S1	2	2	0841LG1-1	McKnight, Rebecca H.	C-04	0.500	35	24	11
						Course Total:	**35**	**24**	**11**

Jefferson H.S.
Section List by Course and Term
For Term: Semester 1

Year: 2025-2026
Report: MST403

Term	Beg	End	Section ID			Staff Name	Room Name	Credit	Max	Total	Open
Course ID:	**0862AVB1**			Course Title:	**AVID 10**						
S1	1	1	0862AVB1-1			Elliott, Susan B.	B-34	0.500	30	30	0
	6	6	0862AVB1-2			Griffin, Luke	D-26	0.500	30	26	4
	8	8	0862AVB1-3			Griffin, Luke	D-26	0.500	30	28	2
								Course Total:	**90**	**84**	**6**
Course ID:	**0862AVC1**			Course Title:	**AVID 11**						
S1	3	3	0862AVC1-3			Fretel, Pamela	C-37	0.500	32	24	8
	6	6	0862AVC1-2			Machuca, Eliana	C-37	0.500	32	16	16
	7	7	0862AVC1-1			Fretel, Pamela	C-37	0.500	32	27	5
	8	8	0862AVC1-4			Machuca, Eliana	C-37	0.500	32	18	14
								Course Total:	**128**	**85**	**43**
Course ID:	**0862AVD1**			Course Title:	**AVID 12**						
S1	1	1	0862AVD1-1			Machuca, Eliana	C-12	0.500	30	29	1
	2	2	0862AVD1-2			Machuca, Eliana	C-12	0.500	30	25	5
	5	5	0862AVD1-3			Machuca, Eliana	C-12	0.500	30	11	19
	7	7	0862AVD1-4			Machuca, Eliana	C-12	0.500	30	21	9
								Course Total:	**120**	**86**	**34**
Course ID:	**0899CW1**			Course Title:	**EL: Creative Writing 1**						
S1	1	1	0899CW1-1			Abel, Abigail K.	C-11	0.500	35	16	19
								Course Total:	**35**	**16**	**19**
Course ID:	**10011**			Course Title:	**English 1**						
S1	1	1	10011-1			Leahy, Dianne M.	C-13	0.500	30	20	10
	3	3	10011-2			Leahy, Dianne M.	C-13	0.500	30	29	1
	4	4	10011-3			Leahy, Dianne M.	C-13	0.500	30	24	6
	7	7	10011-4			Leahy, Dianne M.	C-13	0.500	30	24	6
								Course Total:	**120**	**97**	**23**
Course ID:	**10021**			Course Title:	**English 3**						
S1	3	3	10021-2			Coffey, Daniel J.	B-21	0.500	30	31	-1
	4	4	10021-3			Coffey, Daniel J.	B-21	0.500	30	28	2
	7	7	10021-1			Coffey, Daniel J.	B-21	0.500	30	25	5
								Course Total:	**90**	**84**	**6**
Course ID:	**1003RW1**			Course Title:	**Eng 5: Rdg/Writ 115**						
S1	2	2	1003RW1-1			Abel, Abigail K.	C-11	0.500	30	20	10
	4	4	1003RW1-2			Abel, Abigail K.	C-11	0.500	30	27	3
	5	5	1003RW1-3			Abel, Abigail K.	C-11	0.500	30	26	4
	6	6	1003RW1-4			Abel, Abigail K.	C-11	0.500	30	27	3
								Course Total:	**120**	**100**	**20**
Course ID:	**1004CL1**			Course Title:	**English 7:College Writing & Lit**						
S1	3	3	1004CL1-1			Tews, Nyki M.	C-31	0.500	33	26	7
	4	4	1004CL1-2			Tews, Nyki M.	C-31	0.500	33	26	7
	5	5	1004CL1-3			Tews, Nyki M.	C-31	0.500	33	23	10
	6	6	1004CL1-4			Tews, Nyki M.	C-31	0.500	33	26	7
								Course Total:	**132**	**101**	**31**

Jefferson H.S.
Section List by Course and Term
For Term: Semester 1

Year: 2025-2026
Report: MST403

Term	Beg	End	Section ID		Staff Name	Room Name	Credit	Max	Total	Open
Course ID:	**1061AEL1**		Course Title:	**Emerging ELD 1**						
S1	4	4	1061AEL1-1		Orellana, Jocelyn	B-14	0.500	30	9	21
							Course Total:	**30**	**9**	**21**
Course ID:	**1061DEL1**		Course Title:	**Progressing ELD 4**						
S1	9	9	1061DEL1-KY09		Yocum, Kate	B-14	0.500	40	21	19
							Course Total:	**40**	**21**	**19**
Course ID:	**1109BJD1**		Course Title:	**Jefferson Dancers II**						
S1	9	10	1109BJD1-		Holden-Williams, Demetria	DUNG	0.600	40	17	23
							Course Total:	**40**	**17**	**23**
Course ID:	**1109JD1**		Course Title:	**Jefferson Dancers I**						
S1	9	10	1109JD1-SG0910		Gonzales, Steve R.	DUNG	1.000	40	19	21
							Course Total:	**40**	**19**	**21**
Course ID:	**11121**		Course Title:	**Dance 1**						
S1	7	7	11121-1		Holden-Williams, Demetria	DUNG	0.500	30	18	12
	8	8	11121-2		Holden-Williams, Demetria	DUNG	0.500	30	23	7
							Course Total:	**60**	**41**	**19**
Course ID:	**1113BA1**		Course Title:	**Dance: 3 Ballet**						
S1	6	6	1113BA1-1		Gonzales, Steve R.	DUNG	0.500	30	9	21
							Course Total:	**30**	**9**	**21**
Course ID:	**1113H1**		Course Title:	**Dance: 3 Hip Hop**						
S1	6	6	1113H1-1		Holden-Williams, Demetria	DUNG	0.500	30	9	21
							Course Total:	**30**	**9**	**21**
Course ID:	**1113M1**		Course Title:	**Dance: 3 Modern**						
S1	5	5	1113M1-1		Smith, Lauren R.	DUNG	0.500	30	19	11
							Course Total:	**30**	**19**	**11**
Course ID:	**1114BA1**		Course Title:	**Dance 5: Ballet**						
S1	7	7	1114BA1-1		Gonzales, Steve R.	DUNG	0.500	30	14	16
							Course Total:	**30**	**14**	**16**
Course ID:	**1114J1**		Course Title:	**Dance 5: Jazz**						
S1	8	8	1114J1-1		Gonzales, Steve R.	DUNG	0.500	30	12	18
							Course Total:	**30**	**12**	**18**
Course ID:	**11221**		Course Title:	**Concert Band**						
S1	4	4	11221-1		Hester, Dave B.	BandRoom	0.500	30	9	21
							Course Total:	**30**	**9**	**21**
Course ID:	**11341**		Course Title:	**Percussion Ensemble**						
S1	2	2	11341-1		Hester, Dave B.	BandRoom	0.500	30	13	17
							Course Total:	**30**	**13**	**17**
Course ID:	**11401**		Course Title:	**Instrumental Music: Beginning Guitar**						
S1	7	7	11401-1		Hester, Dave B.	BandRoom	0.500	30	12	18
							Course Total:	**30**	**12**	**18**
Course ID:	**11421**		Course Title:	**Instrumental Music: Beginning Piano**						
S1	1	1	11421-1		Hester, Dave B.	BandRoom	0.500	30	5	25
	3	3	11421-2		Hester, Dave B.	BandRoom	0.500	30	21	9
							Course Total:	**60**	**26**	**34**

Jefferson H.S.
Section List by Course and Term
For Term: Semester 1

Year: 2025-2026
Report: MST403

Term	Beg	End	Section ID		Staff Name	Room Name	Credit	Max	Total	Open
Course ID:	**11501**			Course Title:	**Theatre: Beginning 1**					
S1	2	2	11501-1		Coffey, Daniel J.	B-21	0.500	30	19	11
							Course Total:	**30**	**19**	**11**
Course ID:	**11521**			Course Title:	**Theatre: Intermediate 3**					
S1	2	2	11521-1		Coffey, Daniel J.	B-21	0.500	30	4	26
							Course Total:	**30**	**4**	**26**
Course ID:	**11561**			Course Title:	**Theatre: Advanced 5**					
S1	2	2	11561-1		Coffey, Daniel J.	B-21	0.500	30	3	27
							Course Total:	**30**	**3**	**27**
Course ID:	**11861**			Course Title:	**2D Advanced Visual Arts: Capstone**					
S1	7	7	11861-2		Deland, Anthony	D-21	0.500	30	8	22
							Course Total:	**30**	**8**	**22**
Course ID:	**11921**			Course Title:	**Ceramics: Beginning 1**					
S1	1	1	11921-1		Deland, Anthony	D-31	0.500	35	23	12
	2	2	11921-2		Deland, Anthony	D-31	0.500	35	16	19
	5	5	11921-6		Deland, Anthony	D-31	0.500	35	12	23
	6	6	11921-3		Deland, Anthony	D-31	0.500	35	15	20
	8	8	11921-5		Deland, Anthony	D-31	0.500	35	10	25
							Course Total:	**175**	**76**	**99**
Course ID:	**11931**			Course Title:	**Ceramics: Intermediate 3**					
S1	1	1	11931-1		Deland, Anthony	D-31	0.500	40	9	31
	2	2	11931-2		Deland, Anthony	D-31	0.500	40	8	32
	5	5	11931-6		Deland, Anthony	D-31	0.500	40	5	35
	6	6	11931-3		Deland, Anthony	D-31	0.500	40	9	31
	8	8	11931-5		Deland, Anthony	D-31	0.500	40	9	31
							Course Total:	**200**	**40**	**160**
Course ID:	**1201A1**			Course Title:	**Spanish 1**					
S1	1	1	1201A1-1		Molina, Carlos	C-30	0.500	30	28	2
	3	3	1201A1-2		Molina, Carlos	C-30	0.500	35	30	5
							Course Total:	**65**	**58**	**7**
Course ID:	**1201B1**			Course Title:	**Spanish 3**					
S1	1	1	1201B1-1		Fretel, Pamela	C-29	0.500	30	20	10
	2	2	1201B1-2		Fretel, Pamela	C-29	0.500	30	21	9
	6	6	1201B1-3		Fretel, Pamela	C-29	0.500	30	22	8
							Course Total:	**90**	**63**	**27**
Course ID:	**1201C1**			Course Title:	**Spanish 5**					
S1	7	7	1201C1-1		Molina, Carlos	C-30	0.500	30	11	19
							Course Total:	**30**	**11**	**19**
Course ID:	**12121**			Course Title:	**Printmaking: Intermediate 3**					
S1	7	7	12121-1		Hargrave, Amy L.	D-22	0.500	30	8	22
							Course Total:	**30**	**8**	**22**
Course ID:	**1221C1**			Course Title:	**Mandarin/Chinese 5**					
S1	5	5	1221C1-KW05		Waltner, Kyoko W.	C-32	0.500	40	2	38
							Course Total:	**40**	**2**	**38**

Jefferson H.S.
Section List by Course and Term
For Term: Semester 1

Year: 2025-2026
Report: MST403

Term	Beg	End	Section ID	Staff Name	Room Name	Credit	Max	Total	Open
Course ID: **1221MA1**	Course Title: **Mandarin/Chinese Immersion 1**								
S1	5	5	1221MA1-1	Waltner, Kyoko W.	C-32	0.500	30	2	28
						Course Total:	**30**	**2**	**28**
Course ID: **1221MB1**	Course Title: **Mandarin/Chinese Immersion 3**								
S1	5	5	1221MB1-1	Waltner, Kyoko W.	C-32	0.500	30	1	29
						Course Total:	**30**	**1**	**29**
Course ID: **1223A1**	Course Title: **Japanese 1**								
S1	6	6	1223A1-1	Waltner, Kyoko W.	C-32	0.500	30	17	13
	8	8	1223A1-2	Waltner, Kyoko W.	C-32	0.500	30	9	21
						Course Total:	**60**	**26**	**34**
Course ID: **1223B1**	Course Title: **Japanese 3**								
S1	7	7	1223B1-1	Waltner, Kyoko W.	C-32	0.500	30	11	19
						Course Total:	**30**	**11**	**19**
Course ID: **1223C1**	Course Title: **Japanese 5**								
S1	7	7	1223C1-1	Waltner, Kyoko W.	C-32	0.500	30	2	28
						Course Total:	**30**	**2**	**28**
Course ID: **12301**	Course Title: **Graphic Design: Beginning 1**								
S1	3	3	12301-1	Hargrave, Amy L.	D-22	0.500	30	18	12
						Course Total:	**30**	**18**	**12**
Course ID: **12311**	Course Title: **Digital Media: Intermediate 3**								
S1	4	4	12311-1	Hargrave, Amy L.	C-22	0.500	32	28	4
	8	8	12311-2	Hargrave, Amy L.	C-22	0.500	32	5	27
						Course Total:	**64**	**33**	**31**
Course ID: **12491**	Course Title: **Design: Foundations 1**								
S1	1	1	12491-1	Hargrave, Amy L.	D-21	0.500	30	23	7
	2	2	12491-2	Hargrave, Amy L.	D-21	0.500	32	31	1
						Course Total:	**62**	**54**	**8**
Course ID: **14011**	Course Title: **Health 1**								
S1	5	5	14011-1	Thompson, Raeann S.	D-12	0.500	30	18	12
	6	6	14011-2	Thompson, Raeann S.	D-12	0.500	30	29	1
	8	8	14011-4	Thompson, Raeann S.	D-12	0.500	30	27	3
						Course Total:	**90**	**74**	**16**
Course ID: **15021**	Course Title: **Princ of Biomedical Science 1**								
S1	8	8	15021-1	Johnson, Jaydra	D-27	0.500	30	8	22
						Course Total:	**30**	**8**	**22**
Course ID: **1502BR1**	Course Title: **Biotechnology Research**								
S1	2	2	1502BR1-1	Burkhead, Gregory	D-35	0.500	30	14	16
						Course Total:	**30**	**14**	**16**
Course ID: **17101**	Course Title: **NGSS Biology 1**								
S1	2	2	17101-2	Altieri, Olive D.	D-09	0.500	30	11	19
	3	3	17101-3	Altieri, Olive D.	D-09	0.500	30	25	5
	4	4	17101-4	Altieri, Olive D.	D-09	0.500	30	20	10
	7	7	17101-5	Altieri, Olive D.	D-09	0.500	30	20	10
	8	8	17101-1	Altieri, Olive D.	D-09	0.500	30	19	11
						Course Total:	**150**	**95**	**55**

Jefferson H.S.
Section List by Course and Term
For Term: Semester 1

Year: 2025-2026
Report: MST403

Term	Beg	End	Section ID	Staff Name	Room Name	Credit	Max	Total	Open
Course ID:	**17131**		Course Title:	**Anatomy & Physiology 1: College**					
S1	1	1	17131-1	Altieri, Olive D.	D-09	0.500	35	22	13
						Course Total:	**35**	**22**	**13**
Course ID:	**17201**		Course Title:	**NGSS Chemistry 1**					
S1	4	4	17201-1	Burkhead, Gregory	D-35	0.500	30	25	5
	5	5	17201-2	Burkhead, Gregory	D-35	0.500	30	23	7
	7	7	17201-3	Burkhead, Gregory	D-35	0.500	30	22	8
	8	8	17201-4	Burkhead, Gregory	D-35	0.500	30	20	10
						Course Total:	**120**	**90**	**30**
Course ID:	**17301**		Course Title:	**Physics 1: NGSS**					
S1	1	1	17301-1	Napoli, Michael	D-08	0.500	30	23	7
	4	4	17301-2	Napoli, Michael	D-08	0.500	30	26	4
	5	5	17301-3	Napoli, Michael	D-08	0.500	30	30	0
	7	7	17301-4	Napoli, Michael	D-08	0.500	30	24	6
						Course Total:	**120**	**103**	**17**
Course ID:	**19021**		Course Title:	**Journalism**					
S1	6	6	19021-1	Coffey, Daniel J.	B-21	0.500	30	17	13
						Course Total:	**30**	**17**	**13**
Course ID:	**20311**		Course Title:	**Algebra 1**					
S1	3	3	20311-1	Fantz, Travis	C-38	0.500	30	26	4
	4	4	20311-2	Fantz, Travis	C-38	0.500	30	15	15
	5	5	20311-3	Fantz, Travis	C-38	0.500	30	24	6
	8	8	20311-4	Fantz, Travis	C-38	0.500	30	21	9
						Course Total:	**120**	**86**	**34**
Course ID:	**20341**		Course Title:	**Geometry 1**					
S1	2	2	20341-1	Schroth, Andrew	D-27	0.500	30	20	10
	3	3	20341-2	Schroth, Andrew	D-27	0.500	30	27	3
	4	4	20341-3	Schroth, Andrew	D-27	0.500	30	29	1
	5	5	20341-4	Schroth, Andrew	D-27	0.500	30	13	17
						Course Total:	**120**	**89**	**31**
Course ID:	**20411**		Course Title:	**Adv Algebra 3**					
S1	1	1	20411-4	Rutherford, Jacqueline	B-33	0.500	30	16	14
	2	2	20411-5	Rutherford, Jacqueline	B-33	0.500	30	22	8
	3	3	20411-1	Rutherford, Jacqueline	B-33	0.500	30	23	7
	5	5	20411-3	Rutherford, Jacqueline	B-33	0.500	30	24	6
	8	8	20411-2	Rutherford, Jacqueline	B-33	0.500	30	24	6
						Course Total:	**150**	**109**	**41**
Course ID:	**20531**		Course Title:	**Pre-Calculus 1**					
S1	2	2	20531-1	Ballman, Joseph R.	C-03	0.500	30	18	12
	4	4	20531-2	Ballman, Joseph R.	C-03	0.500	30	20	10
						Course Total:	**60**	**38**	**22**
Course ID:	**20551**		Course Title:	**Calculus 1**					
S1	6	6	20551-1	Rutherford, Jacqueline	B-33	0.500	30	15	15
						Course Total:	**30**	**15**	**15**

Jefferson H.S.
Section List by Course and Term
For Term: Semester 1

Year: 2025-2026
Report: MST403

Term	Beg	End	Section ID		Staff Name	Room Name	Credit	Max	Total	Open
Course ID:	**20791**		Course Title:	**Math in Society: College**						
S1	3	3	20791-1		Ballman, Joseph R.	C-03	0.500	35	21	14
	5	5	20791-2		Ballman, Joseph R.	C-03	0.500	35	23	12
	7	7	20791-3		Ballman, Joseph R.	C-03	0.500	35	17	18
							Course Total:	**105**	**61**	**44**
Course ID:	**23521**		Course Title:	**Mind and Body Intro 1**						
S1	1	1	23521-1		Smith, Lauren R.	B-09	0.500	40	20	20
	3	3	23521-LS03		Smith, Lauren R.	B-09	0.500	40	8	32
	6	6	23521-2		Smith, Lauren R.	B-09	0.500	40	24	16
	8	8	23521-3		Smith, Lauren R.	B-09	0.500	40	22	18
							Course Total:	**160**	**74**	**86**
Course ID:	**23531**		Course Title:	**Sports and Games Intro 1**						
S1	1	1	23531-2		Rindfusz, Laura L.	LGYM	0.500	40	20	20
	2	2	23531-1		Smith, Lauren R.	LGYM	0.500	40	36	4
	5	5	23531-4		Rindfusz, Laura L.	LGYM	0.500	40	25	15
	6	6	23531-3		Rindfusz, Laura L.	LGYM	0.500	40	19	21
							Course Total:	**160**	**100**	**60**
Course ID:	**23541**		Course Title:	**Strength & Conditioning Intro 1**						
S1	2	2	23541-1		Rindfusz, Laura L.	B-27	0.500	25	20	5
	3	3	23541-3		Rindfusz, Laura L.	B-27	0.500	25	21	4
	4	4	23541-2		Rindfusz, Laura L.	B-27	0.500	25	21	4
							Course Total:	**75**	**62**	**13**
Course ID:	**27071**		Course Title:	**Modern World History 1**						
S1	1	1	27071-1		Bulow, Annelies T.	C-14	0.500	30	19	11
	5	5	27071-2		Bulow, Annelies T.	C-14	0.500	30	30	0
	6	6	27071-5		Bulow, Annelies T.	C-14	0.500	30	30	0
	8	8	27071-4		Bulow, Annelies T.	C-14	0.500	30	24	6
							Course Total:	**120**	**103**	**17**
Course ID:	**27211**		Course Title:	**U.S. History**						
S1	2	2	27211-1		Griffin, Luke	D-26	0.500	33	32	1
	5	5	27211-2		Griffin, Luke	D-26	0.500	33	28	5
	7	7	27211-3		Griffin, Luke	D-26	0.500	33	31	2
							Course Total:	**99**	**91**	**8**
Course ID:	**2727ES1**		Course Title:	**Ethnic Studies 1**						
S1	8	8	2727ES1-1		Elliott, Susan B.	B-34	0.500	30	8	22
							Course Total:	**30**	**8**	**22**
Course ID:	**2730SN**		Course Title:	**Government: SR Inquiry**						
S1	3	3	2730SN-1		Shelton, Wendy A.	C-10	0.500	33	28	5
	4	4	2730SN-2		Shelton, Wendy A.	C-10	0.500	33	30	3
	5	5	2730SN-3		Shelton, Wendy A.	C-10	0.500	33	24	9
	6	6	2730SN-4		Shelton, Wendy A.	C-10	0.500	33	19	14
							Course Total:	**132**	**101**	**31**
Course ID:	**2801IXL1**		Course Title:	**IXL High School**						
S1	9	9	2801IXL1-AS09-1		Schroth, Andrew	D-27	0.000	40	15	25
							Course Total:	**40**	**15**	**25**

Jefferson H.S.
Section List by Course and Term
For Term: Semester 1

Year: 2025-2026
Report: MST403

Term	Beg	End	Section ID	Staff Name	Room Name	Credit	Max	Total	Open
Course ID: **2802IXL1**	Course Title: **Intervention IXL**								
S1	9	9	2802IXL1-MP09-1	Pesicek, Mindy	B-32	0.500	40	28	12
						Course Total:	**40**	**28**	**12**
Course ID: **2802L1**	Course Title: **Literacy Support**								
S1	9	9	2802L1-MP09-1	Pesicek, Mindy	B-32	0.500	40	28	12
						Course Total:	**40**	**28**	**12**
Course ID: **2802LC1**	Course Title: **Acad Skills/LC**								
S1	1	1	2802LC1-3	Pesicek, Mindy	B-32	0.500	20	7	13
	1	1	2802LC1-5	Kirk, Kevin	C-39	0.500	20	0	20
	1	1	2802LC1-1	Wellington, Cory R.	C-23	0.500	20	7	13
	6	6	2802LC1-2	Wellington, Cory R.	C-23	0.500	20	6	14
	6	6	2802LC1-6	Kirk, Kevin	C-39	0.500	20	7	13
	6	6	2802LC1-4	Pesicek, Mindy	B-32	0.500	20	9	11
						Course Total:	**120**	**36**	**84**
Course ID: **3061**	Course Title: **Early Dismissal**								
S1	7	7	3061-GG-1-1	Gregory, Garin S.		0.000	100	18	82
	8	8	3061-GG-1-2	Gregory, Garin S.		0.000	100	34	66
						Course Total:	**200**	**52**	**148**
Course ID: **3071**	Course Title: **Late Arrival**								
S1	1	1	3071-GG-1-1	Gregory, Garin S.		0.000	100	32	68
	2	2	3071-GG-1-2	Gregory, Garin S.		0.000	100	18	82
						Course Total:	**200**	**50**	**150**
Course ID: **401PCC3**	Course Title: **PCC Credit Hour = 3**								
S1	1	1	401PCC3-	Johnson, Jaydra		0.000	40	4	36
	2	2	401PCC3-JJ02	Johnson, Jaydra		0.000	40	3	37
	3	3	401PCC3-JJ03	Johnson, Jaydra		0.000	40	11	29
	4	4	401PCC3-JJ04	Johnson, Jaydra		0.000	40	3	37
	5	5	401PCC3-JJ05	Johnson, Jaydra		0.000	40	9	31
	6	6	401PCC3-JJ06	Johnson, Jaydra		0.000	40	11	29
	7	7	401PCC3-1	Johnson, Jaydra		0.000	60	17	43
	8	8	401PCC3-2	Johnson, Jaydra		0.000	60	11	49
						Course Total:	**360**	**69**	**291**
						Grand Total:	**7164**	**3167**	

Jefferson H.S.

Section List by Course and Term

For Term: Semester 1

Year: 2025-2026
Report: MST403

Term	Beg	End	Section ID		Staff Name	Room Name	Credit	Max	Total	Open
Course ID:	**0416CA1**			Course Title:	**Carpentry/Construct: Intro**					
S1	1	1	0416CA1-1		Teacher, Default Jefferson	D-04	0.500	30	0	30
	3	3	0416CA1-2		Teacher, Default Jefferson	D-04	0.500	30	0	30
							Course Total:	**60**	**0**	**60**
Course ID:	**0416CB1**			Course Title:	**Carpentry/Construct: Interm**					
S1	1	1	0416CB1-1		Teacher, Default Jefferson	D-04	0.500	30	0	30
	3	3	0416CB1-2		Teacher, Default Jefferson	D-04	0.500	30	0	30
							Course Total:	**60**	**0**	**60**
Course ID:	**0416CC1**			Course Title:	**Carpentry/Construct: Adv**					
S1	1	1	0416CC1-1		Teacher, Default Jefferson	D-04	0.500	30	0	30
	3	3	0416CC1-2		Teacher, Default Jefferson	D-04	0.500	30	0	30
							Course Total:	**60**	**0**	**60**
Course ID:	**0803VS**			Course Title:	**Virtual Scholars Online Course**					
S1	1	1	0803VS-SL01-1		Lynch, Shannon	B-38	0.000	40	1	39
	3	3	0803VS-NL03		Lipton, Nico A.	D-15	0.000	10	9	1
	4	4	0803VS-1		Lipton, Nico A.	D-15	0.000	10	12	-2
	5	5	0803VS-NL05		Lipton, Nico A.	D-15	0.000	10	3	7
	6	6	0803VS-2		Lipton, Nico A.	D-15	0.000	10	14	-4
	7	7	0803VS-NL07		Lipton, Nico A.	D-15	0.000	10	9	1
	8	8	0803VS-3		Lipton, Nico A.	D-15	0.000	10	9	1
							Course Total:	**100**	**57**	**43**
Course ID:	**08211**			Course Title:	**Teacher Aide**					
S1	7	7	08211-CW07		Wellington, Cory R.	C-23	0.500	40	1	39
							Course Total:	**40**	**1**	**39**

Jefferson H.S.
Section List by Course and Term
For Term: Semester 1

Year: 2025-2026
Report: MST403

Term	Beg	End	Section ID	Staff Name	Room Name	Credit	Max	Total	Open
Course ID: **08212**			Course Title: **Teacher Aide**						
S1	1	1	08212-SL01-1	Lynch, Shannon	B-38	0.500	40	1	39
	1	1	08212-LS01	Smith, Lauren R.	B-09	0.500	40	1	39
	1	1	08212-LR01	Rindfusz, Laura L.	B-27	0.500	40	2	38
	1	1	08212-AD01	Deland, Anthony	D-31	0.500	40	2	38
	2	2	08212-LR02-1	Rindfusz, Laura L.	B-27	0.500	40	2	38
	3	3	08212-LR03	Rindfusz, Laura L.	B-27	0.500	40	1	39
	3	3	08212-RB03	Lynch, Shannon	B-38	0.500	40	1	39
	3	3	08212-MM03	Lynch, Shannon	B-38	0.500	40	0	40
	3	3	08212-PF03-1	Fretel, Pamela	C-29	0.500	40	0	40
	3	3	08212-AS03-1	Schroth, Andrew	D-27		40	0	40
	4	4	08212-RN04	Lynch, Shannon	B-38	0.500	40	1	39
	4	4	08212-LR04-1	Rindfusz, Laura L.	B-27	0.500	40	1	39
	5	5	08212-LR05	Rindfusz, Laura L.	B-27	0.500	40	2	38
	5	5	08212-KW05	Waltner, Kyoko W.	C-32	0.500	40	1	39
	5	5	08212-AD05	Deland, Anthony	D-31	0.500	40	0	40
	5	5	08212-LM05	Morlock, Leigh	LIB	0.500	40	1	39
	6	6	08212-PF06	Fretel, Pamela	C-29	0.500	40	1	39
	6	6	08212-SG06-1	Gonzales, Steve R.	Dance	0.500	40	0	40
	6	6	08212-SL06	Lynch, Shannon	B-38	0.500	40	0	40
	6	6	08212-LR06	Rindfusz, Laura L.	B-27	0.500	40	1	39
	6	6	08212-RT06	Thompson, Raeann S.	D-12	0.500	40	1	39
	6	6	08212-JB06	Ballman, Joseph R.	C-03	0.500	40	0	40
	6	6	08212-JR06	Rutherford, Jacqueline	B-33	0.500	40	0	40
	7	7	08212-JJ07	Johnson, Jaydra	C-28	0.500	40	0	40
	7	7	08212-DIR07	Islam Roberts, Dejha	B-04	0.500	40	1	39
	7	7	08212-DHW07	Holden-Williams, Demetria	DUNG	0.500	40	1	39
	7	7	08212-DC07-1	Coffey, Daniel J.	B-21	0.500	40	2	38
	8	8	08212-DHW08	Holden-Williams, Demetria	DUNG	0.500	40	1	39
	8	8	08212-AH08	Hargrave, Amy L.	C-22	0.500	40	1	39
	8	8	08212-NB08	Brown, Niyah M.	B-04	0.500	40	1	39
	8	8	08212-MM08	Lynch, Shannon	B-38	0.500	40	3	37
	8	8	08212-OL08	Altieri, Olive D.	D-09	0.500	40	1	39
						Course Total:	**1280**	**30**	**1250**
Course ID: **08321**			Course Title: **9th Grade Success**						
S1	4	4	08321-3	Thompson, Raeann S.	D-12	0.500	33	26	7
	7	7	08321-4	Thompson, Raeann S.	D-12	0.500	33	18	15
	7	7	08321-1	Shelton, Wendy A.	C-10	0.500	33	19	14
	8	8	08321-2	Shelton, Wendy A.	C-10	0.500	33	32	1
						Course Total:	**132**	**95**	**37**
Course ID: **0841LG1**			Course Title: **Student Leadership/Government**						
S1	2	2	0841LG1-1	McKnight, Rebecca H.	C-04	0.500	35	24	11
						Course Total:	**35**	**24**	**11**

Jefferson H.S.
Section List by Course and Term
For Term: Semester 1

Year: 2025-2026
Report: MST403

Term	Beg	End	Section ID			Staff Name	Room Name	Credit	Max	Total	Open
Course ID:	**0862AVB1**			Course Title:	**AVID 10**						
S1	1	1	0862AVB1-1			Elliott, Susan B.	B-34	0.500	30	30	0
	6	6	0862AVB1-2			Griffin, Luke	D-26	0.500	30	26	4
	8	8	0862AVB1-3			Griffin, Luke	D-26	0.500	30	28	2
								Course Total:	**90**	**84**	**6**
Course ID:	**0862AVC1**			Course Title:	**AVID 11**						
S1	3	3	0862AVC1-3			Fretel, Pamela	C-37	0.500	32	24	8
	6	6	0862AVC1-2			Machuca, Eliana	C-37	0.500	32	16	16
	7	7	0862AVC1-1			Fretel, Pamela	C-37	0.500	32	27	5
	8	8	0862AVC1-4			Machuca, Eliana	C-37	0.500	32	18	14
								Course Total:	**128**	**85**	**43**
Course ID:	**0862AVD1**			Course Title:	**AVID 12**						
S1	1	1	0862AVD1-1			Machuca, Eliana	C-12	0.500	30	29	1
	2	2	0862AVD1-2			Machuca, Eliana	C-12	0.500	30	25	5
	5	5	0862AVD1-3			Machuca, Eliana	C-12	0.500	30	11	19
	7	7	0862AVD1-4			Machuca, Eliana	C-12	0.500	30	21	9
								Course Total:	**120**	**86**	**34**
Course ID:	**0899CW1**			Course Title:	**EL: Creative Writing 1**						
S1	1	1	0899CW1-1			Abel, Abigail K.	C-11	0.500	35	16	19
								Course Total:	**35**	**16**	**19**
Course ID:	**10011**			Course Title:	**English 1**						
S1	1	1	10011-1			Leahy, Dianne M.	C-13	0.500	30	20	10
	3	3	10011-2			Leahy, Dianne M.	C-13	0.500	30	29	1
	4	4	10011-3			Leahy, Dianne M.	C-13	0.500	30	24	6
	7	7	10011-4			Leahy, Dianne M.	C-13	0.500	30	24	6
								Course Total:	**120**	**97**	**23**
Course ID:	**10021**			Course Title:	**English 3**						
S1	3	3	10021-2			Coffey, Daniel J.	B-21	0.500	30	31	-1
	4	4	10021-3			Coffey, Daniel J.	B-21	0.500	30	28	2
	7	7	10021-1			Coffey, Daniel J.	B-21	0.500	30	25	5
								Course Total:	**90**	**84**	**6**
Course ID:	**1003RW1**			Course Title:	**Eng 5: Rdg/Writ 115**						
S1	2	2	1003RW1-1			Abel, Abigail K.	C-11	0.500	30	20	10
	4	4	1003RW1-2			Abel, Abigail K.	C-11	0.500	30	27	3
	5	5	1003RW1-3			Abel, Abigail K.	C-11	0.500	30	26	4
	6	6	1003RW1-4			Abel, Abigail K.	C-11	0.500	30	27	3
								Course Total:	**120**	**100**	**20**
Course ID:	**1004CL1**			Course Title:	**English 7:College Writing & Lit**						
S1	3	3	1004CL1-1			Tews, Nyki M.	C-31	0.500	33	26	7
	4	4	1004CL1-2			Tews, Nyki M.	C-31	0.500	33	26	7
	5	5	1004CL1-3			Tews, Nyki M.	C-31	0.500	33	23	10
	6	6	1004CL1-4			Tews, Nyki M.	C-31	0.500	33	26	7
								Course Total:	**132**	**101**	**31**

Jefferson H.S.
Section List by Course and Term
For Term: Semester 1

Year: 2025-2026
Report: MST403

Term	Beg	End	Section ID		Staff Name	Room Name	Credit	Max	Total	Open
Course ID:	**1061AEL1**		Course Title:	**Emerging ELD 1**						
S1	4	4	1061AEL1-1		Orellana, Jocelyn	B-14	0.500	30	9	21
							Course Total:	**30**	**9**	**21**
Course ID:	**1061DEL1**		Course Title:	**Progressing ELD 4**						
S1	9	9	1061DEL1-KY09		Yocum, Kate	B-14	0.500	40	21	19
							Course Total:	**40**	**21**	**19**
Course ID:	**1109BJD1**		Course Title:	**Jefferson Dancers II**						
S1	9	10	1109BJD1-		Holden-Williams, Demetria	DUNG	0.600	40	17	23
							Course Total:	**40**	**17**	**23**
Course ID:	**1109JD1**		Course Title:	**Jefferson Dancers I**						
S1	9	10	1109JD1-SG0910		Gonzales, Steve R.	DUNG	1.000	40	19	21
							Course Total:	**40**	**19**	**21**
Course ID:	**11121**		Course Title:	**Dance 1**						
S1	7	7	11121-1		Holden-Williams, Demetria	DUNG	0.500	30	18	12
	8	8	11121-2		Holden-Williams, Demetria	DUNG	0.500	30	23	7
							Course Total:	**60**	**41**	**19**
Course ID:	**1113BA1**		Course Title:	**Dance: 3 Ballet**						
S1	6	6	1113BA1-1		Gonzales, Steve R.	DUNG	0.500	30	9	21
							Course Total:	**30**	**9**	**21**
Course ID:	**1113H1**		Course Title:	**Dance: 3 Hip Hop**						
S1	6	6	1113H1-1		Holden-Williams, Demetria	DUNG	0.500	30	9	21
							Course Total:	**30**	**9**	**21**
Course ID:	**1113M1**		Course Title:	**Dance: 3 Modern**						
S1	5	5	1113M1-1		Smith, Lauren R.	DUNG	0.500	30	19	11
							Course Total:	**30**	**19**	**11**
Course ID:	**1114BA1**		Course Title:	**Dance 5: Ballet**						
S1	7	7	1114BA1-1		Gonzales, Steve R.	DUNG	0.500	30	14	16
							Course Total:	**30**	**14**	**16**
Course ID:	**1114J1**		Course Title:	**Dance 5: Jazz**						
S1	8	8	1114J1-1		Gonzales, Steve R.	DUNG	0.500	30	12	18
							Course Total:	**30**	**12**	**18**
Course ID:	**11221**		Course Title:	**Concert Band**						
S1	4	4	11221-1		Hester, Dave B.	BandRoom	0.500	30	9	21
							Course Total:	**30**	**9**	**21**
Course ID:	**11341**		Course Title:	**Percussion Ensemble**						
S1	2	2	11341-1		Hester, Dave B.	BandRoom	0.500	30	13	17
							Course Total:	**30**	**13**	**17**
Course ID:	**11401**		Course Title:	**Instrumental Music: Beginning Guitar**						
S1	7	7	11401-1		Hester, Dave B.	BandRoom	0.500	30	12	18
							Course Total:	**30**	**12**	**18**
Course ID:	**11421**		Course Title:	**Instrumental Music: Beginning Piano**						
S1	1	1	11421-1		Hester, Dave B.	BandRoom	0.500	30	5	25
	3	3	11421-2		Hester, Dave B.	BandRoom	0.500	30	21	9
							Course Total:	**60**	**26**	**34**

Jefferson H.S.
Section List by Course and Term
For Term: Semester 1

Year: 2025-2026
Report: MST403

Term	Beg	End	Section ID		Staff Name	Room Name	Credit	Max	Total	Open
Course ID:	**11501**			Course Title:	**Theatre: Beginning 1**					
S1	2	2	11501-1		Coffey, Daniel J.	B-21	0.500	30	19	11
							Course Total:	**30**	**19**	**11**
Course ID:	**11521**			Course Title:	**Theatre: Intermediate 3**					
S1	2	2	11521-1		Coffey, Daniel J.	B-21	0.500	30	4	26
							Course Total:	**30**	**4**	**26**
Course ID:	**11561**			Course Title:	**Theatre: Advanced 5**					
S1	2	2	11561-1		Coffey, Daniel J.	B-21	0.500	30	3	27
							Course Total:	**30**	**3**	**27**
Course ID:	**11861**			Course Title:	**2D Advanced Visual Arts: Capstone**					
S1	7	7	11861-2		Deland, Anthony	D-21	0.500	30	8	22
							Course Total:	**30**	**8**	**22**
Course ID:	**11921**			Course Title:	**Ceramics: Beginning 1**					
S1	1	1	11921-1		Deland, Anthony	D-31	0.500	35	23	12
	2	2	11921-2		Deland, Anthony	D-31	0.500	35	16	19
	5	5	11921-6		Deland, Anthony	D-31	0.500	35	12	23
	6	6	11921-3		Deland, Anthony	D-31	0.500	35	15	20
	8	8	11921-5		Deland, Anthony	D-31	0.500	35	10	25
							Course Total:	**175**	**76**	**99**
Course ID:	**11931**			Course Title:	**Ceramics: Intermediate 3**					
S1	1	1	11931-1		Deland, Anthony	D-31	0.500	40	9	31
	2	2	11931-2		Deland, Anthony	D-31	0.500	40	8	32
	5	5	11931-6		Deland, Anthony	D-31	0.500	40	5	35
	6	6	11931-3		Deland, Anthony	D-31	0.500	40	9	31
	8	8	11931-5		Deland, Anthony	D-31	0.500	40	9	31
							Course Total:	**200**	**40**	**160**
Course ID:	**1201A1**			Course Title:	**Spanish 1**					
S1	1	1	1201A1-1		Molina, Carlos	C-30	0.500	30	28	2
	3	3	1201A1-2		Molina, Carlos	C-30	0.500	35	30	5
							Course Total:	**65**	**58**	**7**
Course ID:	**1201B1**			Course Title:	**Spanish 3**					
S1	1	1	1201B1-1		Fretel, Pamela	C-29	0.500	30	20	10
	2	2	1201B1-2		Fretel, Pamela	C-29	0.500	30	21	9
	6	6	1201B1-3		Fretel, Pamela	C-29	0.500	30	22	8
							Course Total:	**90**	**63**	**27**
Course ID:	**1201C1**			Course Title:	**Spanish 5**					
S1	7	7	1201C1-1		Molina, Carlos	C-30	0.500	30	11	19
							Course Total:	**30**	**11**	**19**
Course ID:	**12121**			Course Title:	**Printmaking: Intermediate 3**					
S1	7	7	12121-1		Hargrave, Amy L.	D-22	0.500	30	8	22
							Course Total:	**30**	**8**	**22**
Course ID:	**1221C1**			Course Title:	**Mandarin/Chinese 5**					
S1	5	5	1221C1-KW05		Waltner, Kyoko W.	C-32	0.500	40	2	38
							Course Total:	**40**	**2**	**38**

Jefferson H.S.
Section List by Course and Term
For Term: Semester 1

Year: 2025-2026
Report: MST403

Term	Beg	End	Section ID		Staff Name	Room Name	Credit	Max	Total	Open
Course ID:	**1221MA1**		Course Title:	**Mandarin/Chinese Immersion 1**						
S1	5	5	1221MA1-1		Waltner, Kyoko W.	C-32	0.500	30	2	28
							Course Total:	**30**	**2**	**28**
Course ID:	**1221MB1**		Course Title:	**Mandarin/Chinese Immersion 3**						
S1	5	5	1221MB1-1		Waltner, Kyoko W.	C-32	0.500	30	1	29
							Course Total:	**30**	**1**	**29**
Course ID:	**1223A1**		Course Title:	**Japanese 1**						
S1	6	6	1223A1-1		Waltner, Kyoko W.	C-32	0.500	30	17	13
	8	8	1223A1-2		Waltner, Kyoko W.	C-32	0.500	30	9	21
							Course Total:	**60**	**26**	**34**
Course ID:	**1223B1**		Course Title:	**Japanese 3**						
S1	7	7	1223B1-1		Waltner, Kyoko W.	C-32	0.500	30	11	19
							Course Total:	**30**	**11**	**19**
Course ID:	**1223C1**		Course Title:	**Japanese 5**						
S1	7	7	1223C1-1		Waltner, Kyoko W.	C-32	0.500	30	2	28
							Course Total:	**30**	**2**	**28**
Course ID:	**12301**		Course Title:	**Graphic Design: Beginning 1**						
S1	3	3	12301-1		Hargrave, Amy L.	D-22	0.500	30	18	12
							Course Total:	**30**	**18**	**12**
Course ID:	**12311**		Course Title:	**Digital Media: Intermediate 3**						
S1	4	4	12311-1		Hargrave, Amy L.	C-22	0.500	32	28	4
	8	8	12311-2		Hargrave, Amy L.	C-22	0.500	32	5	27
							Course Total:	**64**	**33**	**31**
Course ID:	**12491**		Course Title:	**Design: Foundations 1**						
S1	1	1	12491-1		Hargrave, Amy L.	D-21	0.500	30	23	7
	2	2	12491-2		Hargrave, Amy L.	D-21	0.500	32	31	1
							Course Total:	**62**	**54**	**8**
Course ID:	**14011**		Course Title:	**Health 1**						
S1	5	5	14011-1		Thompson, Raeann S.	D-12	0.500	30	18	12
	6	6	14011-2		Thompson, Raeann S.	D-12	0.500	30	29	1
	8	8	14011-4		Thompson, Raeann S.	D-12	0.500	30	27	3
							Course Total:	**90**	**74**	**16**
Course ID:	**15021**		Course Title:	**Princ of Biomedical Science 1**						
S1	8	8	15021-1		Johnson, Jaydra	D-27	0.500	30	8	22
							Course Total:	**30**	**8**	**22**
Course ID:	**1502BR1**		Course Title:	**Biotechnology Research**						
S1	2	2	1502BR1-1		Burkhead, Gregory	D-35	0.500	30	14	16
							Course Total:	**30**	**14**	**16**
Course ID:	**17101**		Course Title:	**NGSS Biology 1**						
S1	2	2	17101-2		Altieri, Olive D.	D-09	0.500	30	11	19
	3	3	17101-3		Altieri, Olive D.	D-09	0.500	30	25	5
	4	4	17101-4		Altieri, Olive D.	D-09	0.500	30	20	10
	7	7	17101-5		Altieri, Olive D.	D-09	0.500	30	20	10
	8	8	17101-1		Altieri, Olive D.	D-09	0.500	30	19	11
							Course Total:	**150**	**95**	**55**

Jefferson H.S.
Section List by Course and Term
For Term: Semester 1

Year: 2025-2026
Report: MST403

Term	Beg	End	Section ID	Staff Name	Room Name	Credit	Max	Total	Open
Course ID: **17131**	Course Title: **Anatomy & Physiology 1: College**								
S1	1	1	17131-1	Altieri, Olive D.	D-09	0.500	35	22	13
						Course Total:	**35**	**22**	**13**
Course ID: **17201**	Course Title: **NGSS Chemistry 1**								
S1	4	4	17201-1	Burkhead, Gregory	D-35	0.500	30	25	5
	5	5	17201-2	Burkhead, Gregory	D-35	0.500	30	23	7
	7	7	17201-3	Burkhead, Gregory	D-35	0.500	30	22	8
	8	8	17201-4	Burkhead, Gregory	D-35	0.500	30	20	10
						Course Total:	**120**	**90**	**30**
Course ID: **17301**	Course Title: **Physics 1: NGSS**								
S1	1	1	17301-1	Napoli, Michael	D-08	0.500	30	23	7
	4	4	17301-2	Napoli, Michael	D-08	0.500	30	26	4
	5	5	17301-3	Napoli, Michael	D-08	0.500	30	30	0
	7	7	17301-4	Napoli, Michael	D-08	0.500	30	24	6
						Course Total:	**120**	**103**	**17**
Course ID: **19021**	Course Title: **Journalism**								
S1	6	6	19021-1	Coffey, Daniel J.	B-21	0.500	30	17	13
						Course Total:	**30**	**17**	**13**
Course ID: **20311**	Course Title: **Algebra 1**								
S1	3	3	20311-1	Fantz, Travis	C-38	0.500	30	26	4
	4	4	20311-2	Fantz, Travis	C-38	0.500	30	15	15
	5	5	20311-3	Fantz, Travis	C-38	0.500	30	24	6
	8	8	20311-4	Fantz, Travis	C-38	0.500	30	21	9
						Course Total:	**120**	**86**	**34**
Course ID: **20341**	Course Title: **Geometry 1**								
S1	2	2	20341-1	Schroth, Andrew	D-27	0.500	30	20	10
	3	3	20341-2	Schroth, Andrew	D-27	0.500	30	27	3
	4	4	20341-3	Schroth, Andrew	D-27	0.500	30	29	1
	5	5	20341-4	Schroth, Andrew	D-27	0.500	30	13	17
						Course Total:	**120**	**89**	**31**
Course ID: **20411**	Course Title: **Adv Algebra 3**								
S1	1	1	20411-4	Rutherford, Jacqueline	B-33	0.500	30	16	14
	2	2	20411-5	Rutherford, Jacqueline	B-33	0.500	30	22	8
	3	3	20411-1	Rutherford, Jacqueline	B-33	0.500	30	23	7
	5	5	20411-3	Rutherford, Jacqueline	B-33	0.500	30	24	6
	8	8	20411-2	Rutherford, Jacqueline	B-33	0.500	30	24	6
						Course Total:	**150**	**109**	**41**
Course ID: **20531**	Course Title: **Pre-Calculus 1**								
S1	2	2	20531-1	Ballman, Joseph R.	C-03	0.500	30	18	12
	4	4	20531-2	Ballman, Joseph R.	C-03	0.500	30	20	10
						Course Total:	**60**	**38**	**22**
Course ID: **20551**	Course Title: **Calculus 1**								
S1	6	6	20551-1	Rutherford, Jacqueline	B-33	0.500	30	15	15
						Course Total:	**30**	**15**	**15**

Jefferson H.S.
Section List by Course and Term
For Term: Semester 1

Year: 2025-2026
Report: MST403

Term	Beg	End	Section ID	Staff Name	Room Name	Credit	Max	Total	Open
Course ID: **20791**	Course Title: **Math in Society: College**								
S1	3	3	20791-1	Ballman, Joseph R.	C-03	0.500	35	21	14
	5	5	20791-2	Ballman, Joseph R.	C-03	0.500	35	23	12
	7	7	20791-3	Ballman, Joseph R.	C-03	0.500	35	17	18
						Course Total:	**105**	**61**	**44**
Course ID: **23521**	Course Title: **Mind and Body Intro 1**								
S1	1	1	23521-1	Smith, Lauren R.	B-09	0.500	40	20	20
	3	3	23521-LS03	Smith, Lauren R.	B-09	0.500	40	8	32
	6	6	23521-2	Smith, Lauren R.	B-09	0.500	40	24	16
	8	8	23521-3	Smith, Lauren R.	B-09	0.500	40	22	18
						Course Total:	**160**	**74**	**86**
Course ID: **23531**	Course Title: **Sports and Games Intro 1**								
S1	1	1	23531-2	Rindfusz, Laura L.	LGYM	0.500	40	20	20
	2	2	23531-1	Smith, Lauren R.	LGYM	0.500	40	36	4
	5	5	23531-4	Rindfusz, Laura L.	LGYM	0.500	40	25	15
	6	6	23531-3	Rindfusz, Laura L.	LGYM	0.500	40	19	21
						Course Total:	**160**	**100**	**60**
Course ID: **23541**	Course Title: **Strength & Conditioning Intro 1**								
S1	2	2	23541-1	Rindfusz, Laura L.	B-27	0.500	25	20	5
	3	3	23541-3	Rindfusz, Laura L.	B-27	0.500	25	21	4
	4	4	23541-2	Rindfusz, Laura L.	B-27	0.500	25	21	4
						Course Total:	**75**	**62**	**13**
Course ID: **27071**	Course Title: **Modern World History 1**								
S1	1	1	27071-1	Bulow, Annelies T.	C-14	0.500	30	19	11
	5	5	27071-2	Bulow, Annelies T.	C-14	0.500	30	30	0
	6	6	27071-5	Bulow, Annelies T.	C-14	0.500	30	30	0
	8	8	27071-4	Bulow, Annelies T.	C-14	0.500	30	24	6
						Course Total:	**120**	**103**	**17**
Course ID: **27211**	Course Title: **U.S. History**								
S1	2	2	27211-1	Griffin, Luke	D-26	0.500	33	32	1
	5	5	27211-2	Griffin, Luke	D-26	0.500	33	28	5
	7	7	27211-3	Griffin, Luke	D-26	0.500	33	31	2
						Course Total:	**99**	**91**	**8**
Course ID: **2727ES1**	Course Title: **Ethnic Studies 1**								
S1	8	8	2727ES1-1	Elliott, Susan B.	B-34	0.500	30	8	22
						Course Total:	**30**	**8**	**22**
Course ID: **2730SN**	Course Title: **Government: SR Inquiry**								
S1	3	3	2730SN-1	Shelton, Wendy A.	C-10	0.500	33	28	5
	4	4	2730SN-2	Shelton, Wendy A.	C-10	0.500	33	30	3
	5	5	2730SN-3	Shelton, Wendy A.	C-10	0.500	33	24	9
	6	6	2730SN-4	Shelton, Wendy A.	C-10	0.500	33	19	14
						Course Total:	**132**	**101**	**31**
Course ID: **2801IXL1**	Course Title: **IXL High School**								
S1	9	9	2801IXL1-AS09-1	Schroth, Andrew	D-27	0.000	40	15	25
						Course Total:	**40**	**15**	**25**

Jefferson H.S.
Section List by Course and Term
For Term: Semester 1

Year: 2025-2026
Report: MST403

Term	Beg	End	Section ID		Staff Name	Room Name	Credit	Max	Total	Open
Course ID:	**2802IXL1**			Course Title:	**Intervention IXL**					
S1	9	9	2802IXL1-MP09-1		Pesicek, Mindy	B-32	0.500	40	28	12
							Course Total:	**40**	**28**	**12**
Course ID:	**2802L1**			Course Title:	**Literacy Support**					
S1	9	9	2802L1-MP09-1		Pesicek, Mindy	B-32	0.500	40	28	12
							Course Total:	**40**	**28**	**12**
Course ID:	**2802LC1**			Course Title:	**Acad Skills/LC**					
S1	1	1	2802LC1-3		Pesicek, Mindy	B-32	0.500	20	7	13
	1	1	2802LC1-5		Kirk, Kevin	C-39	0.500	20	0	20
	1	1	2802LC1-1		Wellington, Cory R.	C-23	0.500	20	7	13
	6	6	2802LC1-2		Wellington, Cory R.	C-23	0.500	20	6	14
	6	6	2802LC1-6		Kirk, Kevin	C-39	0.500	20	7	13
	6	6	2802LC1-4		Pesicek, Mindy	B-32	0.500	20	9	11
							Course Total:	**120**	**36**	**84**
Course ID:	**3061**			Course Title:	**Early Dismissal**					
S1	7	7	3061-GG-1-1		Gregory, Garin S.		0.000	100	18	82
	8	8	3061-GG-1-2		Gregory, Garin S.		0.000	100	34	66
							Course Total:	**200**	**52**	**148**
Course ID:	**3071**			Course Title:	**Late Arrival**					
S1	1	1	3071-GG-1-1		Gregory, Garin S.		0.000	100	32	68
	2	2	3071-GG-1-2		Gregory, Garin S.		0.000	100	18	82
							Course Total:	**200**	**50**	**150**
Course ID:	**401PCC3**			Course Title:	**PCC Credit Hour = 3**					
S1	1	1	401PCC3-		Johnson, Jaydra		0.000	40	4	36
	2	2	401PCC3-JJ02		Johnson, Jaydra		0.000	40	3	37
	3	3	401PCC3-JJ03		Johnson, Jaydra		0.000	40	11	29
	4	4	401PCC3-JJ04		Johnson, Jaydra		0.000	40	3	37
	5	5	401PCC3-JJ05		Johnson, Jaydra		0.000	40	9	31
	6	6	401PCC3-JJ06		Johnson, Jaydra		0.000	40	11	29
	7	7	401PCC3-1		Johnson, Jaydra		0.000	60	17	43
	8	8	401PCC3-2		Johnson, Jaydra		0.000	60	11	49
							Course Total:	**360**	**69**	**291**
							Grand Total:	**7164**	**3167**	

Temporary Science labs:

FFE components

- Mobile lab tables on casters
- Lockable chemical storage carts
- Portable eyewash stations
- Rolling demonstration benches
- Plug-in lab equipment (hot plates, microscopes, etc.)

Pros

- Lower upfront cost
- Fast deployment
- Flexible use (science by period, general classroom otherwise)

Cons

- Limited plumbing and ventilation
- Not ideal for higher-risk chemistry
- Often restricted to biology, environmental science, physics demos

1. Fume Hood Strategy

Primary Recommendation: Ductless Filtered Fume Hoods

This is the industry standard for temporary high school labs.

Requirements to get approval:

- Hood is UL-listed and ASHRAE 110 tested
- Filters rated for:
    - General acids (HCl, H_2SO_4 diluted)
    - Bases
- Chemical list submitted in advance
- Written filter replacement and monitoring plan

Typical hood size

- 4 ft ductless hood (1 per room is usually sufficient)

Alternate (Only if ductless is rejected)

- Portable ducted hood exhausted through a window insert
- Requires:
    - Temporary permit
    - Make-up air acknowledgement
    - Fire Marshal sign-off

2. Chemical Use & Curriculum Controls

For temporary labs, reviewers expect curriculum reduction.

Allowed

- Dilute acids/bases
- Salt solutions
- Simple reactions
- Teacher demos inside hood

Typically prohibited

- Volatile organic solvents
- Open flame (Bunsen burners)
- Strong oxidizers
- Gas-generating reactions

This should be documented as a "Temporary Lab Chemical Scope".

3. Acid Waste Handling (FFE-Only)

- Poly waste containers with secondary containment
- Clearly labeled: "Acid Waste – Corrosive"
- Spill kit with acid neutralizer
- PPE station

Process

- Waste stored temporarily
- Picked up by district hazardous waste contractor
- OR transferred to permanent lab once operational

4. Emergency Equipment (Temporary-Compliant)

- Self-contained eyewash (15-minute)
- Fire extinguisher (ABC)
- Fire blanket
- First aid kit

- Spill response kit

  Safety showers are often waived in temporary labs if:
- Chemical quantities are limited
- Written justification is provided

5. Room & Furniture Setup

- Hard flooring (no carpet)
- Clear egress
- Lockable when not supervised
- Chemical-resistant lab tables
- Mobile teacher demo table
- Lockable chemical storage cabinets:
    - Acid cabinet (poly-lined)
    - Flammable cabinet (if applicable)

6. Ventilation Expectations (Without Construction)

- Ductless hood satisfies point-source control
- General room HVAC must:
    - Not recirculate hood exhaust
    - Maintain reasonable air turnover
- No return grilles directly above lab benches

Documentation That Makes This Pass Review

Prepare a Temporary Lab Safety Package:

1. Floor plan
2. Hood cut sheets
3. Chemical inventory (reduced)
4. Waste handling SOP
5. Emergency equipment list
6. Statement of temporary duration
7. Statement that permanent lab is under construction

What Districts Commonly Approve

In practice, districts often approve:

- 1 ductless hood
- Limited chemistry
- FFE-only eyewash
- Haz waste pickup
- No gas, no flame









Self-contained eyewash





Ductless fume hood

Phased Building Study

Early Occupation of First & Second Floors

Ed Spec

Classroom Utilization Tables Page 24
Based on 20-30 students per classroom

2025 100% SD
1700 students at 85% Utilization with Adjustments

	Total SF	/	SF/TS	=	TS	*	Util	*	Students Per Classroom Range		=	Student - low	Student - high	
General Classroom	34,300		950		40		85%	*	20	30		680	1,020	[39] General Classrooms + [1] ELL
Science	16,500		1,500		11		85%	*	20	30		187	281	[11] Science Labs
Specialized Instruction			*varies*		11		75%		20	30		165	248	[5] VAPA + [6] CTE
Dance			*2,000*		2		85%	**	20	30		34	51	[2] Dance Studios
PE/Athletics			*varies*		4		75%	***	20	30		60	90	[1] Main Gym, [1] Aux Gym, [1] Mat Rm, [1] Weight Rm
Special Education			*varies*		5		70%		15	24		53	84	[2] Int skills + [3] LRC
Small Instructional	5,000		1,250		4		0%		15	20		-	-	[4] Small Instruction
Total	**281,098**				**77**							**1,179**	**1,773**	

* Supported by [5] Teacher Collaboration rooms
** Added Dance Studios with 85% Utilization
*** Increased utilization to 75% due to support Aux Gym and Mat Room use for Dance

Early Occupation of First & Second Floors
770 students at 85% Utilization with Adjustments

	Total SF	/	SF/TS	=	TS	*	Util	*	Students Per Classroom Range		=	Student - low	Student - high	Includes:	Replaces:
General Classroom			950		15		85%	*	20	30		255	383	[16] General Classrooms	[1] VAPA****
Temporary Science			1,500		2		85%	*	20	30		34	51	[2] Temp Science "Labs" at full size	[1] CTE, [2] General Education
Temporary Science (Undersized)			1,100		2		85%	*	15	22	**	26	37	[2] Temp Science "Labs" at reduced size	[1] CTE, [1] Maker Space
Specialized Instruction			*varies*		8		75%		20	30		120	180	[4] VAPA + [4] CTE	
Dance			*2,000*		2		85%	*	20	30		34	51	[2] Dance Studios	
PE/Athletics			*varies*		4		35%	***	20	30		28	42	[1] Main Gym, [1] Aux Gym, [1] Mat Rm, [1] Weight Rm	
Special Education			*varies*		3		70%		15	24		32	50	[2] Int skills + [1] LRC	
Small Instructional			500		-		0%		15	20		-	-	No Small Instruction	
Total	**281,098**				**36**							**528**	**794**		

* Supported by [3] Teacher Collaboration rooms
** Reduced student capacity with reduced room size
*** Assume half utilization at 770 students for room qty sized for 1700 students
**** Assume JHS will continue to not offer Choir in 2028
