RESOLUTION No. 7188

Resolution Authorizing Amending of the Cleveland High School Modernization Revised Comprehensive Plan

RECITALS

A. The Board of Education adopted resolutions 6901 authorizing a Comprehensive Plan for the modernization of Cleveland High School.

B. The District has proposed revisions to the Cleveland High School Comprehensive Plan to, among other things, revise the size of the modernized school to approximately 297,000 square feet and to begin construction of the new building at the start of summer 2026, concluding in the end of summer of 2029. Those revisions were presented to the Facilities Improvement & Operations Committee on September 16th 2025.

RESOLUTION

1. The Board of Education authorizes a revised Cleveland High School Comprehensive Plan [as detailed on Exhibit A–or otherwise described somewhere definitive].

Exhibit A

mahlum STUDIO PETRETTI ARCHITECTURE

CHS Modernization Comprehensive Plan

Executive Summary Update

04 AUGUST 2025

Exhibit A

[This page intentionally left blank for the purpose of double-sided printing.]



Views from NE corner (SE Franklin and 28th Ave)

CLEVELAND HIGH SCHOOL MODERNIZATION

INTRODUCTION


This document summarizes the design changes that were implemented as a result of the PPS Board of Education Framework for Delivering Modernized High Schools with Cost Reductions, dated February 11, 2025. The purpose of this framework is to steward public dollars by making targeted cost reductions to the high school projects.

The design team is co-led by Mahlum Architects and Studio Petretti and supported by a team of experts. The reduced-cost proposal is a collaboration between the design team and Skanska USA Building Inc, the Construction Manager/General Contractor (CMGC) hired by PPS. Through in-depth analysis, coordination with District-provided standards, and a Design Advisory Group meeting, **the design team has developed a proposed recommendation for Cleveland high School that meets the vision and goals established in the Comprehensive Plan, which was adopted by the Board in May 2024, and the February 2025 Framework.**

Above: Schematic Design rendering of the Modernized Cleveland High School, as seen from SE 28th Avenue and SE Franklin Streets. Rendering depicts concept before the building size was reduced.

Below: Existing Cleveland High School



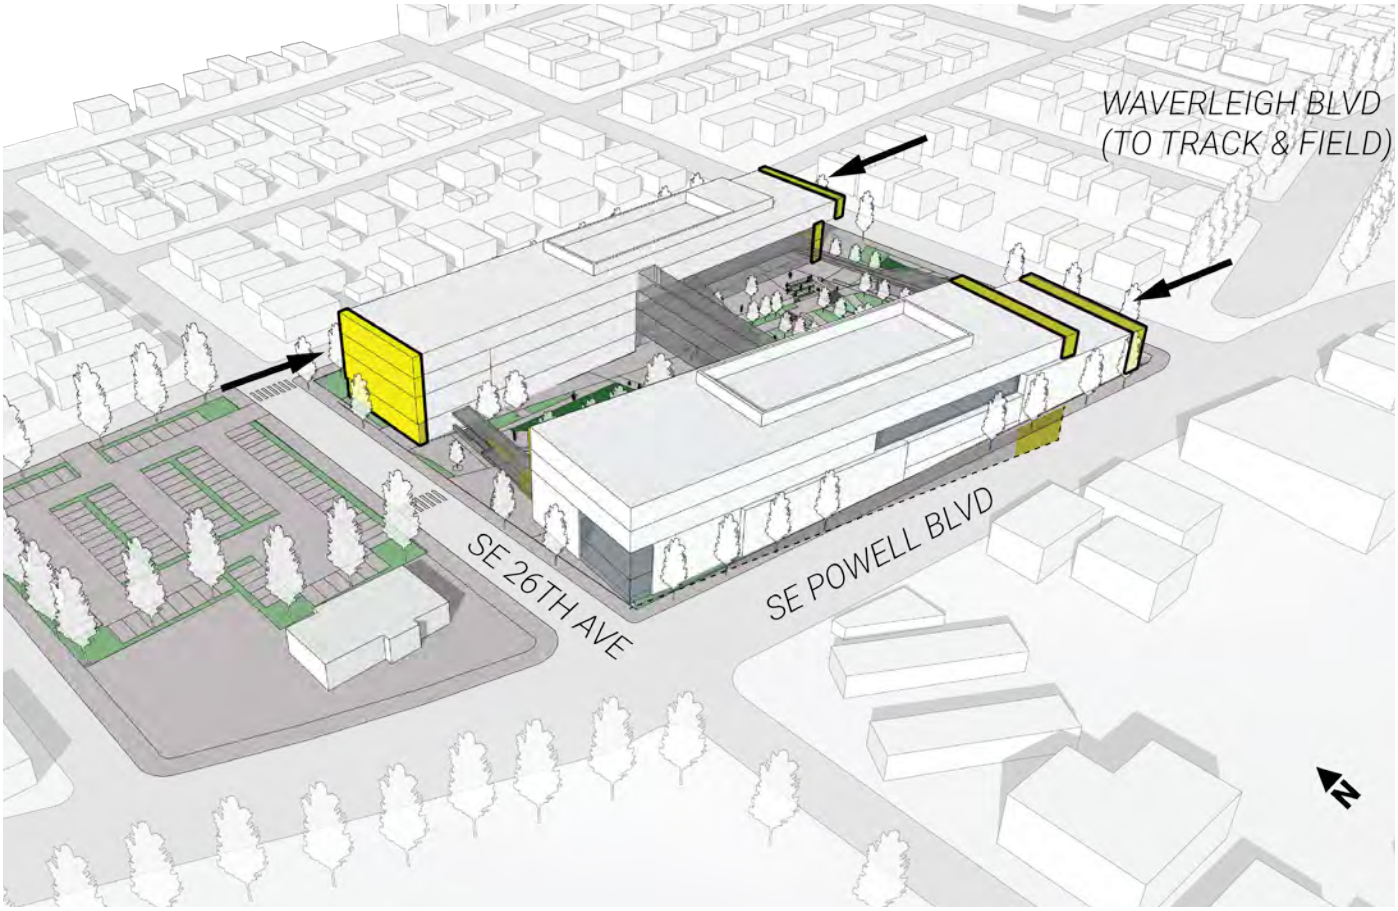

PROPOSED MODIFICATIONS

The following points summarize the major changes that are incorporated in the reduced-cost proposal:

> **Building Area:** The proposed building area has been reduced from 318,000sf to 297,000sf. The impacts of this change are:
  - 3 general education classrooms
  - 1 science room
  - Quantity of extended learning spaces
  - Size of athletic spaces
  - Size of performing arts spaces
  - Loading dock
  - Custodial / back-of-house / storage areas
  - Size of health clinic and teen parent center
  - Indoor track

> **Health Center:** The health center is included in the CHS project. Multnomah County, the current service provider, provided a Letter of Intent agreeing to continue operating the clinic at the modernized Cleveland facility and during the relocation to the Marshall campus during construction.

> **Teen Parent Center:** PPS program staff is in the process of providing data for the individual school community needs for services. This proposal includes a reduced-size center.

> **Electric infrastructure:** The design will maintain an all-electric infrastructure.

> **Equity in Contracting:** PPS Staff is working with the CMGC to create a procurement plan that maximizes certified business participation and minimizes additional costs.

> **Athletics:** The project will include the scope outlined in the 2024 Comprehensive Plan: Updated track and field, field house with hitting facility, grandstands, storage, practice field, and off-site softball and baseball fields. Changes include the size of the field house (number of team rooms) and configuration of storage facilities.

> **Climate Policy:** In addition to retaining the all-electric building infrastructure, the design team continues to optimize building systems and structure related to embodied carbon, durability and cost. PPS staff are exploring options other than LEED Gold Certification.

> **Basement construction:** The proposed design is integrated into the site, which slopes almost 20-feet between SE 26th Avenue and SE 28th Avenue. New basement construction has been reduced by 37%.

> **Additional Cost Reductions:** In addition to cost reductions identified in November 2024, the team continues to develop efficiencies in the building layout, systems, and materials. These include reduced excavation, structural revisions, facade (envelope) revisions, and reduced electrical service.

Exhibit A



The views on this spread show the proposed areas of reduction. Areas highlighted in yellow will be removed from the building volume.

SITE CONNECTIVITY

The Comprehensive Plan's site strategy will be maintained. The overall layout of the main site intentionally connects the three CHS properties. Visitors and staff will often arrive on the west side at the parking lot. The team will explore adding a mid-block crosswalk and enhancing the existing crossing at SE Franklin Street and SE 26th Avenue. A person approaching the school from the east will be able to visually orient themselves to the classroom wing and larger gathering areas (cafeteria, auditorium, gyms).

The auditorium and indoor PE/athletics spaces will have exit points on the east side of the block, near SE 28th Avenue and the start of Waverleigh Boulevard. This placement will encourage the visual and physical connections between the main property and the Cleveland Stadium property. The design proposal includes improvements to the crossings at SE 28th Avenue, SE 28th Place, SE 29th Avenue, and SE 31st Avenue.

The track property will maintain the current track location and better support athletes and events. An entry plaza, aligned with the Waverleigh Boulevard approach will greet people as they arrive. The existing stadium will be enhanced, adding restrooms and a new field house building that will house team rooms, storage, and a multi-purpose space. The remaining open areas on the west side of the track site will be improved to accommodate multiple athletic practices.

PPS is proposing a plan to Portland Parks and Recreation to make improvements to Powell Park and or Hosford Middle School, including adding a softball field.



Landscape site plan of the three parcels that form the Cleveland High School site. This image depicts concept before the building size was reduced.



Site Diagram



SCHOOL BUILDING

The proposed design is similar to the 2024 Comprehensive Plan. It organizes the school program into two main volumes: a classroom wing and a gymnasium/arts wing.

These two primary academic wings are connected by an elevated connector above the central courtyard. This configuration creates a large, secure outdoor courtyard at the heart of the school. The protected open space will serve several functions: main entry, event entry, and key student learning and social spaces.

The gym and theater are located along Powell Boulevard. With more noise, faster speeds and taller buildings, this location is a better location for these uses. These large volumes do not need many windows and could be designed with strategically placed glass walls that act as signifiers for the activities within. By contrast, the classroom wing will feature many smaller windows, each closer in scale to the residences that line SE Franklin and SE 28th streets.

The building will be optimized for solar orientation. Most windows will face north and south, where sun angles can be more easily addressed (compared to the east and west, where its angles are nearly horizontal). Windows to the north receive primarily diffused sunlight and require little shading or glare control. Windows to the south receive direct sunlight, which can be managed with exterior shading and blinds.

The entry level of the classroom wing will feature the student commons (cafeteria). Above this level, most of the rooms are smaller, regular-sized rooms, such as classrooms and offices. The classroom building is shown with a regular 30-foot by 35-foot grid. This rigorous layout is intentional, as it sets the proper framework for the use of mass timber construction in the north wing. The south wing, with its large volume spaces, is designed with a steel and concrete structure.

Major Anticipated Building Features:

- **297,000 gsf**
- **North Wing with Administration, Commons, Classrooms**
- **Connector**
- **South Wing with Athletics, Performing Arts & Labs**
- **Central Outdoor Gathering Courtyard**
- **All-electric infrastructure**

Powell Park Athletic Fields

Plans are in development to improve athletic fields at Powell Park currently used by PPS athletic programs. The design includes a multi-purpose field for baseball, soccer, and lacrosse, along with a new softball field adjacent to the east. These fields will have turf surfacing, field lighting, restrooms, concessions and storage for equipment.



PROGRAM SUMMARY


A building program summary is shown below. An expanded building program is available as a separate document.

PPS Comprehensive High School Area Program: COST REDUCTION OPTION 1 - 1700 Student Capacity (Meets Ed Spec)

SUMMARY

Recommended / Preferred / Optional	Recommended	Pref / Opp	S.F.
AREA	Quantity		S. F. Total
COMPREHENSIVE HIGH SCHOOL PROGRAM - TEACHING STATIONS			
General Education (Gen-Ed) Classrooms	41		46,315
Science Labs	11		16,145
Fine & Performing Arts (Drama, Theater)	6		26,940
Career Preparation/CTE	7		11,160
Athletics (incudes area for P.E. instruction)	4		36,480
Education Support			66,540
SPED	8		
ELL	1		
Sub-Total Recommended Teaching Stations	***78***		***201,580***
Community Partners			690
Wrap-Around Service Providers			4,055
Sub-Total			***4,745***
SUB-TOTAL COMPREHENSIVE HIGH SCHOOL REQUIRED AREA			***206,325***
Net to Gross Ratio	***43%***		
TOTAL COMPREHENSIVE HIGH SCHOOL (1,700 Students)			***297,017***

PROPOSED SCHEDULE

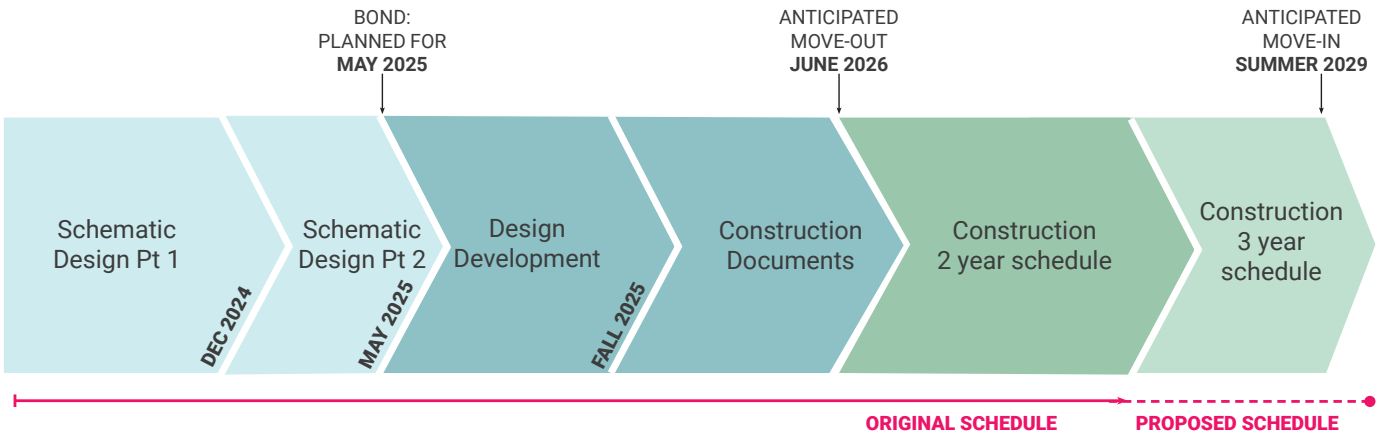

*TIMELINE IS DEPENDENT ON CONSTRUCTION SCHEDULE AND SCHOOL BOARD DIRECTIVES

As part of the November 2024 cost reductions, the project team made the recommendation to change the construction schedule from 2-years to 3-years. Due to the site constraints and restrictions on construction logistics, it would be too expensive to complete construction in 2 years. Construction worker overtime hours would significantly increase costs and safety risks.

The project team is studying ways that the stadium improvements and field improvements for baseball and softball can be completed before the main building.

COST SUMMARY

The revised overall project budget is based on hard cost savings accomplished during the Cost Reduction Study, additional related design fees, and a re-evaluation of owner cost items.

CHS Project Budget - Comprehenisve Plan Update

		2024	2025
COMPONENT	**COMMENTS**	**BOE APPROVED COMPREHENSIVE PLAN**	**REVISED COMPREHENSIVE PLAN**
Hard Cost	Building & Site Work 2025: Includes actuals paid-to-date to CM/GC	$ 377,654,178	$ 364,284,431
1.5% Green Energy Tech		$ 5,664,813	$5,529,547
Subtotal		**$ 383,318,991**	**$ 369,813,978**
Owner Direct Hard Costs	Off site improvements, utility costs not included above	**$ 1,650,000**	**$ 1,200,000**
TOTAL HARD COSTS		**$ 384,968,991**	**$ 371,013,978**
Soft Costs	Approx. 9.3% of Hard Costs	$ 33,155,000	$ 34,580,000
Fixtures, Furniture & Equipment, including technology	Approx. $34/SF	$ 8,700,000	$ 10,000,000
Moves / Swing Space / Temp Facilities	Budget increase for Marshall Improvements	$500,000	$1,500,000
Contingency	10% of Total Costs (additional 5% CM/GC contingency included in Hard Cost Estimate)	$ 41,320,859	$ 40,459,782
Escalation	Included in Hard & Soft Costs		
ON SITE PROJECT BUDGET		**$ 468,644,850**	**$ 457,553,760**
SAVINGS FROM 2024 DESIGN			**$(11,091,090)**
OFF SITE ATHLETIC FIELDS	Work may include fields at Powell park and/or Hosford MS		$ 15,000,000
TOTAL PROJECT BUDGET	CHS Modernization + Off Site Fields		$ 472,553,760
